



Pattonville Prop S - Phase 1 Construction Update

September 2023


Monthly Construction Update

Upcoming Highlights September 2023

- Holman CMU Walls and MEP Wall and Above Ceiling Rough in Locker Room Area
- Holman Site Utilities and Concrete Foundations for Gym B Addition
- Parkwood Concrete Foundations for Storm Shelter Addition and Site Plumbing
- Parkwood New Administration Suite Renovations Completed
- Parkwood New Secure Vestibule Turnover
- Willow Brook Shoring & Concrete Foundations for Storm Shelter Addition
- Willow Brook Secure Vestibule Renovation
- Bridgeway Stage Addition CMU Walls
- Bridgeway Concrete Foundations for Storm Shelter Addition and Site Plumbing



Construction Activity: Holman - CMU Partitions & MEP Rough in Locker Area

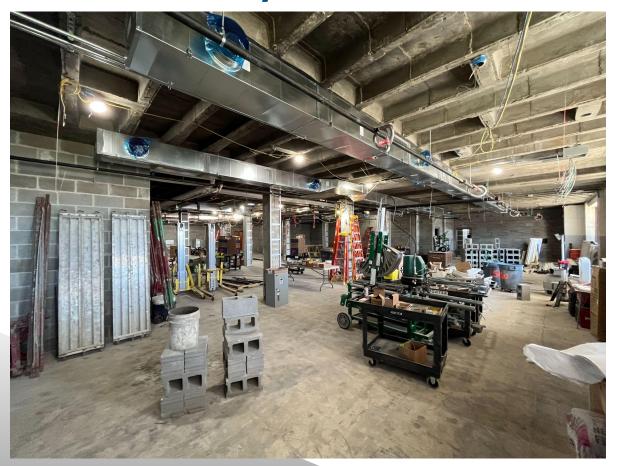





Construction Activity: Holman - Site Plumbing and Foundations









Construction Activity: Parkwood - Storm Shelter Concrete Foundations










Construction Activity: Parkwood - New Administration Suite



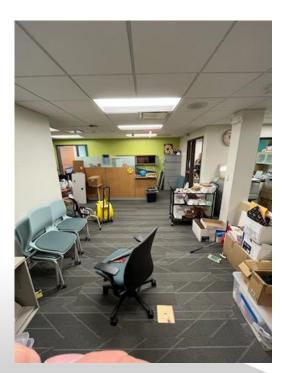









Construction Activity: Parkwood - New Vestibule at Front Entrance

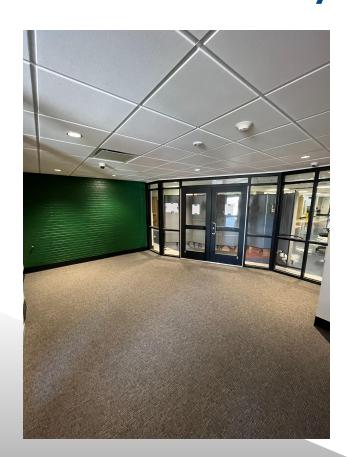

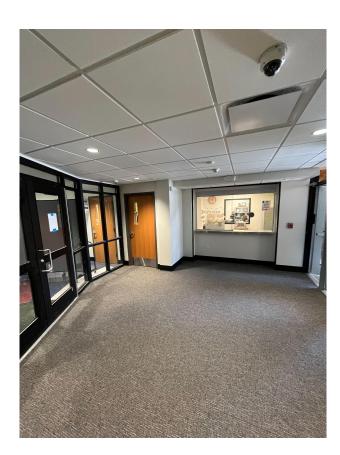





Construction Activity: Willow Brook - Shoring for Storm Shelter Addition









Construction Activity: Willow Brook - Phase 1 Interior Renovation












Construction Activity: Bridgeway - Stage Addition Foundations & Openings

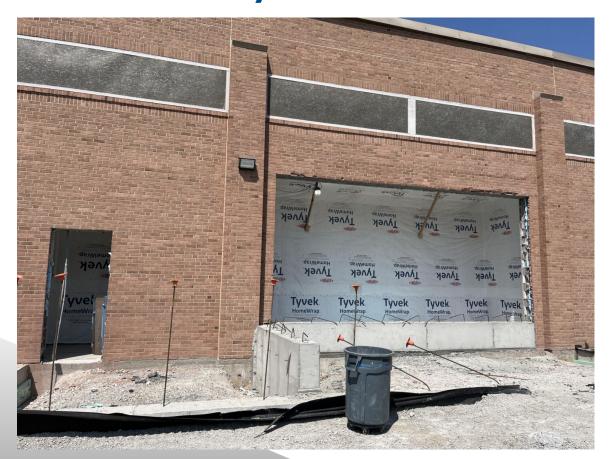





Construction Activity: Bridgeway - Storm Shelter Foundations and Site Plumbing










Pattonville School District - Phase 1 Budget Dashboard:


Thru August Billing 2023

Owner Allowances



Owner Allowances: \$896,199 Used to date: \$284,192

GMP Value Billed to Date



GMP Total: \$39,165,341 Billed to date: \$8,959,023

