



Pattonville Prop S – Phase 1 Construction Update

June 2023

Monthly Construction Update

Upcoming Highlights June 2023

- Holman - Relocate existing condensing units for new elevator for Gym B
- Holman - Continue site selective demolition and new site utilities for Gym B addition
- Holman - Continue selective interior demo at existing locker & fitness center
- Willow Brook - Continue fire sprinkler upgrades to existing school
- Willow Brook - Sitework mobilization & site utilities for addition
- Willow Brook - Begin selective demolition in existing school for renovations
- Parkwood - Sitework mobilization, site selective demolition, & site utilities for new addition
- Parkwood - Selective demolition in Administration renovation area
- Bridgeway - Continue fire sprinkler upgrades to existing school
- Bridgeway - Sitework mobilization, site selective demolition, & site utilities for new addition

Construction Activity: Holman – Demolition in Lower Lockers Area



Construction Activity: *Holman - Asbestos Abatement in Lower Lockers*



Construction Activity: Willow Brook - Fire Sprinkler Main in Corridors



Construction Activity: Willow Brook - *Site Mobilization for new Addition*



Construction Activity: Parkwood - Selective Demolition in Admin Offices



Construction Activity: Parkwood - Site Demolition for Storm Shelter Addition



Construction Activity: *Bridgeway - Fire Sprinkler Installation in Classrooms*



Construction Activity: *Bridgeway - Storm Shelter Layout & Site Mobilization*



Pattonville School District – Phase 1


Budget Dashboard:

Thru May Billing 2023

Owner Allowances

District Allowances


● Available ● Used to Date

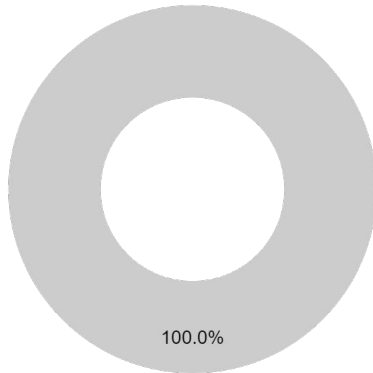

Owner Allowances: \$896,199
Used to date: \$0

GMP Value Billed to Date

Billed To Date
6.2%

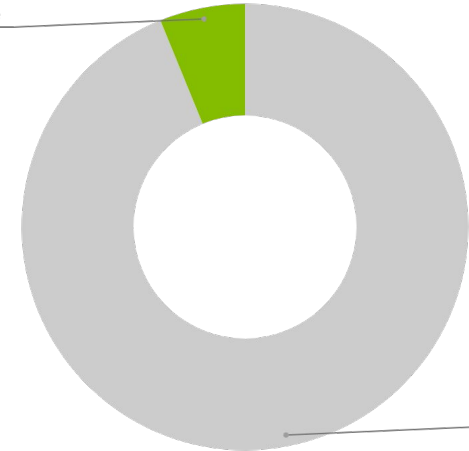

GMP Total: \$39,165,341
Billed to date: \$2,427,372
