


Measure BB Bond

21st Century Classroom Improvements


May 9, 2024



CUMMING
GROUP



HLPUSD MEASURE BB - SUMMARY

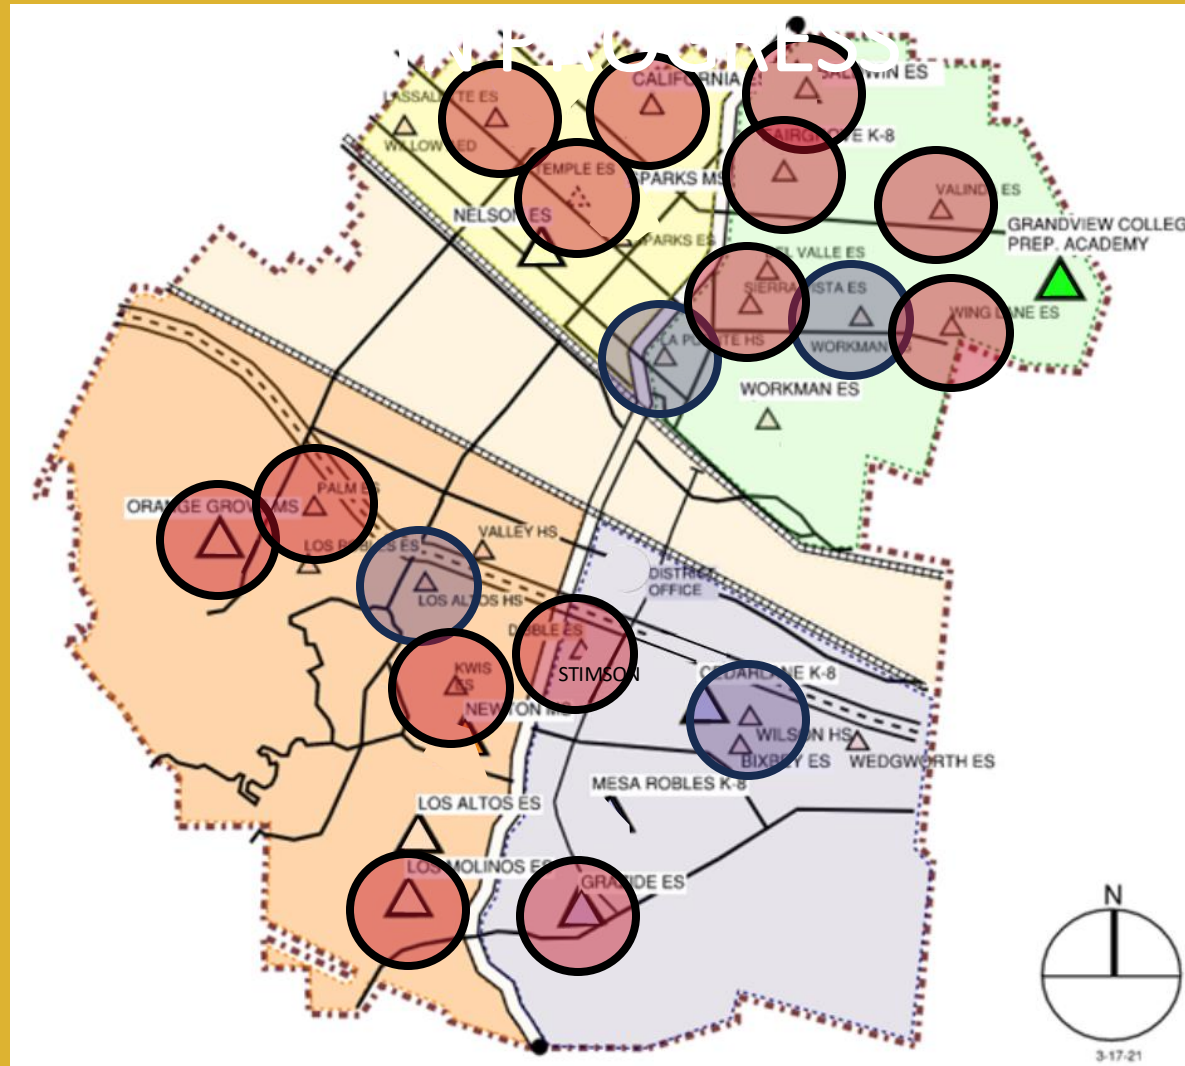

IN PROGRESS CONSTRUCTION

- La Puente HS
- Workman HS
- Los Altos HS
- Wilson HS
- Stimson EC

PREP FOR BID

- California ES
- Baldwin ES

AT DSA FOR REVIEW

- Los Molinos ES
- Graziade ES

IN DESIGN

- Kwis ES
- Lassalette ES
- Fairgrove K-8
- Orange Grove MS
- Sierra Vista MS
- Palm ES
- Valinda ES
- Sparks ES
- Wing Lane ES

IN DESIGN PROPOSAL PHASE

- Valley Alternative

COMPLETED

- Nelson ES
- Los Altos ES
- Workman ES
- Mesa Robles K-8
- Cedarlane K-8
- Sparks MS
- Newton MS
- Grandview K-8

PHASE B PROGRESS

- 1. Baldwin ES Construction Documents to DSA 1/23/2024 Back-Check with DSA 4/29/2024
- 2. California ES Construction Documents to DSA 1/23/2024 Back-Check with DSA 5/6/2024

Anticipated Construction Start Fall of 2024

- 3. Los Molinos ES Construction Documents at DSA 3/12/2024 Anticipated Plan Check Completion TBD
- 4. Grazide ES Construction Documents at DSA 3/12/2024 DSA Plan Check Returned 4/18/2024

Anticipated Construction Start Winter of 2024

- 5. Kwis ES Construction Documents Design Development
- 6. Lassalette ES Construction Documents Design Development

Anticipated Construction Start New Year of 2025

- 7. Palm ES Construction Documents Schematic Design
- 8. Valinda ES Construction Documents Schematic Design

Anticipated Construction Start Spring of 2025

- 9. Fairgrove K-8 Construction Documents Design Development
- 10. Orange Grove MS Construction Documents Schematic Design

Anticipated Construction Start Summer of 2025

- 11. Sierra Vista Construction Documents Design Contract Awarded
- 12. Sparks ES Construction Documents Design Contract Awarded

Anticipated Construction Start Summer -Fall of 2025


- 13. Wing Lane ES Construction Documents Design Contract Awarded
- 14. Valley Alternative Construction Documents Design Proposal

Anticipated Construction Start Fall of 2025




HIGH SCHOOL
REFRESH
PROJECTS

HIGH SCHOOL REFRESH GROUP 1

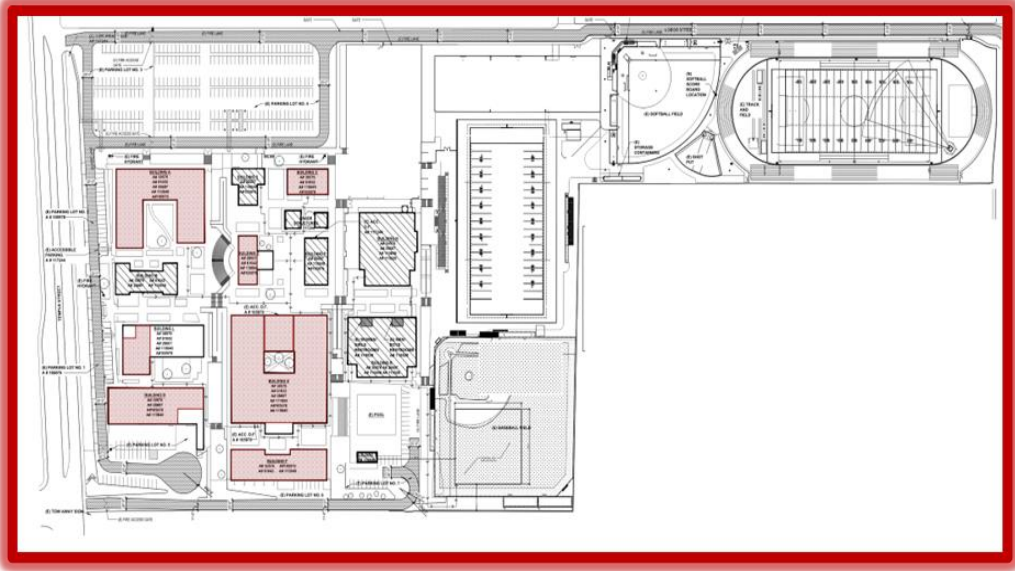

WORKMAN HIGH SCHOOL

43 CLASSROOMS

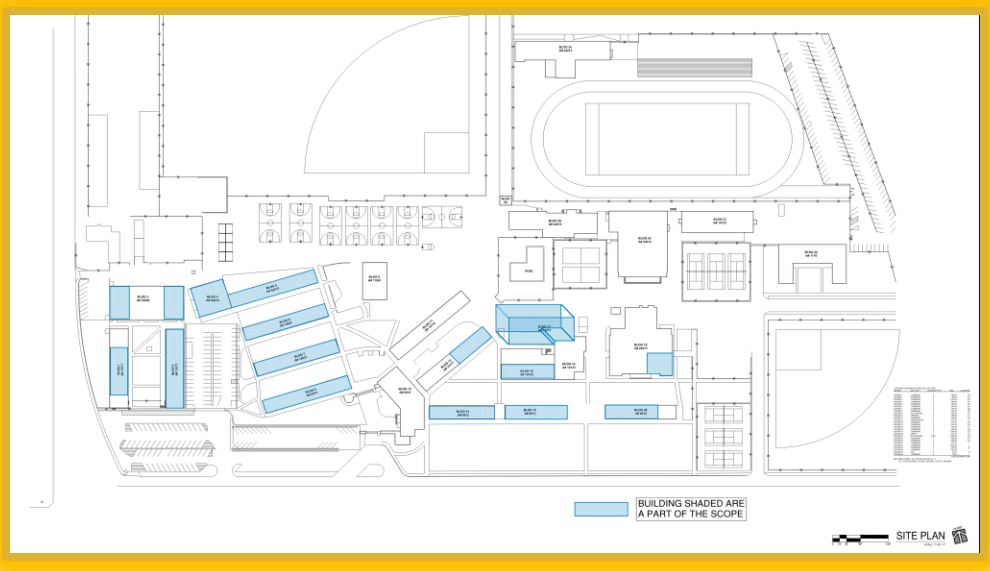

LA PUENTE HIGH SCHOOL

55 CLASSROOMS

SCHOOL	START DATE	ANTICIPATED COMPLETION DATE
WORKMAN HS	1/16/2024	11/1/2024
LA PUENTE HS	1/16/2024	11/1/2024
WILSON HS	3/4/2024	2/21/2025
LOS ALTOS HS	3/4/2024	4/18/2025


REFRESH GROUP 1
Workman Classroom
Phase 2: Punch List Pending




Room A-20




HIGH SCHOOL REFRESH GROUP 2

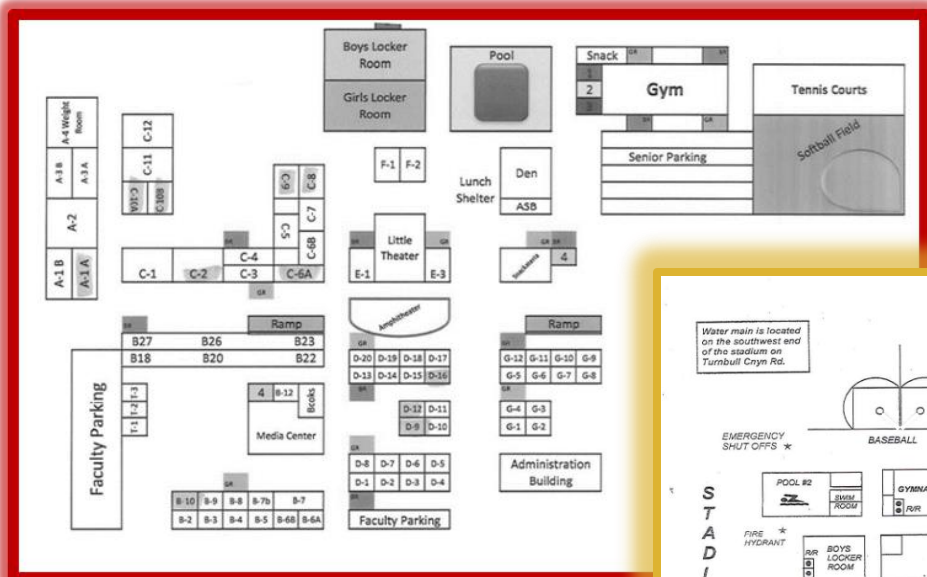

WILSON HIGH SCHOOL
59 CLASSROOMS

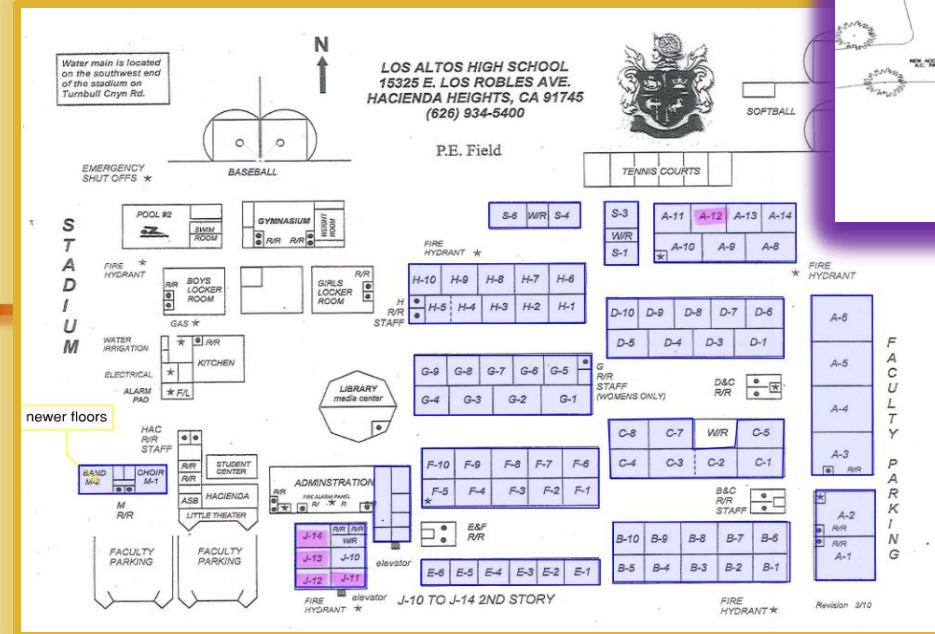

LOS ALTOS HIGH SCHOOL
69 CLASSROOMS

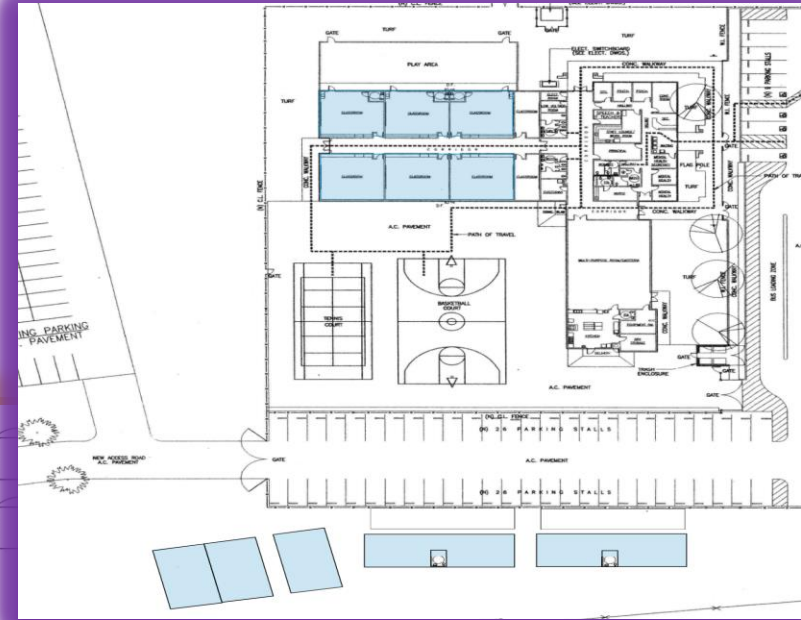

STIMSON LEARNING CENTER
10 CLASSROOMS

REFRESH GROUP 2



REFRESH GROUP 2

Los Altos HS Phase 1
Classroom B-4. Before and
During Demo




C.B.O.C. SITE TOUR

“Thank you for taking the time for the site visit on Tuesday at Grandview and La Puente High School. As an educator who’s seen many, many classrooms, **the upgrades, especially the floors and walls, look fantastic!** I was also thrilled to hear that my 9th grade daughter’s 1st period classroom at Wilson High School will be getting the same treatment.

Positive learning environments can make a big difference. I believe these upgrades will give instruction a real edge by fostering a more positive atmosphere for students and teachers alike.”

Jason Hinojosa, C.B.O.C.

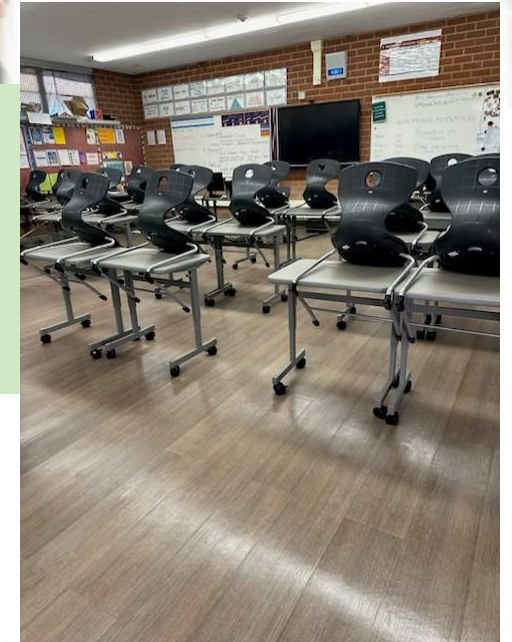

Grandview College Prep Academy

La Puente High School



QUESTIONS & ANSWERS
