




# Mary E. Britton Middle School

## ➤ **Completed Work:**

- Complete Structural Steel and Decking at Storm Shelter (Inspected 5/8/24)
- Complete Load Bearing CMU All Areas
- Complete Handrails at Area A and Area C Platform
- Continuing Brick Veneer at Cafeteria, Kitchen and Gym Entrance/Dock
- Continuing CMU Plumbing walls area C
- Grinding Floors for Terrazzo Area A First Floor
- Installing Restroom Tile (Approved Mock Room on 5/6/24)
- Installing ACM Panel Area F at Locker Room

## ➤ **Upcoming Work/Look Ahead:**

- Pour Storm Shelter Roof (5/16/24)
- Continue Interior CMU and Brick Veneer
- Finish Joist and Decking at E Area and Structural Steel at Gym Entrance
- Roofing at B and D Area starting 5/13/24
- Standing Seam Roofing starting 5/20/24 Area A
- Continue Exterior Framing
- Continue Sheetrock Area A Second Floor
- Start Priming and first coat of classrooms at Area A
- Continue MEP and Sprinkler Rough Ins

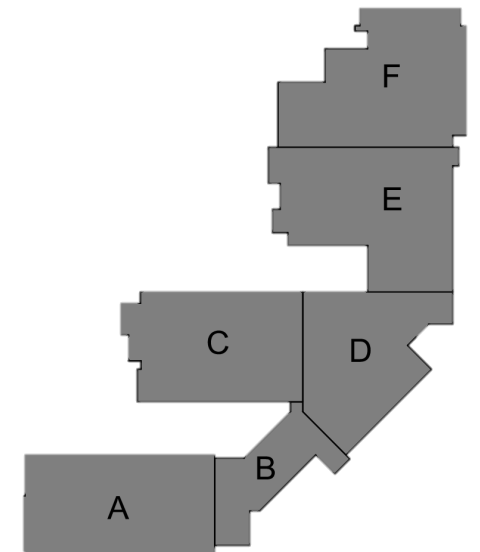



# Mary E. Britton Middle School

Area A – Blockfill Complete in Corridor



Week Ending May 10, 2024

# Mary E. Britton Middle School



## Area C – Metal Framing at Penthouse



Week Ending May 10, 2024



# Mary E. Britton Middle School



## Area C – Penthouse Railings Complete



Week Ending May 10, 2024

# Mary E. Britton Middle School

Area E – Blockfill has started in Kitchen and Cafeteria



Week Ending May 10, 2024

# Mary E. Britton Middle School



## Area E – Storm Shelter Roof Decking Installed



Week Ending May 10, 2024



# Mary E. Britton Middle School



Area F – ACM Panels Started at Gym



Week Ending May 10, 2024

# Mary E. Britton Middle School



Area F – Brick Continuing around Kitchen



Week Ending May 10, 2024



# Mary E. Britton Middle School



## Area F – Canopy Framing



Week Ending May 10, 2024
