

PROJECT STATUS UPDATE

Farmington Public Schools

Bid Package # 10

2020 Bond Issue – New Central Office Renovations

New Central Office

Project Description:


This project includes interior renovations of the old Visions Unlimited building, in order to provide a new space for the Central Office.



New Central Office

Project Overview:

- Demolition of the existing exterior ramp near the meeting room has begun.

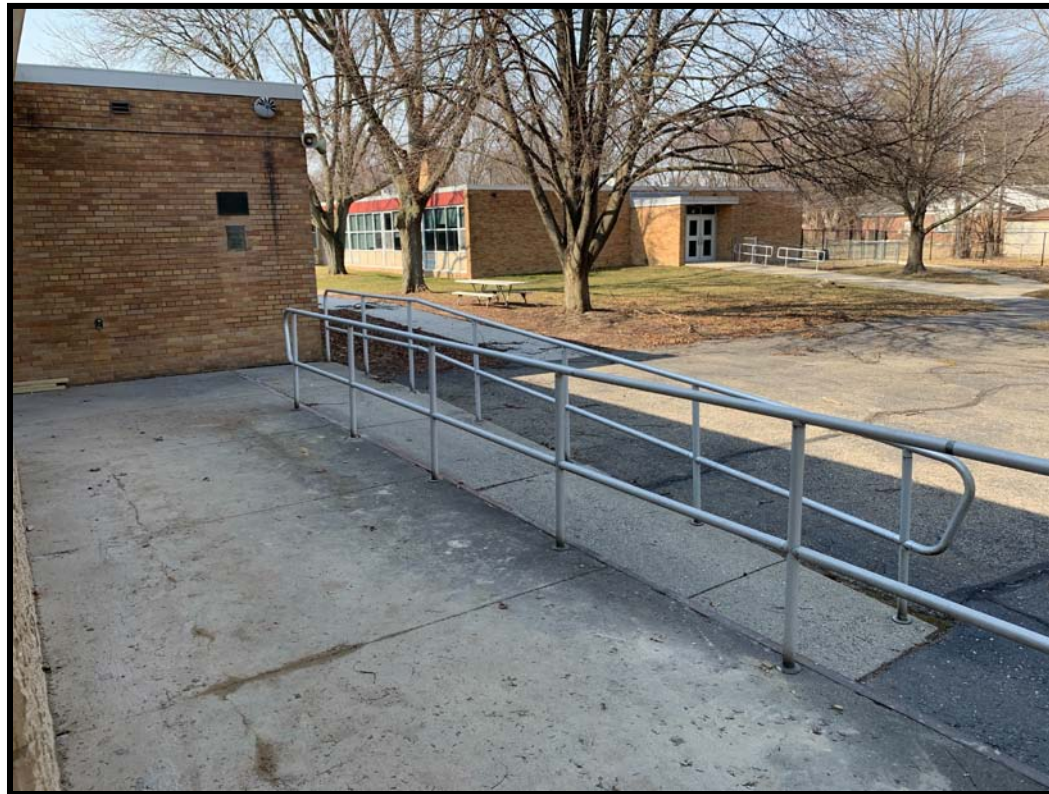

New Central Office

Project Overview:

- Installation of new HVAC units is ongoing throughout the building.



New Central Office

Project Overview:

- Sound dampening drywall installation is ongoing for the new office areas.




New Central Office

Project Overview:

- The boiler room floor has been primed and painted with new epoxy paint.



New Central Office – Look Ahead Schedule

		Farmington Public Schools Bid Pack 10: New Central Offices																								Period Start: 3/4/2024	
		3-WEEK LOOK-AHEAD SCHEDULE																								Period End: 3/10/2024	
		Prepared By: Jeff Robinette																								Page: 1 of 1	
Activity Description	Contractor	Scheduled Start	Week 1 3/4/2024							Week 2 3/11/2024							Week 3 3/18/2024							Scheduled Finish	Remarks		
			4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24				
			M	T	W	Th	F	S	S	M	T	W	Th	F	S	S	M	T	W	Th	F	S	S				
New Central Office																											
Drywall: 1-sided	AAC & P	2/26/24	X	X																					3/5/24		
Framing/Drywall - Back Side of Ext ERP Panels	AAC & P	3/4/24	X	X	X	X	X			X	X														3/12/24		
HVAC Piping	Gee Missler	1/29/24			X	X	X			X	X	X	X	X											3/15/24	Location of RWP required for complete installation - RFI 9.	
Pull Wiring to New Panels	Max Elec	3/4/24	X	X	X	X	X			X	X	X	X	X											3/15/24		
Electrical Power/Land Wiring	Max Elec	2/19/24	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				3/22/24		
Unit Vent/Radiant Wall Panel Install	Gee Missler	3/4/24										X	X	X			X	X	X	X	X				3/15/24	Location of RWP required for complete installation - RFI 9. Need Bulletin for	
Drywall: 2nd Side	AAC & P	3/13/24										X	X	X			X	X							3/19/24		
Mud/Tape/Finish Drywall	AAC & P	3/11/24								X	X	X	X	X			X	X	X	X	X				3/27/24		
Site Concrete	Midtown Group	3/11/24								X	X	X	X	X											3/15/24		
Overhead Ductwork	Gee Missler	3/18/24															X	X	X	X	X				3/29/24		
Roofing: Remove and Replace	Superior Services	3/18/24															X	X	X	X	X				4/12/24		
Prime/Paint: New Office Walls	Trio Paint/Tile	3/25/24																							3/29/24		
Acoustical Ceiling Grid	AAC & P	3/27/24																							4/5/24		
Ceiling Tile: Perimeter Cuts	AAC & P	4/3/24																							4/12/24		
Drop Office Lighting	Max Elec	4/1/24																							4/19/24		
Mechanical Diffusers, Grilles	Gee Missler	4/1/24																							4/12/24		
Flooring	Cohns	4/8/24																							4/26/24		
