

PROJECT STATUS UPDATE

Farmington Public Schools

Bid Package # 9

2020 Bond Issue – Beechview & Kenbrook Elementary



Beechview & Kenbrook – Project Description

Project Description:

This project involves selective interior architectural, mechanical, electrical, and plumbing renovations to the existing Beechview and Kenbrook elementary schools. As well as, exterior playground equipment replacement.



Beechview Elementary

Project Overview:


Unit Ventilators are being disconnected and prepared for demo. All resilient base on exterior walls has been removed.



Beechview Elementary

Project Overview:

Selective toilets and sinks have been removed in the bathrooms. Selective existing convectors/cabinet unit heaters have been removed.

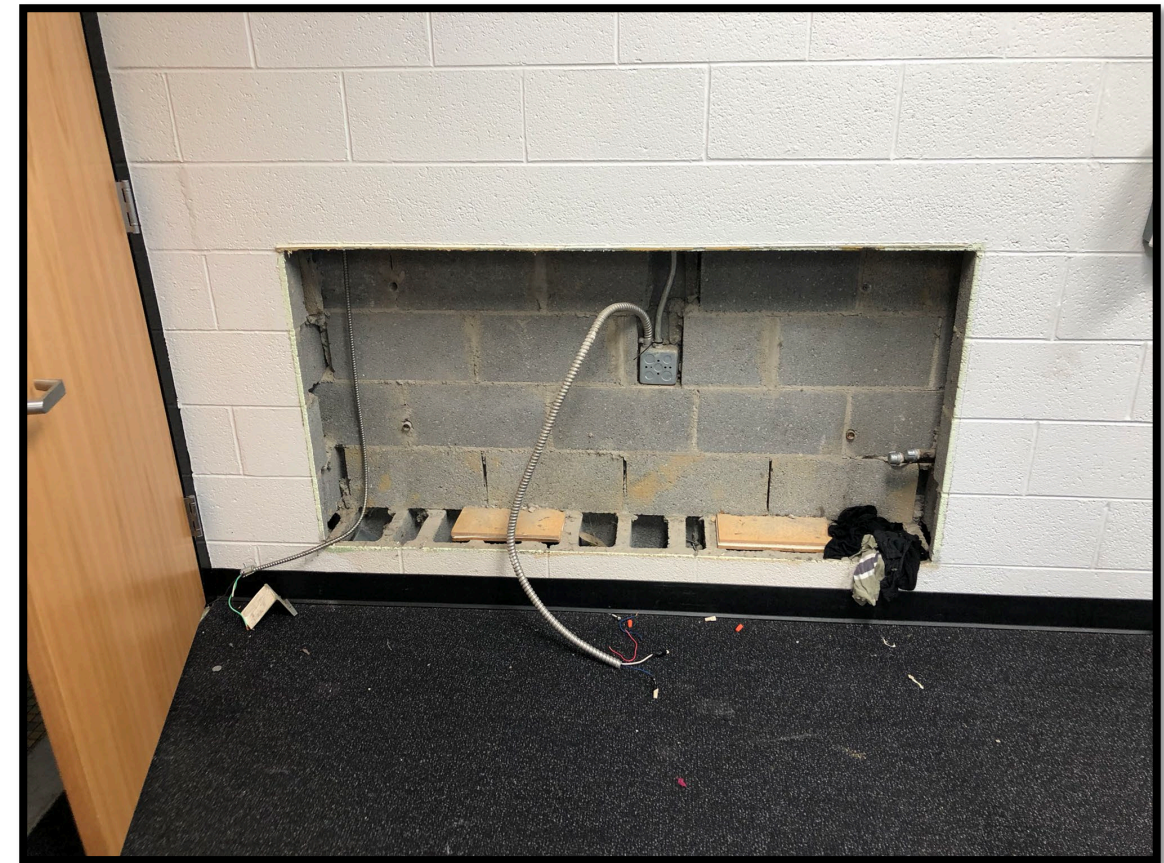


Beechview Elementary

Project Overview:

New blinds in the cafeteria have been installed. Selective acoustical ceiling tiles have been removed in corridors and bathrooms.



Beechview Elementary – Three Week Look Ahead

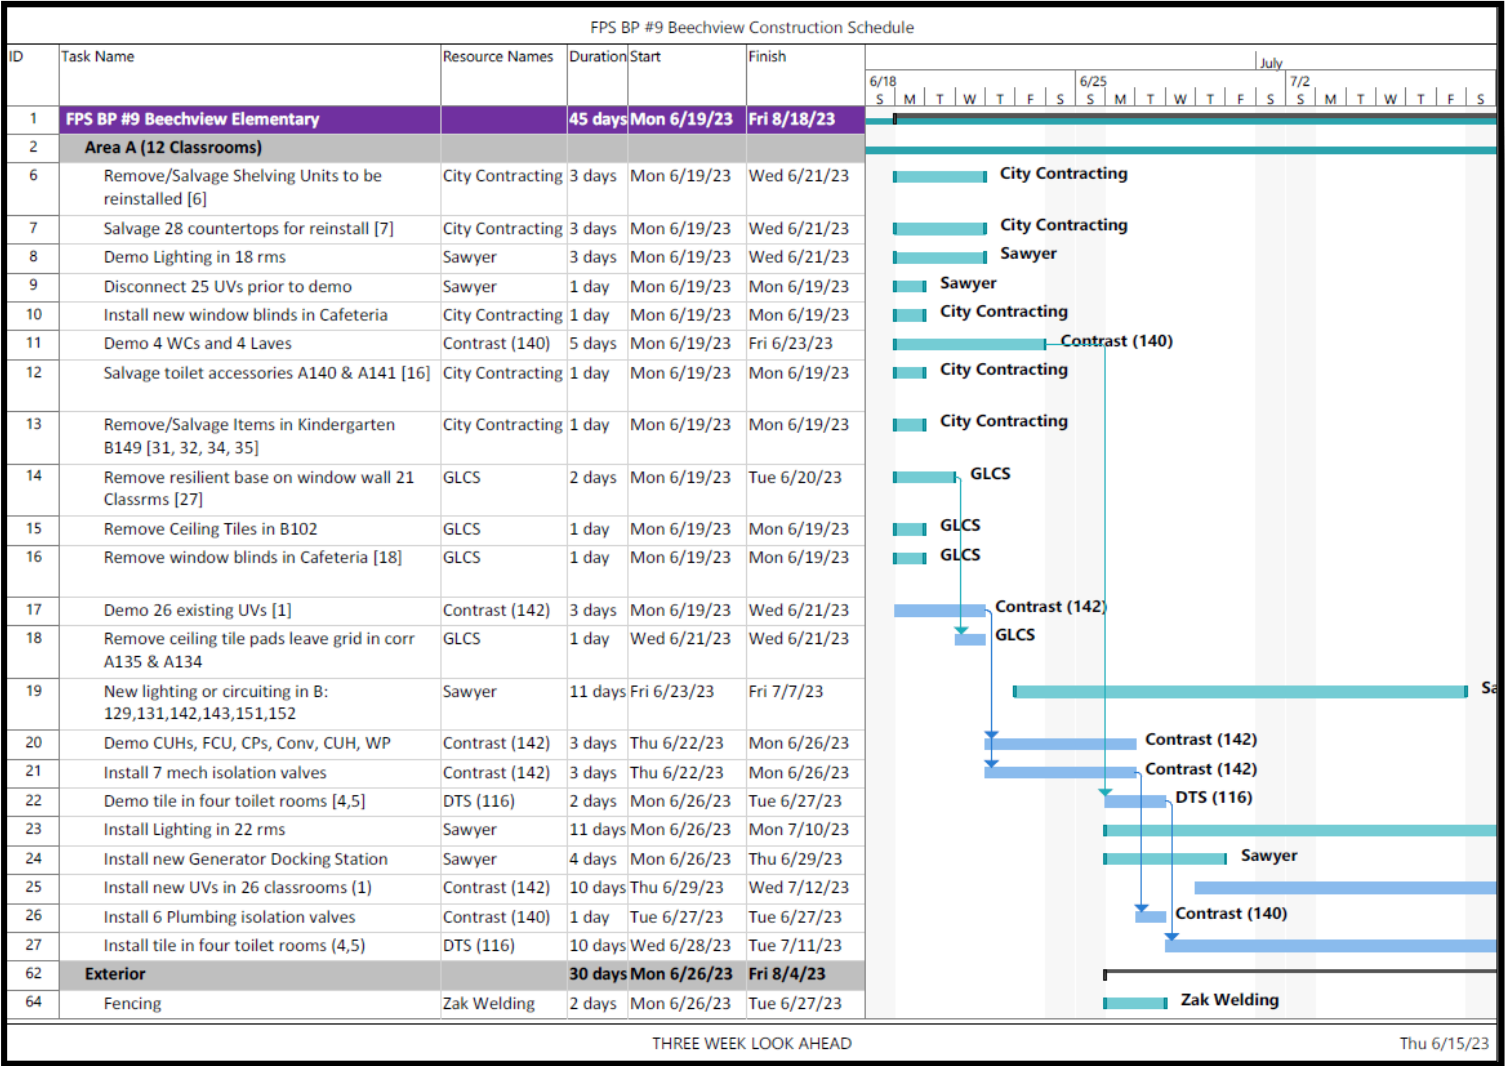

Kenbrook Elementary

Project Overview:

Unit Ventilators have been disconnected and are ready for demo. All resilient base on exterior walls has been removed.



Kenbrook Elementary

Project Overview:

Selective exterior concrete demo is finished in preparation for new. Selective existing playground equipment is being demoed in preparation for new.



Kenbrook Elementary – Three Week Look Ahead

FPS BP #9 Kenbrook Construction Schedule						
ID	Task Name	Resource Names	Duration	Start	Finish	Predecessors
1	FPS BP #9 Kenbrook Elementary	Contractor	215 days?	Wed 2/22/23	Tue 12/19/23	
2	Building			Mon 6/19/23		
8	Abatement: wall section and flooring in A132 and A123 Door	NOVA	2 days	Mon 6/19/23	Tue 6/20/23	
9	Remove resilient base on window wall [27]	GLCS	2 days	Mon 6/19/23	Tue 6/20/23	
10	Remove 8 sinks Rm A102-4, A130, A132, A174 and B103 [9]	Contrast (140)	1 day	Mon 6/19/23	Mon 6/19/23	
11	Demo Plam in 25 Classrooms and 1 Art Rm [8]	GLCS	3 days	Mon 6/19/23	Wed 6/21/23	
12	Remove window stools in 25 classrooms [12]	City Contracting	2 days	Mon 6/19/23	Tue 6/20/23	
13	Remove 49 Shelving to be reinstalled [6]	City Contracting	2 days	Thu 6/22/23	Fri 6/23/23	11
14	Remove Toilet accessories B115 (will be reinstalled) [16]	City Contracting	1 day	Mon 6/19/23	Mon 6/19/23	
15	Disconnect 25 UVs prior to demo	Sawyer	1 day	Mon 6/19/23	Mon 6/19/23	
16	Replace motor in exist AHU (Trane? or JCI?)	Contrast (142)	2 days	Mon 6/19/23	Tue 6/20/23	
17	Demo 32 existing UVs [1]	Contrast (142)	5 days	Mon 6/19/23	Fri 6/23/23	
18	Remove part of ceiling for new Mech Unit B112 <1	DTS (117)	1 day	Mon 6/19/23	Mon 6/19/23	
19	Disconnect 6 mechanical units prior to demo	Sawyer	1 day	Tue 6/20/23	Tue 6/20/23	
20	Demo upper wall cabinet patch walls B115 [17]	GLCS	1 day	Wed 6/21/23	Wed 6/21/23	
21	Underground for Generator	Sawyer	6 days	Wed 6/21/23	Wed 6/28/23	
22	Demo casework in B103 NOT MAILBOXES [14, 23]	GLCS	1 day	Wed 6/21/23	Wed 6/21/23	
23	Paint toilet room walls and ceiling B115 <3>	Papa's Painting	2 days	Thu 6/22/23	Fri 6/23/23	20,14
24	Remove plam and casewk in A132 [14]	GLCS	1 day	Thu 6/22/23	Thu 6/22/23	
26	CMU work Rm A174 (15)	Papa's Painting	2 days	Mon 6/26/23	Tue 6/27/23	17
29	Install 5 Conv, 1 CUH, 3 CP, 1 Ceiling UV, 2 ACUs	Contrast (142)	10 days	Mon 6/19/23	Fri 6/30/23	
44	Roof		13 days	Tue 6/27/23	Thu 7/13/23	
45	Disconnect 19 EFs on Roof	Sawyer	1 day	Tue 6/27/23	Tue 6/27/23	46SS-5
49	Exterior		15 days	Mon 6/19/23	Fri 7/7/23	
50	Concrete Demo	McCarthy	2 days	Mon 6/19/23	Tue 6/20/23	
51	Playground	Sinclair	15 days	Mon 6/19/23	Fri 7/7/23	
52	Fencing: Dumpster Enclosure	Zak Welding	2 days	Mon 6/19/23	Tue 6/20/23	

THREE WEEK LOOK AHEAD

Thu 6/15/23
