




# Mary E. Britton Middle School

## ➤ **Completed Work:**

- Pour Storm Shelter Roof (5/16/24)
- Continue Interior CMU and Brick Veneer
- Continue Joist and Decking at E Area and Structural Steel at Gym Entrance
- Roofing at B and D Area starting 5/16/24, Delayed due to Rain
- Standing Seam Roofing starting 5/20/24 Area A
- Continue Exterior Framing and Sheetrock in Area A second floor.
- Start Priming and first coat of classrooms at Area A
- Continue MEP and Sprinkler Rough Ins

## ➤ **Upcoming Work/Look Ahead:**


- Finish Decking Area E, Structural Steel and Decking at Gym Entrance
- Finish CMU at Plumbing Chase Walls
- Continue Brick Veneer at Cafeteria and ACM Panels at Area F
- Continue Roofing Area B and D Flat Roofs and Standing Seam Trim out at Area A
- Continue Painting Area A (Prime and First Coat at Classrooms)
- Continue Terrazzo Area A First Floor
- Finish Installing Sheetrock Area A Second Floor
- Exterior Wall Furring/Framing Continuing
- Start Installing Sheetrock Area C First Floor
- Mechanical and Plumbing Rough In Continuing at Area E and Area D

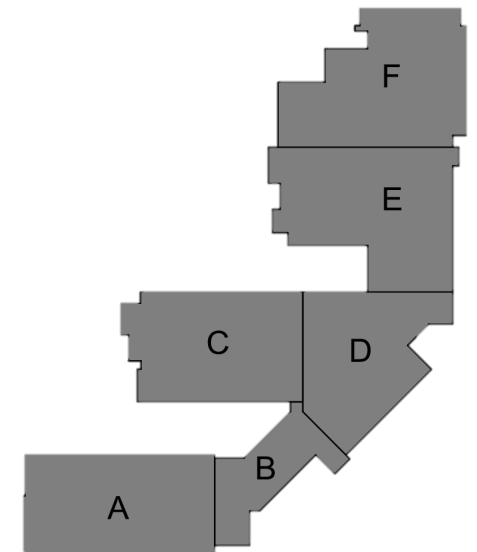

# Mary E. Britton Middle School



## Area A – Classroom Accent Wall Paint

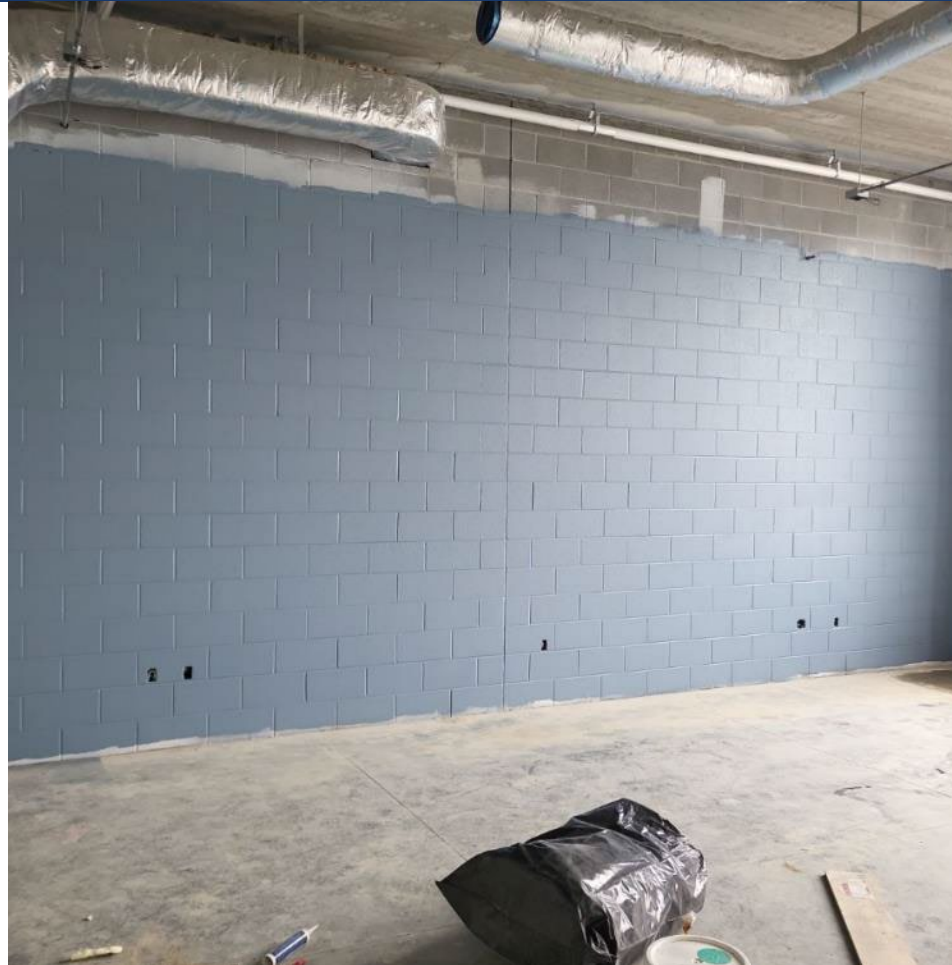

Week Ending May 17, 2024

# Mary E. Britton Middle School



## Area A – Window Boxouts Complete



Week Ending May 17, 2024



# Mary E. Britton Middle School



Area B – Metal Panel Furring has begun



Week Ending May7, 2024

# Mary E. Britton Middle School



Area E – Storm Shelter Roof Ready to Pour



Week Ending May 17, 2024





# Mary E. Britton Middle School

## Area F – ACM Panels on Gym



Week Ending May 17, 2024

# Mary E. Britton Middle School



## Area F – Bus Canopy Framing



Week Ending May 17, 2024



# Mary E. Britton Middle School



## Area F – Kitchen Brick Veneer



Week Ending May 17, 2024



# Mary E. Britton Middle School



Area F – Loading Dock Ready to Pour



Week Ending May 17, 2024
