

Suquamish Elementary School Gym Addition

Project Status Report
April 2024



Project Description:

The elementary school is currently adding a 4,200-square-foot gymnasium. The addition includes separate secure entrances for community use and is a dedicated space for physical education classes, allowing increased flexibility for learning throughout the school.

Construction Budget & Timeline:

- The construction budget for this project is \$2,989,700
- The completion timeline for this project is the September of 2024

In The Month of April:

- Contractor mobilized to the site April 16th, 2024
- Demolition of walkways and asphalt
- Storm and sewer exploration
- Installation of new sewer maintenance holes began
- Catch basins for storm drainage were delivered

One Month Look Ahead:

- Sewer maintenance hole installation will reach completion
- New to existing sewer tie-in assembly will be completed
- Installation of storm drainage will continue
- Relocation of fire hydrant assembly will begin
- Fire line installation will initiate




Contractor Mobilization



Demolition



Storm and Sewer Exploration

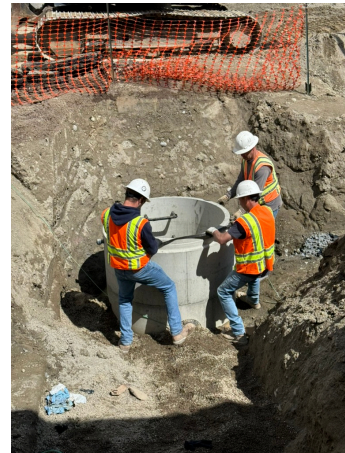

Storm Drain Catch Basin Installation
