


Phase 1.1 - June 2015 - August 2015

Site Setup, Abatement, Demolition, & Permanent Busway & Parking, & Temporary Parking

Key Changes

- South Building Parking Lots Prepped for Construction
Parking Spaces Lost - 35 Spaces
- Temporary Parking Lots Constructed
Parking Spaces Provided - 75 Spaces
- Permanent Parking Lot Constructed
Parking Spaces Added - 197 Spaces
- Partial Demolition of South Building
Program Space Lost - XX Classrooms
- Partial Renovation of Cafeteria Seating Area
Program Space Lost - 0 (Completed prior to school year)
- Bus Loop Established

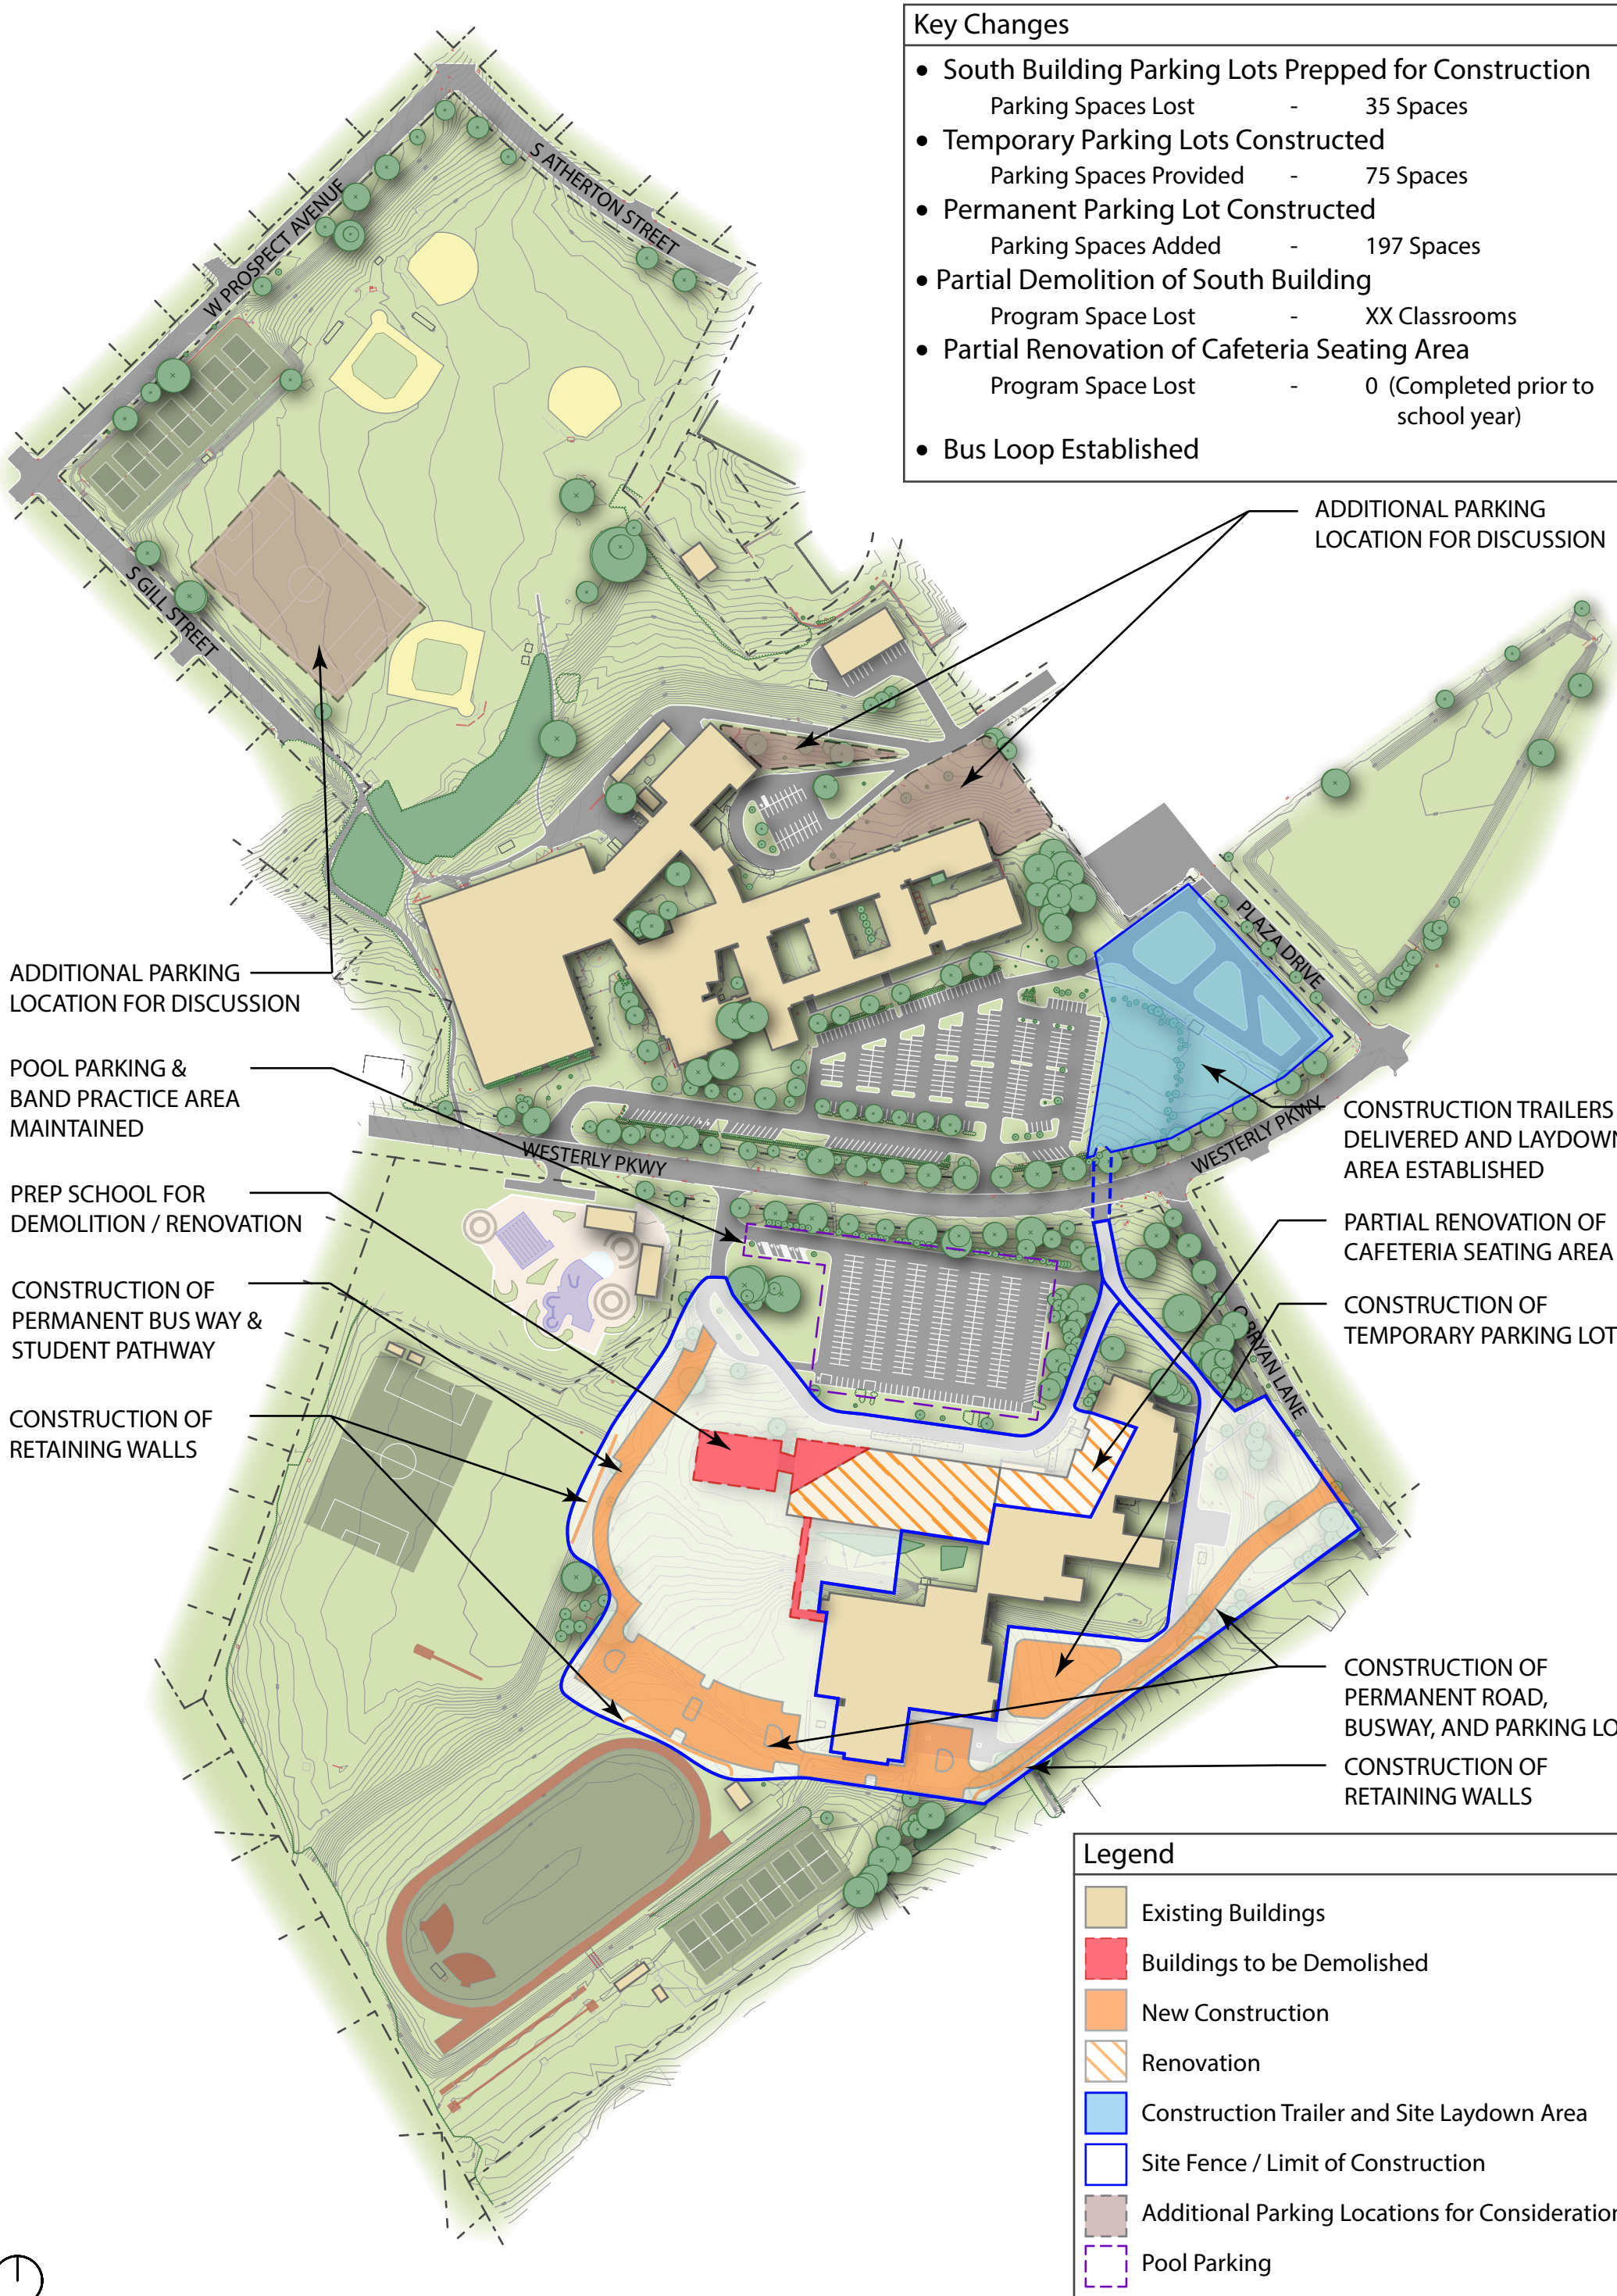

ADDITIONAL PARKING LOCATION FOR DISCUSSION

POOL PARKING & BAND PRACTICE AREA MAINTAINED

PREP SCHOOL FOR DEMOLITION / RENOVATION

CONSTRUCTION OF PERMANENT BUS WAY & STUDENT PATHWAY

CONSTRUCTION OF RETAINING WALLS

ADDITIONAL PARKING LOCATION FOR DISCUSSION

CONSTRUCTION TRAILERS DELIVERED AND LAYDOWN AREA ESTABLISHED

PARTIAL RENOVATION OF CAFETERIA SEATING AREA

CONSTRUCTION OF TEMPORARY PARKING LOTS

CONSTRUCTION OF PERMANENT ROAD, BUSWAY, AND PARKING LOT

CONSTRUCTION OF RETAINING WALLS

Legend

- Existing Buildings
- Buildings to be Demolished
- New Construction
- Renovation
- Construction Trailer and Site Laydown Area
- Site Fence / Limit of Construction
- Additional Parking Locations for Consideration
- Pool Parking

Phase 1.2 - September 2015 - January 2017

Construction of 4 Wings and Mechanical Room of New Building

Key Changes

- South Building Parking Lot Demolished
 - Parking Spaces Lost - 290 Spaces
- Temporary Parking Lots Constructed
 - Parking Spaces Provided - 50 Spaces
- Permanent Parking Lost Constructed
 - Spaces Added (Ph 1.1) - 197 Spaces
 - Spaces Added (Ph 1.2) - 29 Spaces
 - 52 Spaces Add'l for Pool
- Partial Demo / Reno of South Building
 - Program Space Lost - XX Classrooms
- Relocation of Band Practice Area
- Renovation of Kitchen (Jan 2016 - Aug 2016)



ADDITIONAL PARKING LOCATION FOR DISCUSSION

PARKING LOT CONSTRUCTED (SUMMER 2016)

CONSTRUCTION OF 4 NEW WINGS OF BUILDING

CONT. RENOVATION OF EXISTING BUILDING

SCHOOL BUS QUEUE

DEDICATED STUDENT PATHWAY

STUDENT ENTRANCES

ADDITIONAL PARKING LOCATION FOR DISCUSSION

CONSTRUCTION ENTRANCES

DEDICATED STUDENT PATHWAY

RENOVATION OF KITCHEN (JAN 2016 - AUG 2016)

TEMPORARY FOOD SERVICE TRAILERS (DISTRICT FOOD SERVICE RELOCATED TO MNMS)

CONSTRUCTION OF NEW MECHANICAL ROOM

SCHOOL BUS QUEUE

STUDENT DROP-OFF LOCATION

BAND PRACTICE RELOCATED TO TRACK/FIELD

Legend

- Existing Buildings
- Demolished Buildings
- New Construction
- Renovation
- Construction Trailer and Site Laydown Area
- Site Fence / Limit of Construction
- Temporary Parking Lots
- Dedicated Student Pathway
- School Bus Queue

Phase 2.1 - January 2017 - May 2017

Continued Construction of New Building / Renovation of South Building

Key Changes

- Temporary Parking Lots
 - Spaces Added (Ph 1) - 50 Spaces
 - Spaces Removed (Ph 2) - 50 Spaces
- Permanent Parking Lots Constructed
 - Spaces Added (Ph 1) - 226 Spaces
 - 52 Spaces Add'l for Pool
- Remaining Demo / Reno of South Building
 - Program Space Lost (Ph 1) - XX Classrooms
 - Program Space Lost (Ph 2) - XX Classrooms
- Construction Started on Remaining South Bldg
- Renovation of Existing South Building
- West Wings Occupied by Students (Jan 2017)
 - Program Space Added - XX Classrooms
- East Wings Occupied by Students (Sept 2017)
 - Program Space Added - XX Classrooms

ADDITIONAL PARKING LOCATION FOR DISCUSSION

EAST WINGS COMPLETED (AUG 2017)

PARKING LOT COMPLETED (SUMMER 2016)

NEW STUDENT DROP OFF LOCATION

BUS QUEUE

DEMOLITION OF REMAINING SOUTH BUILDING (COMPLETED APRIL 2017)

CONSTRUCTION ENTRANCES

RENOVATION OF EXISTING SOUTH BUILDING (KITCHEN AND CAFETERIA IN OPERATION)

NEW CONSTRUCTION OF SOUTH BUILDING TO START APRIL 2017

BAND PRACTICE RELOCATED TO TRACK/FIELD

Legend


- Existing Buildings
- Demolished Buildings
- New Construction
- Renovation
- Construction Trailer and Site Laydown Area
- Site Fence / Limit of Construction
- Temporary Parking Lots
- Dedicated Student Pathway
- School Bus Queue

Phase 2.2 - June 2017 - August 2017

Continued Construction of New Building / Demolition of North Building

Key Changes

- South Building Parking Lot Demolished
 - Spaces Lost (Ph 1) - 290 Spaces
- Permanent Parking Lots Constructed
 - Spaces Added (Ph 1) - 226 Spaces
 - Spaces Added (Ph 2.2) - 52 Spaces Add'l for Pool
 - Spaces Added (Ph 2.2) - 88 Spaces
 - Spaces Added (Ph 2.2) - 20 Spaces for Bus Queue
- Remaining Renovation of South Building
 - Program Space Lost (Ph 1) - XX Classrooms
 - Program Space Lost (Ph 2) - XX Classrooms
- South Bldg Wings Completed & Occupiable by Students
 - Program Space Added - XX Classrooms
- Continued Construction of South Building
- Busway Constructed

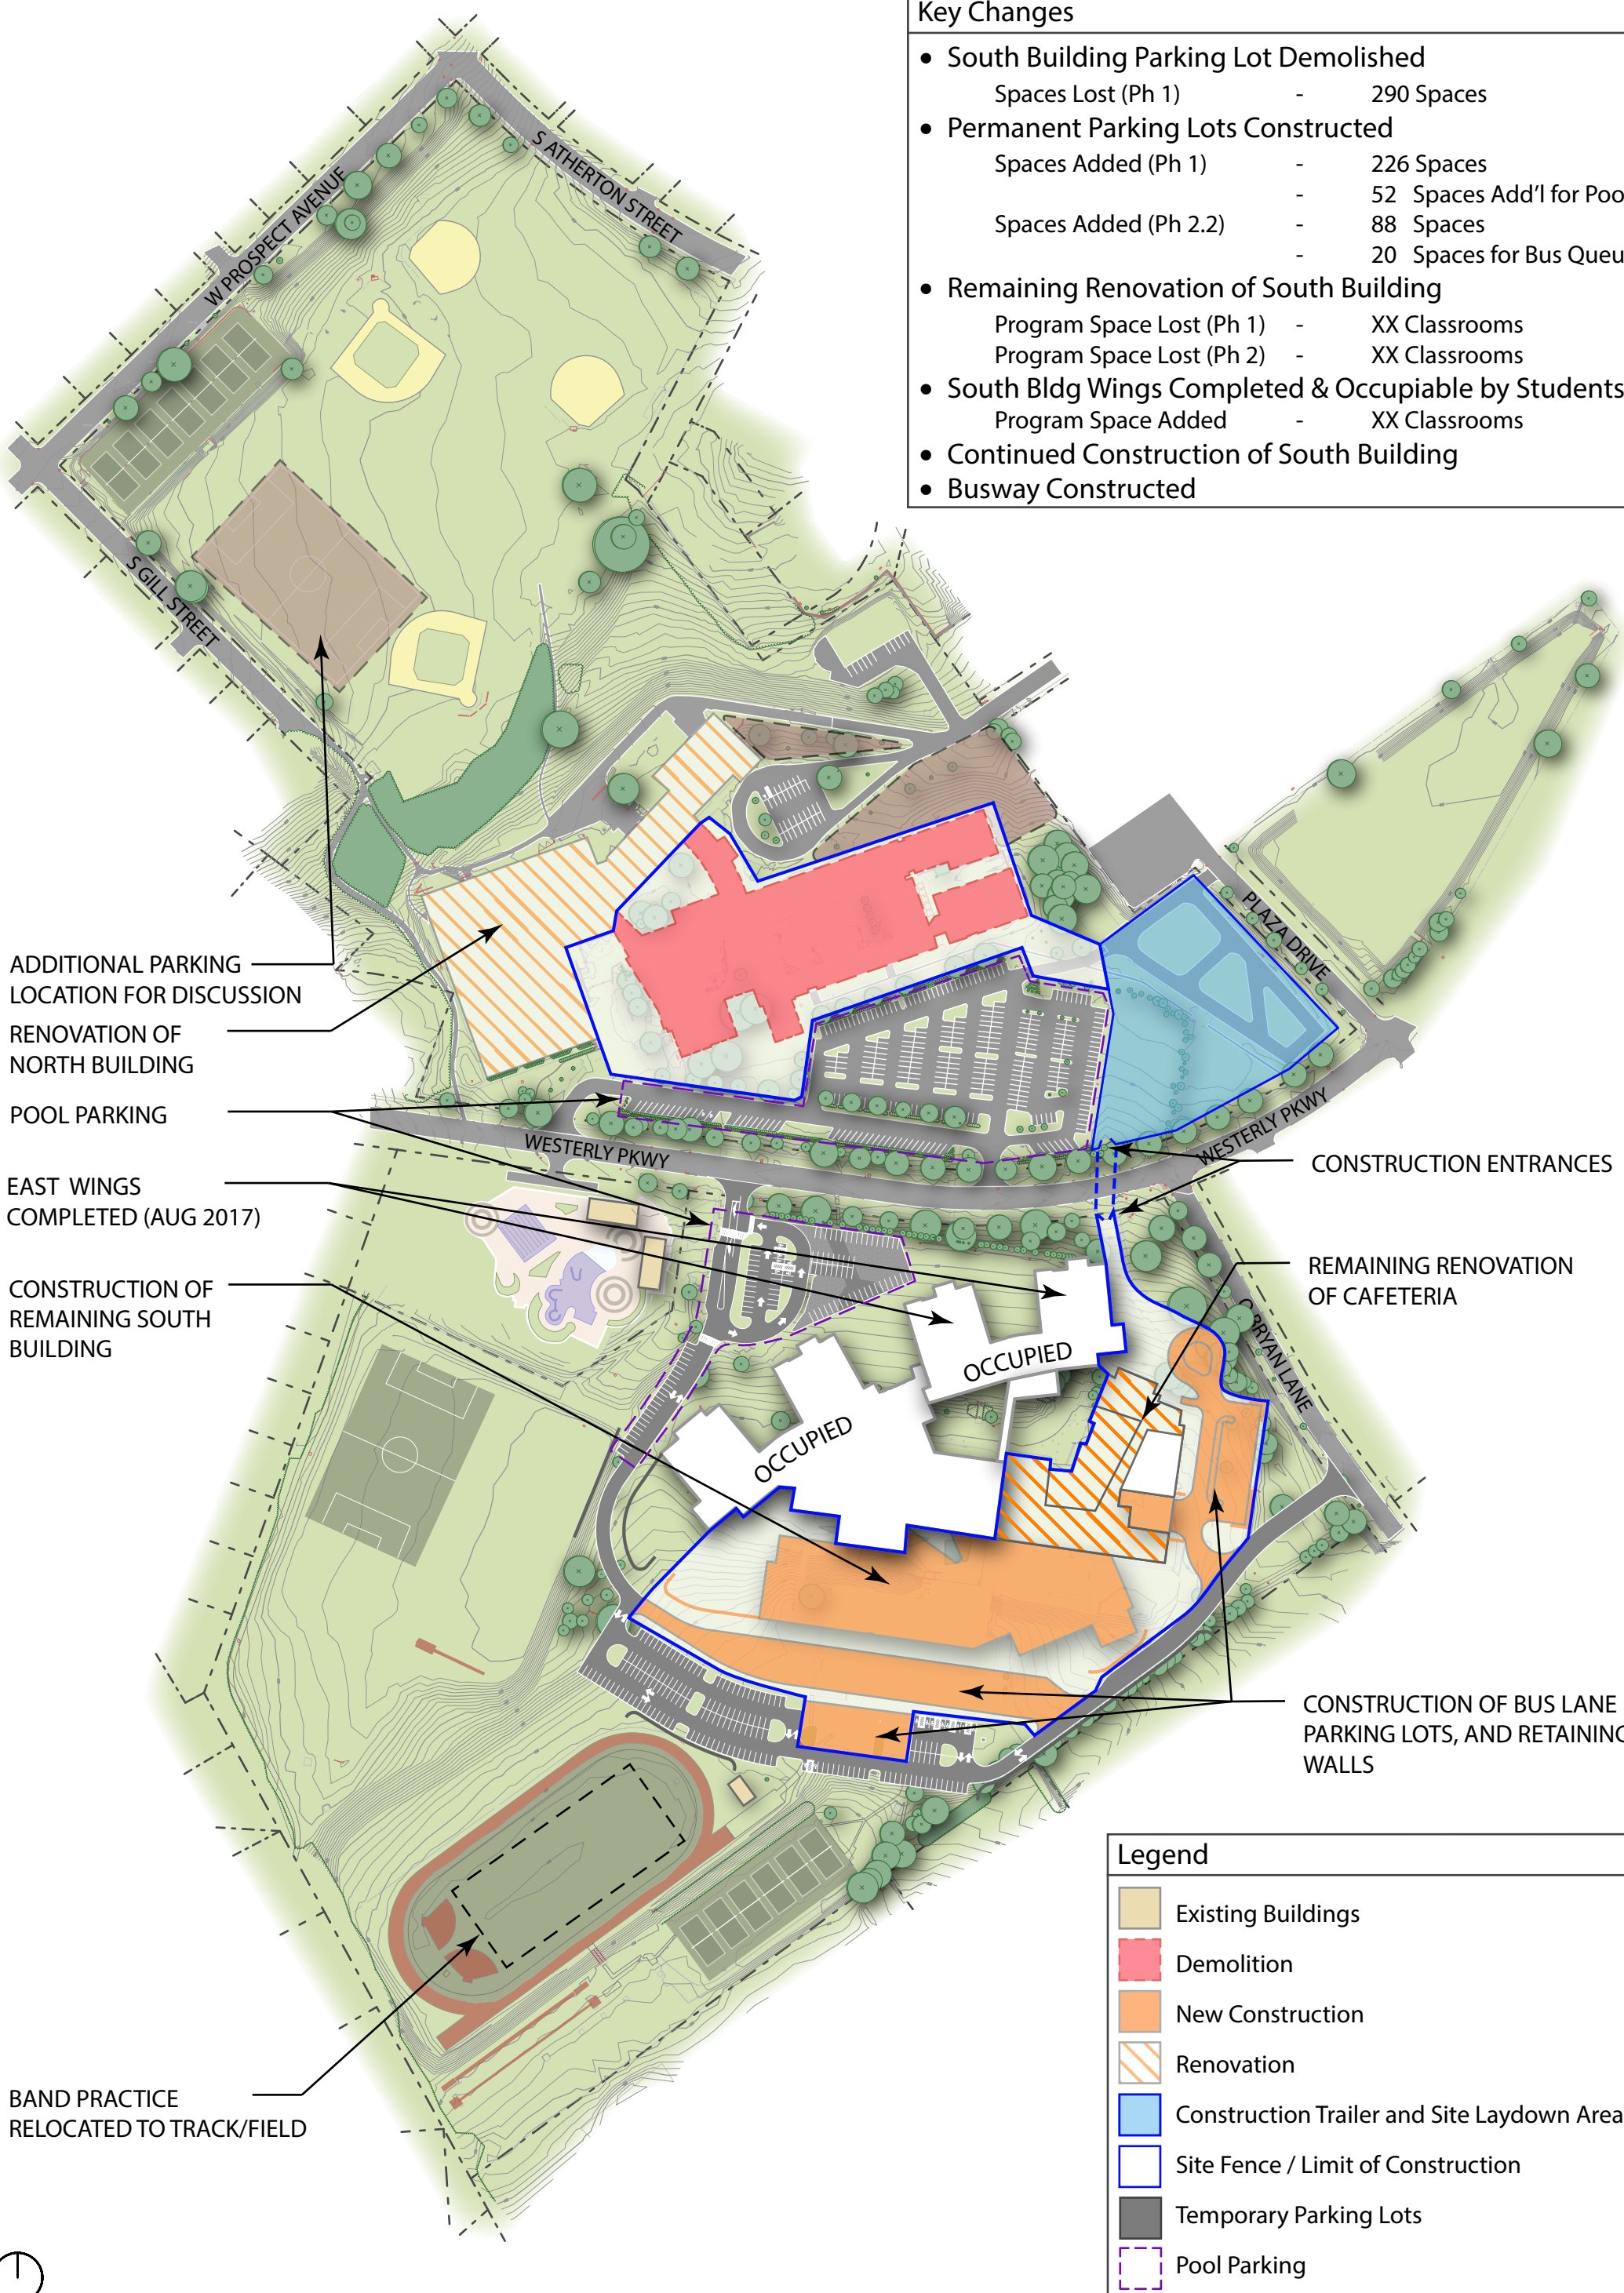

ADDITIONAL PARKING LOCATION FOR DISCUSSION

RENOVATION OF NORTH BUILDING

POOL PARKING

EAST WINGS COMPLETED (AUG 2017)

CONSTRUCTION OF REMAINING SOUTH BUILDING

BAND PRACTICE RELOCATED TO TRACK/FIELD

CONSTRUCTION ENTRANCES

REMAINING RENOVATION OF CAFETERIA

CONSTRUCTION OF BUS LANE PARKING LOTS, AND RETAINING WALLS

Legend


- Existing Buildings
- Demolition
- New Construction
- Renovation
- Construction Trailer and Site Laydown Area
- Site Fence / Limit of Construction
- Temporary Parking Lots
- Pool Parking

Phase 3.1 - September 2017 - May 2018

Renovation and Addition to North Building

Key Changes

- Permanent Parking Lots Constructed
 - Spaces Added (Ph 1) - 226 Spaces
 - Spaces Added (Ph 2) - 52 Spaces Add'l for Pool
 - Spaces Added (Ph 2) - 88 Spaces
 - Spaces Added (Ph 2) - 20 Spaces for Bus Queue
- Demolition of North Building
 - Program Space Lost (Ph 3) - XX Classrooms
- Renovation of North Building
 - Program Space Lost (Ph 3) - XX Classrooms
- South Building Completed
 - Program Space Total - XX Classrooms
- Construction of Delta Program

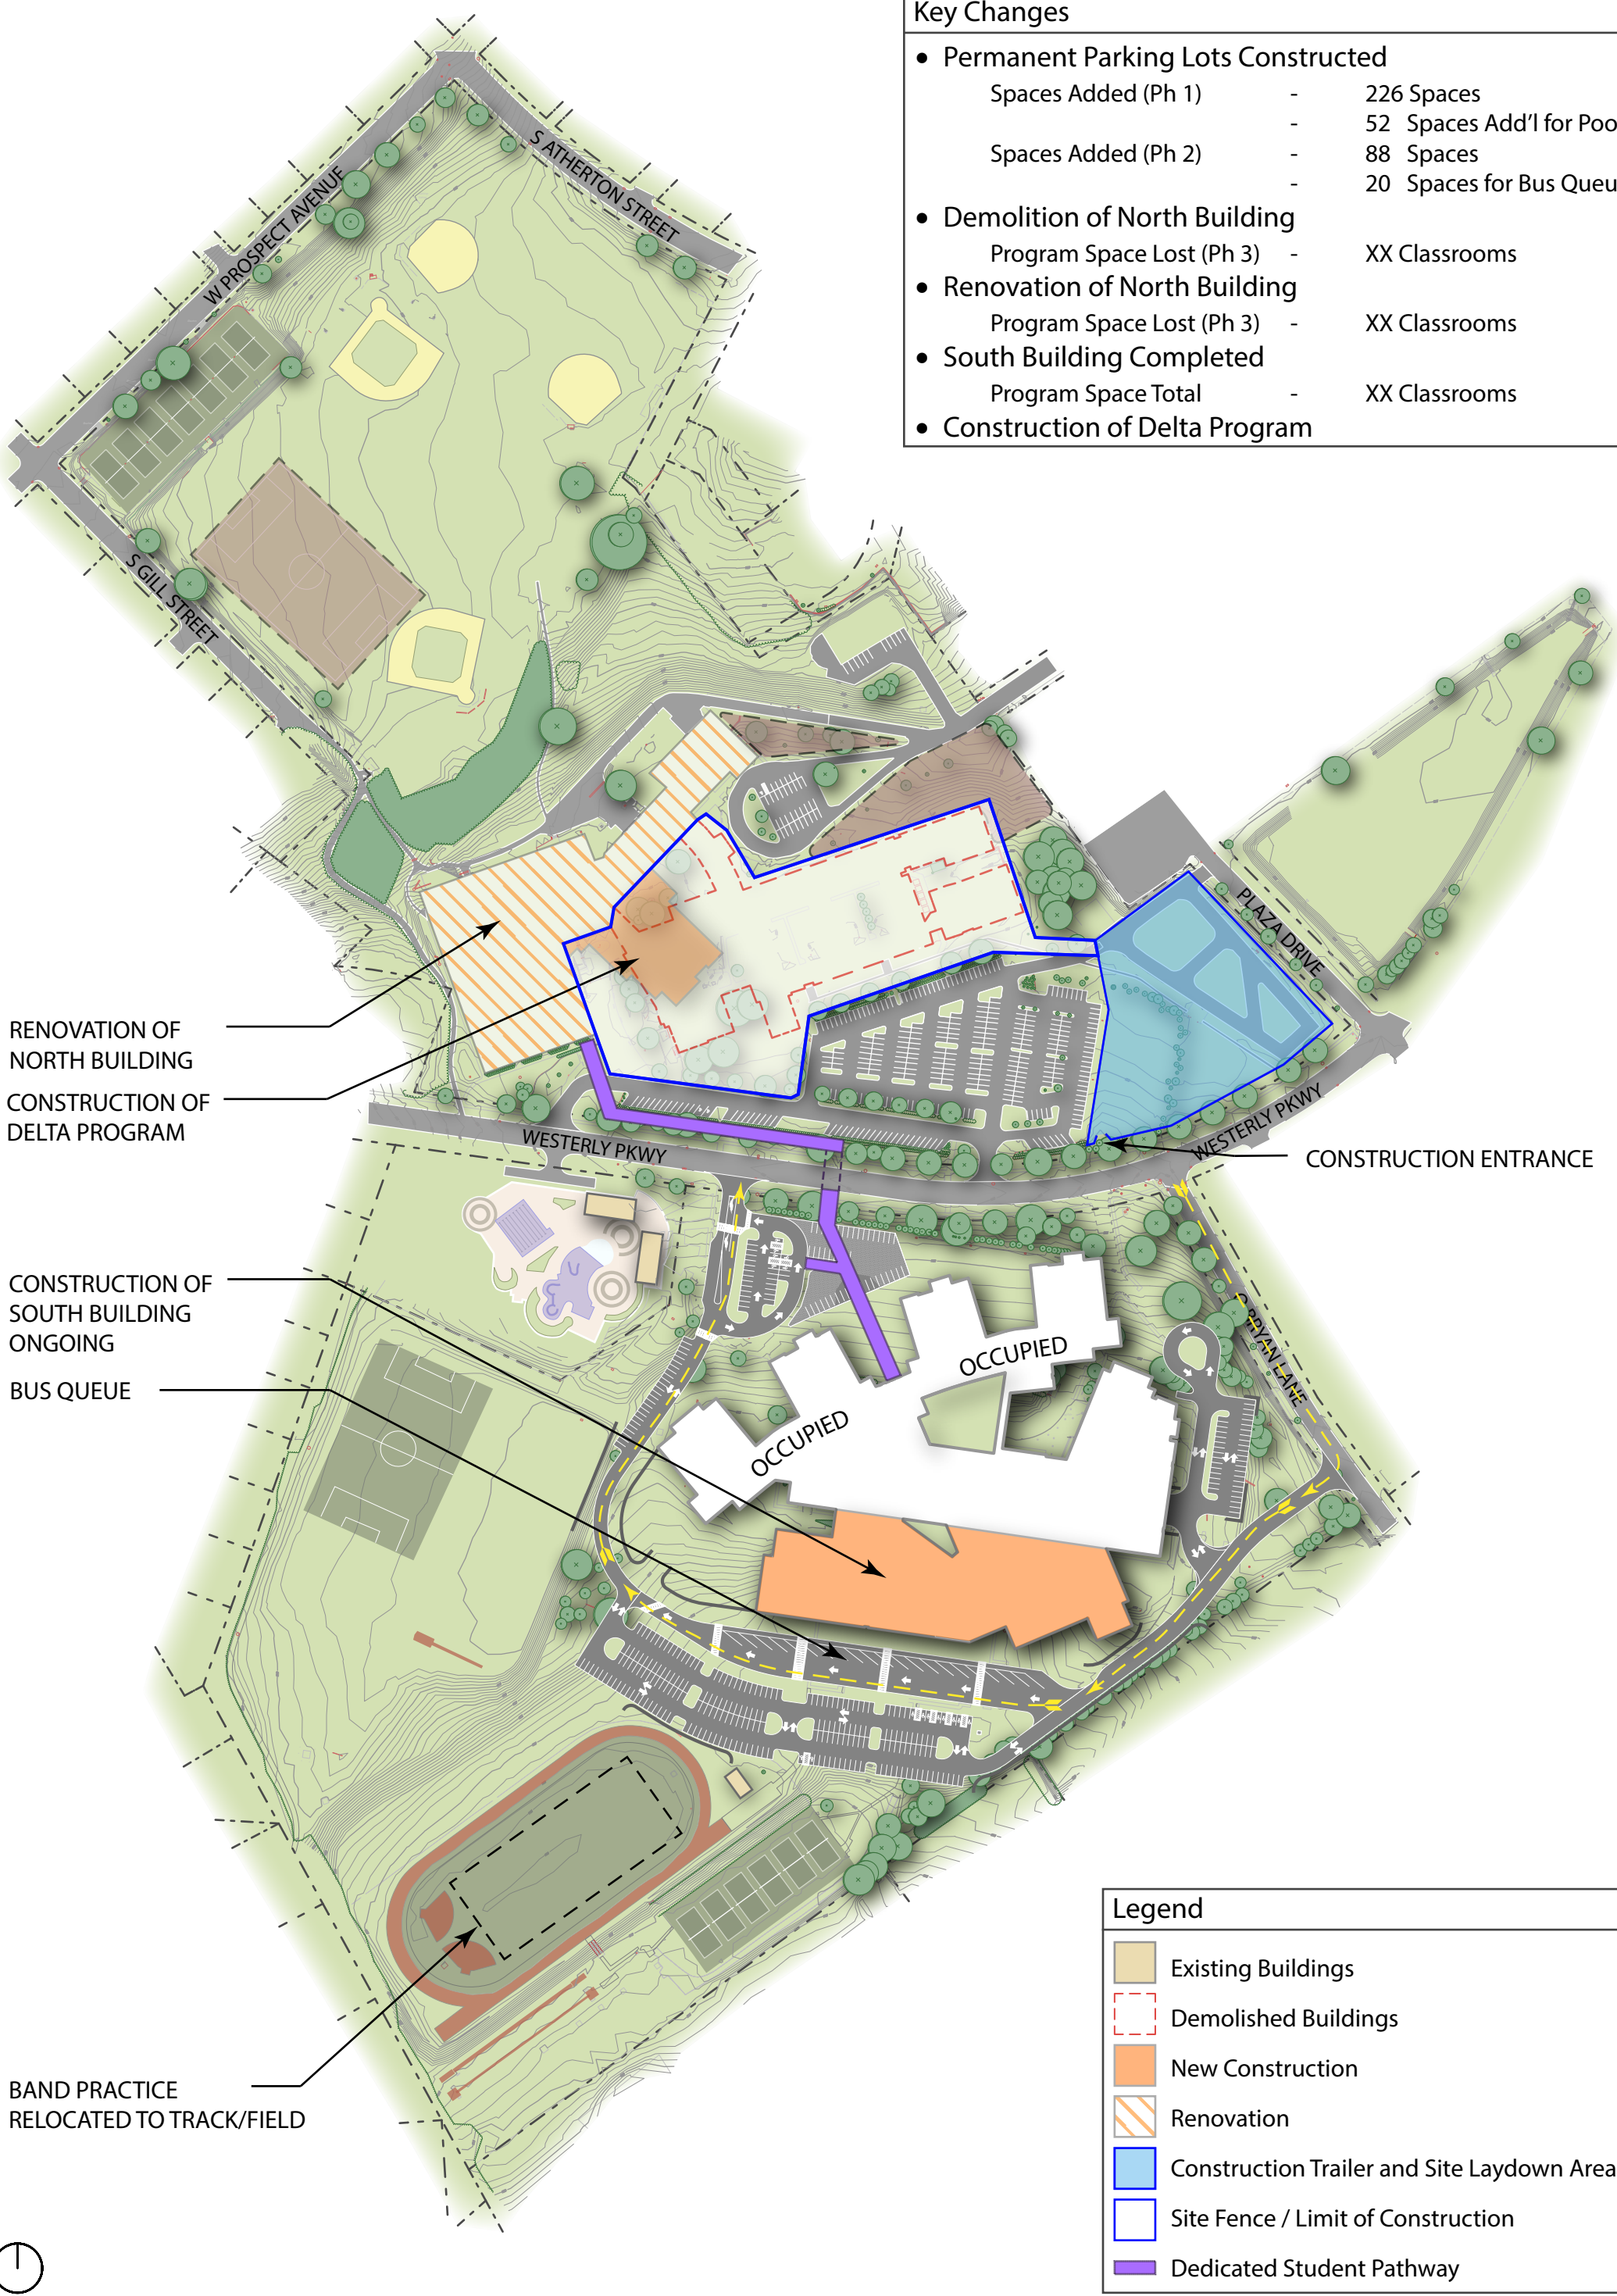

Legend

- Existing Buildings
- Demolished Buildings
- New Construction
- Renovation
- Construction Trailer and Site Laydown Area
- Site Fence / Limit of Construction
- Dedicated Student Pathway

Phase 3.2 - June 2018 - July 2018

North Building Move-in, Parking and Site Work

Key Changes

- North Building Parking Lot Demolished
Parking Spaces Lost - 350 Spaces
- Sitework and North Parking Lot Constructed
Spaces Added (Ph 3) - 464 Spaces
- North and South Buildings Complete
- Construction Trailers Demobilized
- All Construction Completed



CONSTRUCTION OF NORTH BUILDING COMPLETE

CONSTRUCTION OF SOUTH BUILDING COMPLETE

CONSTRUCTION TRAILERS DEMOBILIZED

SITE WORK AND PARKING LOTS

Legend

- Existing Buildings
- Demolished Buildings
- New Construction
- Renovation
- Construction Trailer and Site Laydown Area
- Site Fence / Limit of Construction
- Temporary Parking Lots
- Dedicated Student Pathway
- School Bus Queue
