

Update on FCPS Construction / Renovation Projects

June 24, 2024

Mary E. Britton Middle School



Mary E. Britton Middle School



- Architect: JRA Architects
- General Contractor: Rising Sun Developing Co.
- GC Contract Sum: \$69,964,000.00
- Total Project Cost: \$82,680,000.00
- Change Orders to Date (5): \$41,080.23
- Scheduled Contract Completion Date: April 2025
- % of Contract Completed: 64%
- Revised Completion Date per GC: No Change
- Weekly Construction Updates:

<http://www.fcps.net/msconstruction>

Mary E. Britton Middle School




➤ Completed Work:

- Start storm drain installation and layout north of Gym Area F.
- Prep main islands to grade and prep mow strips at back of curb and gutter.
- Fire sprinkler rough-ins at Area C, 2nd floor.
- Start blackout ceiling Area A, 2nd floor. Prime classrooms area A, 2nd floor following drywall.
- Continue setting bar joists and decking at 2nd floor/low roof Area F beside Gym Lobby corridor, as well as A-frames and bracing at high roof of Area E/Gym Lobby entrance.
- Continue roof insulation, cover board and membrane roofing at main roof of Area D.
- Continue exterior framing at Stage south walls ahead of panels and Area E Cafeteria walls into Area C exterior.
- Terrazzo floor prep at middle corridors of A, 1st Floor, first hallway near completion.

➤ Upcoming Work/Look Ahead:

- Continue structural steel and decking at Gym entrance lobby.
- Continue brick veneer at Areas C and A; then move to exterior Area B.
- Start ACM panels at Area E Cafeteria side, then move to Areas C and A.
- Start stone and brick veneer at Area B.
- Continue Terrazzo Area A, 1st floor.
- Continue membrane roofing at flat roof of Area D, then move to Storm Shelter, Area E.
- Continue hanging sheetrock at Area C, 1st Floor.
- Continue blackout ceilings and priming classrooms Area A, 2nd Floor.

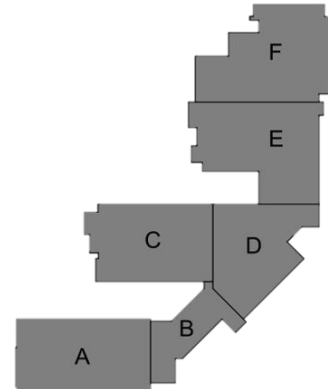

Mary E. Britton Middle School



Area A – Brick Continues



Week Ending June 7, 2024

Mary E. Britton Middle School



Area A – Interior Drywall Finishing



Week Ending June 7, 2024

Mary E. Britton Middle School




Area A – Terrazzo in Corridor



Mary E. Britton Middle School



Area B – Admin Stud Walls Complete

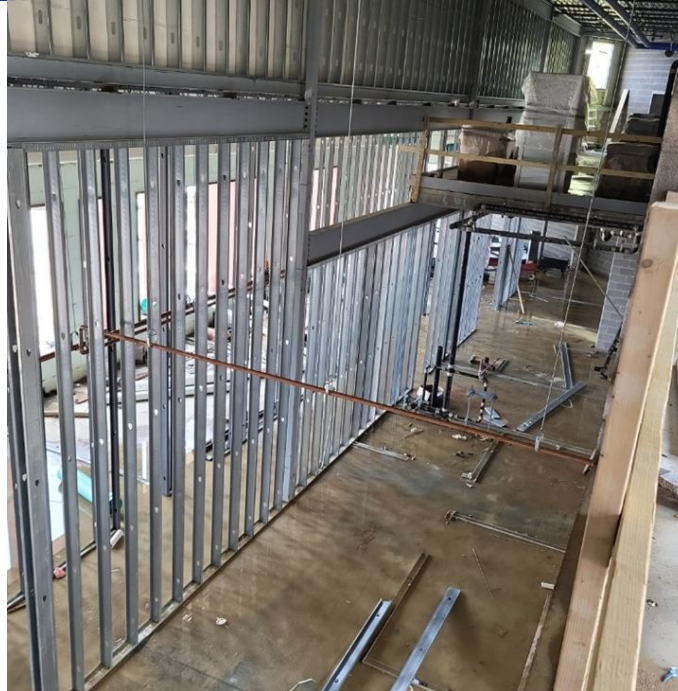

Week Ending June 7, 2024

Mary E. Britton Middle School



Area B – Roofing Continues



Week Ending June 7, 2024

Mary E. Britton Middle School



Area C – Brick Continuing



Week Ending June 7, 2024

Mary E. Britton Middle School




Area C – Furring for Metal Panels



Mary E. Britton Middle School



Area C – Tile in Restrooms

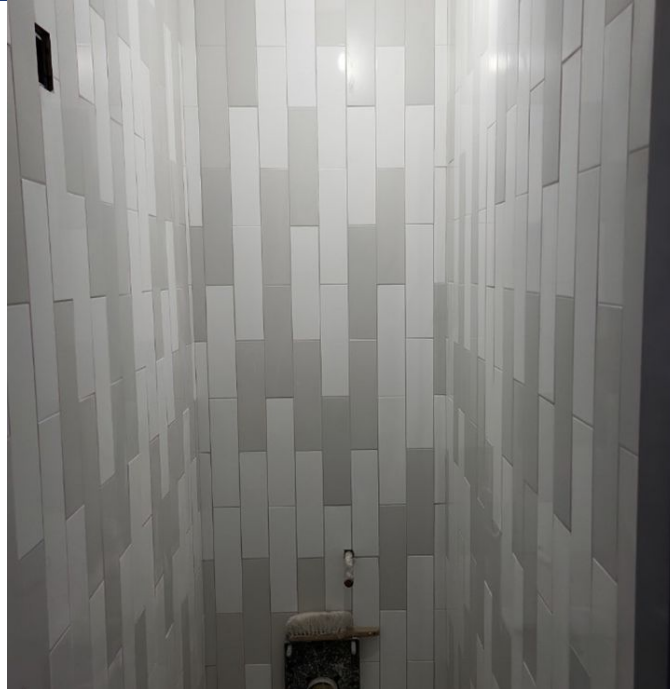

The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



- Architect: EOP Architects
- General Contractor: D.W. Wilburn Inc.
- GC Contract Sum: \$50,700,288.00
- Total Project Cost: \$64,712,240.00
- Change Orders to Date (8): \$1,023,085.32
- Scheduled Contract Completion Date: February 2025
- % of Contract Completed: 82%
- Revised Completion Date per GC: March 2025
- Weekly Construction Updates: <http://www.fcps.net/cteconstruction>

The Hub for Innovative Learning & Leadership (The HILL)



Completed Work:

- CMU work on all floors continued.
- Ceilings continued on Levels 3.
- Metal stud and drywall work continuing on all levels.
- Window glazing continued on all levels.
- Electrical devices and lighting continued on Levels 4 and 3.
- Plumbing above ceiling continued on all floors.



Upcoming Work/Look Ahead:

- CMU work should near completion.
- Ceilings to continue on Levels 3 and 2.
- Curtain walls and glazing to continue, nearing completion.
- Ductwork installation to continue.
- Electrical and plumbing wall rough-ins to continue with masonry and electrical devices being installed.
- There will be a partial shutdown, and at times a complete shutdown, of Indiana Avenue for roofing work.

The Hub for Innovative Learning & Leadership (The HILL)



Drywall Install at Level 1 Administration



Week Ending June 7, 2024

The Hub for Innovative Learning & Leadership (The HILL)



Gypsum Board Install at Commons Area Ceiling Clouds



The Hub for Innovative Learning & Leadership (The HILL)



Display Cases Framing at Level 1



The Hub for Innovative Learning & Leadership (The HILL)



Insulation of Lighting Fixtures at Level 3 Culinary Seating



The Hub for Innovative Learning & Leadership (The HILL)



Rubber Flooring at Law Enforcement Lab



The Hub for Innovative Learning & Leadership (The HILL)



Casework Install in Health Sciences Simulation Lab



The Hub for Innovative Learning & Leadership (The HILL)



Grading Work at East and West Sides of Building



Week Ending June 7, 2024

The Hub for Innovative Learning & Leadership (The HILL)



Window Trim-outs Nearing Completion



Week Ending June 7, 2024

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



➤ Architect:	Ross Tarrant Architects
➤ General Contractor:	Momentum Construction
➤ GC Contract Sum:	\$3,998,400.00
➤ Total Project Cost:	\$4,886,547.24
➤ Change Orders to Date (0):	\$0
➤ Scheduled Contract Completion Date:	December 2025
➤ % of Contract Completed:	3%
➤ Revised Completion Date per GC:	N/A
➤ Weekly Construction Updates:	www.fcps.net/harrisonpreschool

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



- **Completed Work:**
 - Preparing for water and sewer shutdown scheduled for week of June 10.
 - Initiated grading operations on the playground.
 - Demolishing concrete at the egress path.
 - Started demolition of the existing stairway.

- **Upcoming Work/Look Ahead:**
 - Transition of sewer and water systems.
 - Continuation of stormwater management.
 - Ongoing grading operations.
 - Demolition of underground utilities at the addition site.

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Grading Operations on the Playground in Progress



Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Demo of Concrete at the Egress Path



Week Ending June 7, 2024

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Demo of Existing Stairway



Rise STEM Academy for Girls Early Demolition Package



➤ Architect:	Ross Tarrant Architects
➤ Demolition Contractor:	Cornerstone Demolition
➤ GC Demo Contract Sum:	\$205,100.00
➤ Change Orders to Date (0):	\$0
➤ Scheduled Contract Completion Date:	August 2024
➤ % of Contract Completed:	5%
➤ Revised Completion Date per Demo Contractor:	N/A
➤ Weekly Construction Updates:	www.fcps.net/risestem

Rise STEM Academy for Girls Early Demolition Package



- **Completed Work:**
 - Contractor has commenced work.
 - Erosion control measures have been installed, and the necessary permit has been issued.
 - Interior salvage process is 80% complete.
 - Fence removal is complete 50%
 - Electrical demolition is 60% complete
 - Awaiting confirmation on gas and water abandonment.

- **Upcoming Work/Look Ahead:**
 - Complete the remaining salvage, fence, and electrical demolition work.
 - Begin and complete building demolition.
 - Continue on-site grading work.

Rise STEM Academy for Girls Early Demolition Package



Erosion Control Measures



Rise STEM Academy for Girls Early Demolition Package



Interior Salvage Process in Progress



Week Ending June 7, 2024


Rise STEM Academy for Girls Early Demolition Package



Fence Removal in Progress



Week Ending June 7, 2024

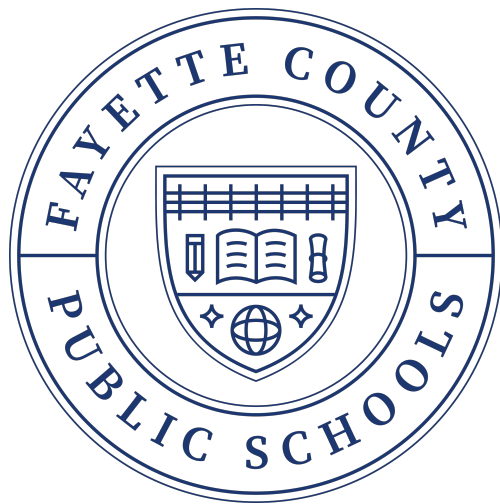

Thank you!
