


Mary E. Britton Middle School

➤ **Completed Work:**

- Structural Steel and Decking Completed
- Load Bearing CMU complete in all Areas
- Prep Kitchen for Quarry Tile
- Fire Main Underground Complete. Start Riser
- Electrical Power Distribution to 75% Complete all Areas
- Continue Overhead MEP and Sprinkler Rough-in multiple areas
- Continue Controls Area A and Area C
- Steel framing at Bus Canopy Complete

➤ **Upcoming Work/Look Ahead:**

- Continue Exterior Concrete
- Start Protective Canopy Supports and Start Exterior Stair Area A
- Finish Stone Veneer, continue Brick Veneer
- Complete Area A Standing Seam
- Continue Interior framing at Area C second Floor
- Continue Terrazzo Area A First Floor
- Start Quarry Tile at Kitchen
- Continue MEP and Sprinkler Rough Ins, Wire Pulls and Controls

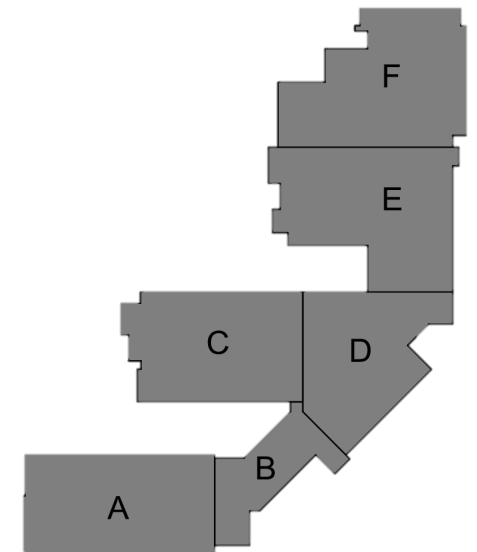

Mary E. Britton Middle School



Overall Aerial – Site Progress



Week Ending June 28, 2024

Mary E. Britton Middle School



Area F – ACM Panels Complete at Gym



Week Ending June 28, 2024

Mary E. Britton Middle School



Area F – Kitchen Loading Dock Poured



Week Ending June 28, 2024

Mary E. Britton Middle School



Area A - Roof Panels on Back Side Installed



Week Ending June 28, 2024

Mary E. Britton Middle School



Area C - Terrazzo on 2nd Floor Continues



Week Ending June 28, 2024

Mary E. Britton Middle School



Area D - Art Room Display Case



Week Ending June 28, 2024

Mary E. Britton Middle School



Area D - Limestone Continues at Media Center



Week Ending June 28, 2024

Mary E. Britton Middle School



Site - Sidewalks Continuing



Week Ending June 28, 2024
