




# Mary E. Britton Middle School

## ➤ **Completed/Work in Progress:**

- Continue Sidewalk Prep and Pours at the Front of Building. Pour on 7/18
- Continue Island Grading, Topsoil Spread, Seed and Straw, and Geothermal Field Grading
- Continue MCM Panels at Gym Lobby Wall and Area E into Courtyards
- Continue Interior Stud Framing at Area B Administration
- Continue Peel and Stick Membrane at Area E Windows into C Ahead of Panels
- Continue Classroom Priming and Paint as well as Soffit Painting
- Continue Terrazzo Pouring in Area A and Installing Tile on 2<sup>nd</sup> floor Area A.
- Continuing Standing Seam Panels at Area C Roof (75% Complete) and Low Slope Roofing at Storm Shelter (60%)
- Continuing MEP Following Other Trades and Sprinkler Rough Ins at 2<sup>nd</sup> Floor Corridor

## ➤ **Upcoming Look Ahead:**

- Continue Site Concrete and Storm at Exterior.
- Continue Canopy Work Exterior
- Continue Stairs Work A then Move to C
- Continue Blockfill of Corridors and Classroom Painting, Misc. Chase Walls and Locker Bases
- Continue Interior Framing at B
- Continue MCM Panel Installation Area F and Area E
- Continue Terrazzo Area A, and Start Tile Area A 2<sup>nd</sup> Floor
- Continue Low Slope Roofing Install at Storm Shelter
- Standing Seam Panels at Area C Roof then Move to Cafeteria Roof
- Continue Controls Testing

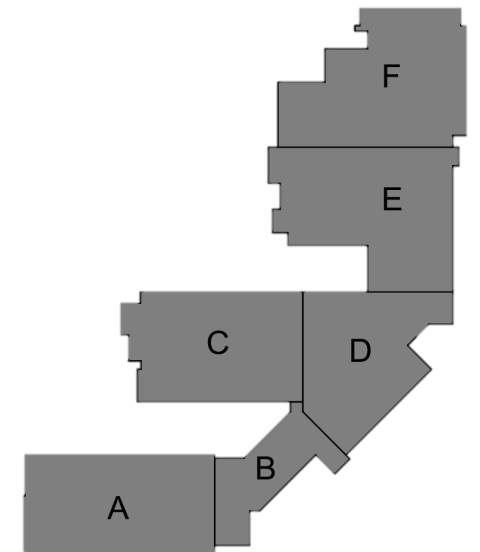

# Mary E. Britton Middle School



## Area A – Roof Fascia and Gutter Installed



Week Ending July 19, 2024



# Mary E. Britton Middle School

## Area A - Stair



Week Ending July 19, 2024

# Mary E. Britton Middle School



## Area B – Tile Flooring Continues in Restrooms



Week Ending July 19, 2024

# Mary E. Britton Middle School



## Area C – Classroom Progress



Week Ending July 19, 2024

# Mary E. Britton Middle School

## Area C – Metal Roofing Continues



# Mary E. Britton Middle School



## Area C – Mezzanine MEP Work Continues



Week Ending July 19, 2024

# Mary E. Britton Middle School



## Area E – Brick on Storm Shelter Continues



Week Ending July 19, 2024

# Mary E. Britton Middle School

Area F – Bus Canopy Steel Decking Installed



Week Ending July 19, 2024
