

# Harrison ES – Preschool Classrooms Addition & HVAC Upgrades





# Harrison ES – Preschool Classrooms Addition & HVAC Upgrades

## ➤ **Completed Work:**

- Backfilled lines to the cooling tower, and lines into building
- Demoed sidewalk and curb, cut grade and put in new entrance on Jefferson St.
- Finished pathway from the school to the dumpster, and set up fence
- Construction sign was installed on the fence facing Bruce St.
- Total power ran 2" conduit from the switchgear to the new addition
- Four HVAC units are scheduled to be delivered today, Friday the 2nd


## ➤ **Upcoming Work / Look Ahead:**

- New water meter and new water line will be installed by Kentucky American Water.
- Momentum is scheduled to do water transmission from old service to the new service next weekend.
- Miracle Creation is scheduled to install playground equipment next week.

# Harrison Elementary – Preschool Classrooms Addition & HVAC



Construction sign is installed on-site

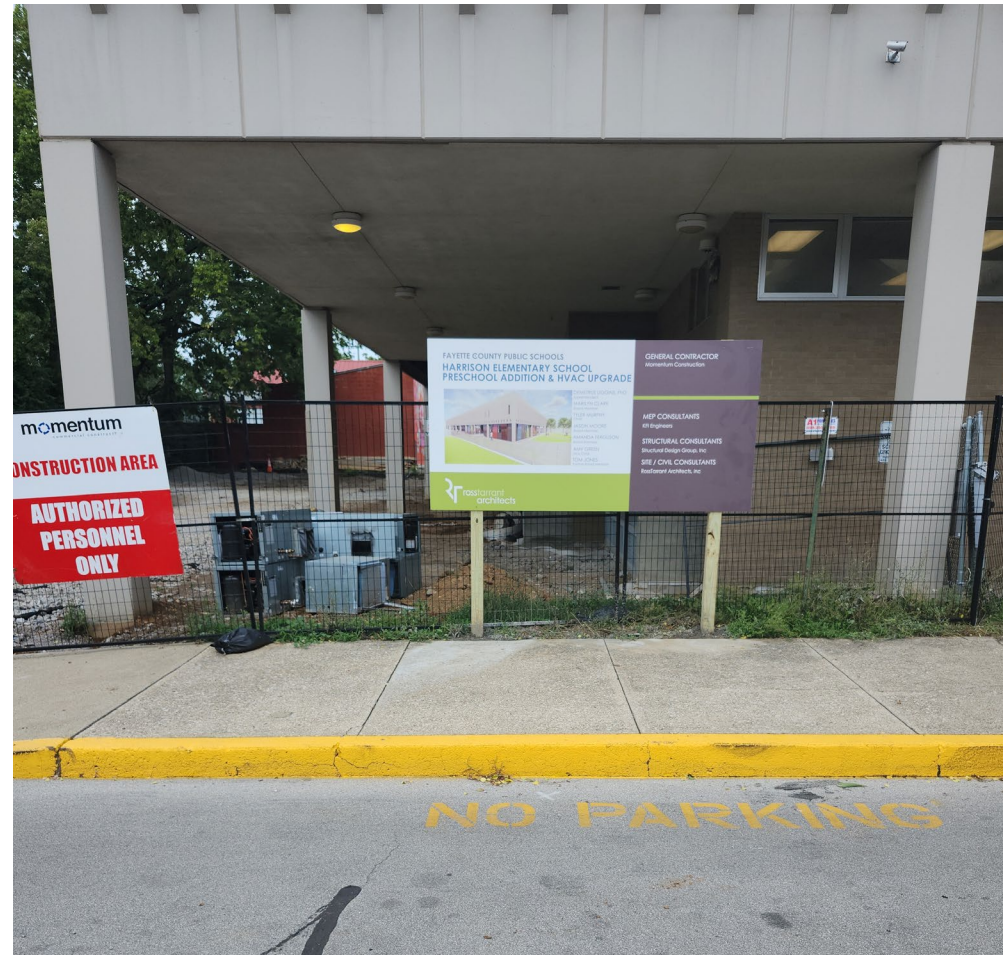

Week Ending August 02, 2024



# Harrison Elementary – Preschool Classrooms Addition & HVAC

Heat Pump has been stored in enclosed storage



Week Ending August 02, 2024

# Harrison Elementary – Preschool Classrooms Addition & HVAC



The pathway to the dumpster has been graveled



Week Ending August 02, 2024



# Harrison Elementary – Preschool Classrooms Addition & HVAC

Electrical work above the ceiling is in progress.



Week Ending August 02, 2024

# Harrison Elementary – Preschool Classrooms Addition & HVAC



New entrance on Jefferson Street



Week Ending August 02, 2024
