


Mary E. Britton Middle School

➤ **Completed/Work in Progress:**

- Continuing Sidewalks/Ramps and Exterior Storm Drainage
- Continuing Canopy Supports
- Masonry Demobilizing
- Continue Exterior Metals MCM and Batten Seam at Area C
- Started Window Frame Installation
- Continuing Wall tile and Terrazzo at Area A Second Floor
- Started Elevator Install and Complete Next Week
- Continue Sprinkler at Area D finish Next Week, Continue Overhead Plumbing at Strom Shelter
- Continue Electrical Rough In and Equipment/Panel Set UP

➤ **Upcoming Look Ahead:**

- Continue Site Concrete and Set Up For Curb and Gutter Installation
- Install Stairs at Area C
- Finish Install all Canopy Brackets and field measure for Canopies
- Continue Exterior Framing
- Continue Interior Soffit and Wall Framing at Area D
- Continue Hanging and Finishing Sheetrock
- Finish Wall Tile Area C Second Floor and Terrazzo Area C Second Floor
- Continue Window Frame Installation Area B/D Locker Room and Misc Store Front
- Continue MCM Panel Install at Boxed Sill Windows
- Sprinkler Finish A, B, C and D by Next Week

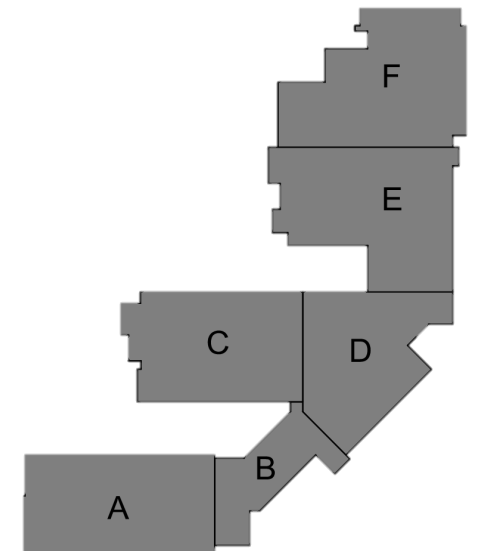

Mary E. Britton Middle School



Area A – Box Out Framing Continues



Week Ending August 23, 2024



Mary E. Britton Middle School

Area A – Furring for ACM Panels Continues



Week Ending August 23, 2024

Mary E. Britton Middle School



Area B- Electrical Roughins Continue in Admin Suite



Week Ending August 23, 2024



Mary E. Britton Middle School

Area B – Metal Soffit Framing Complete in Corridor



Week Ending August 23 2024

Mary E. Britton Middle School



Area C – Framing at Roof Continues



Week Ending August 23, 2024



Mary E. Britton Middle School

Area C – Media Center Windows Started



Week Ending August 23, 2024

Mary E. Britton Middle School



Area E – Cafeteria Box Outs Complete



Week Ending August 23, 2024



Mary E. Britton Middle School

Area E – Cafeteria Vertical Metal Panel Started



Week Ending August 23, 2024
