

# Crown Point Community School Corporation Construction Projects

## Board Report August 26, 2024



# **Crown Point Community School Corporation Construction Projects**

## **Table of Contents**

**Board Report**  
August 26, 2024

- **High School Additions & Renovations**
- **Colonel John Wheeler Middle School Additions & Renovations**
- **Solon Robinson Elementary Additions & Renovations**
- **Winfield Elementary Additions & Renovations**
- **Lake Street Elementary Additions & Renovations**





# Progress Photographs



**Hallway Renovation Completion**

## **High School Additions & Renovations:**

- Started metal fascia cover to north ticket booths
- Started landscaping restoration to varsity softball and varsity baseball outfield areas, behind masonry remediation
- Completed rubber base around all locker bases in the new commons area
- Completed VCT & base to Performing Arts addition corridor
- Completed all concrete sidewalk replacement to the 4 north entrances



# Progress Photographs



**New Locker Commons Area**

## **High School Additions & Renovations:**

### **Next Four Weeks**

- Complete added ornamental gate installation - gates in fabrication
- Complete punch list corrections in the athletic fields
- Complete combi-oven and espresso machine installation to the satellite kitchen
- Complete the owner change for VCT accent VCT tile to the 2<sup>nd</sup> floor corridor
- Complete missing locker number plates and missing trim pieces
- Change out TV studio sound doors and trim
- Start pool pump room renovation




# Progress Photographs



**New Media Center Furniture**

**Finished Main Corridor**

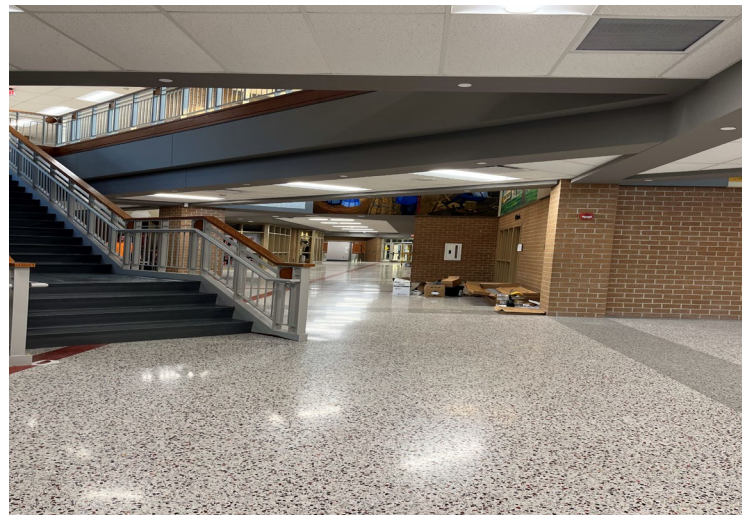

## **John Wheeler Middle School**

### **Additions & Renovations:**

- Completed flooring
- Completed painting
- Completed furniture
- Completed punch list items

### **Next Four Weeks**

- Fire annunciator map will be installed during fall break



# Progress Photographs



**Art Room**

## **Solon Robinson Elementary School** **Additions & Renovations:**

- Finished Unit A addition CMU
- Finished setting Unit A structural steel
- Finished installing Unit E classroom carpet
- Finished installing Unit E epoxy
- Finished roofing cafeteria addition
- Finished playground sitework
- Began Unit A addition mechanical piping and roofing
- Finished painting gym
- Finished installing Unit E casework
- Finished bus drop-off sitework



# Progress Photographs



**Unit D Hallway**

## **Solon Robinson Elementary School** **Additions & Renovations:**

### **Next Four Weeks**

- Finish Unit A addition brick
- Finish setting kitchen addition structural steel
- Finish installing Unit E corridor carpet
- Finish roofing kitchen addition
- Begin painting cafeteria addition
- Begin installing playground equipment
- Continue Unit A addition roofing
- Begin installing gym athletic equipment
- Continue re-roofing existing building



# Progress Photographs



**New Media Center Progress**

## Winfield Elementary School

### Additions & Renovations:

- Started the RTU in the media center
- Finished flooring in media center, STEM and SGI rooms
- Finished installation of the markerboards and tack boards
- Finished painting all the walls in the new media center and around the school
- Installed all the cabinets in STEM and media center
- Finished the concrete pad in the courtyard
- Roofers re-roofed the rest of the area above classrooms
- Installed all the technology items in kitchen, cafeteria, and media center



# Progress Photographs



**Hill Removal in Courtyard**

## Winfield Elementary School

### Additions & Renovations:

#### Next Four Weeks

- Finish working on the punch list items
- Finish coping on the roof
- Seed the area around the cafeteria
- Start working on Insulated panels
- Modify the gate in the northwest side of the parking lot
- Install last 2 aluminum storefronts in existing mechanical room



# Progress Photographs



## Lake Street Elementary School Additions & Renovations:

- Completed new playground
- Completed gymnasium rubber floor
- Completed stage flooring
- Completed cafeteria renovations
- Completed clearstory entrance storefront
- Completed stage curtain install and owner training
- Completed new detention pond and stormwater drainage piping



**Completed Hallway**



# Progress Photographs



## Lake Street Elementary School

### Additions & Renovations:

#### Next Four Weeks

- Complete east elevation building facia metal and roof edge metal
- Complete gymnasium floor striping
- Complete stage wood trim and handrails
- Complete entire building EIFS
- Complete wheelchair lift inspection and owner training
- Complete cafeteria sound system and owner training



**New Playground Progress**
