

MCHS

CONSTRUCTION PROJECT UPDATE – NOVEMBER 4, 2019



CONSTRUCTION PROJECT UPDATE

- **BUILDINGS – COMPLETED LAST 30 DAYS**

- CTE...CEILING TILE COMPLETED. CARPET IN OFFICE AREA COMPLETE. VCT COMPLETE. FINAL PAINTING IN PROGRESS. CASEWORK HAS BEGUN. FENCING HAS BEGUN. ALL FINISH WORK CONTINUES TOWARDS CERTIFICATE OF OCCUPANCY (CO).
- HS...OUTSIDE POLE LIGHTS INSTALLED. ROADWAY PAVING HAS BEGUN. ATHLETIC FIELDS IN PROGRESS. ATHLETIC BUILDINGS IN PROGRESS. AREA A MECHANICAL IS COMPLETED. AUDITORIUM CEILING WORK IS IN FINAL STAGES (A LOT OF WORK HERE!)

CONSTRUCTION PROJECT UPDATE

- **NEXT 30 DAYS**

- CTE – GOAL IS TO ACHIEVE CERTIFICATE OF OCCUPANCY, THEN THE MOVING BEGINS!
- HS –IN WALL AND OVERHEAD ROUGH IN MEP TO CONTINUE FIRST AND SECOND FLOORS OF ALL AREAS (CARRY OVER). CONTINUE BLOCK FILL. POUR SLAB ON GRADE OF KITCHEN (CARRY OVER, WEATHER RELATED). COMPLETE AUDITORIUM OVERHEAD AND REMOVE SCAFFOLDING SYSTEM.
- SITE –CONTINUE TO PAVE ROADWAYS AND PARKING LOTS. COMPLETE FINAL GRADING TASK. BEGIN HOME SIDE BLEACHER INSTALLATION. CONTINUE INSTALLING SITE FENCING.



CTE SUBSTANTIAL COMPLETION DATE – November 22, 2019
(+17 days from last month, +119 days from contract date
July 26, 2019) **NOTE: Scheduling Company met 10/30/2019.**
Completion dates pending review.

MCHS SUBSTANTIAL COMPLETION DATE – March 23, 2020
(-2 days from last month, +46 days from contract date of
February 6, 2020). **NOTE: Pending Review.**


Second Semester Start Date for Students – January 23, 2020

Next Meeting Date 11/7/2019



CTE Main Courtyard


KEY PLAN





CTE Courtyard Circular Loop


KEY PLAN

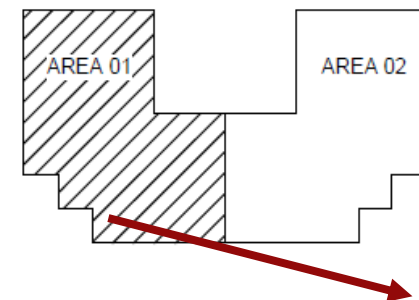



Parking for the CTE Building and Walkway


KEY PLAN





East Face of Construction Trades - Courtyard


KEY PLAN

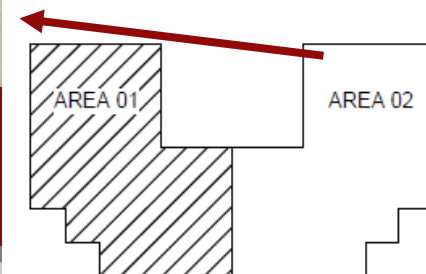



Work In Progress:
Electrical work for Woodworking
Equipment

KEY PLAN




Woodworking Shop



**Work In Progress:
Mr. Kerns setting new Planner
into location**

KEY PLAN




Mr. Kerns and Mr. Blankenship set the new planner



Work In Progress:
Dale and Jed constructing the
wall panels for the paint booth.

KEY PLAN




Dale Davis and Jed Scott construct the paint booth



AG-Science

KEY PLAN





MCS- Robotics


KEY PLAN





Main Corridor CTE Building


KEY PLAN





Front Reception


KEY PLAN

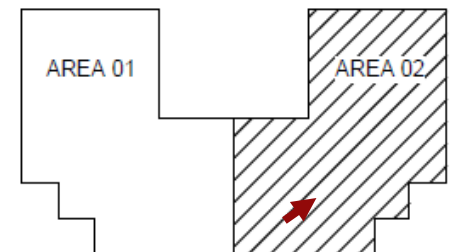



Office Area


KEY PLAN

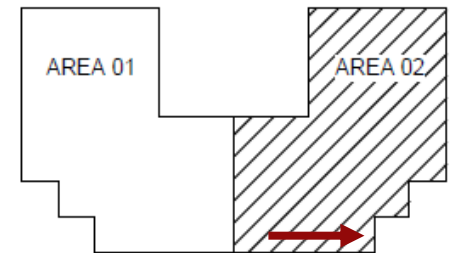



Work In Progress:
Electrical work in Flex Lab
Painting Interior Walls

KEY PLAN

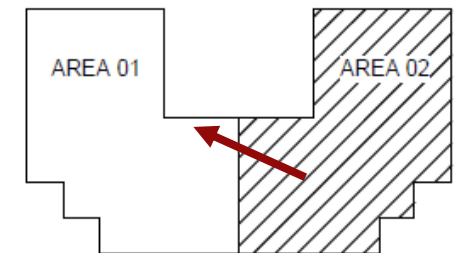

Flex Labs



**Work In Progress:
Electrical Work on the Bus Bar**

KEY PLAN




MCS Robotics



Work In Progress:
Finish work, painting and overhead
ceilings


KEY PLAN

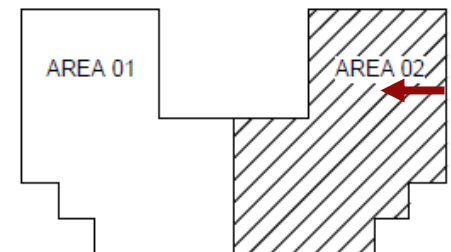

Industrial Maintenance/Welding Classroom



KEY PLAN

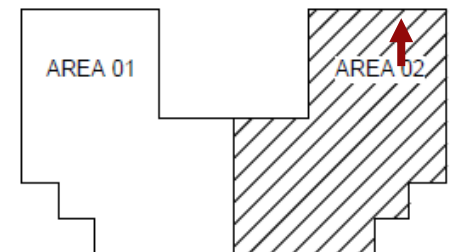


Welding Shop



Automotive Shop


KEY PLAN

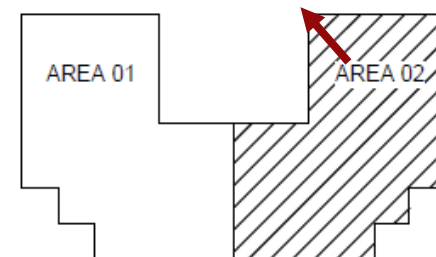



Work In Progress:
Painting window frames.
Touch up paint


KEY PLAN

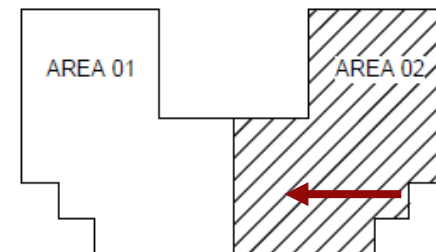

Second Floor Main Corridor



Health Occupations Casework

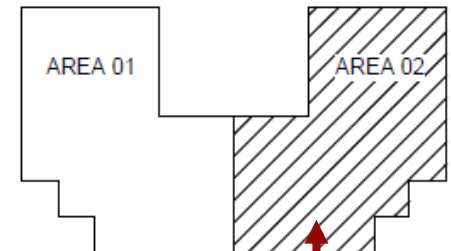



Second Floor Center Corridor


KEY PLAN





Second Floor Boys Gang Restroom


KEY PLAN





**Work In Progress:
Pouring HD Concrete for
Courtyard to Access Road
Connector**

KEY PLAN




One of Four Health Occupations Labs – Note Bed Locations



**Work In Progress:
Pouring HD Concrete for
Courtyard to Access Road
Connector**

KEY PLAN




Opposite View of Same Health Lab-Note Washer/Dryer Location




West Facing Wall of Automotive – Weight Room in Background

KEY PLAN

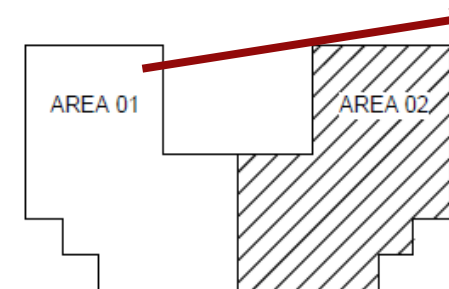



**Work In Progress:
Placing stone in Athletic Field
Access Road**

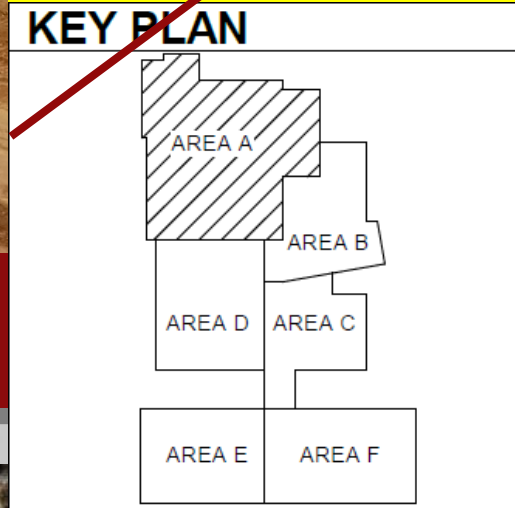


Tennis Courts and Athletic Facilities



Work In Progress:
Grading work for Access Road

KEY PLAN

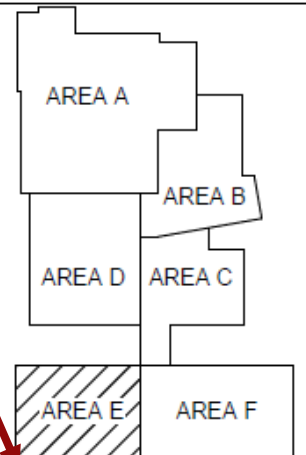


Band Room – North/West Faces of Area E



South/East Faces of Area F


KEY PLAN

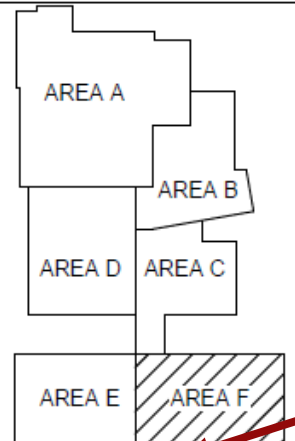



Area C Media/Office Left – Area B Dining Right


KEY PLAN

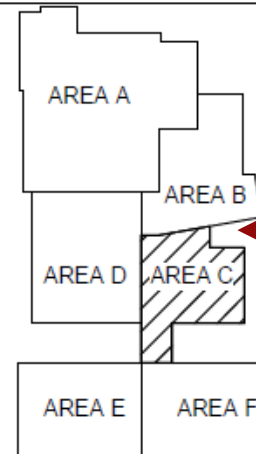



Area B Dining/Kitchen/Main Receiving


KEY PLAN

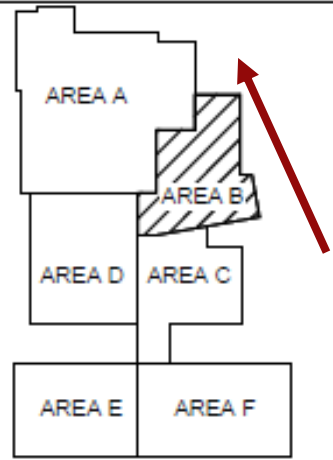



Main Student Parking Lot – Visitor Ticket Booth in background


KEY PLAN

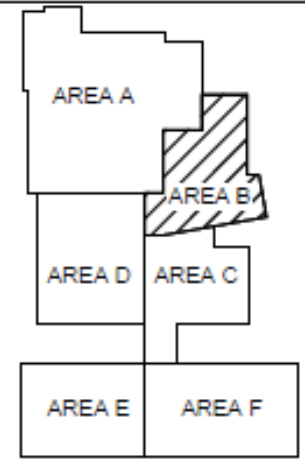



Work In Progress:
Bleacher Crew from Texas is starting to layout home side bleacher footings.

SITE KEY PLAN

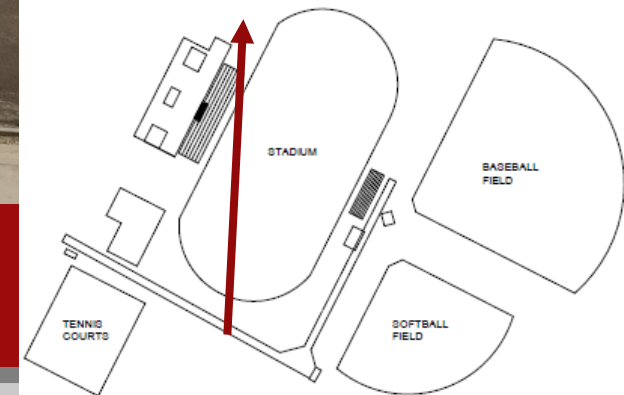


Home Side Athletic Facilities




Football Field and Running Track

SITE KEY PLAN

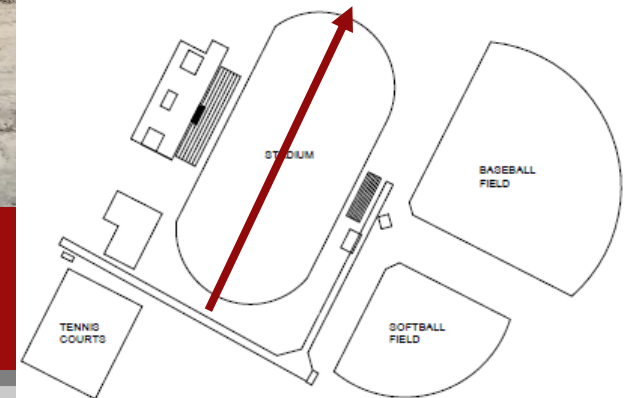




Visitor Side Ramp and Stairs

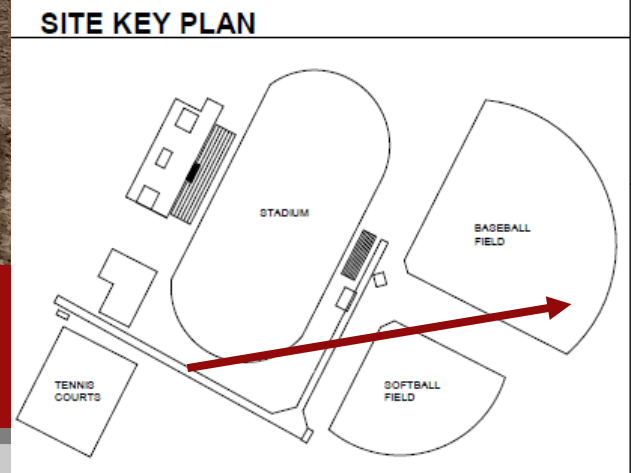



Sidewalk to Home Side Ticket Booth

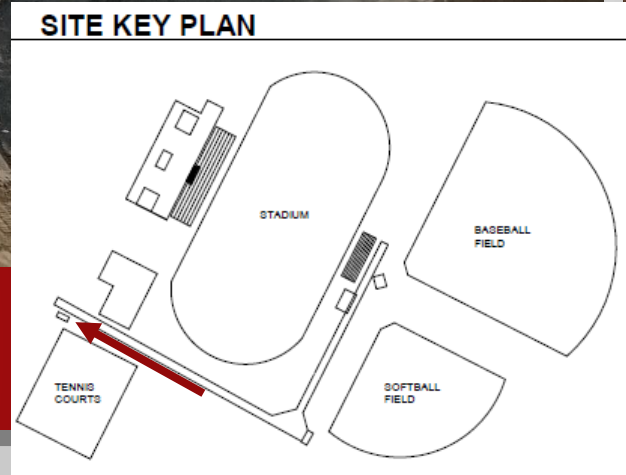




Main Road facing Glenn Road




Bus Access Drive to Athletic Fields

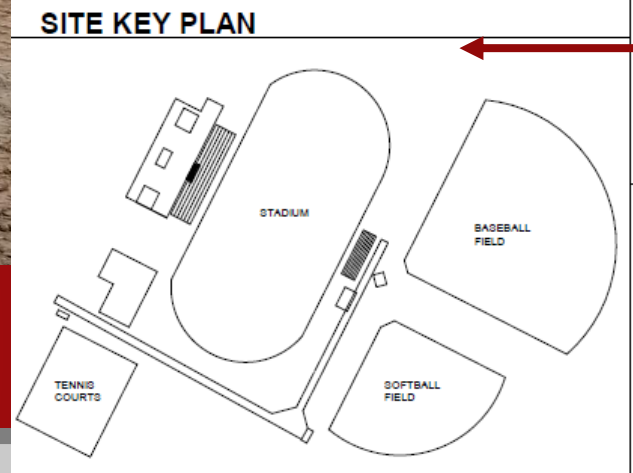




Back of Boys Baseball Field – Note Retaining Wall

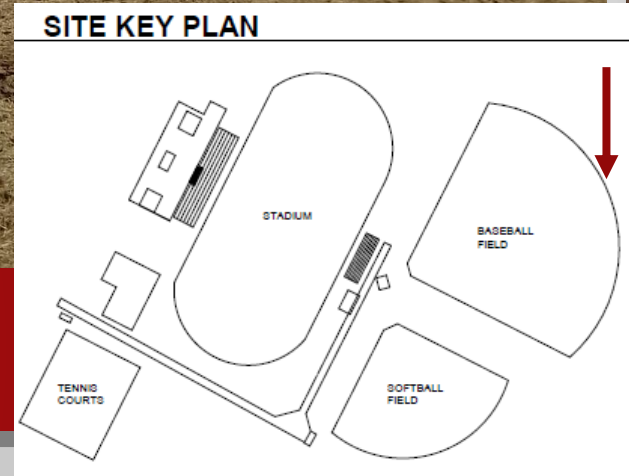












Lower Retaining Pond Filled In

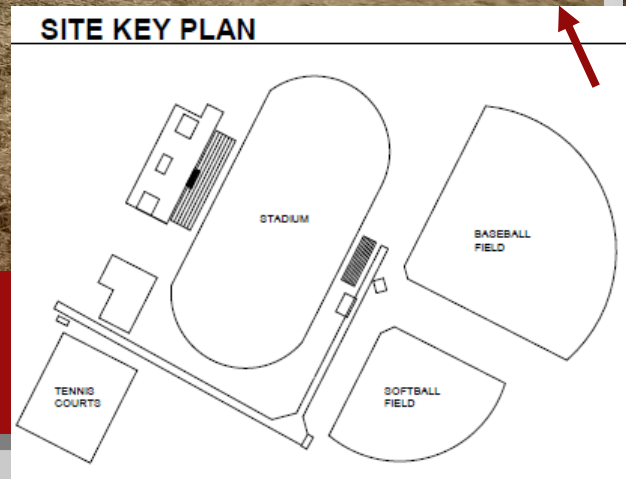



END SLIDE – QUESTIONS???

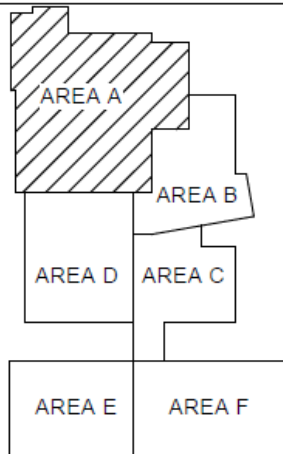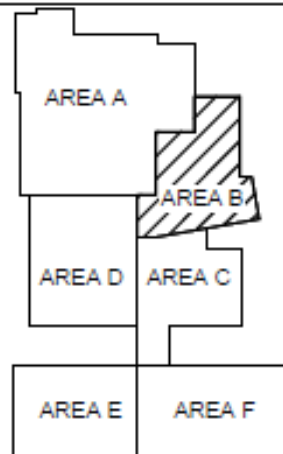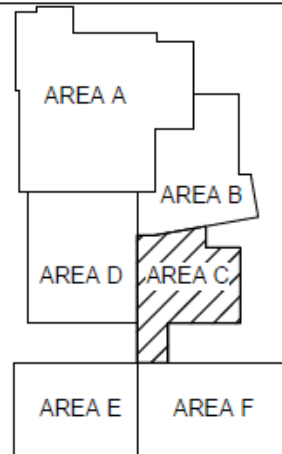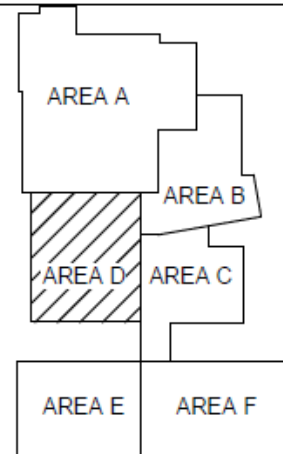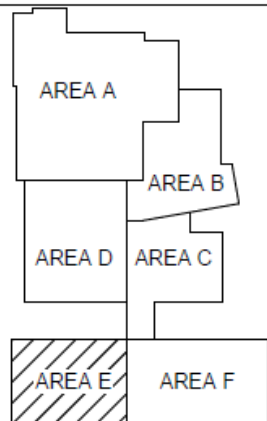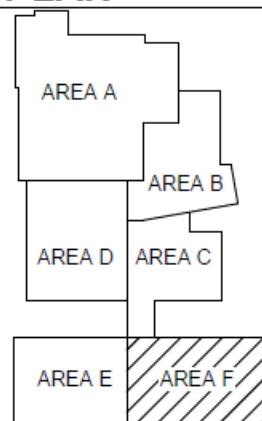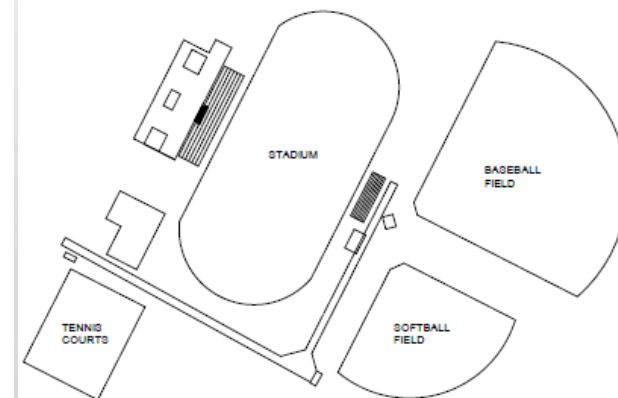KEY PLAN**KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****KEY PLAN****SITE KEY PLAN**

KEY BLOCK – DO NOT DELETE



