

Measure BB Bond

21st Century Classroom Improvements
SEPTEMBER 26, 2024



CUMMING
GROUP



HLPUSD MEASURE BB - SUMMARY

SCHOOLS IN PROGRESS



IN PROGRESS-CONSTRUCTION

- La Puente HS
- Los Altos HS
- Wilson HS

BIDDING CURRENTLY

- California ES
- Baldwin ES
- Los Molinos ES
- Graziade ES

AT DSA FOR REVIEW

- Kwis ES
- Lassalette ES
- Fairgrove K-8
- Sierra Vista MS

IN DESIGN

- Orange Grove MS
- Palm ES
- Valinda ES
- Sparks E
- Wing Lane ES
- Valley Alternative

COMPLETED

- Nelson ES
- Los Altos ES
- Workman ES
- Mesa Robles K-8
- Cedarlane K-8
- Sparks MS
- Newton MS
- Grandview K-8
- Stimson EC
- Workman HS

PHASE B PROGRESS

Anticipated Construction Start Fall of 2024

1. Baldwin ES	Construction Documents	First Bid advertisement 8/14/2024	Open Sept 24, 2024
2. California ES	Construction Documents	First Bid advertisement 8/14/2024	Open Sept 24, 2024
3. Los Molinos ES	Construction Documents	First Bid advertisement 8/14/2024	Open Sept 24, 2024
• Interim Housing Los Robles (Tentative)			
4. Graziade ES	Construction Documents	First Bid advertisement 8/14/2024	Open Sept 24, 2024
• Interim Housing Bixby (Tentative)			

Anticipated Construction Start Fall of 2024

5. Kwis ES	Construction Documents	At DSA for Plan Review	Submitted 8/9/2024
6. Lassalette ES	Construction Documents	At DSA for Plan Review	Submitted 8/9/2024 Anticipated

Construction Start New Year of 2025

7. Palm ES	Construction Documents	50% Const. Docs.	District Review 8/16/2024
• Interim Housing Los Robles (Tentative)			
8. Valinda ES	Construction Documents	50% Const. Docs.	District Review 8/16/2024
9. Fairgrove K-8	Construction Documents	At DSA for Plan Review	Submitted 8/12/2024
• Interim Housing Del Valle (Tentative)			

Anticipated Construction Start Spring of 2025

10. Orange Grove MS	Construction Documents	Schematic Design	
---------------------	------------------------	-------------------------	--

Anticipated Construction Start Summer of 2025

11. Sierra Vista	Construction Documents	At DSA for Plan Review	Submitted 9/17/2024
12. Sparks ES	Construction Documents	Design Development	District Reviewed 8/2/2024
• Interim Housing Sunset (Tentative)			

Anticipated Construction Start Summer -Fall of 2025

13. Wing Lane ES	Construction Documents	Design Development	District Reviewed 9/18/2024
14. Valley Alternative	Construction Documents	Design Development	District Reviewed 9/19/2024

Anticipated Construction Start Fall of 2025

DSA PLAN APPROVAL GRAZIDE ELEMENTARY



8/29/2024 - APPROVAL OF PLAN(S)

Dr. Alfonso Jimenez
HACIENDA-LA PUENTE UNIFIED SCHOOL DISTRICT
15959 EAST GALE AVENUE
CITY OF INDUSTRY, CA 91745

Project: Los Molinos Elementary School

Total Scope of Project: Alterations to 6-Classroom Bldgs. A, P-17, P-18, P-20, P-21, and P-22 (A-23396, A03-104589, A03-106053, A03-117077, A03-117371, A03-118064, A120183).

Increment #: 0

Application #: 03-124134

File #: 19-38


“Drawings and specifications for the subject project have been examined and stamped by the Division of the State Architect (DSA) 8/29/2024.”

Drawings and specifications for the subject project have been examined and stamped by the Division of the State Architect (DSA) for identification on 8/29/2024. This letter constitutes the “written approval of the plans as to the safety of design and construction” required before letting any contract for construction, and applies to the work shown on these drawings and specifications. The date of this letter is the DSA approval date.




HIGH SCHOOL
REFRESH
PROJECTS

HIGH SCHOOL REFRESH GROUP 1

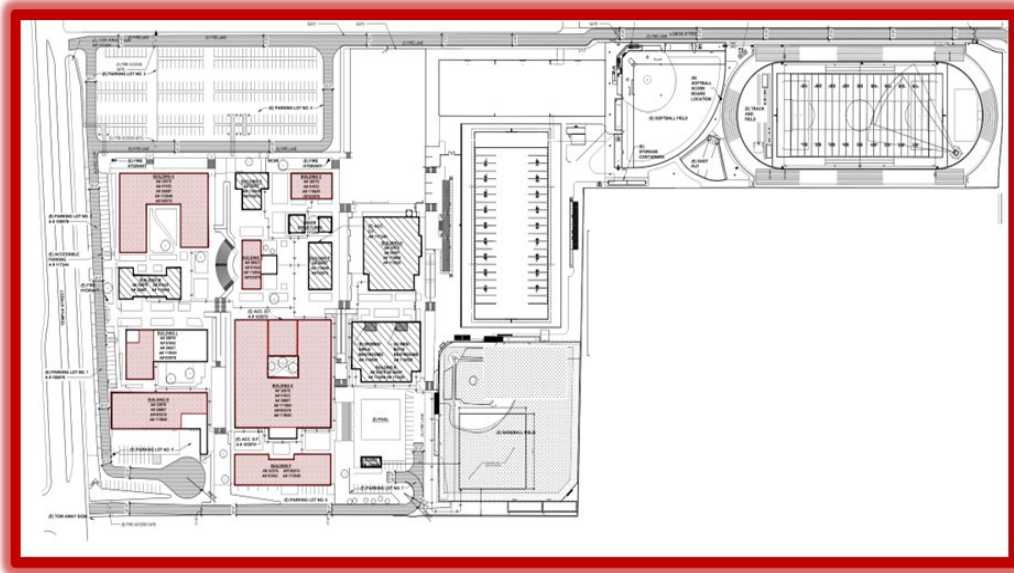

WORKMAN HIGH SCHOOL

43 CLASSROOMS

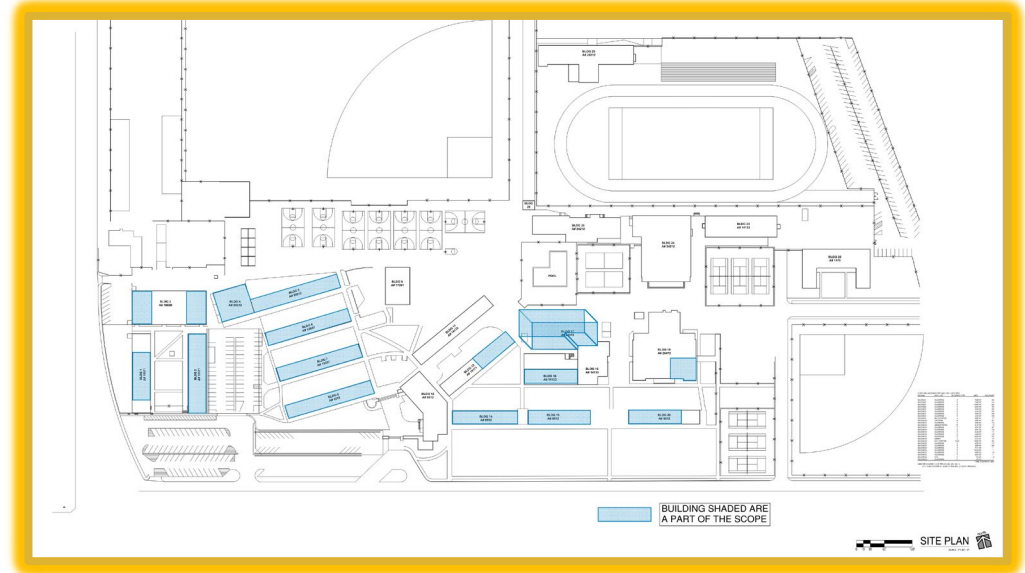

LA PUENTE HIGH SCHOOL

55 CLASSROOMS

SCHOOL	START DATE	ANTICIPATED COMPLETION DATE
WORKMAN HS	1/16/2024	9/13/2024 Completed
LA PUENTE HS	1/16/2024	11/1/2024

REFRESH GROUP 1

Workman HS Phase 4: Classroom C-2 Risers Removed




REFRESH GROUP 1


La Puente HS Phase 4: Classroom A-12 Before and




HIGH SCHOOL REFRESH GROUP 2

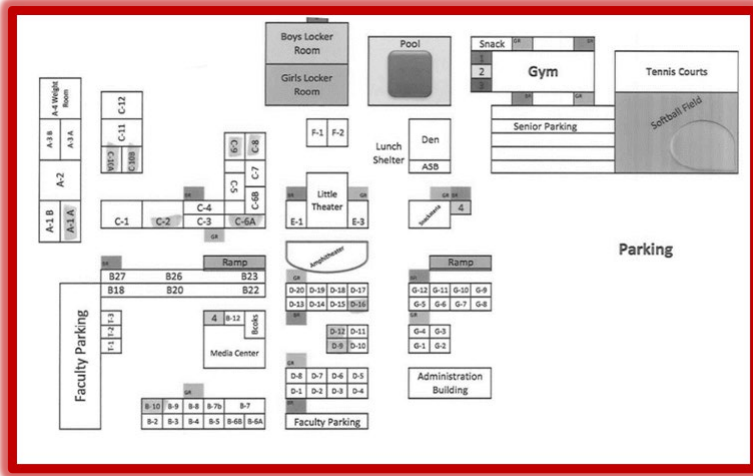

WILSON HIGH SCHOOL
59 CLASSROOMS

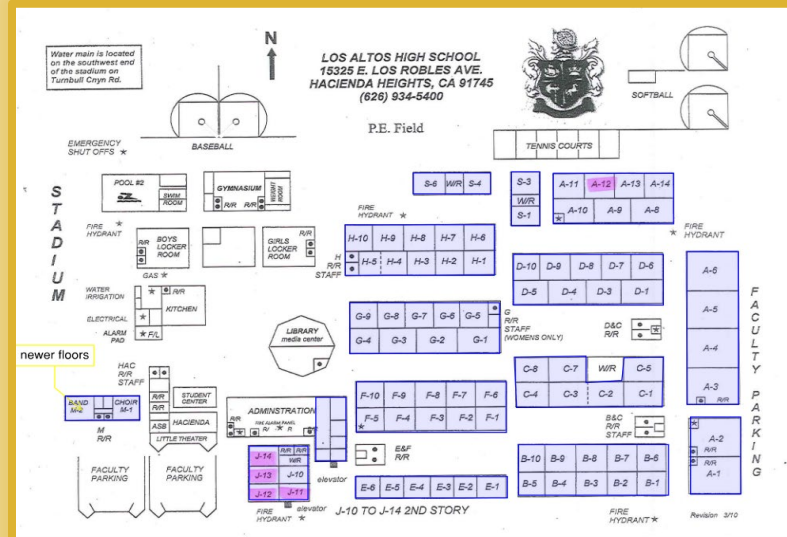

LOS ALTOS HIGH SCHOOL
69 CLASSROOMS

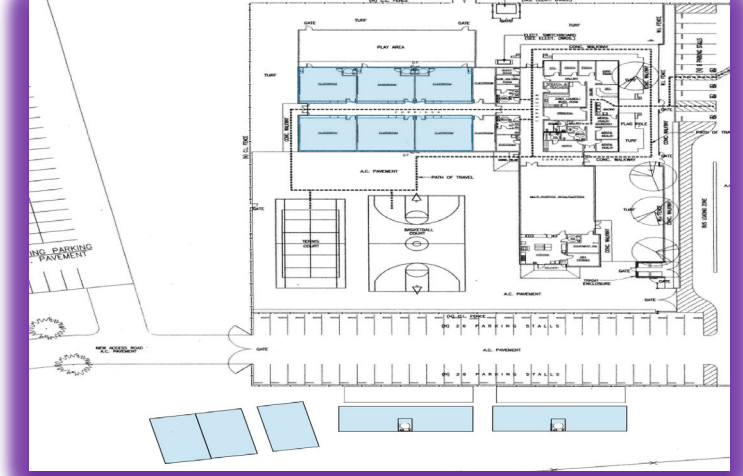

STIMSON LEARNING CENTER
10 CLASSROOMS

SCHOOL	START DATE	ANTICIPATED COMPLETION DATE
WILSON HS	3/4/2024	2/21/2025
LOS ALTOS HS	3/4/2024	4/18/2025
STIMSON EC	7/1/2024	7/31/24 COMPLETED

REFRESH GROUP 2
Wilson HS Phase 2
Classroom D-2 Before
and After



REFRESH GROUP 2

Los Altos HS Phase 4 Completed Classrooms





QUESTIONS
