




2023 BOND

MAJOR PROJECTS UPDATE

OCTOBER 2024



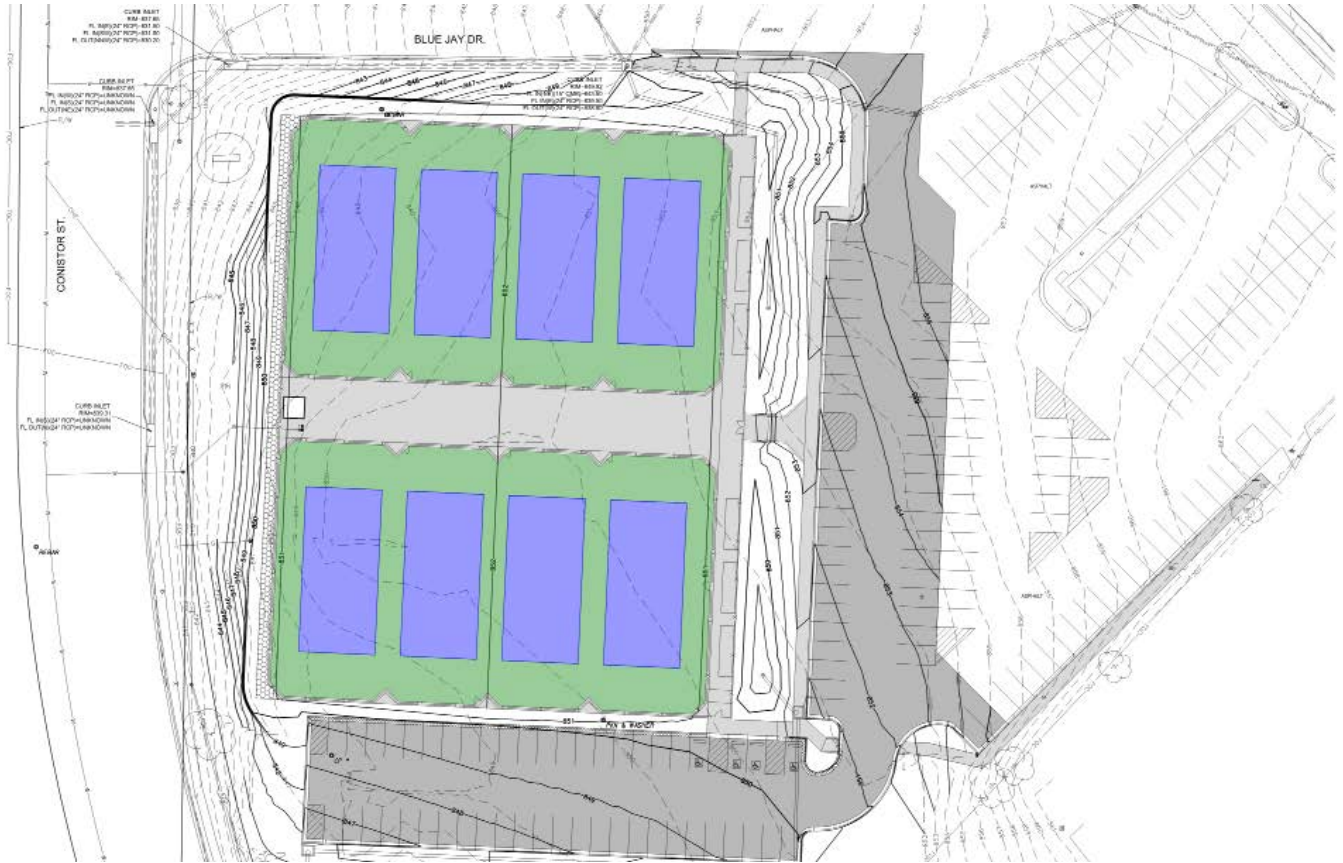

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

UPCOMING

Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North


WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

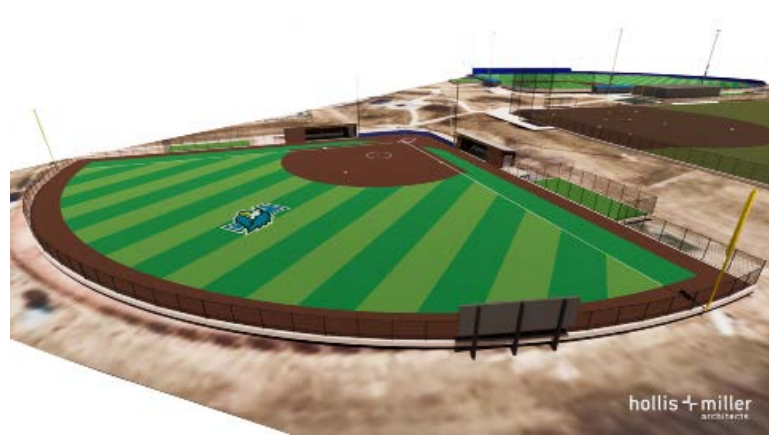

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024



Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

**WEEKLY
PROGRESS
REPORT**

LPS Ball Fields 08/09/2024

Liberty Public Schools



PROJECT STATUS

- LNHS
- Punch List Completion
 - Final Inspection Passed

- LHS
- Punch List Completion
 - Retaining Wall Ongoing
 - Final Sod Ongoing

UPCOMING

- LHS
- City Inspection

Project Completion
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

PROJECT STATUS

South Valley MS - Upgrades Complete
Discovery MS - Upgrades Complete
EPiC Elementary - Upgrades Complete
Liberty North High School - Upgrades Ongoing

UPCOMING

Energy Inspections - All Four Schools
Emergency LED Fixtures

Project Completion
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

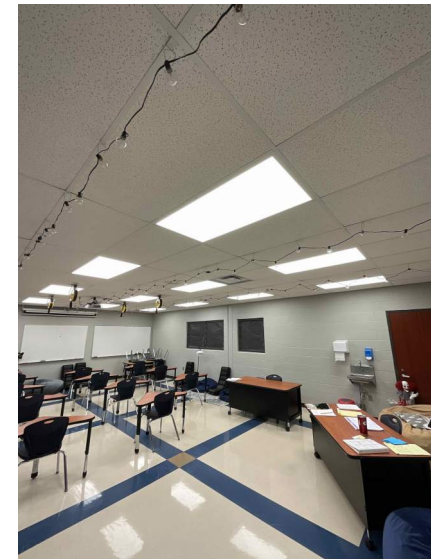

Liberty North HS

PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


UPCOMING

Energy Inspections All Four Schools
Emergency LED Fixtures

Project Completion
December 2023

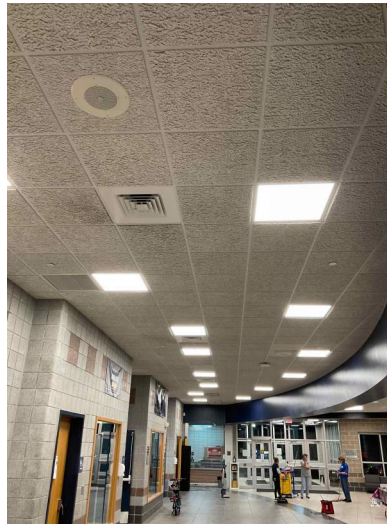


South Valley Middle School

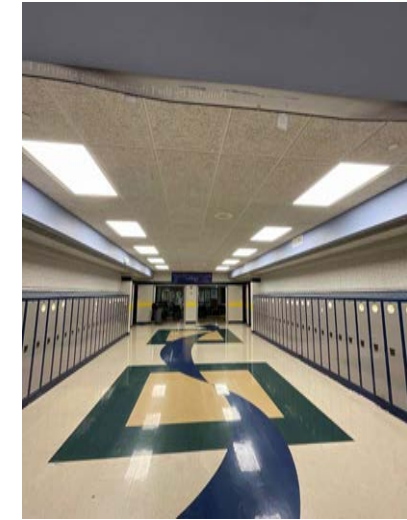

South Valley Middle School



Discovery Middle School

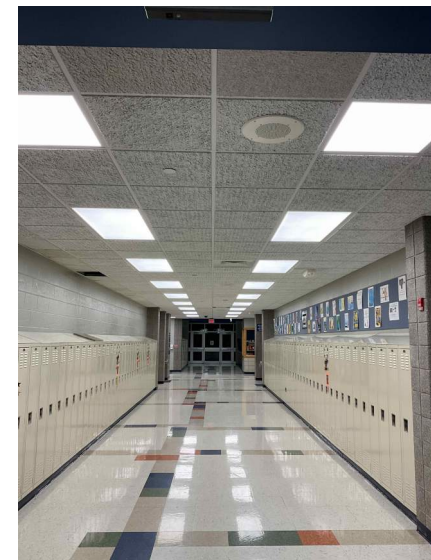

Discovery Middle School

WEEKLY PROGRESS REPORT



Epic Elementary



Epic Elementary



Liberty North High School




Liberty North High School



EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

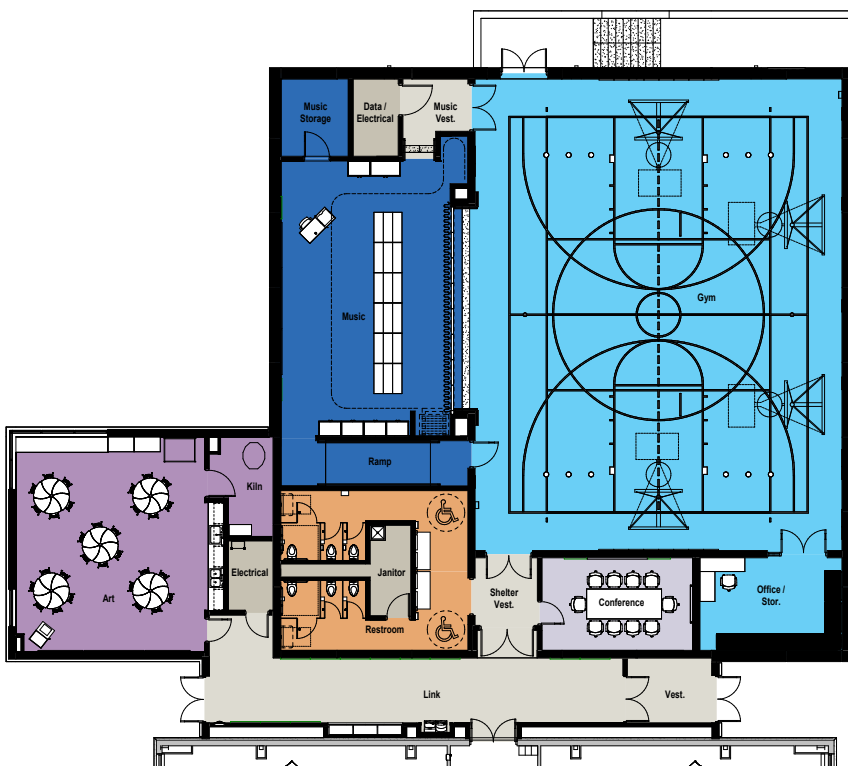

▲ Addition



▲ Renovation Area


PROJECT STATUS

- EPiC Elementary
- Remaining under-slab MEP complete
 - SOG complete
 - Waterproofing complete
 - MEP roof penetrations complete
 - Gym roofing and flashing on going
 - Interior CMU on going

UPCOMING

- EPiC Elementary
- Art room roofing and flashing
 - Art room metal panels
 - Exterior masonry
 - Art room window install
 - North Gym retaining wall
 - Perimeter sidewalks


Project Completion
EPiC February 2025

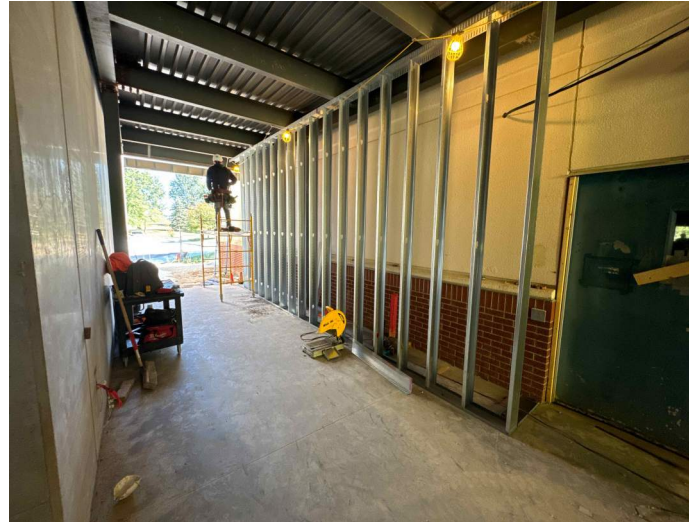

EPiC Elementary



EPiC Elementary

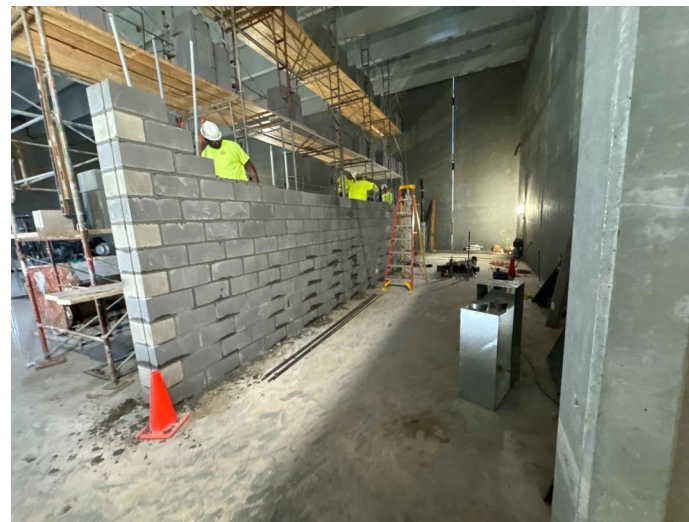

EPiC Elementary





EPiC Elementary



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

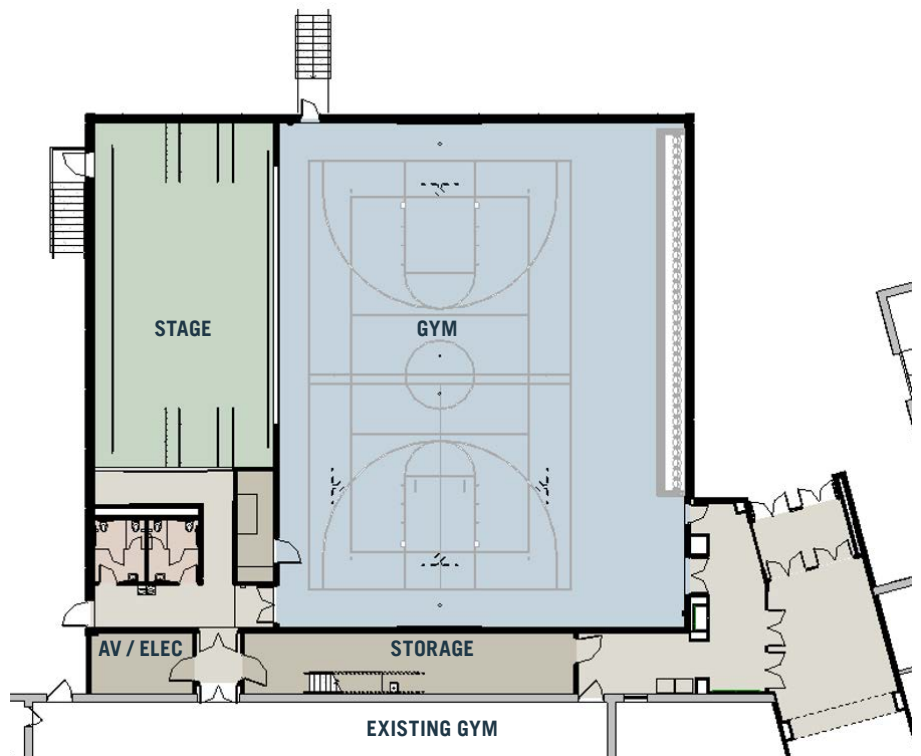

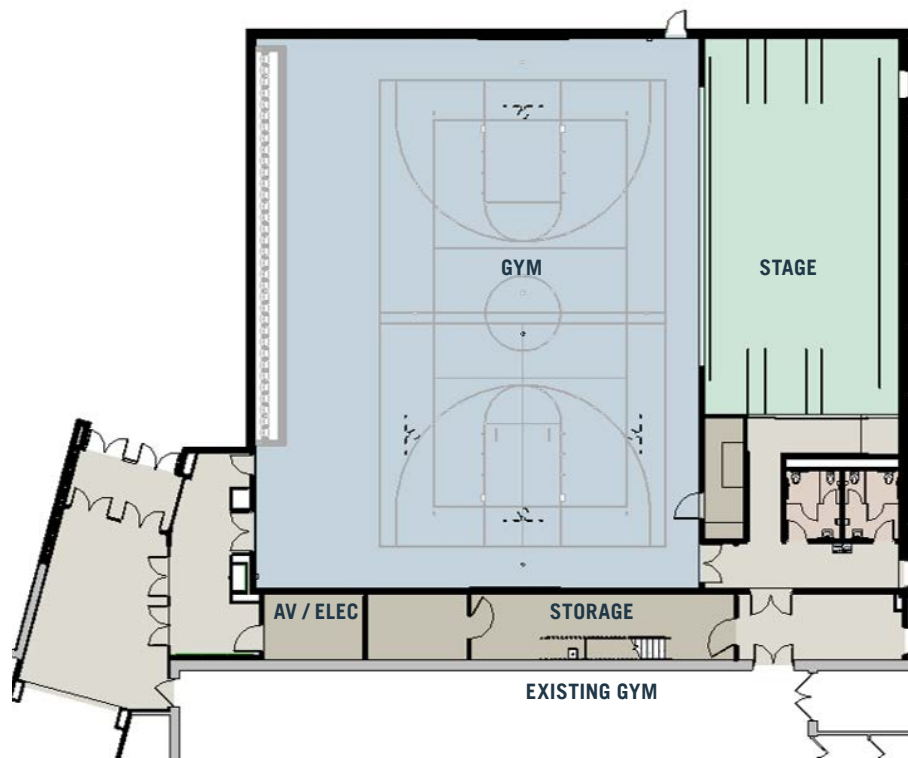

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025


PROJECT STATUS

- SVMS and DMS
- Pre-cast complete
 - Steel erection complete
 - Pre-cast waterproofing complete
 - SOG prep and pour ongoing at entry and link
 - SVMS roof blocking ongoing
 - DMS MEP under-slab ongoing

UPCOMING

- SVMS and DMS
- SOG at gym and theater
 - Interior CMU
 - DMS Roof blocking

Project Completion
SVMS and DMS June 2025

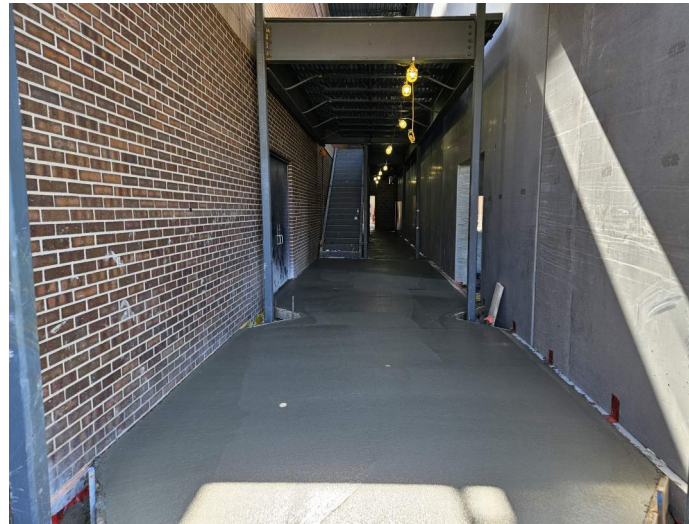

SVMS - Link SOG



SVMS - Gym SOG prep



DMS - Pre-cast



DMS - MEP Under-slab



hollis + miller



hollis + miller



hollis + miller



hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



10/7/24

PROJECT STATUS

- Interior framing complete
- Dryfall above freezer complete
- Canopy East framing complete
- Sequence 1 site fencing complete
- Refrigeration lines set
- MEP rough in 95% complete
- CMU trash enclosure complete

UPCOMING

- Metal panel Install ongoing
- Freezer panel install upcoming
- Canopy west framing ongoing
- Drywall upcoming
- Generator pad upcoming
- Dock levelers & overhead doors upcoming.

Project Completion
May 2025



Metal Panels East Wall



Metal Panels North Wall



CMU Trash Enclosure



Dryfall Above Freezer



Overhead Doors



Nutritional services



Dry Storage / Freezer



Warehouse

Fine Arts
Kid's Zone
Technology
Shared Amenities
Building Systems
Future Phase



District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

7/12/24

PROJECT STATUS

District Technology Center:
-Completed Communications Install
-Completed Interior Paint
-Completed All Exterior Paint
-Completed Floor Install
-Completed Data Pod Install
-Completed HVAC Equipment Install
-Completed Landscaping/Fence Install
-Completed Generator Install
-Certificate of Occupancy - Received July 9th

UPCOMING

District Technology Center:
-Complete Punchlist Work
-Complete Furniture Move In
-Server Switchover July 13th
-Staff Move in July 16th

Project Completion July 2024



IT Reception



Exterior



Kid's Zone Open Office



Fine Arts Open Office



Fine Arts Workshop



Restrooms



Breakroom



Data Pod Install



Exterior



Medium Conference Room



Kid's Zone Storage



IT Open Office



LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
 - Integrated SPED resources
 - Renovated cafeteria & scramble
 - Restroom renovations
- Exterior masonry repair & window replacement
 - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

10/4/24

PROJECT STATUS

Heritage Middle School

1964 Wing:

- Completed Overhead MEP Rough In
- Completed Overhead MEP Inspections
- Installed Roof Top Units
- Completed Drywall Install/Finish
- Continued Paint
- Began Ceiling Grid Install
- Began Storefront Install
- Began Flooring Prep
- Began Tile Install

UPCOMING

Heritage Middle School

1964 Wing:


- Complete Paint
- Complete Ceiling Grid Install
- Complete Tile Install
- Complete Window Installation
- Continue Casework Install
- Continue MEP Trimout
- Begin Flooring Install
- Begin Wall Paneling Install



1964 (Area A) Progress



1964 (Area A) Progress

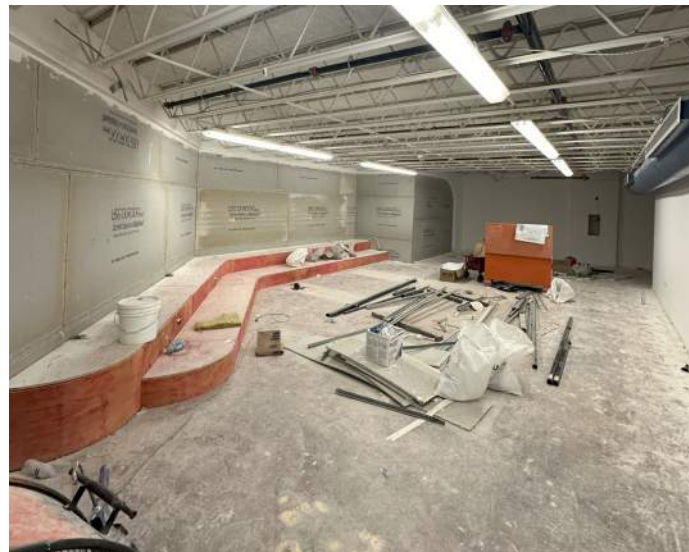

1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress




1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress

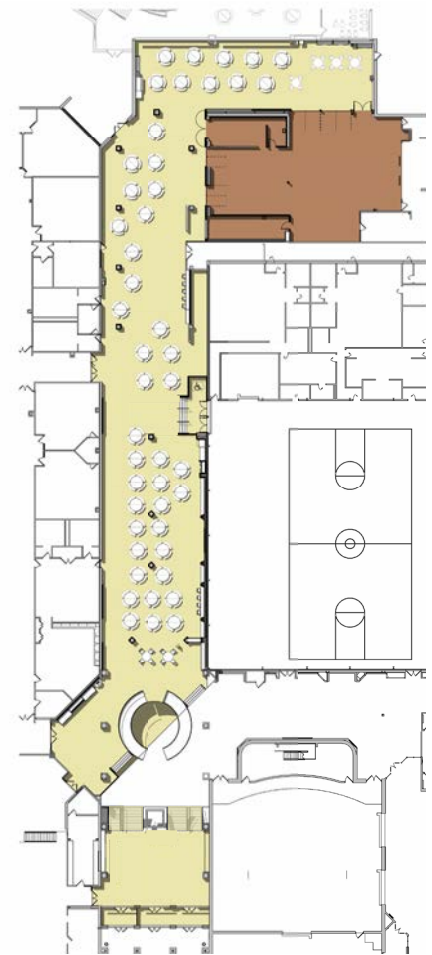

PHASE 2

Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025



PHASE 1

**WEEKLY
PROGRESS
REPORT**

Liberty High School

Liberty Public Schools



10/4/24

PROJECT STATUS

- Liberty High School
Build Back of 100's Wing Classrooms
- Completed MEP Overhead Rough In
 - Completed Overhead Rough In Inspections
 - Completed Ceiling Grid Install
 - Completed Drywall Finishing
 - Continued Paint
 - Continued Casework Install
 - Completed Tile Install
 - Begin Flooring Install

UPCOMING

- Liberty High School
Build Back of 100's Wing Classrooms:
- Complete Resinous Flooring
 - Begin Drop Ceiling Tiles
 - Complete Paint
 - Complete Casework Install
 - Complete Flooring Install
 - Begin Punchlist
 - Install Doors and Hardware
 - Install all Specialty Finishes

Project Completion: November 2024




Progress 100's Wing



Progress 100's Wing



Progress 100's Wing

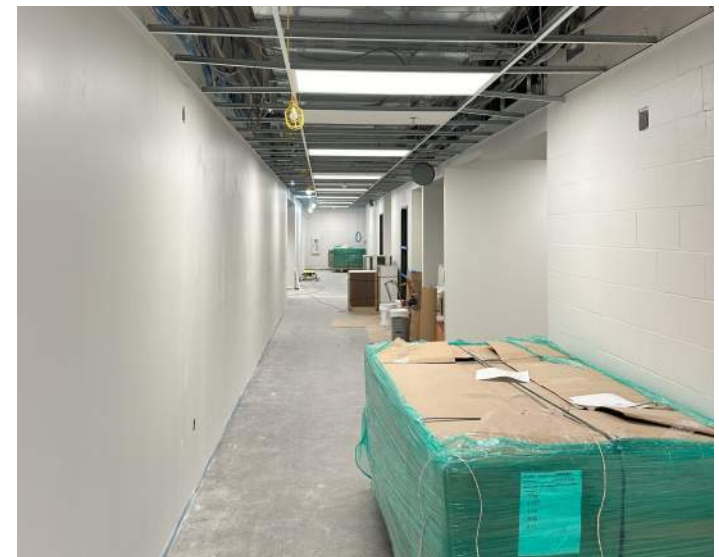

Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing




Progress 100's Wing



Shop Building


- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

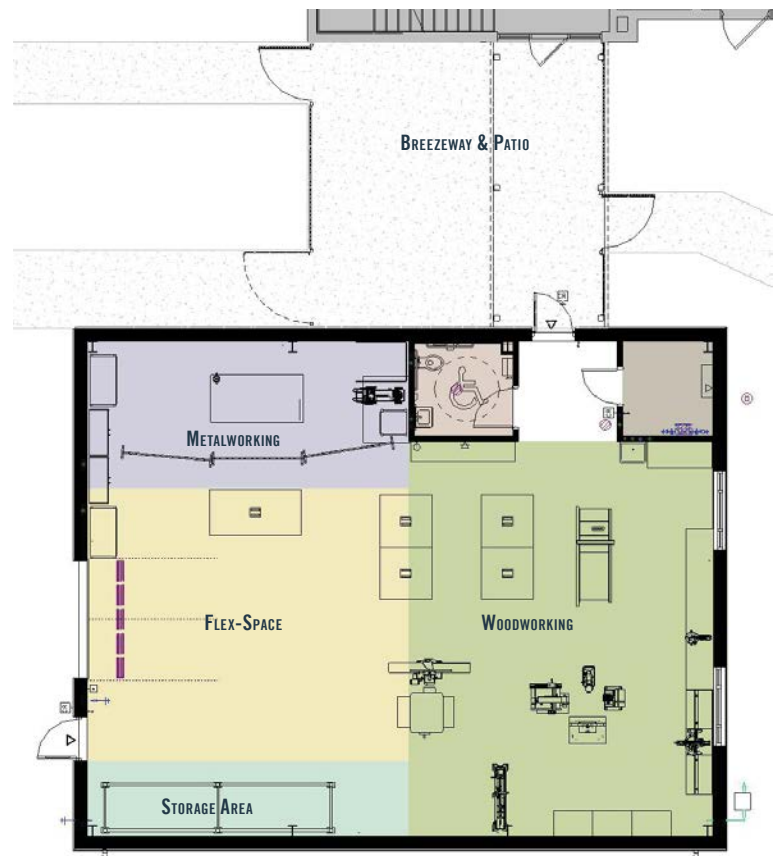


▲ Floor Plan

Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:
Spring 2024–Spring 2025

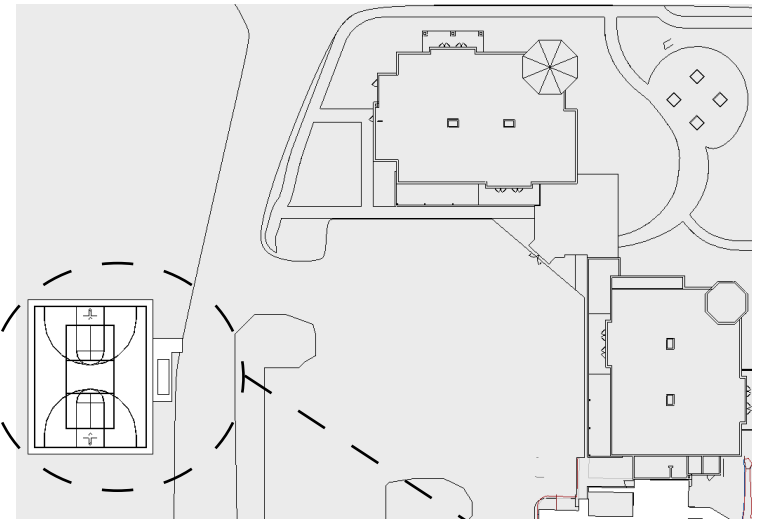


Overall Site Plan

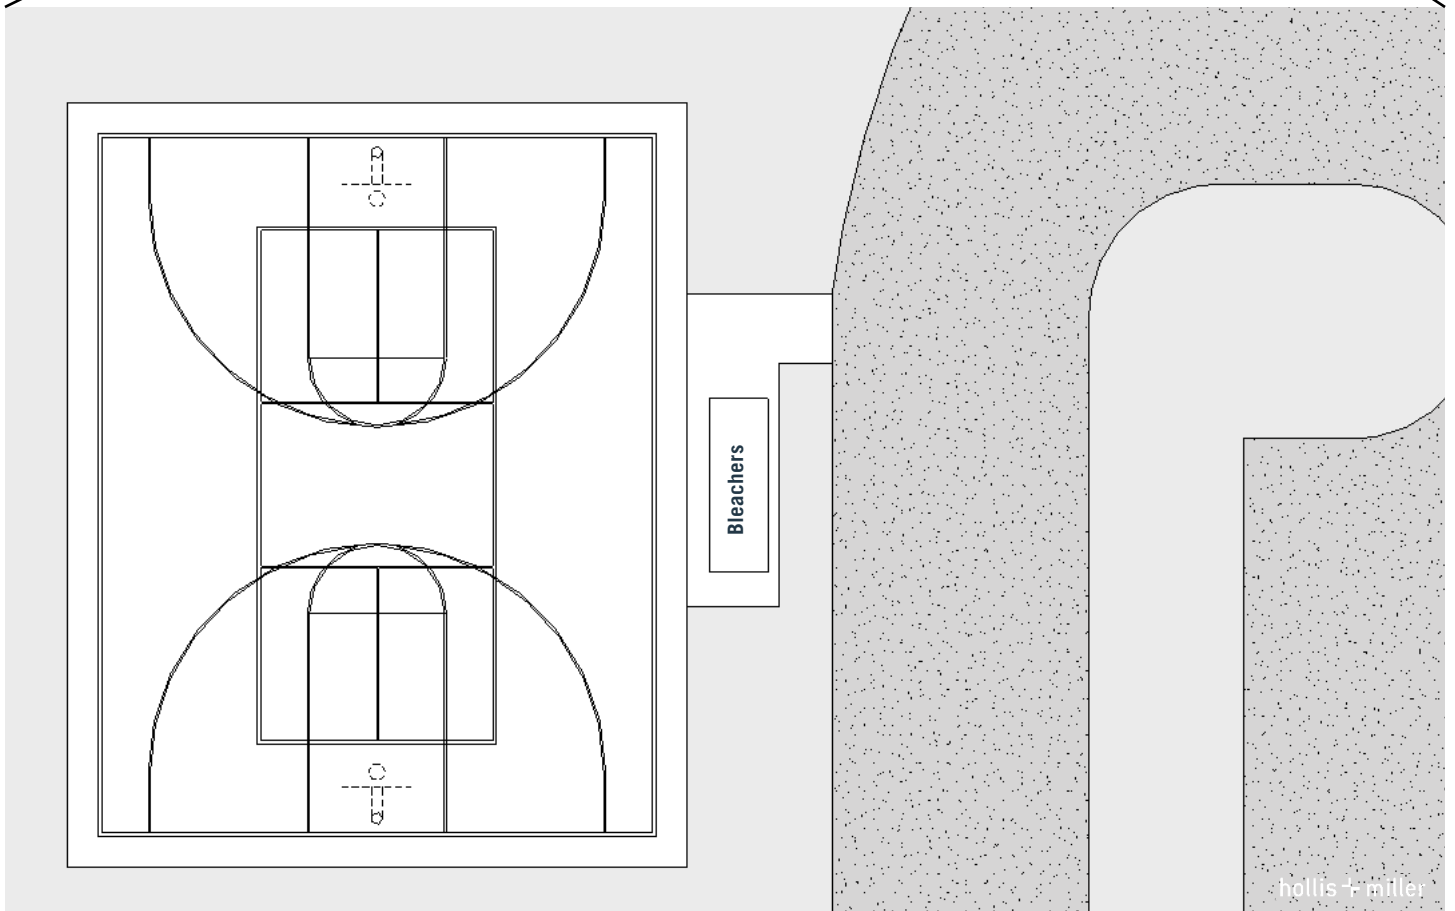

Enlarged Site Plan

Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:
May 2024 - August 2025

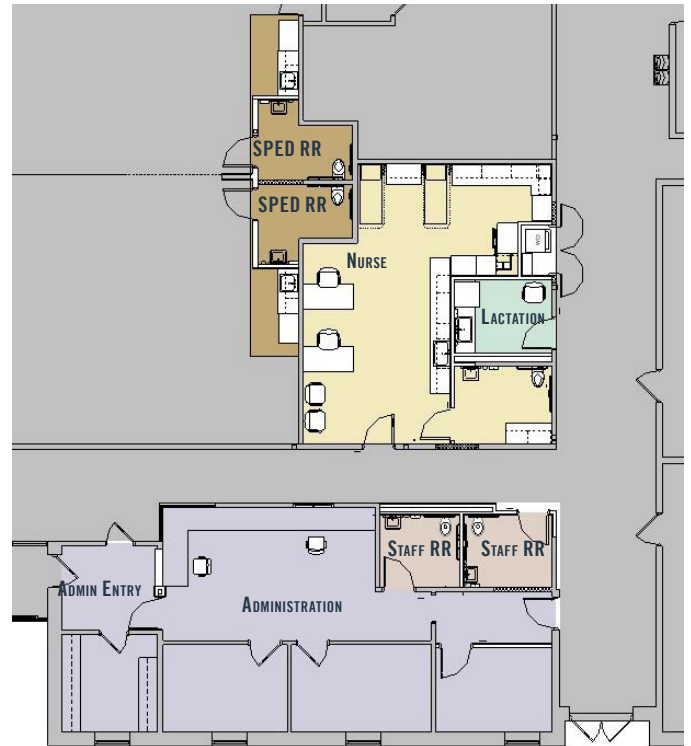

▲ Enlarged Floor Plan




▲ Overall Floor Plan

Interior Renovation

- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:
May 2024 - August 2025



Administration

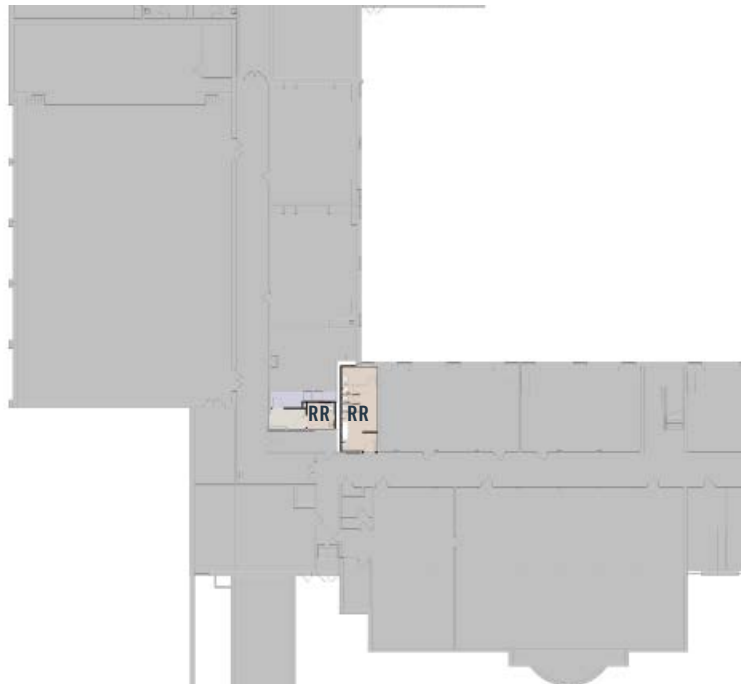

Partial First Level Floor Plan




Overall Second Level Floor Plan

Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule: May 2024 - August 2025



Administration

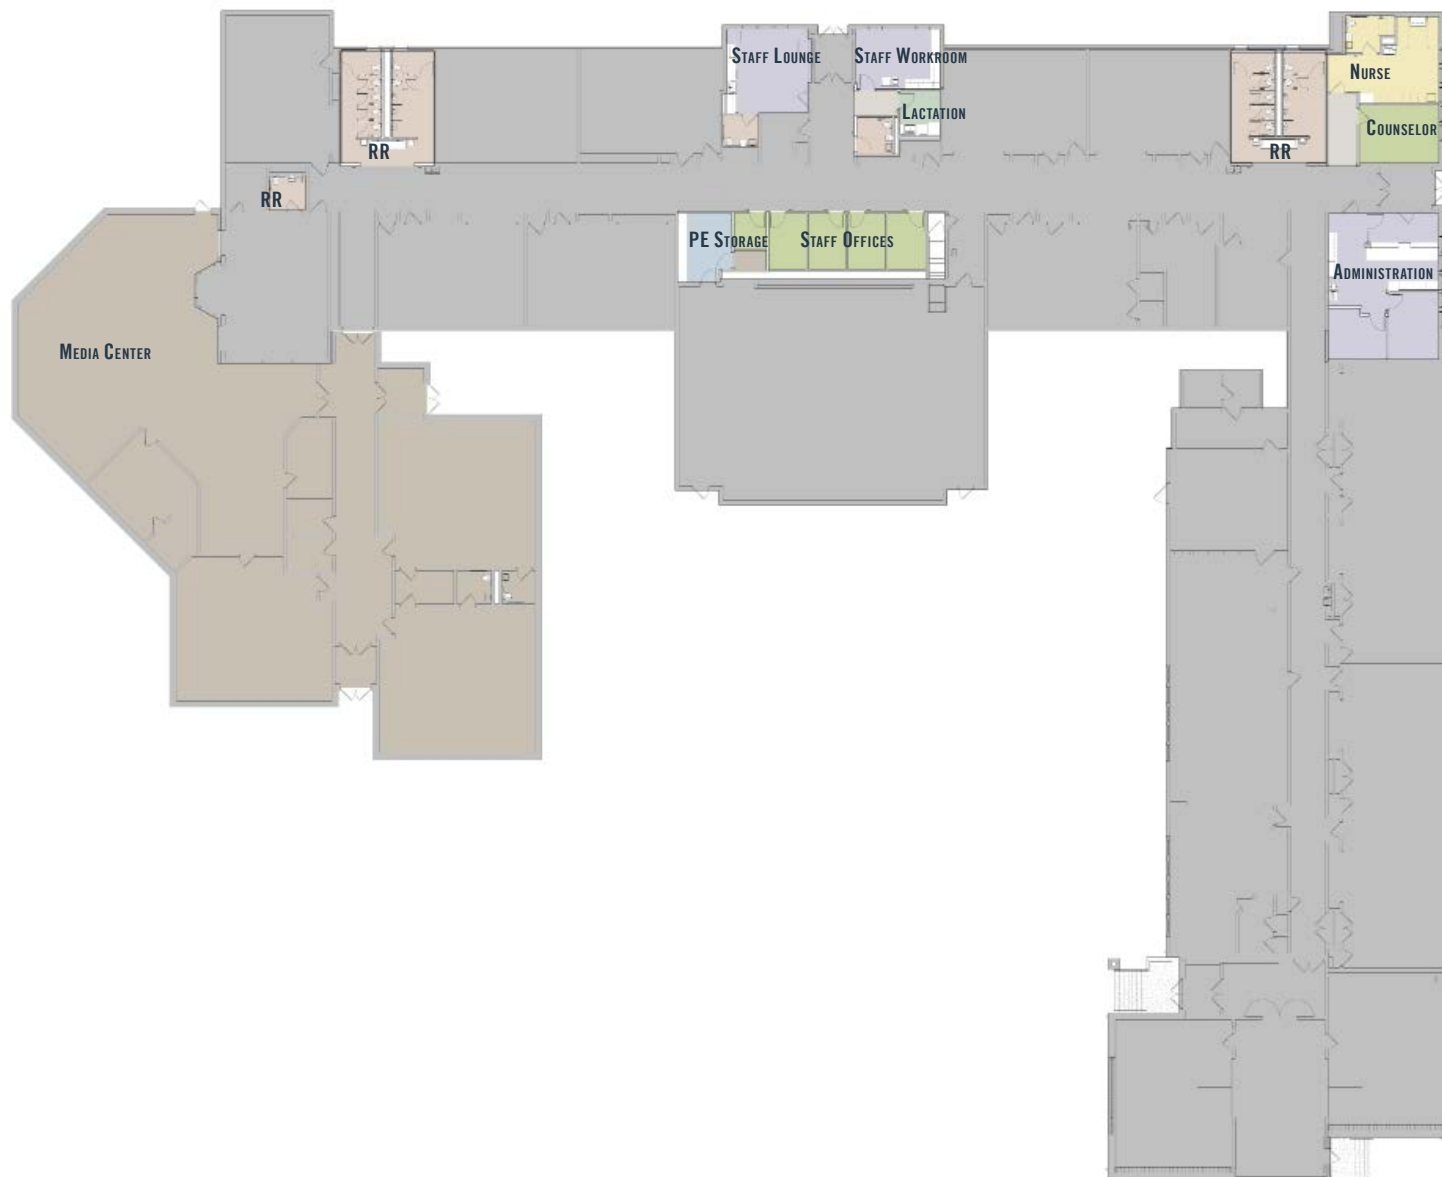

Overall Floor Plan

**WEEKLY
PROGRESS
REPORT**

**Doniphan, Franklin, and Ridgeview
Summer Renovation Projects
Liberty Public Schools**



8/9/24

PROJECT STATUS

- Doniphan, Franklin, and Ridgeview:
- Completed MEP Install
 - Completed Drywall Install
 - Completed Ceiling Grid Install
 - Completed Paint
 - Completed Tile
 - Completed Casework Install
 - Completed Flooring Install
 - Completed Epoxy Install
 - Completed Specialties Install
 - Began Punch List Work

UPCOMING

- Doniphan, Franklin, and Ridgeview:
- Complete Punch List Work
 - Complete Final Inspections
 - Furniture Move-In

Project Completion: August 2024



Franklin - Main Office



Franklin - Restrooms



Franklin - Workroom



Ridgeview - Level 2 Restroom



Ridgeview - Main Office



Doniphan - Main Office



Doniphan - Assistant Principal Office



Doniphan - Teacher's Lounge
