




# Mary E. Britton Middle School

## ➤ **Completed/Work in Progress:**

- Work continued – fill dirt around outside perimeter of curb
- Work continued – rough grading
- Finished install Stairs behind Stage
- Finished Hood installation started in Kitchen
- Finished Tile Area B bathroom walls. Floors prepped and started
- Tile completed in Cooler/Freezer
- Finished paint on Gym Ceiling and walls down to stripe
- Finish paint on door frames Area A 2<sup>nd</sup> Floor
- Finished first coat of paint on Area E and F
- Exterior weather/air barrier complete. (Touch ups in various areas)

## ➤ **Upcoming Look Ahead:**

- Complete handrail and other related items to stairs
- Another load of MCM panels delivery the week of 10-28-24
- Rough Grading at Entrance Slopes
- Complete Permeable Pavers Scheduled for week of 10/28/24
- Complete Hydroseed and Sod in areas that are ready. Starting 10-14-24
- Finish Hanging Sheetrock area B
- Canopy Install (Mobilization scheduled for week of 10-21-24)
- Install glass in frames available. Starting 10/21/24
- Plumbing vent penetrations through roof
- Continue Tile work in Area C and move forward to Area D

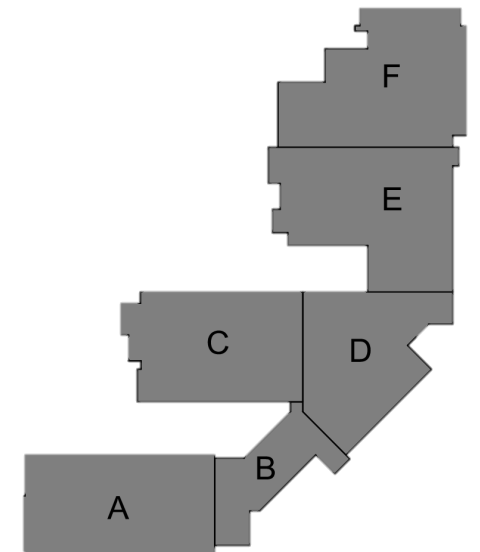

# Mary E. Britton Middle School



Area A – Ceiling Grid has Begun



Week Ending October 18, 2024



# Mary E. Britton Middle School



## Area A – Vertical Metal Panels Continue



Week Ending October 18, 2024



# Mary E. Britton Middle School

Area A and B – Vertical Metal Panels Continue



Week Ending October 18, 2024

# Mary E. Britton Middle School



## Area B – 2<sup>nd</sup> Floor MEP Above Ceiling Continues





# Mary E. Britton Middle School



## Area B – Media Center Framing Continues



Week Ending October 18, 2024

# Mary E. Britton Middle School



## Area B – Soffit Framing for Main Entry



Week Ending October 18, 2024



# Mary E. Britton Middle School

## Area F – Roofing Continues



Week Ending October 18, 2024



# Mary E. Britton Middle School



Site – Aerial of Progress



Week Ending October 18, 2024
