



**September 2024**

## **ARPA Monthly Progress Report**

for

# **East Ramapo Central School District**

Time Period: 9/9/2024 - 10/8/2024

Issued on 10/8/24 by:

**Jacobs Construction Management Services**

## Table of Contents

### **1. Construction Update**

- a. **ARPA Project Overview Statement & Description**
- b. **ARPA Schedule Overview (Level 3, 4 & 6) v.16. (DRAFT Update 10-8-24)**
- c. **Remaining Construction Sequence & Schedule Overview (DRAFT Update 10-8-24)**
- d. **ARPA Construction – Financial Update (DRAFT Update 10-8-24)**
- e. **Phase 1A – Flooring**  
**Kakiat:** Awaiting approval from CSArch for final payment.
- f. **Phase 1A – MEP Upgrades**  
**Kakiat:** UV installations and Casework are complete at 71 locations. UV Countertops were completed on 9/11/2024 at the 9 remaining locations. Continuing balancing, commissioning, and building controls.  
**Margetts:** UV installations and Casework are complete at 34 locations. UV Countertops were completed on 9/11/2024 at the 3 remaining locations. Continuing balancing, commissioning, and building controls.
- g. **PHASE 1A – MEP (Flooring Abatement & Replacement Work + UV Casework/Flooring at Elmwood)**  
**Elmwood:** Classroom Casework Demolition & Abatement is 100% complete. Finned Tube enclosures are Complete with Finned tube vertical closures remaining. New Scope added: Additional flooring completed.
- h. **Phase 1B – Doors/Hardware & Window Replacement**  
Interior door and hardware installations are 100% complete at Elmwood, Margetts and Kakiat (3 of 5 schools) with only punch list and door frame painting remaining. Interior Door Installation 75% complete at Ramapo. Window replacements are 95% completed at Elmwood, Margetts, and Kakiat (3 of 3 schools).
- i. **Phase 1B – ADA Toilet Room & Select Drinking Fountain Upgrades**  
All base bid bathrooms and drinking fountains are substantially complete. Ramapo HS handicap ramp handrails have been installed. Spring Valley HS handicap lift has been ordered; installation is tentatively scheduled for December break. Smoke doors arriving early October. New Scope added: District has requested 61 additional drinking fountains to be installed at 13 buildings beginning in early October with a target completion date to be 12/31/24.
- j. **PHASE 3B – Doors/Hardware Replacement**  
Interior door and hardware installation is 98% complete at Fleetwood, Grandview, Summit Park, Eldorado, Lime Kiln, Hempstead, Chestnut Ridge, and Pomona (8 of 8 schools). Contractor door is working on resolution of punch list items.
- k. **PHASE 3C – ADA Toilet Room & Select Drinking Fountain Upgrades**  
All base bid toilet rooms and drinking fountains are substantially complete. Smoke door work is scheduled to be installed in early October. New Scope added: District has requested 61 additional drinking fountains to be installed at 13 buildings beginning in early October with a target completion date to be 12/31/24.
- l. **PHASE 3D – Window Replacement**  
Windows have been ordered for all seven (7) schools. Lime Kiln is complete (1 of 7 schools) with Grandview 98% complete, Eldorado, Chestnut Ridge, Fleetwood, Summit Park, Hempstead to follow.
- m. **Exterior Door and related Window Replacements**  
District has requested deteriorated exterior doors and related store fronts to be replaced due to egress issues at 5 schools i.e. Pomona at Phase 3B, Ramapo and Spring Valley at Phase 1B, Chestnut Ridge and Fleetwood at Phase 3B.  
Scope of works is being finalized and cost proposal be received by 9/30/24 for submission to the District.



## **2. Health and Safety Update**

- a. Project Safety Reports – Reports indicating no incidents to-date.

## **3. Appendices**

- a. Phase 1A MEP – RFI, Submittal, CIC, Cost Proposal - Status Logs
- b. Phase 3A – RFI, Submittal - Status Logs
- c. Phase 1B – RFI, CIC, Cost Proposal - Status Logs
- d. Phase 3B – RFI, CIC, Cost Proposal - Status Logs
- e. Phase 3C – RFI, CIC, Cost Proposal - Status Logs
- f. Phase 3D – RFI, CIC, Cost Proposal - Status Logs
- g. Progress Photos
- h. KH Final Signed Punch Lists are available upon request.



## 1. Construction Update

### a. ARPA Project Overview Statement

#### **Project Statement:**

*The East Ramapo Central School District has embarked on a major district-wide capital improvement project through the American Rescue Plan Act of 2021 (ARPA) funding, expanding the program in the following areas:*

- 1) Select Indoor air quality improvements including mechanical*
- 2) District-wide security improvements including interior doors & hardware*
- 3) Hazardous materials removals & replacements*
- 4) District-wide ADA improvements including drinking fountains & toilet rooms*
- 5) Window replacements & other energy related saving measures*

#### **Project Areas Expanded:**

#### **1. Select Indoor Air Quality improvements including mechanical:**

##### **MEP Upgrades**

- Major Mechanical upgrades at Two (2) Schools

#### **2. District-wide security improvements including interior doors & hardware:**

##### **Doors & Hardware Replacements**

- Up to Thirteen (13) Schools

#### **3. Hazardous Materials Removals & Replacements:**

##### **Flooring Abatement & Replacements**

- Eleven (11) Schools (+/-) 720,000 sf

##### **Kitchen Hood Abatement & Replacements**

- Eleven (11) Schools

#### **4. ADA Improvements including drinking fountains & toilet rooms:**

##### **ADA Upgrades**

- At Thirteen (13) Schools

#### **5. Window replacements & other energy related saving measures**

##### **Window Replacements**

- Entire or partial at Ten (10) Schools

### b. ARPA Project Description

#### **PHASE 1:**

##### **EMERGENCY PROJECT: Flooring Abatement & Replacements - (state contract)**

- Spring Valley High School +/- 120,000 sf

#### **PHASE 1A:**

##### **Flooring Abatement & Replacements - (state contract)**

- **Four (4) Schools +/- 300,000 sf**
  - Elmwood Elementary School
  - Kakiat Elementary School
  - Margetts Elementary School
  - Pomona Middle School





- **Remaining Flooring & UV Casework**
  - Elmwood Elementary School

**Kitchen Hood Abatement & Replacements - (multi-prime contracts)**

- **Phase #1 2022: Six (6) Schools**
  - Chestnut Ridge Elementary School
  - Elmwood Elementary School
  - Hempstead Elementary School
  - Kakiat Elementary School
  - Pomona Middle School
  - Margetts Elementary School
- **Phase #2 2023: Five (5) schools**
  - Eldorado Elementary School
  - Fleetwood Elementary School
  - Grandview Elementary School
  - Summit Park Elementary School
  - Lime Kiln Elementary School

**MEP Upgrades - (OMNIA Direct Procurement Contract)**

- Kakiat ES & Margetts ES

**PHASE 1B:**

- **ADA Upgrades - (TIPS Direct Procurement Contract)**
  - Ramapo High School
  - Spring Valley High School
  - Elmwood Elementary School
  - Kakiat Elementary School
  - Margetts Elementary School
- **Doors & Hardware Replacements - (TIPS Direct Procurement Contract)**
  - Ramapo High School
  - Spring Valley High School
  - Elmwood Elementary School
  - Kakiat Elementary School
  - Margetts Elementary School
- **Window Replacements - (TIPS Direct Procurement Contract)**
  - Margetts Elementary School
  - Elmwood Elementary School
  - Kakiat Elementary School

**Note:** District has requested 61 additional drinking fountains to be installed at 13 buildings beginning in early October with a target completion date to be 12/31/24.

District has requested deteriorated exterior doors and related store fronts to be replaced due to egress issues at Ramapo and Spring Valley. Scope of works is being finalized and cost proposal be received by 9/30/24 for submission to the district.



**PHASE 3A:**

**Flooring Abatement & Replacements - (Bayshore Direct Procurement Contract)**

- Seven (7) Schools
  - Eldorado Elementary School
  - Fleetwood Elementary School
  - Grandview Elementary School
  - Summit Park Elementary School
  - Hempstead Elementary School
  - Lime Kiln Elementary School
  - Elmwood Elementary School
- Includes Piping covers, Fixed & Movable Casework and Windowsills

**PHASE 3B:**

**Doors & Hardware Replacements - (TIPS Direct Procurement Contract)**

- Eight (8) Schools
  - Chestnut Ridge Middle School
  - Fleetwood Elementary School
  - Grandview Elementary School
  - Summit Park Elementary School
  - Hempstead Elementary School
  - Lime Kiln Elementary School
  - Pomona Middle School
  - Eldorado Elementary School

**Note:** District has requested deteriorated exterior doors and related store fronts to be replaced due to egress issues at Pomona, Chestnut Ridge, and Fleetwood. Scope of works is being finalized and cost proposal be received by 9/30/24 for submission to the district.

**PHASE 3C:**

**ADA Upgrades - (TIPS Direct Procurement Contract)**

- Eight (8) Schools
  - Chestnut Ridge Middle School
  - Fleetwood Elementary School
  - Grandview Elementary School
  - Summit Park Elementary School
  - Hempstead Elementary School
  - Lime Kiln Elementary School
  - Pomona Middle School
  - Eldorado Elementary School

**Note:** District has requested 61 additional drinking fountains to be installed at 13 buildings beginning in early October with a target completion date to be 12/31/24.

**PHASE 3D:**

**Window Replacements - (TIPS Direct Procurement Contract)**


- Seven (7) Schools
  - Chestnut Ridge Middle School




- Fleetwood Elementary School
- Grandview Elementary School
- Summit Park Elementary School
- Hempstead Elementary School
- Lime Kiln Elementary School
- Eldorado Elementary School



b. ARPA Schedule Overview (Level 3) – v.16. DRAFT Update (10/8/24)

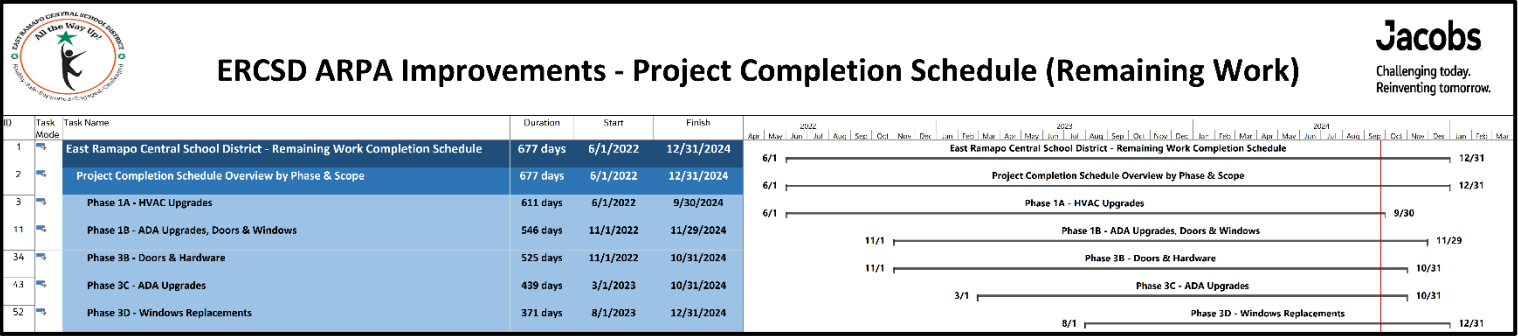

b. ARPA Schedule Overview (Level 5) – v.16. DRAFT Update (10/8/24)

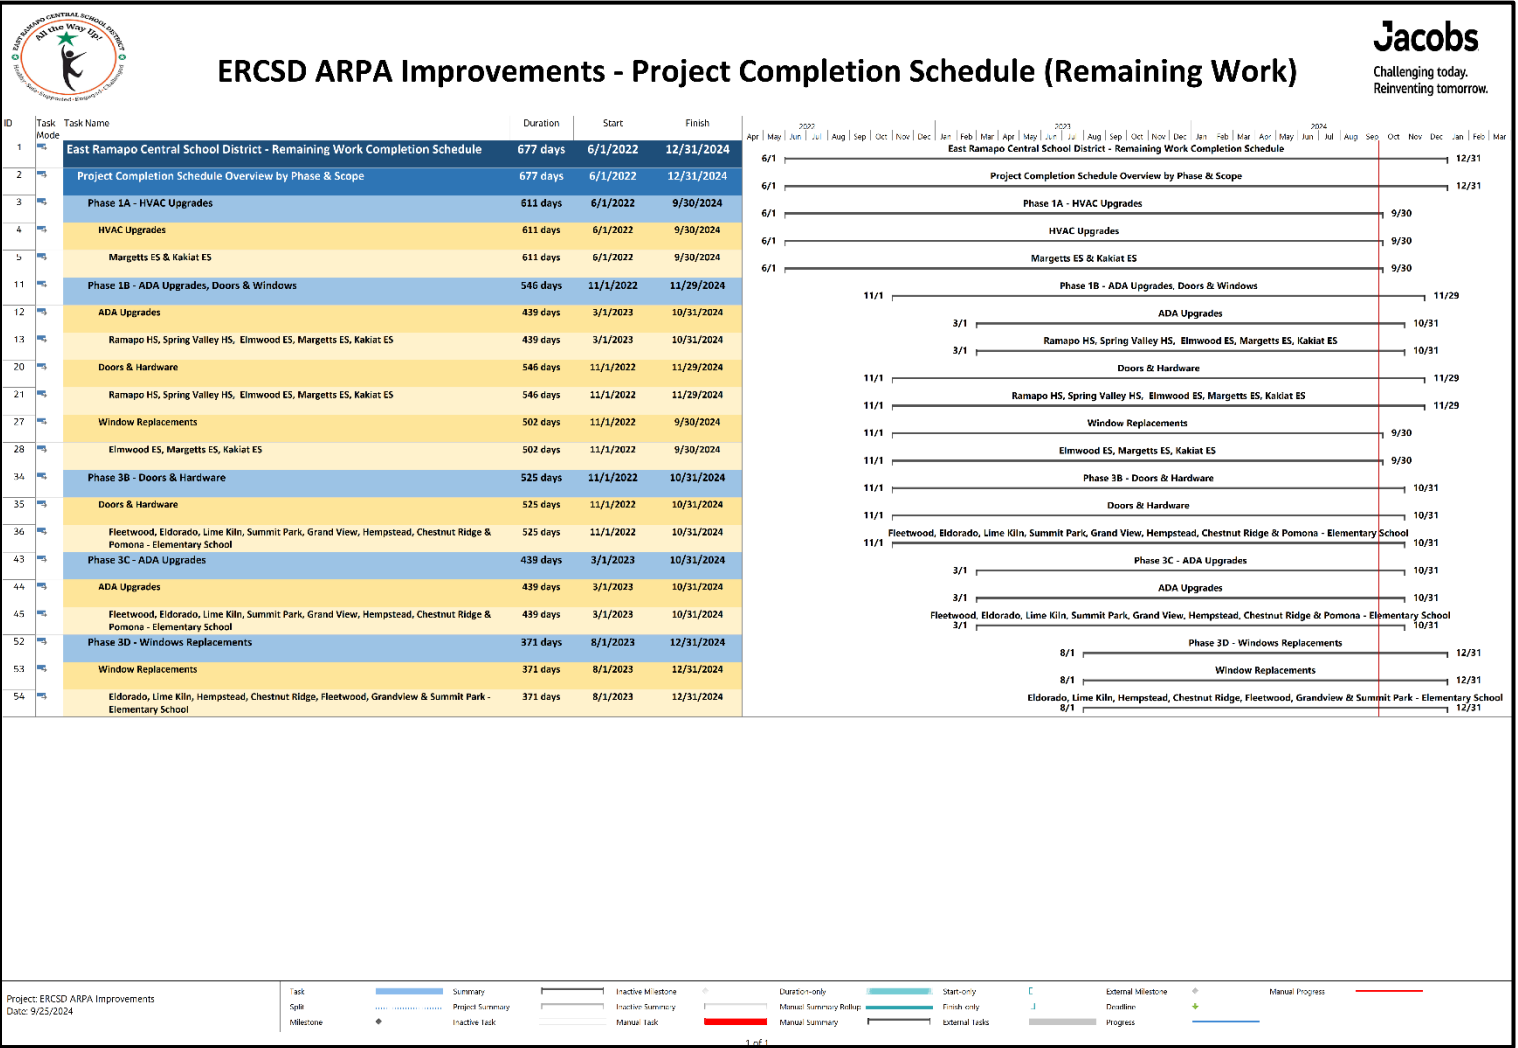




Challenging today.  
Reinventing tomorrow.

1 of 2



b. Schedule Overview (Level 6) – v.16. DRAFT Update (10/8/24) – (Page 2 of 2)

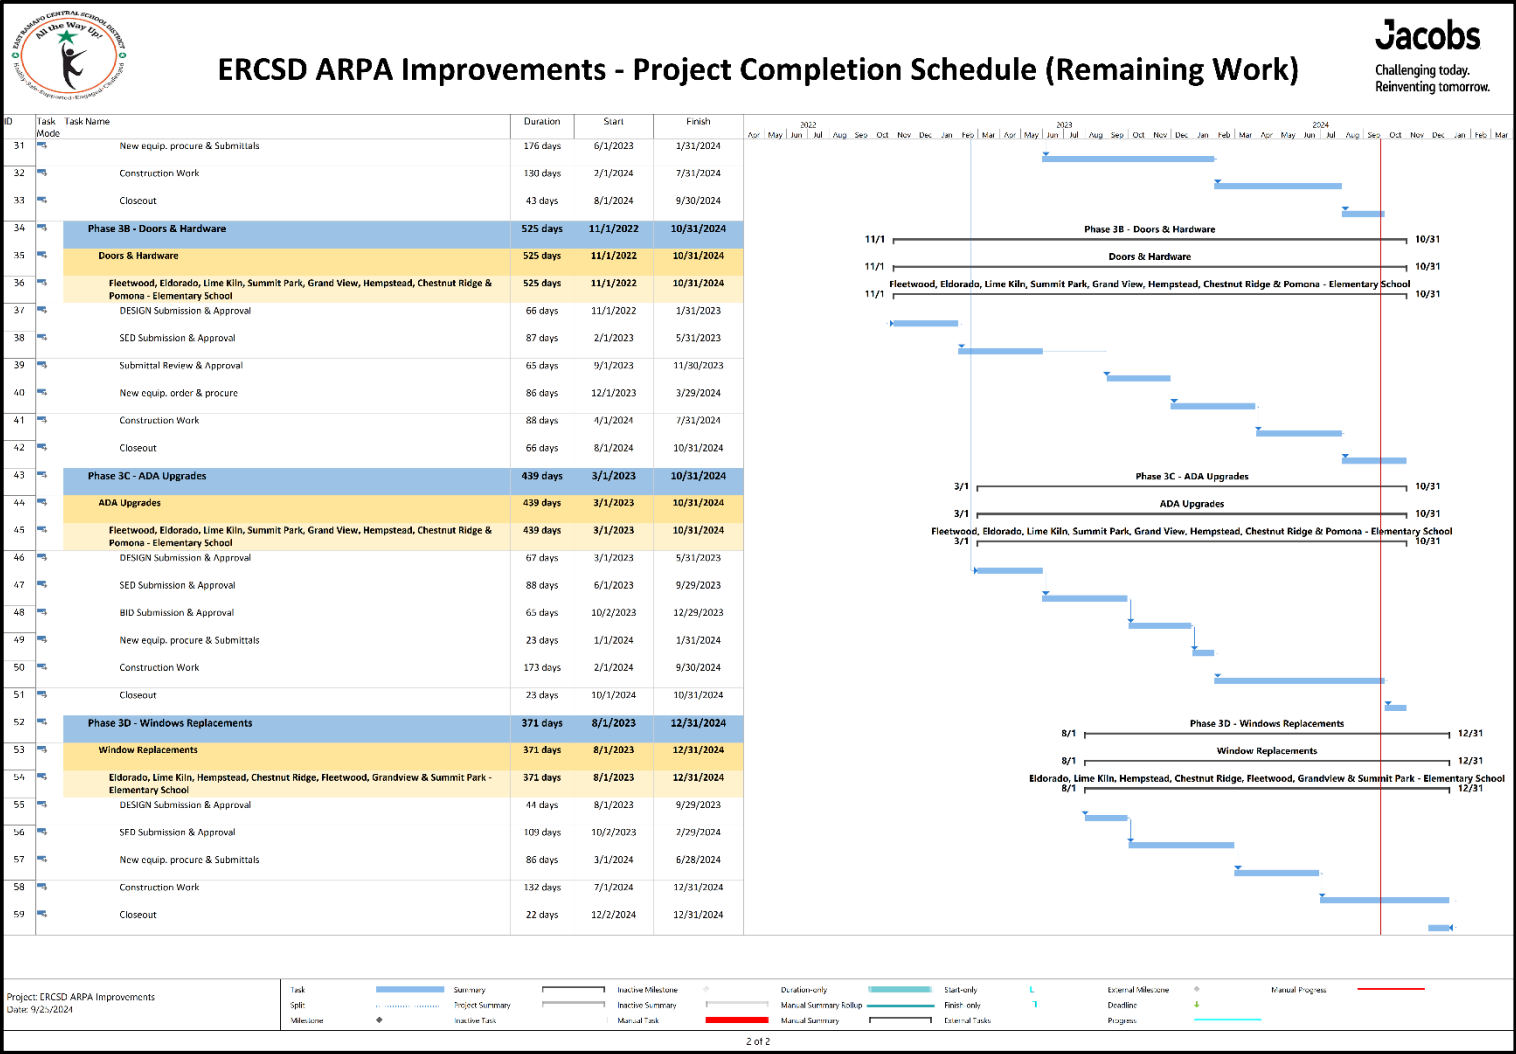

## c. ARPA Project - Projected Construction Work Areas - 2024 - DRAFT Update (10/8/24)

ERCSD ARPA - 2024 Construction Sequence & Schedule Overview														DRAFT	
10/4/2024															
School	Work Description	24-Apr	24-May	24-Jun	24-Jul	24-Aug	24-Sep	24-Oct	24-Nov	24-Dec	25-Jan	25-Feb	25-Mar	25-Apr	
<b>Elmwood</b>															
	1B Doors				vacant school										
Abatement	1B Windows	2	2												
Abatement	1B Windows Courtyards (Ordered/Fab)							2							
Abatement	1B ADA + fountains	2	2		1	1									
	1A MEP Casework				1	1									
<b>Margetts</b>															
	1B Doors				vacant school										
Abatement	1B Windows		2	2											
Abatement	1B Windows Courtyards (Ordered/Fab)						2								
Abatement	1B ADA + fountains				1	1									
Abatement	1A Unit Ventilator Replacements				1	1	2								
<b>Kakiat</b>															
Abatement	ERCSD Gym Floor Replacement (District Work) x2				1	1									
	1B Doors	2	2												
	1B Windows (Stored Onsite)			2											
Abatement	1B ADA + fountains				1	1									
Abatement	1A Unit Ventilator Replacements				1	1	2								
<b>Ramapo</b>															
Abatement	ERCSD Gym Floor Replacement (District Work) x2				1	1									
	1B Doors (Ordered/Fab)				1	1	1	2							
Abatement	1B ADA + fountains	2	2		1	1									
<b>Spring Valley</b>															
Abatement	ERCSD Gym Floor Replacement (District Work)				1	1									
	1B Doors (Ordered/Fab)							2	2	2					
Abatement	1B ADA + fountains				1	1									
	1B ADA Lift							2							
<b>Pomona</b>															
Abatement	ERCSD Gym Floor Replacement (District Work) x2				1	1									
	3B Doors (Ordered/Fab)				1										
Abatement	3C ADA + fountains	2			1	1									
<b>Chestnut Ridge</b>															
	3B Doors (Ordered/Fab)				1										
	3D Windows (Ordered/Fab)										2	2			
Abatement	3C ADA + fountains	2 +	2 +		1 +	1 +	2 +								
<b>Hempstead</b>															
Abatement	ERCSD Gym Floor Replacement (District Work)				1	1									
	3B Doors (Ordered/Fab)			2											
	3D Windows (Ordered - October Delivery)											2	2		
Abatement	3C ADA + fountains	2 +	2 +		1 +	1 +	2 +								
<b>Eldorado</b>															
	3B Doors		2												
	3D Windows (Ordered/Fab)					1									
	3D Windows Courtyards (Ordered/Fab)							2	2						
Abatement	3C ADA + fountains	2 +	2 +		1 +	1 +	2 +								
<b>Fleetwood</b>															
	ERCSD Emergency Canopy Shoring (District Work)				1	1									
	3B Doors	2													
Abatement	3D Windows (Ordered - August Delivery)								2						
Abatement	3C ADA + fountains	2 +	2 +		1 +	1 +									
<b>Grandview</b>															
	ERCSD Emergency Canopy Shoring (District Work)				1	1									
	3B Doors	2													
Abatement	3D Windows (Ordered - August Delivery)					1 +	2								
Abatement	3C ADA + fountains	2 +	2 +		1 +	1 +									
<b>Summit Park</b>															
	ERCSD Emergency Canopy Shoring (District Work)				1	1									
	3B Doors	2													
Abatement	3D Windows (Ordered - August Delivery)								2		2				
Abatement	3C ADA + fountains	2 +	2 +		1 +	1 +									
<b>Lime Kiln</b>															
	3B Doors		2	2											
	3D Windows (Ordered/Fab)				1										
Abatement	3C ADA + fountains				1	1									

### Key

	Doors		District Work
	Windows		ERCSD Gym Floor Replacement
	ADA + fountains		ERCSD Auditorium Work
	UV		ERCSD Emergency Canopy Shoring

### Notes

1 - First Shift Work (7am-330pm)  
2 - Second Shift Work (330pm-10/11)

1+ - This work will change shifts, mainly completed during first shift



## d. ARPA Construction - Financial Update 10.8.24

### 1. Phase 1 Projects

#### i. Phase 1 Spring Valley EMERGENCY PROJECT - Flooring Replacement Work

##### Awarded Contracts:

RENU:	\$ 2,326,580.00	Bay Shore State Contract
-------	-----------------	--------------------------

Milburn:	\$ 1,550,005.06	Bay Shore State Contract
----------	-----------------	--------------------------

COMBINED TOTAL:	\$ 3,876,585.06	
-----------------	-----------------	--

##### Change Orders To-Date (Approved):

RENU:	(\$ 51,540.33)	
-------	----------------	--

Milburn:	\$ 0.00	
----------	---------	--

COMBINED TOTAL:	(\$ 51,540.33)	
-----------------	----------------	--

##### Paid To-Date:

RENU:	\$ 2,275,039.67	
-------	-----------------	--

Milburn:	\$ 1,546,480.59	
----------	-----------------	--

COMBINED TOTAL:	\$ 3,821,520.26	
-----------------	-----------------	--

#### ii. Phase 1A Flooring Replacement Work (Summer 2022)

##### Awarded Contracts:

RENU:	\$ 5,630,303.47	Bay Shore State Contract
-------	-----------------	--------------------------

Milburn:	\$ 4,818,037.66	Bay Shore State Contract
----------	-----------------	--------------------------

COMBINED TOTAL:	\$10,448,341.13	
-----------------	-----------------	--

##### Change Orders To-Date (Approved):

RENU:	\$ 127,594.11	
-------	---------------	--

COMBINED TOTAL:	\$ 127,594.11	
-----------------	---------------	--

##### Paid To-Date:

RENU:	\$ 5,624,124.20	
-------	-----------------	--

Milburn:	\$ 4,819,346.66	
----------	-----------------	--

COMBINED TOTAL:	\$ 10,443,470.99	
-----------------	------------------	--

### 2. Kitchen Hoods Replacement Project

#### i. Kitchen Hoods & Equipment Replacement Project (Summer 2022)

##### Awarded Contracts: (Multi-Prime Bids)

Renu Interiors:	\$ 963,000.00	GC-01 (General Construction Contract)
-----------------	---------------	---------------------------------------

Rockland Electric:	\$ 280,000.00	EC-02 (Electrical Contract)
--------------------	---------------	-----------------------------

Bertussi Contracting:	\$ 1,188,188.00	MC-03 (Mechanical Contract)
-----------------------	-----------------	-----------------------------

Mace Contracting:	\$ 558,700.00	PC-04 (Plumbing Contract)
-------------------	---------------	---------------------------

Joe Flihan Co.:	\$ 344,732.00	KC-05 (Kitchen Equipment State Contract)
-----------------	---------------	--

COMBINED TOTAL:	\$ 3,334,620.00	
-----------------	-----------------	--

##### Change Orders To-Date (Approved):

Renu Interiors:	\$ 163,613.51	
-----------------	---------------	--

Rockland Electric:	\$ 1,118.50	
--------------------	-------------	--

Bertussi Contracting:	\$ (29,700.00)	
-----------------------	----------------	--

Mace Contracting:	\$ (29,700.00)	
-------------------	----------------	--

COMBINED TOTAL:	\$ 105,332.01	
-----------------	---------------	--

##### Paid To-Date:

Renu Interiors:	\$1,126,613.51	
-----------------	----------------	--

Rockland Electric:	\$ 281,118.50	
--------------------	---------------	--

Bertussi Contracting:	\$ 1,158,488.00	
-----------------------	-----------------	--

Mace Contracting:	\$ 497,325.00	
-------------------	---------------	--

Joe Flihan Co.:	\$ 344,732.00	
-----------------	---------------	--

COMBINED TOTAL:	\$ 3,408,277.01	
-----------------	-----------------	--



## 3. Phase 3A – Flooring Abatement & Replacements

### Awarded Contracts 1:

RENU: \$ 4,731,207.00

Milburn: \$ 5,004,097.00

COMBINED TOTAL: \$ 9,735,304.00

### Change Orders To-Date (Approved):

RENU: \$ 207,685.83

Milburn: \$ 62,669.71

COMBINED TOTAL: \$ 270,355.54

### Paid To-Date:

RENU: \$ 5,439,790.55

Milburn: \$ 5,066,766.88

COMBINED TOTAL: \$10,506,557.43

## 4. Phase 1B – Door/Hardware & Window Replacements

### Awarded Contracts:

C&M Doors & Arrow: \$ 7,077,689.00

TOTAL: \$ 7,077,689.00

### Change Orders To-Date (Approved):

C&M Doors & Arrow: \$ 65,935.50

### Paid To-Date:

C&M Doors: \$ 4,735,730.91

COMBINED TOTAL: \$ 4,735,730.91

## 5. Phase 3B – Doors/Hardware Replacements

### Awarded Contracts:

Renu/Sunrise Doors: \$ 3,350,919

TOTAL: \$ 3,350,919

### Change Orders To-Date (Approved):

Renu/Sunrise Doors: \$ 70,308.00

### Paid To-Date:

Renu: \$ 2,712,599.66

COMBINED TOTAL: \$ 2,712,599.66

## 6. Phase 3D – Window Replacements

### Awarded Contracts:

C&M Doors & Arrow: \$ 11,367,750

TOTAL: \$ 11,367,750

### Change Orders To-Date (Approved):

C&M Doors & Arrow: \$ (540,500.00)

### Paid To-Date:

C&M Doors: \$ 3,227,807.82

COMBINED TOTAL: \$ 3,227,807.82

## 7. Phase 1B & 3C – ADA Improvement Projects

### Awarded Contracts:

Essential Constructs: \$ 9,847,657.79

TOTAL: \$ 9,847,657.79

### Paid To-Date:

Essential Constructs: \$ 7,366,813.55

COMBINED TOTAL: \$ 7,366,813.55

## 8. Phase 1A – HVAC Work

### Awarded Contracts:

Trane - Margetts & Kakiat: \$ 15,320,290.29 (Turnkey & Equipment Contracts)

Renu/Milburn (Elmwood): \$ 591,952.97

TOTAL: \$ 15,912,243.26

### Paid To-Date:

Trane - Margetts & Kakiat: \$ 3,593,199.60

COMBINED TOTAL: \$ 3,593,199.60

---

**Total Combined Paid To-Date: \$ 50,175,977.23**

## Pending Work:

## 9. Classroom Casework (free standing)

### Pending Contracts:

Casework: \$ 260,000

TOTAL: \$ 260,000

---

**Total Pending Work: \$ 260,000**

## Financial Summary:

**Total Combined Paid To-Date : \$ 50,175,977.23**

**Total Remaining Work : \$ 25,035,132.01**

---

**Sub Total Work : \$ 75,211,109.24**

**Total Approved CO's To-Date : \$ 47,484.83 (0.06%)**

---

**Sub Total Work (Including Approved CO's) : \$ 75,258,594.07**

**Pending PCO's : \$ 1,224,115.63**

---

**Grand Total Work (Incl. CO + PCO's – Rem. Allowances) : \$ 76,482,709.70**

**Total ARPA Budget (Hard Cost) : \$ 77,115,829.00**

**Grand Total Work (Incl. CO + PCO's – Rem. Allowances) : \$ 76,482,709.70**

---

**\* Allowances Remaining in Contract : \$ (863,728.45)**

**Construction Contingency Remaining : \$ 1,496,846.59 (1.94%)**



## 2. Health and Safety Update

### a. Project Safety Report

<u>Safety</u>	<u>This Period</u> <u>9/9/24-</u> <u>10/8/24</u>	<u>Cumulative</u> <u>To-Date</u>
First AID Cases:	0	0
Recordable Injuries:	0	0
Recordable Illnesses:	0	0
Lost Workdays Cases:	0	0
<b><u>Project Total Injuries/Cases Reported:</u></b>	<b>0</b>	<b>0</b>
<b><u>OSHA Incident Rate (OIR):</u></b>	<b>0</b>	<b>0</b>

**Note:**

1. OSHA incident Rate = Total number of injuries & illnesses multiplied by 3,874 (OSHA Labor Hours) divided by the number of hours worked by all employees.
2. Jacobs internal Safety field walk occurred on 23<sup>rd</sup> July 2024.



## **Appendices**

- a. Phase 1A MEP – RFI, Submittal, CIC, Cost Proposal - Status Logs
- b. Phase 1B – RFI, CIC, Cost Proposal - Status Logs
- c. Phase 3B – RFI, CIC, Cost Proposal - Status Logs
- d. Phase 3C – RFI, CIC, Cost Proposal - Status Logs
- e. Phase 3D – RFI, CIC, Cost Proposal - Status Logs
- f. Progress Photos
- g. KH Final Signed Punch Lists are available upon request.

Category	RFI #	Description	From Subcontractor		From Contractor		From Construction Manager		Review by Consultant			Review by Architect		Returned to Contractor		Returned to Sub		Remarks	
			Date	Type	Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned to Arch.	File	Returned to Construction Manager	File	Date	Type	Date		Type
01 - GC Trans	GC-001	Mason Veneer																Arch.: For Record Purposes Only	
	GC-002	Margetts Demo of AHU																Arch.: For Record Purposes Only	
	GC-003	Kakiat UV 35																Arch.: For Record Purposes Only	
	GC-004	Kakiat and Margetts Electrical																Arch.: For Record Purposes Only	
	GC-005	Ramapo HS - Fire Alarm																Arch.: For Record Purposes Only	
	GC-006	Ramapo HS Light Fixtures/Security Vendor																Arch.: For Record Purposes Only	
	GC-007	Kakiat Louvered Penthouse																Arch.: For Record Purposes Only	
	GC-008	General - Fittings																Arch.: For Record Purposes Only	
	GC-009	Margetts ERV Outdoor Rated																Arch.: For Record Purposes Only	
	GC-010	HS Electric MC Feeder Cable																Arch.: See attached.	
	GC-011	HS Structural																Arch.: See Consultant Review	
	GC-012	Kakiat Nurses Office UV/24																Arch.: See Consultant Review Consultant: Please ve...	
	GC-013	Ramapo HS Steel Location -ERCSD																Arch.: See Consultant Review	
	GC-014	Margetts Baseboard System																Arch.: See Consultant Review Contractor: Ramapo HS...	
	GC-015	Margetts Kakiat Countertop Specs - ERCSD																Arch.: See Consultant Review Contractor: Margetts ...	
	GC-016	Margetts Kakiat Updated Electrical Drawi...																Arch.: See attached. Contractor: Margetts Kakiat U...	
	GC-017	RFI #17 Spring Valley HS Asbestos																Consuliant: No Comments, not our project. Submitti...	
	GC-018	Margetts Grille Spec - ERCSD (RFI GC-018...																Contractor: Margetts Grille Spec	
	GC-019	Margetts Drawing AD811 - ERCSD (RFI GC-0...																Arch.: See attached for response to RFI. Construct...	
	GC-020	Room 13A Spring Valley HS- ERCSD (RFI GC-27)																Consuliant: Not our project- submitting to remove ...	
	GC-021	Girls Gym Ducts - Spring Valley HS- ERCSD ...																Arch.: See Consultant Review Contractor: Girls Gym...	
	GC-022	Weight Room - Spring Valley HS- ERCSD (RF...																Arch.: See Consultant Review Contractor: Weight Ro...	
	GC-023	Offices Demo - Spring Valley HS- ERCSD ...																Arch.: See Consultant Review Contractor: Office De...	
	GC-024	Margetts & Kakiat AHERA Reports																Consuliant: Not our project- submitting to remove ...	
	GC-025	Glycol Quantity - Spring Valley HS - ERCS...																Arch.: See the attached for response to RFI.	
	GC-026	AIA Billing Requirements (RFI GC-026)																Arch.: See Consultant Review	
	GC-028	Margetts Ceiling Office ACM - ERCSD (RFI...																Arch.: CSARCH worked with Energia to prepare attac...	
	GC-027	Kakiat Floor Rate - ERCSD (RFI GC-28)																Arch.: See Consultant Review	
	GC-028	Environmental Consultant Info - ERCSD (R...																Arch.: See Consultant Review	
	GC-029	Kakiat Louvers - ERCSD (RFI GC-29)																Arch.: See Consultant Review	
	GC-030	ACCUAH Condenser																Arch.: See Consultant Review	
	GC-030	Kakiat & Margetts CAD Drawings -ERCSD (R...																Arch.: See Consultant Review	
	GC-031	Margetts Electrical Circuit - ERCSD (RFI G...																Arch.: See Consultant Review	
	GC-031.1	Response -Margetts Electrical Circuit - ...																Arch.: See Consultant Review	
	GC-032	Countertop style and color																Arch.: See attached for response. Consuliant rev...	
	GC-033	Margetts VRF Condensate - ERCSD (RFI GC-3...																Arch.: See attached for comments and response.	
	GC-034	Margetts VRF OA Intake - ERCSD (RFI #34)																Arch.: See Consultant Review Contractor: VRF Work ...	
	GC-035	Margetts RP-1 Location - ERCSD (RFI GC-3...																Arch.: See Consultant Review	
	GC-036	Margetts Kakiat Roof Info - ERCSD(RFI 36...																Arch.: See attached. Construction Manager: Jacobs ...	
	GC-037	Margetts VRF OA Damper - ERCSD (RFI GC-3...																Arch.: See Consultant Review	
GC-038	Margetts VRF OA Product Info - ERCSD (RF...																Arch.: See Consultant Review		
GC-039	Margetts Transfer Ducts - ERCSD (RFI GC-...																Arch.: See Consultant Review		
GC-040	RP-1 relocation																Arch.: See Consultant Review		
GC-041	Margetts UV Breakers - ERCSD (RFI GC-41)																Arch.: See Consultant Review		
GC-042	Margetts Reading Room 35 - ERCSD (RFI GC-...																Arch.: See Consultant Review		
GC-043	Margetts UV Breakers - ERCSD (RFI GC-43)																Arch.: See Consultant Review Contractor: Response ...		
GC-043	Library Shelving - ERCSD (RFI GC-44)																Arch.: See Consultant Review		
GC-045	Margetts UV Power - ERCSD (RFI GC-45)																Arch.: See Consultant Review Contractor: In Respon...		
GC-046	Margetts																Arch.: The attached is not an RFI in its proper fo...		
GC-047	Margetts Library Piping - ERCSD (RFI GC-...																Arch.: See Consultant Review Contractor: Urgent		
GC-048	Margetts																Arch.: What was submitted is not an RFI and appear...		
	001	Margetts UV Power - ERCSD (RFI GC-49)																	
02 - GC Milburn																			
03 - GC Renu																			



Phase 1A – MEP Package – Submittal Log – To Date

East Ramapo Central School District								
Phase 1A MEP - Submittal Log						<div>Jacobs</div>		
Initial Review: 10 WD/ Re Submittal Review: 7 WD								
Submittal Spec Section / Submittal No.	Description	School	Date Submitted	Due Date (10 WD)	Date Returned	Status -000	Final Status	
238223/001	Metal Storage Shelving Systems	Margetts ES	3/22/2023	4/5/2023	4/21/2023	AAN	AAN	
236200/001	Variable Refrigerant Volume Systems (VRF)	Kakiat ES	2/13/2023	2/27/2023	3/31/2023	AAN	AAN	
236200/002	Variable Refrigerant Volume Systems (VRF)	Margetts ES	2/13/2023	2/27/2023	3/31/2023	AAN	AAN	
236423/001	Scroll Water Chillers - Air Cooled	Spring Valley HS, Ramapo HS	3/22/2023	4/5/2023	4/25/2023	NET	NET	
237223/001	Packaged Rooftop DOAS Unit with Energy Recovery	Ramapo HS	3/17/2023	3/31/2023	4/14/2023	NET	NET	
237223/002	Packaged Rooftop DOAS Unit with Energy Recovery	Spring Valley HS	3/21/2023	4/4/2023	4/19/2023	AAN	AAN	
237413/001	Packaged Rooftop Air Conditioning Units	Spring Valley HS, Ramapo HS	3/21/2023	4/4/2023	4/8/2023	NET	NET	
237416.14/001	Packaged Rooftop Units with Energy Recovery	Kakiat ES	3/10/2023	3/24/2023	3/10/2023	NET	NET	
237416.14/002	Packaged Rooftop Units with Energy Recovery	Margetts ES, Elmwood ES	3/10/2023	3/24/2023	3/13/2023	NET	NET	
238129/001	Variable Refrigerant Flow System - Shop Drawings RHS VRF	Spring Valley HS, Ramapo HS	3/13/2023	3/27/2023	5/11/2023	AAN	AAN	
238129/002	Variable Refrigerant Flow System - SVHS ACCU-2 VRF System	Spring Valley HS	3/30/2023	4/13/2023	4/19/2023	AAN	AAN	
238129/003	Variable Refrigerant Flow System - PD ACCU-1	Ramapo HS	4/2/2023	4/16/2023	4/19/2023	AAN	AAN	
238129/004	Variable Refrigerant Flow System - PD ACCU-1	Spring Valley HS	4/2/2023	4/16/2023	4/21/2023	AAN	AAN	
238216/002	Coils - Shop Drawings	Spring Valley HS, Ramapo HS	4/2/2023	4/16/2023	4/19/2023	MCN	MCN	
238216/003	Coils - Resubmittal - Product Data	Spring Valley HS, Ramapo HS	4/26/2023	5/10/2023	5/5/2023	NET	NET	
238219/001	Blower Coil Units	Spring Valley HS, Ramapo HS	3/13/2023	3/27/2023	5/11/2023	MCN	MCN	
238223/001	Unit Ventilators	Margetts ES	2/23/2023	3/9/2023	2/23/2023	AAN	AAN	
238223/002	Unit Ventilators	Kakiat ES, Elmwood ES	3/10/2023	3/24/2023	3/21/2023	R&R	R&R	
238239/001	Unit Heaters	Spring Valley HS, Ramapo HS	3/30/2023	4/13/2023	5/10/2023	AAN	AAN	
237313/001	Air Handling Units	Spring Valley HS	4/3/2023	4/17/2023	5/8/2023	R&R	R&R	
237313/002	Air Handling Units	Ramapo HS	4/3/2023	4/17/2023	5/8/2023	R&R	R&R	
105613/002	Metal Storage Shelving Systems	Kakiat ES	10/12/2023	10/26/2023	11/17/2023	R&R	R&R	
105613/003	Metal Storage Shelving Systems	Kakiat ES	12/19/2023	1/2/2024	2/13/2024	MCN	MCN	
230910-001	Automatic Temperature Controls	Kakiat ES	10/27/2023	11/10/2023	11/3/2023	AAN	AAN	
230910-002	Automatic Temperature Controls	Margets ES & Elmwood	10/30/2023	11/13/2023	11/14/2023	AAN	AAN	
236200/003	Variable Refrigerant Volume Systems (VRF)	Elmwood ES	10/12/2023	10/26/2023	11/21/2023	AAN	AAN	
237313.13-001	Indoor, Basic Air-Handling Units (Kes Mes Ewes)	Kakiat, Margets & Elmwood ES	10/6/2023	10/20/2023	11/3/2023	NET	NET	
238223/003	Unit Ventilators	Elmwood ES	10/6/2023	10/20/2023	11/3/2023	NET	NET	
262416/001	Panelboards - Product Data	Margets ES	12/14/2023	12/28/2023	12/22/2023	AAN	AAN	
262416/002	Panelboards - Product Data	Kakiat ES	12/15/2023	12/29/2023	12/22/2023	AAN	AAN	
260526/001	Grounding & Bonding - Product Data	Margets ES	1/12/2024	1/26/2024	2/7/2024	AAN	AAN	
260526/002	Grounding & Bonding - Product Data	Kakiat ES	1/15/2024	1/29/2024	2/7/2024	AAN	AAN	
020810-001	Asbestos Abatement Pre-Work Submittals	Margetts & Kakiat	2/21/2024	3/6/2024	4/9/2024	NET	NET	
020810-002	Asbestos Abatement Documents	Margetts & Kakiat	5/8/2024	5/22/2024				
089119-002	Fixed Louvers - Product Data	Margetts	5/7/2024	5/21/2024	6/4/2024	MCN	MCN	
230719	Pipe Insulation	Kakiat, Margets & Elmwood ES	4/18/2024	5/2/2024				
083113-003	Access Doors and Frames - Product Data		5/8/2024	5/22/2024	5/23/2024	MCN	MCN	
083113-004	Access Doors and Frames - Qualification Data		5/29/2024	6/12/2024	6/10/2024	MCN	MCN	
232300-001	Refrigerant Piping	Kakiat, Margets & Elmwood ES	4/8/2024	4/22/2024				
232300-002	Refrigerant Piping Shop Drawings	Kakiat ES	7/8/2024	7/22/2024				
233425	Roof Accessories for HVAC Systems	Kakiat, Margets & Elmwood ES	4/8/2024	4/22/2024				
238236-EW	Finned-Tube Radiation Enclosures - Shop Drawings		5/9/2024	5/23/2024	6/4/2024	MCN	MCN	
020810-EW	Asbestos Plan & Posting	Elmwood ES	6/11/2024	6/25/2024				
089119-003	Fixed Louvers - Design Submittal		6/10/2024	6/24/2024	6/14/2024	MCN	MCN	
105613/004	Metal Storage Shelving UV Elevation	Kakiat ES	6/4/2024	6/18/2024	6/10/2024	R&R	R&R	
105613/005	Metal Storage Shelving UV Elevation	Margets ES	6/4/2024	6/18/2024	6/10/2024	R&R	R&R	
230713-001	Duct Insulation	Kakiat, Margets & Elmwood ES	8/3/2024	8/17/2024				

[illegible]



Phase 1B – RFI Log – To Date

ORACLE Primavera Submittal Exchange																	
Project: East Ramapo CSD ARPA Phase 1B Project Number: 209-2107.01																	
JACOBS RFI																	
View: My Activity   All Activity   Download Multiple Files																	
Sort By: Category   Numeric																	
Category: C1-GC-01   ADA-EC   ADA-GC   ADA-MC   ADA-PC																	
Category	RFI #	Description	From Subcontractor		From Contractor		From Construction Manager		Review by Consultant				Review by Architect		Returned to Contractor	Returned to Sub	Remarks
			Date	Type	Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned to Arch.	File	Returned to Construction Manager	File	Date	Date	
C1-GC-01	001	Window Shop Drawing RFI	8/23/23		8/30/23		9/1/23		9/1/23				9/6/23		9/6/23	9/6/23	Arch.: See attached.
	002	Door Hardware RFI	8/30/23		8/30/23		9/1/23		9/1/23				9/6/23		9/6/23	9/6/23	Arch.: See attached.
	003	Door Height RFI	8/30/23		8/30/23		9/1/23		9/1/23				10/26/23		10/26/23	10/26/23	Arch.: See attached for response to RFI 4.
	004	Elmwood ES RFI	9/21/23		9/21/23		9/21/23		9/21/23				11/28/23		11/28/23	11/28/23	Arch.: See UPDATED RESPONSE. Consultant: ANSWERED
	005	Transom Panel RFI	11/21/23		11/21/23		11/21/23		11/21/23	11/22/23	11/22/23		11/28/23		11/28/23	11/28/23	Arch.: See attached for response to RFI. Consultan...
	006	Hollow Metal Frame Paint RFI	1/2/24		1/2/24		1/2/24		1/8/24	1/8/24	1/9/24		1/17/24		1/17/24	1/17/24	Arch.: See attached for response.
	007	Wood Sidelite Panel RFI	1/22/24		1/22/24		1/22/24		1/22/24				1/24/24		1/24/24	1/24/24	Arch.: See response provided by consultant.
	008	Aluminum Threshold RFI	2/15/24		2/15/24		2/15/24		2/15/24	2/21/24			2/22/24		2/22/24	2/22/24	Arch.: See attached for response.
	009	Rabbetted Transom Panel Updated RFI	3/28/24		3/28/24		3/28/24		3/28/24				4/9/24		4/9/24	4/9/24	
	010	CIC-01 GC-005-MES RFI	5/9/24		5/9/24		5/9/24		5/9/24				5/20/24		5/20/24	5/20/24	
	011	Elmwood 01 Sign RFI	5/21/24		5/21/24		5/21/24		5/21/24								
	012	CIC-01 GC-003-SVHS Keying	9/23/24		9/23/24		9/23/24		9/23/24								
	013	CIC-01 GC-003-RHS Keying	9/23/24		9/23/24		9/23/24		9/23/24								
	014	CIC-01 GC-005-MES Keying	9/23/24		9/23/24		9/23/24		9/23/24								
	015	CIC-01 GC-007-EWES Keying	9/23/24		9/23/24		9/23/24		9/23/24								
	016	CIC-01 GC-004R-KES Keying	9/23/24		9/23/24		9/23/24		9/23/24								
ADA-EC	001	Lighting 104 A	5/14/24		5/14/24		5/14/24		5/14/24	5/14/24	5/17/24		5/17/24		5/17/24	5/17/24	Arch.: See Consultant Review
	002	Light clearance SVHS	7/14/24		7/14/24		7/15/24		7/15/24								Contractor: need low profile fixture if ceiling lo...
ADA-GC	001	Tile Colors			3/12/24		3/12/24		3/12/24	3/12/24			4/12/24		4/12/24	4/12/24	Arch.: See attached for response.
	002	Door Hardware Already Installed			3/20/24		3/25/24		3/25/24	3/25/24							
	003	Door Hardware Already Installed			4/12/24		4/15/24		4/15/24	4/15/24			5/6/24		5/6/24	5/6/24	
	004	EWES Asbestos Elbow			4/12/24		4/15/24		4/15/24	4/15/24			4/26/24		4/26/24	4/26/24	Arch.: see attached
	005	Epoxy Floor Saddles			4/15/24		4/15/24		4/15/24	4/15/24							
	006	Epoxy Floor & Wall Transition			4/15/24		4/15/24		4/15/24	4/15/24							
	007	Resinous Floor System - Chip or Quartz			4/24/24		4/24/24		4/24/24	4/24/24							
	008	Ceilings			4/26/24		4/26/24		4/26/24	4/26/24			5/8/24		5/8/24	5/8/24	
	009	Bathroom 104B			4/26/24		4/26/24		4/26/24	4/26/24			5/8/24		5/8/24	5/8/24	
	010	SVHS LVT Accent Color			5/7/24		5/8/24		5/8/24	5/8/24							
	011	Handicap Lift Concerns			5/8/24		5/8/24		5/8/24	5/8/24			5/9/24		5/9/24	5/9/24	
	012	Door Glazing Corrections			5/8/24		5/8/24		5/8/24	5/8/24			5/9/24		5/9/24	5/9/24	
	013	CIC-002-003-EWES - Questions	5/14/24		5/14/24		5/14/24		5/14/24	5/14/24			6/26/24		6/26/24	6/26/24	Arch.: See attached for response.
	014	Smoke Doors	5/28/24		5/28/24		5/29/24		5/29/24	5/29/24			5/30/24		5/30/24	5/30/24	Arch.: See the attached. Contractor: Elmwood - New...
	015	Hardware	5/28/24		5/28/24		5/29/24		5/29/24	5/29/24			5/30/24		5/30/24	5/30/24	Arch.: See attached response, Contractor: Elmwood ...
	016	Door 105	5/28/24		5/28/24		5/29/24		5/29/24	5/29/24			6/25/24		6/25/24	6/25/24	Arch.: See attached. Construction Manager: Issue r...
	016R	Door 105	6/7/24		6/7/24		6/10/24		6/10/24	6/10/24			6/25/24		6/25/24	6/25/24	Arch.: See attached. Construction Manager: No comm...
	017	CIC-02-003R Questions	5/28/24		5/28/24		5/29/24		5/29/24	5/29/24			5/29/24		5/29/24	5/29/24	Arch.: See attached for response.
	018	Wall Tile	6/7/24		6/7/24		6/10/24		6/10/24	6/10/24			6/25/24		6/25/24	6/25/24	Arch.: See attached.
	019	Frame Throat size	6/7/24		6/7/24		6/10/24		6/10/24	6/10/24			6/11/24		6/11/24	6/11/24	Arch.: See attached.
	020	RSHS ADA Ramp			6/27/24		6/28/24		6/28/24	6/28/24			7/22/24		7/22/24	7/22/24	Arch.: See attached for response.
	021	Asbestos Scope	6/28/24		6/28/24		7/1/24		7/1/24	7/1/24							Contractor: Please review this as soon as possible...
	022	RSHS Concrete Scope			7/1/24		7/1/24		7/1/24	7/1/24			7/1/24		7/1/24	7/1/24	Arch.: See attached, provide additional informatio...
	022 R1	RSHS Concrete Scope R1			7/2/24		7/2/24		7/2/24	7/2/24			7/22/24		7/22/24	7/22/24	Arch.: See attached for Response
ADA-MC	001	Elmwood - Question about asbestos in pen...	7/26/24		7/26/24		7/26/24		7/26/24	7/26/24			7/29/24		7/29/24	7/29/24	Arch.: The gypsum wall board/sheetrock does not co...
	001	Clarifications of water cooler model			3/15/24		3/18/24		3/18/24	3/18/24			3/22/24		3/22/24	3/22/24	Arch.: CSARCH has reviewed the attached response w...
ADA-PC	002	Water Cooler			3/25/24		3/25/24		3/25/24	3/25/24			5/23/24		5/23/24	5/23/24	
	003	Plumbing Rough-ins			4/26/24		4/26/24		4/26/24	4/26/24			5/9/24		5/9/24	5/9/24	
	004	Plumbing Rough Ins			5/14/24		5/14/24		5/14/24	5/14/24			5/23/24		5/23/24	5/23/24	
	005	Kakiat & Spring Valley Plumbing Rough-In...	7/11/24		7/11/24		7/11/24		7/11/24	7/11/24			7/26/24		7/26/24	7/26/24	Arch.: See the following.



## Phase 1B – CIC Log – To Date

**ORACLE** Primavera Submittal Exchange

Project: East Ramapo CSD ARPA Phase 1B Project Number: 209-2107.01



CIC's

View: **My Activity** | All Activity | Download Multiple Files

Sort By: **Category** | Numeric

Category: CICs - Doors | ADA-EC | ADA-GC | ADA-MC | ADA-PC

Category	CIC's #	Description	Posted		Remarks
			Date	File	
CICs - Doors	CIC 01 GC-004MES	Window limit stops at non-egress/rescue windows	12/22/23		Limit the clear opening of operational non-egress/...
	CIC 01 GC-005KES	Replacement Removable Key Core Cylinders	5/9/24		Per direction from the district the following door...
	CIC 01 GC-006EWES	Window limit stops at non-egress/rescue windows	12/22/23		Limit the clear opening of operational non-egress/...
	CIC 01-GC-002EWESRHS	Door B101	10/19/23		Door B101, door hardware for B101, and constructio...
	CIC 01-GC-002KES	Storefront Finish -KES	12/18/23		Provide the following finish for the storefront sy...
	CIC 01-GC-002RHS	Ramapo High School- Doors F100 & G100	10/19/23		Doors F100 and G100, door hardware for doors F100 ...
	CIC 01-GC-002SVHS	SVHS - Additional Exterior Doors - Vestibules V101 and V102	1/30/24		Additional Exterior Doors at Vestibules V101 and V...
	CIC 01-GC-003 RH	CIC 01-GC-003 RH- additional doors	4/2/24		Additional Doors because of reduction of ADA Phase...
	CIC 01-GC-003-MES	Storefront Finish-MES	12/18/23		Provide the following finish for the storefront sy...
	CIC 01-GC-003KES	Window limit stops at non-egress/rescue windows	12/22/23		Limit the clear opening of operational non-egress/...
	CIC 01-GC-004-KES	KES - Additional Doors	3/8/24		The following doors and associated hardware shall ...
	CIC 01-GC-004R-KES	Additional Doors KES -REVISED	5/6/24		REVISED CIC 01-GC-004R-KES. Revision to hardware ...
	CIC 01-GC-005-EWES	Storefront Finish-EWES	12/18/23		Provide the following finish for the storefront sy...
	CIC 01-GC-005-MES	MES - Additional Doors	3/11/24		The following doors and associated hardware shall ...
	CIC 01-GC-007-EWES	EWES - Additional Doors	3/8/24		The following doors and associated hardware shall ...
	CIC 01-GC-008 EWES	Additional Operable Windows	5/2/24		Rooms to be provided with an operable casement win...
	CIC 01GC-003-SVHS	CIC 01GC-003-SVHS Additional Doors	4/2/24		Additional Doors because of reduction of ADA Phase...
	CIC01 GC-002MES	Revisions to Storefront Types S2, S9, and S12	10/20/23		Revisions to Storefront Types S2, S9, and S12, pro...
	CIC01 GC-004RHS	Additional Keys	6/11/24		Provide additional Maint.2 keys (middle school/hig...
	CIC01GC-0-001EWES	Lead Test Report Elmwood ES	9/19/23		The following are lead testing results completed f...
	CIC01GC-0-001MES	Lead Test Report Margetts	9/19/23		The following are lead testing results completed f...
	CIC01GC-0-001RHS	Lead Test Report Ramapo HS	9/19/23		The following are lead testing results completed f...
	CIC01GC-0-001SVHS	Lead Testing Results SVHS	9/19/23		The following are lead testing results completed f...
	CIC01GC-003EWES	Revisions to Storefront Types and Add Entry Doors	10/24/23		Revisions to Storefront Types for Classroom 111 an...
	CIC01GC-004EWES	EWES - Doors at Stairs B101S and C101S	12/20/23		EWES - Changes to the scope of work for doors at S...
	CIV 01 GC-008R-EWES	Revisions to Additional Operable Windows	5/15/24		Note revised location of operable window in Room 1...
ADA-EC	CIC 03-001 – EWES PH1B ADA	03-001 – EWES PH1B ADA - EC	4/15/24		Revisions to Nurse 105, Electrical Field Directive...
	CIC 03-001-KES-PH1B-ADA-E	Toilet Room 127C and Nurse Toilet 202A Updated Electrical La...	7/26/24		Based on newfound existing conditions, the electri...
	CIC 03-002-EWES PH1B ADA	CIC 03-002-EWES PH1B ADA - EC	4/25/24		Electrical Revisions to Storage Room 104A - Elmwoo...
	CIC 03-003 EWES Ph1B ADA	REVISED 03-003R EWES Ph1B ADA - EC	5/17/24		ALL REVISIONS ARE INDICATED IN RED. Electrical Re...
	CIC 03-003-RSHS-PH1B-ADA-	Drinking Fountain - Cafeteria	9/23/24		Based on discussions with the district, the follow...
	02-001-RSHS-PH1B-ADA-EC	Electrical Revisions Rooms 080 and 081E	6/18/24		Based on discussions with the district and existin...
	02-007-EWES-PH1B-ADA-GC	Existing duct riser in Nurse Room 105	7/19/24		Based on existing conditions the existing duct ris...
	03-001-MES-PH1B-ADA-EC	Revisions to Health Office 41	6/26/24		Per the district's request revisions have been mad...
	03-001-SVHS Ph1B-ADA	Lift Power	6/11/24		Clarifications for the Lift Power.
	03-002 – SVHS PH1B ADA	Electrical Fixture Revisions	6/11/24		Per the district request the ceiling material has ...
	03-002-RSHS-PH1B-ADA-EC	Drinking Fountains	9/16/24		Based on discussions with the district, the follow...
	04-002 EWES PH1B ADA-MC	Mechanical revisions to Rooms 104A, 104B, 105A and 105	7/23/24		Based on unforeseen field conditions mechanical re...
ADA-GC	05-001-SVHS-Ph1B ADA-PC	Existing Storm Piping Relocation in Girls Toilet 21	7/29/24		Due to unforeseen site conditions existing vertica...
	CIC 02-001-EWES-001 PH1B	CIC ADA-GC-EWES-001-Nurse 105	4/8/24		THIS CIC HAS BEEN REVISED; REVISIONS ARE NOTED ON ...
	CIC 02-003-MES-PH1B-ADA-G	Paint Color Selections	8/2/24		All Door Frames in project scope shall be painted ...
	CIC 02-004-KES-PH1B-ADA-G	Paint Color Selections	8/2/24		All Door Frames in project scope shall be painted ...
	CIC 02-004-RSHS-PH1B-ADA-	Exterior Ramp Detail revisions based on existing conditions	7/31/24		Based on field conditions see the following pages ...
	CIC 02-005-EWES-PH1B-ADA-	Doors: Interchangeable Cores	6/25/24		Provide interchangeable cores as manufactured by M...
	CIC 02-005-RSHS-PH1B-ADA-	Paint Color Selections	8/2/24		All Door Frames in project scope shall be painted ...
	CIC 03-001-KES-PH1B-ADA-E	Toilet Room 127C and Nurse Toilet 202A Updated Electrical La...	7/26/24		Based on newfound existing conditions, the electri...
	EC CIC 03-003R EWES	FOR REFERENCE ONLY	5/28/24		Electrical Contract CIC 03-003R – EWES PH1B ADA - ...
	PC CIC 05-002 EWES	FOR REFERENCE ONLY	5/28/24		Plumbing Contract CIC 05-002 – EWES PH1B ADA - PC ...
	02-001-KES-PH1B-ADA-GC	RCP and Finishes Updates to Toilet Rooms 127C and 202A	6/25/24		Based on discussions with the district, changes to...
	02-001-MES-PH1B-ADA-GC	RCP and finish updates at Nurse 41, Toilet 41T and Toilet 6T	6/26/24		Based on discussions with the district, updates to...
	02-001-RSHS-PH1B-ADA-GC	RCP and Finishes Update; Additional Abatement	6/18/24		Based on discussions with the district and existin...
	02-001-SVHS Ph1B-ADA	Revisions to Finishes	6/11/24		Based on discussions with the district, updates to...
	02-002-EWES PH1B-ADA-GC	02-002-EWES PH1B-ADA-GC	4/15/24		Removal and disposal additional of asbestos contal...
	02-002-KES-PH1B-ADA-GC	Doors: Interchangeable Cores	6/25/24		Provide interchangeable cores as manufactured by M...
	02-002-MES-PH1B-ADA-GC	Doors: Interchangeable Cores	6/25/24		Provide interchangeable cores as manufactured by M...
	02-002-RSHS-PH1B-ADA-GC	Doors: Interchangeable Cores	6/25/24		Provide interchangeable cores as manufactured by M...
	02-002-SVHS-PH1B ADA	Doors: Interchangeable Cores	6/25/24		Provide interchangeable cores as manufactured by M...
	02-003-KES-PH1B-ADA-GC	Nurse Toilet 202A Updated Layout	7/11/24		Based on newfound existing conditions, the layout ...
	02-003-SVHS-Ph1B ADA-GC	ADA Wheelchair Lift in Stair RS1	6/27/24		The existing 1" high concrete pad located under th...
	02-003R-EWES PH1B-ADA GC	Revisions to Toilet Room 104B	5/8/24		REVISED LAYOUT TO TOILET ROOM 104B. REVISIONS TO T...
	02-003R-RSHS-PH1B-ADA-GC	Exterior Ramp Revisions	7/22/24		See the attached for clarifications and revisions ...
	02-004-EWES PH1B-ADA-GC	Acoustical Panel Specification	5/8/24		Based discussions with the district regarding fini...
	02-004-SVHS-PH1B ADA-GC	Revisions to Toilet Room 225	7/12/24		After discussions on site and approval from the di...
	02-005R-SVHS-Ph1B ADA-GC	REVISED Additional Toilet Room Dimensions	7/18/24		See attached drawings sheets for additional dimens...
	02-006-SVHS-Ph1B ADA-GC	Parapet Infill Section	7/30/24		Abatement activities at Toilet Room 21 and 22 remo...
	02-006R-EWES-PH1B-ADA-GC	Updates to Interior Finishes at Toilet Rooms 104B, 105A, 230...	6/25/24		REVISED Based on discussions with the district a...
	02-006R-RSHS-PH1B-ADA-GC	Drinking Fountains	9/23/24		REVISED to include changes in Cafeteria, painting ...
	02-007-EWES-PH1B-ADA-GC	Existing duct riser in Nurse Room 105	7/19/24		Based on existing conditions the existing duct ris...
	02-007-SVHS-Ph1B ADA-GC	Clarifications for the ADA Lift	7/29/24		The existing ADA lift was not constructed so that ...
	02-008-EWES-PH1B-ADA-GC	Paint Color Selections	8/2/24		All Door Frames in project scope shall be painted ...
	02-008-SVHS-Ph1B ADA-GC	Paint Color Selections	8/2/24		All Door Frames in project scope shall be painted ...
	02-009-SVHS-Ph1B ADA-GC	Wall Bracing in Boys Toilet 22	8/2/24		Due to existing field conditions the new CMU part...
	04-002 EWES PH1B ADA-MC	Mechanical revisions to Rooms 104A, 104B, 105A and 105	7/23/24		Based on unforeseen field conditions mechanical re...
	05-001-SVHS-Ph1B ADA-PC	Existing Storm Piping Relocation in Girls Toilet 21	7/29/24		Due to unforeseen site conditions existing vertica...
ADA-MC	CIC 03-001-KES-PH1B-ADA-E	Toilet Room 127C and Nurse Toilet 202A Updated Electrical La...	7/26/24		Based on newfound existing conditions, the electri...
	02-007-EWES-PH1B-ADA-GC	Existing duct riser in Nurse Room 105	7/19/24		Based on existing conditions the existing duct ris...
	04-001 – EWES PH1B ADA -	Revisions to Rooms 104A and 104B	5/29/24		Mechanical Revisions to Storage Room 104A and Toi...
	04-001-KES-PH1B-ADA-MC	Mechanical Changes	6/25/24		Revisions to Toilet Room 127C and Toilet Room 202A...
	04-001-MES-PH1B-ADA-MC	Revisions to Health Office 41	6/26/24		Per the district's request revisions have been mad...
	04-001-SVHS Ph1B-ADA	Mechanical Revisions at Acoustical Ceiling Tile	6/11/24		Per the district request the ceiling material has ...
ADA-PC	04-002 EWES PH1B ADA-MC	Mechanical revisions to Rooms 104A, 104B, 105A and 105	7/23/24		Based on unforeseen field conditions mechanical re...
	05-001-SVHS-Ph1B ADA-PC	Existing Storm Piping Relocation in Girls Toilet 21	7/29/24		Due to unforeseen site conditions existing vertica...
	CIC 03-001-KES-PH1B-ADA-E	Toilet Room 127C and Nurse Toilet 202A Updated Electrical La...	7/26/24		Based on newfound existing conditions, the electri...
	CIC 05-001-KES-PH1B-ADA-P	Plumbing Revisions to Nurse Room	7/24/24		Based on newfound existing conditions, near the Nu...
	CIC 05-001EWES 1B ADA -PC	CIC 05-001EWES 1B ADA -PC	4/10/24		Revisions to Nurse 105
	CIC 05-002-RSHS-PH1B-ADA-	Drinking Fountain - Cafeteria	9/23/24		Based on discussions with the district, the follow...
	CIC 05-002EWES 1B ADA -PC	Revisions to Toilet Room 104B	5/28/24		Plumbing revisions for Toilet Room 104B. Gener...
	02-005R-SVHS-PH1B ADA-GC	REVISED Additional Toilet Room Dimensions	7/18/24		See attached drawings sheets for additional dimens...
	02-007-EWES-PH1B-ADA-GC	Existing duct riser in Nurse Room 105	7/19/24		Based on existing conditions the existing duct ris...
	04-002 EWES PH1B ADA-MC	Mechanical revisions to Rooms 104A, 104B, 105A and 105	7/23/24		Based on unforeseen field conditions mechanical re...
	05-001-MES-PH1B-ADA-PC	Revisions to Health Office 41	6/26/24		Per the district's request revisions have been mad...
	05-001-RSHS-PH1B-ADA-PC	Drinking Fountains	9/16/24		FOR REFERENCE THE FOLLOWING RELATED CIC'S ARE INCLU...
	05-001-SVHS-Ph1B ADA-PC	Existing Storm Piping Relocation in Girls Toilet 21	7/29/24		Due to unforeseen site conditions existing vertica...
	05-003 – EWES PH1B ADA -	Revision to Custodial Room D201A	6/26/24		Removal and replacement of mop sink in Custodial R...



Phase 1B – Cost Proposal Log – To Date

ORACLE Primavera Submittal Exchange

Project: East Ramapo CSD ARPA Phase 1B Project Number: 209-2107.01

JACOBS Cost Proposals

View: My Activity | Download Multiple Files | Edit Expected Items

Sort By: Category | Numerically  
Category: C1-GC-01 | ADA-EC | ADA-GC | ADA-MC | ADA-PC

Category	Cost Proposals #	Description	From Contractor		From Construction Manager		Review by Consultant			Review by Architect		Returned to Contr		Amount	Status	Action	Remarks	
			Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned Arch.	File	Returned to Construction Manager	File	Date					Type
C1-GC-01	001	Elmwood ES Additional Door Proposal	11/8/23	PDF	11/8/23	PDF	11/8/23	11/8/23			1/18/24	PDF	1/18/24	\$5,634.00			Arch.: Architect has reviewed with consultant. See...	
	001R2	Elmwood ES Additional Door Revised Propo...	2/20/24	PDF	2/22/24	PDF	2/22/24	2/22/24			3/26/24	PDF	3/26/24	\$5,634.00			Arch.: No O&P until allowance has been exhausted. ...	
	004	Revised Transom Panel Proposal	1/3/24	PDF	1/19/24	PDF	1/19/24	1/19/24			1/23/24	PDF	1/24/24	\$8,257.56		1/23/2024	Arch.: Reviewed with consultant. Revise per attac...	
	004R2	Update Revised Transom Proposal	2/20/24	PDF	2/22/24	PDF	2/22/24	2/22/24			3/27/24	PDF	3/27/24	\$8,257.56			Arch.: See attached for comments.	
	004R3A	AIA - RHVS Transom Rev2	4/26/24	PDF	4/30/24	PDF	4/30/24	4/30/24						\$5,012.99				
	004R3B	AIA - SVHS Transom Rev	4/29/24	PDF	4/30/24	PDF	4/30/24	4/30/24						\$3,767.22				
	005	Revised Cost Proposal Elmwood ES Aluminu...	1/10/24	PDF	1/19/24	PDF	1/19/24	1/19/24			1/23/24	PDF	1/24/24	\$30,475.00			Arch.: See attached for comments.	
	005R2	Revised Elmwood Alum Door Hardware Propo...	1/26/24	PDF	1/29/24	PDF	1/29/24	1/29/24			2/16/24	PDF	2/16/24	\$26,500.00			Arch.: See attached for comments. Construction Man...	
	005R3	3rd Revision Elmwood Alum Door Hardware ...	2/26/24	PDF	2/27/24	PDF	2/27/24	2/27/24			3/28/24	PDF	3/28/24	\$33,280.00	Approved		Arch.: Hardware is acceptable, Cost Proposal amoun...	
	006	Revised Cost Proposal Margetts Aluminum ...	1/10/24	PDF	1/19/24	PDF	1/19/24	1/19/24						\$61,180.00				
	006R2	Revised Cost Proposal Margetts Aluminum ...	1/26/24	PDF	1/29/24	PDF	1/29/24	1/29/24						\$53,200.00			Construction Manager: Bill towards allowance.	
	006R3	3rd Revision Margetts Alum Door Hardware...	2/26/24	PDF	2/27/24	PDF	2/27/24	2/27/24			3/28/24	PDF	3/28/24	\$64,156.00	Approved			
	007	Revised Cost Proposal Elmwood Aluminum D...	1/10/24	PDF	1/19/24	PDF	1/19/24	1/19/24						\$33,878.75				
	007R2	Revised Cost Proposal Elmwood Doors C100...	1/26/24	PDF	1/29/24	PDF	1/29/24	1/29/24						\$23,729.00			Construction Manager: Revise per comments -	
	007R3	3rd Revision Elmwood Door C100 C100A Doo...	2/26/24	PDF	2/27/24	PDF	2/27/24	2/27/24			3/28/24	PDF	3/28/24	\$24,853.00			Arch.: Hardware is acceptable, Cost Proposal amoun...	
	008	SVHS Vestibules V101 and V102 Proposal	2/15/24	PDF	2/28/24	PDF	2/28/24	2/28/24			3/27/24	PDF	3/27/24	\$58,666.90			Arch.: See attached for comments.	
	009	Paint Cost Proposal	3/25/24	PDF	3/27/24	PDF	3/27/24	3/27/24								Rejected		Construction Manager: Please revise & resubmit add...
	010	Elmwood Additional Door Updated Revised ...	4/25/24	PDF	4/26/24	PDF	4/26/24	4/26/24							\$5,634.00	Rejected		Construction Manager: Please make corrections
	010R2	AIA - Elmwood Additional Doors Rev 2	4/26/24	PDF	4/30/24	PDF	4/30/24	4/30/24			5/7/24	PDF	5/8/24		\$5,692.16	Approved		Arch.: Reviewed with the district and this will pr...
	011	AIA - CIC-01 GC-002-SVHS	4/26/24	PDF	4/30/24	PDF	4/30/24	4/30/24			5/14/24	PDF	5/14/24		\$55,057.40	Approved		
	012	AIA - CIC-01 GC-003-SVHS	4/26/24	PDF	4/30/24	PDF	4/30/24	4/30/24			5/10/24	PDF	5/10/24		\$13,312.01	Approved		
	013	AIA - CIC-01 GC-004-KES	4/26/24	PDF	4/30/24	PDF	4/30/24	4/30/24			5/6/24	PDF	5/7/24		\$32,632.16			Arch.: Revise and resubmit per comments.
	013R2	AIA - CIC-01 GC-004R-KES	5/9/24	PDF	5/10/24	PDF	5/10/24	5/10/24			7/10/24	PDF	7/11/24		\$17,335.23	Approved		Arch.: This was sent to the BOE for the 6/04/2024 ...
	014	AIA - CIC-01 GC-005-MES	4/26/24	PDF	4/30/24	PDF	4/30/24	4/30/24			5/7/24	PDF	5/8/24		\$10,878.10	Approved		Arch.: Provide 540BLN Lockset Function for doors 1...
015	AIA - CIC-01 GC-007-EWES	4/26/24	PDF	4/30/24	PDF	4/30/24	4/30/24			5/7/24	PDF	5/8/24		\$13,938.59	Approved		Arch.: Provide 540BLN Lockset Function for doors 1...	
016	AIA - CIC-01 GC-003-RHS	5/1/24	PDF	5/3/24	PDF	5/3/24	5/3/24			7/10/24	PDF	7/11/24		\$39,186.97	Approved		Arch.: This was sent to the BOE for the 6/4/2024 m...	
017	Kakiat Window Abatement Credit	4/30/24	PDF	5/13/24	PDF	5/13/24	5/13/24			8/6/24	PDF	8/8/24		\$2,384.71	Approved		Construction Manager: CM Approved & Updated. AOR t...	
018	AIA - CIC-01 GC-005-KES	5/14/24	PDF	5/15/24	PDF	5/15/24	5/15/24			8/6/24	PDF	8/8/24		\$2,384.71	Approved		Arch.: Approved for \$2,384.71, apply towards allow...	
019	CIC-01 GC-008R-EWES	6/3/24	PDF	6/4/24	PDF	6/4/24	6/4/24			7/23/24	PDF	7/23/24		\$20,926.41	Approved		Arch.: This has been reviewed by the district and ...	
020	Kakiat ES Doors 118, 127, 131 Cost Propo...	6/13/24	PDF	6/14/24	PDF	6/14/24	6/14/24			8/6/24	PDF	8/8/24		\$3,640.56	Approved		Arch.: Approved for \$3,640.56 and apply towards al...	
034	CIC-01 GC-004-RHS	7/2/24	PDF	7/26/24	PDF	7/26/24	7/26/24			8/6/24	PDF	8/8/24		\$1,380.00	Approved		Arch.: Approved for \$1,380.00 to be applied to all...	
ADA-EC	001EC	CIC ADA-EWES-001 Nurse 105	4/17/24	PDF	4/17/24	PDF	4/17/24	4/17/24								Rejected		
	002EC	EC-PH1B-CO-EC-001 Lighting	6/5/24	PDF	6/5/24	PDF	6/5/24	6/5/24			6/19/24	PDF	6/20/24		\$901.00	Rejected		Arch.: Revise per the attached. Construction Manag...
	002ECR1	EC-PH1B-CO-EC-001 Lighting R1	6/23/24	PDF	6/23/24	PDF	6/23/24	6/23/24							\$1,053.00			
	003EC	EC-PH1B-CO-EC-002 CIC 02-002-SVHS-PH1B A...	6/23/24	PDF	6/23/24	PDF	6/23/24	6/23/24							\$1,755.00			
	004EC	EC-PH1B-CO-EC-003-CIC 03-001-RSHS-ROOM 8...	6/23/24	PDF	6/23/24	PDF	6/23/24	6/23/24							\$963.26			Construction Manager: CM approved. AOR to review & ...
	005EC	EC-PH1B-CO-EC-004-CIC 03-001-SVHS PH1B A...	6/24/24	PDF	6/24/24	PDF	6/24/24	6/24/24							\$1,913.92			Construction Manager: CM approved. AOR to review & ...
ADA-GC	005EC	EC-PH1B-CO-EC-004-RSHS Nurse Suite	8/27/24	PDF	8/27/24	PDF	8/27/24	8/27/24										Construction Manager: Jacobs Reviewed
	002GC	↑ Epoxy Flooring	4/22/24	PDF	5/30/24	PDF	5/29/24	5/29/24			6/20/24	PDF	6/20/24		(\$12,133.00)	Approved		Arch.: Credit amount has been reviewed and accepte...
	003GC	EC-PH1B-CO-GC-002 Gypsum to ACT Ceilings	5/30/24	PDF	6/4/24	PDF	5/30/24	5/30/24			6/20/24	PDF	6/20/24		(\$6,759.60)	Approved		Arch.: Credit amount has been reviewed and accepte...
	004GC	EC-PH1B-CO-GC-003 CIC 02-003R-EWES	6/2/24	PDF	6/2/24	PDF	6/2/24	6/2/24			6/20/24	PDF	6/20/24			Rejected		Arch.: See Cost Proposal 005GC for revisions and c...
	005GC	EC-PH1B-CO-GC-003 CIC 02-003R-EWES	6/14/24	PDF	6/14/24	PDF	6/14/24	6/14/24			6/20/24	PDF	6/20/24		\$11,984.43	Approved		Arch.: Cost Proposal has been reviewed and accepte...
	021	EC-PH1B-CO-GC-004 CIC02-003-SVHS-PH1B AD...	6/30/24	PDF	6/30/24	PDF	6/30/24	6/30/24			7/25/24	PDF	7/25/24		\$2,920.32	Approved		Arch.: PCO approved for removals only, provide sep...
	022	EC-PH1B-CO-GC-005 CIC 02-006R-EWES-ABATE	7/1/24	PDF	8/5/24	PDF	7/1/24	7/1/24			9/17/24	PDF	9/17/24		\$56,847.61	Approved		Arch.: Approved as a Change Order in the amount of...
	023	EC-PH1B-CO-GC-006 CIC 02-001-RSHS-PH1B	7/1/24	PDF	7/1/24	PDF	7/1/24	7/1/24			9/10/24	PDF	9/10/24		\$17,320.89	Approved		Arch.: Approved for \$17,320.89 as an allowance dis...
	024	EC-PH1B-CO-GC-007 CIC 02-002-SVHS-PH1B A...	7/1/24	PDF	7/1/24	PDF	7/1/24	7/1/24			7/8/24	PDF	7/9/24		\$594.00	Approved		Arch.: See attached. Construction Manager: CM appr...
	025	EC-PH1B-CO-GC-008 CIC 02-002-KES-PH1B AD...	7/1/24	PDF	7/1/24	PDF	7/1/24	7/1/24			7/8/24	PDF	7/9/24		\$223.00	Approved		Arch.: See attached. Construction Manager: Cm appr...
	026	EC-PH1B-CO-GC-009 CIC 02-002-MES-PH1B AD...	7/1/24	PDF	7/1/24	PDF	7/1/24	7/1/24			7/8/24	PDF	7/9/24		\$371.00	Approved		Arch.: See attached. Construction Manager: CM appr...
	027	EC-PH1B-CO-GC-010 CIC 02-002-RSHS-PH1B A...	7/1/24	PDF	7/1/24	PDF	7/1/24	7/1/24			7/8/24	PDF	7/9/24		\$74.00	Approved		Arch.: See attached. Construction Manager: CM Appr...
	028	EC-PH1B-CO-GC-011 CIC 02-005-EWES PH1B A...	7/1/24	PDF	7/1/24	PDF	7/1/24	7/1/24			7/8/24	PDF	7/9/24		\$520.00	Approved		Arch.: See attached. Construction Manager: CM appr...
	029	CIC 02-001-MES-PH1B-ADA-GC_rcp and finis...	7/2/24	PDF	7/2/24	PDF	7/2/24	7/2/24										Construction Manager: CO Approved
	030	EC-PH1B-CO-GC-013 CIC 02-001-RSHS-VAT	7/3/24	PDF	7/3/24	PDF	7/3/24	7/3/24			9/10/24	PDF	9/10/24		\$15,590.34	Approved		Arch.: Approved for Change Order in the amount of ...
	031	EC-PH1B-CO-GC-014-SVHS Abate of Wall	7/9/24	PDF	7/9/24	PDF	7/9/24	7/9/24			7/30/24	PDF	7/31/24		\$46,447.00	Approved		Arch.: See attached for comments. Construction Man...
	032	EC-PH1B-CO-GC-015-CIC02-004-SVHS-ADA_CMU...	7/15/24	PDF	7/15/24	PDF	7/17/24	7/15/24			8/13/24	PDF	8/15/24		\$17,501.76	Approved		Arch.: REVISED - Approved for \$17,501.76 applied...
	033	EC-PH1B-CO-GC-016-FD 01-KES JAN ABATE	7/17/24	PDF	7/17/24	PDF	7/17/24	7/17/24			8/1/24	PDF	8/1/24		\$8,500.00	Approved		Arch.: Approved for \$8,500.00 to be applied toward...
	035	EC-PH1B-CO-GC-017-FD 01-EWES 230A & 230B...	8/2/24	PDF	8/2/24	PDF	8/2/24	8/2/24			8/14/24	PDF	8/15/24		\$8,500.00	Approved		Arch.: Approved for \$8,500.00 to be applied to the ...
	036	EC-PH1B-CO-GC-018-_ramp details	8/13/24	PDF	8/13/24	PDF	8/13/24	8/13/24										Construction Manager: Jacobs Reviewed 8/14/24 - Th...
	037	EC-PH1B-CO-GC-019-RSHS Floor Leveling	8/14/24	PDF	8/14/24	PDF	8/14/24	8/14/24			9/5/24	PDF	9/6/24		\$1,320.00	Approved		Arch.: Apply towards allowance, approved for \$1,32...
	038	EC-PH1B-CO-GC-020-RSHS Additional Equipm...	8/15/24	PDF	8/15/24	PDF	8/15/24	8/15/24			9/12/24	PDF	9/12/24		\$4,600.00	Approved		Arch.: Approved for \$4,600.00 to be taken as an al...
	039	EC-PH1B-CO-GC-021-EWES Trenching for Ele...	8/25/24	PDF	8/25/24	PDF	8/25/24	8/25/24			9/17/24	PDF	9/17/24		\$3,265.32	Approved		Arch.: Apply towards allowance, approved in the am...
	040	EC-PH1B-CO-GC-022-MES Roof Drain	8/25/24	PDF	8/25/24	PDF	8/25/24	8/25/24								Approved		Construction Manager: Jacobs Approved
	041	EC-PH1B-CO-GC-023-Temporary Doors	8/25/24	PDF	8/25/24	PDF	8/25/24	8/25/24										Construction Manager: Jacobs Approved
	042	EC-PH1B-CO-GC-024-RSHS Nurses 081 New Wa...	8/25/24	PDF	8/25/24	PDF	8/25/24	8/25/24			9/3/24	PDF	9/9/24		\$25,879.50	Approved		Arch.: Approved for a Change Order in the amount o...
	043	EC-PH1B-CO-GC-025-Bathrooms 221 & 225	8/25/24	PDF	8/25/24	PDF	8/25/24	8/25/24			9/12/24	PDF	9/12/24		\$33,801.64	Approved		Arch.: Approved as a Change Order in the amount of...
	044	EC-PH1B-CO-GC-026-Heavy Floor Prep KES-M...	8/25/24	PDF	8/25/24	PDF	8/25/24	8/25/24										Construction Manager: Jacobs Approved
	046	EC-PH1B-CO-GC-027-CIC 02-006R-EWES	9/4/24	PDF	9/4/24	PDF	9/4/24	9/4/24										
	047	EC-PH1B-CO-GC-028-EWES Corian Tops	9/11/24	PDF	9/11/24	PDF	9/11/24	9/11/24										
	048	EC-PH1B-CO-GC-029-MES Corian Tops	9/11/24	PDF	9/11/24	PDF	9/11/24	9/11/24										
049	EC-PH1B-CO-GC-030-KES Corian Tops	9/11/24	PDF	9/11/24	PDF	9/11/24	9/11/24											
ADA-MC																		



## Phase 3B – RFI Log – To Date

ORACLE Primavera Submittal Exchange












































































































































































Project: East Ramapo Central School District - ARPA - Phase 3B - Door Replacement and Related Work Project Number: 209-2107.02 & 209-2107.03

JACOBS RFI

View: My Activity | All Activity | Download Multiple Files

Sort By: Category | Numeric

Category: C1-GC-01

Category	RFI #	Description	From Subcontractor		From Contractor		From Construction Manager		Review by Consultant		Review by Architect		Returned to Contractor	Returned to Sub	Remarks	
			Date	Type	Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned to Arch.	File	Returned to Construction Manager	File		Date
C1-GC-01	001	Signage Eldorado 01	10/24/23		10/24/23		10/25/23		10/25/23	10/25/23		5/29/24		5/29/24	Arch.: see attached. Contractor: Attached are a fe...	
	002	Door RFI #1	11/21/23		11/21/23		11/21/23		11/21/23	11/22/23		11/29/23		11/29/23	Arch.: See attached for additional information. Co...	
	003	Door RFI #2	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached for response to RFI. Consultan...	
	004	Door RFI #3	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached for response to RFI. Consultan...	
	005	Door RFI #4	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached for response to RFI. Consultan...	
	006	Door RFI #5	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached for response to RFI. Consultan...	
	007	Door RFI #6	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached for response to RFI. Consultan...	
	008	Door RFI #7	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached for response to RFI. Consultan...	
	009	Door RFI #8	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached for response to RFI. Consultan...	
	010	Door RFI #9	12/1/23		12/1/23		12/4/23		12/4/23	12/4/23		12/19/23		12/19/23	Arch.: See attached response to RFI. Consultant: A...	
	011	Door RFI #10	12/8/23		12/8/23		12/8/23		12/8/23	12/12/23		12/19/23		12/19/23	Arch.: See attached comments from hardware consult...	
	012	Door RFI #11	12/8/23		12/8/23		12/8/23		12/8/23	12/12/23		12/19/23		12/19/23	Arch.: See attached comments from hardware consult...	
	013	Door RFI #12	12/8/23		12/8/23		12/8/23		12/8/23	12/12/23		12/19/23		12/19/23	Arch.: See attached response from hardware consult...	
	014	Door RFI #13	12/8/23		12/8/23		12/8/23		12/8/23	12/12/23		12/19/23		12/19/23	Arch.: See attached response from hardware consult...	
	015	Door RFI #14	12/8/23		12/8/23		12/8/23		12/8/23	12/12/23		12/19/23		12/19/23	Arch.: See attached response from hardware consult...	
	016	Door RFI #15	12/8/23		12/8/23		12/8/23		12/8/23	12/12/23		12/19/23		12/19/23	Arch.: See attached hardware consultants response ...	
	017	Door RFI #16	12/8/23		12/8/23		12/8/23		12/8/23	12/12/23		12/19/23		12/19/23	Arch.: See attached response from hardware consult...	
	018	Door RFI #17	12/14/23		12/14/23		12/14/23		12/14/23	12/14/23		1/16/24		1/16/24	Arch.: See attached response for RFI 17. These re...	
	019	Door RFI #18	12/14/23		12/14/23		12/14/23		12/14/23	12/14/23		1/3/24		1/3/24	Arch.: See attached for response.	
	020	Door RFI #19	1/15/24		1/15/24		1/16/24		1/16/24	1/16/24		1/30/24		1/30/24	Arch.: See attached for response.	
	021	Abatement RFI #1	1/12/24		1/12/24		1/16/24		1/16/24	1/16/24		1/30/24		1/30/24	Arch.: See attached for response.	
	022	Question for RFI 18	1/15/24		1/19/24		1/23/24		1/23/24	1/23/24		1/30/24		1/30/24	Arch.: See attached for response. Contractor: RFI ...	
	023	Sign RFI 02	1/25/24		1/25/24		1/29/24		1/29/24	1/29/24		5/8/24		5/8/24	Contractor: Need answer asap on this and signage ...	
	024	Door Frame Color	2/1/24		2/1/24		2/1/24		2/1/24	2/1/24		2/6/24		2/6/24	Arch.: See attached for response. This RFI does n...	
	025	Question for RFI 19 Lead Handling	2/1/24		2/1/24		2/1/24		2/1/24	2/1/24		2/7/24		2/7/24	Arch.: See the attached for response. Contractor: ...	
	026	ML209 Hotel Lock Function	2/21/24		2/21/24		2/21/24		2/21/24	2/21/24	2/21/24		2/27/24		2/27/24	Arch.: See attached for response.
	027	Security Door Prop	2/29/24		2/29/24		2/29/24		2/29/24	2/29/24		4/23/24		4/23/24	Arch.: See attached for response. Contractor: Plea...	
	028	Paint Color CRES/PES	3/26/24		3/26/24		4/1/24		4/1/24	4/1/24		4/9/24		4/9/24	4/9/24	Arch.: See attached for response. Contractor: Per ...
	029	Cores for Pomona tag G100A G100C	5/10/24		5/10/24		5/10/24		5/10/24	5/10/24		5/17/24		5/17/24	5/17/24	Contractor: Please confirm which doors we are proc...
	030	Confirmation of CIC 004 LKES and 006 EDE...	5/10/24		5/10/24		5/10/24		5/10/24	5/10/24		5/14/24		5/14/24	5/14/24	Contractor: Please confirm the Hardware for LKES J...
	031	Hardware/keying LKES CIC	5/20/24		5/20/24		5/20/24		5/20/24	5/20/24		5/22/24		5/22/24	5/22/24	Arch.: See attached response. Contractor: There is...
	032	HM Door Paint Color	5/23/24		5/23/24		5/23/24		5/23/24	5/23/24		5/29/24		5/29/24	5/29/24	Arch.: See attached. Contractor: Please see Attach...
	033	Fleetwood Tags C003A/C003AA	5/30/24		5/30/24		6/10/24		6/10/24	6/10/24		7/1/24		7/1/24	7/1/24	Arch.: See attached response. Contractor: There is...
	034	El Dorado Cores	6/10/24		6/11/24		6/11/24		6/11/24	6/11/24		7/30/24		7/30/24	7/30/24	Arch.: See attached for response. Contractor: Plea...
	035	Chestnut Cores	6/10/24		6/11/24		6/11/24		6/11/24	6/11/24		7/30/24		7/30/24	7/30/24	Arch.: See attached for response. Contractor: Plea...
	036	Hollow Metal Door Colors	6/11/24		6/11/24		6/12/24		6/12/24	6/12/24		7/1/24		7/1/24	7/1/24	Arch.: See attached for response. Contractor: Plea...
	037	Fleetwood Cores	6/12/24		6/18/24		6/18/24		6/18/24	6/18/24		7/30/24		7/30/24	7/30/24	Arch.: See attached for response. Contractor: Plea...
	038	CIC 006 EDES	6/27/24		6/27/24		6/28/24		6/28/24	6/28/24						Contractor: Please see attached RFI #38 for CIC 00...
	039	Unique Cores	7/3/24		7/3/24		7/3/24		7/3/24	7/3/24						Contractor: Please see attached RFI 39 for Unique ...

## Phase 3B – Cost Proposal Log – To Date

ORACLE

Primavera Submittal Exchange

Project: East Ramapo Central School District - ARPA - Phase 3B - Door Replacement and Related Work Project Number: 209-2107.02 & 209-2107.03

JACOBS

Cost Proposals

View: **My Activity** | [Download Multiple Files](#) | [Edit Expected Items](#)

Sort By: **Category** | [Numeric](#)

Category: C1-GC-01

Category	Cost Proposals #	Description	From Contractor		From Construction Manager		Review by Consultant				Review by Architect		Returned to Contr		Amount	Status	Action	Remarks
			Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned Arch.	File	Returned to Construction Manager	File	Date	Type				
C1-GC-01	001	AIA C/O Per CIC	7/15/24		Send										\$138,614.00	Pending		Arch.: Revise per comments, see attached. Provide... Construction Manager: Back up for PCO 001 Construction Manager: As per 2.13.24 Meeting Minut... Construction Manager: Backup already provided in P... Construction Manager: Jacobs added Sunrise Backup ... Construction Manager: As per Direction from ERCSD ... Construction Manager: As per 2.13.24 Meeting Minut... Construction Manager: Jacobs added Sunrise Backup ... Construction Manager: Jacobs added Sunrise Backup ... Construction Manager: As per direction of ERCSD Me...
	001B	CIC 001 EDES Tag 240A REV1	1/24/24			1/31/24		1/31/24	1/31/24		2/8/24		2/9/24		\$3,615.00	Pending		
	002	Sunrise Backup CIC 001 EDES Tag 240A	3/19/24			5/13/24		5/13/24	5/13/24						\$1,630.08	Rejected		
	002B	CO#02 LKES Stairwell Doors	2/7/24			2/20/24		2/20/24	2/20/24						\$60,472.50	Rejected		
	002R1	LKES CO#01 REVISED	4/2/24			5/13/24		5/13/24	5/13/24						\$20,079.00	Rejected		
	002R2	LKES CO#1 R2 Metal Doors	2/26/24			3/1/24		3/1/24	3/1/24						\$35,154.00	Rejected		
	002R3.1	LKES CO#1 R2 Metal Doors	3/15/24			3/18/24		3/18/24	3/18/24						\$35,154.00	Pending		
	002R3.2	LKES PCO#1 - Stairwell Doors - METAL OPT...	4/11/24			5/13/24		5/13/24	5/13/24						\$50,079.00	Rejected		
	003	LKES PCO#1 - Stairwell Doors - WOOD OPTI...	4/11/24			5/13/24		5/13/24	5/13/24						\$65,592.00	Rejected		
	003R1	CO#03 EDES Stairwell Doors	2/7/24			2/20/24		2/20/24	2/20/24						\$20,079.00	Rejected		
	003R2	EDES CO#02 REVISED	2/28/24			3/1/24		3/1/24	3/1/24						\$35,154.00	Rejected		
	003R3.1	EDES CO #02 R2 Metal	3/15/24			3/18/24		3/18/24	3/18/24						\$35,154.00	Pending		
	003R3.2	EDES PCO#2 - Stairwell Doors Tags - META...	4/11/24			5/13/24		5/13/24	5/13/24						\$50,079.00	Rejected		
	004	EDES PCO#2 - Stairwell Doors Tags - WOOD...	4/11/24			5/13/24		5/13/24	5/13/24						\$4,922.00	Rejected		
	004R1	CRMS CO#01 - Lead Handling - Allowance A...	2/28/24			3/1/24		3/1/24	3/1/24						\$4,922.00	Pending		
	006	CRMS PCO#1 - LEAD Handling	4/11/24			5/13/24		5/13/24	5/13/24						\$2,461.00	Rejected		
	006R1	EDES CO#03 - Lead Handling	4/11/24			5/13/24		5/13/24	5/13/24						\$2,461.00	Pending		
	007	PMS PCO#1 Pomona tags G100A & G100C - CI...	4/19/24			5/13/24		5/13/24	5/13/24						\$6,094.53	Pending		
	008	Pomona Cores	9/12/24			9/13/24		9/13/24	9/13/24						\$3,430.85	Pending		
	009	Pomona Door Repairs	9/5/24			9/13/24		9/13/24	9/13/24						\$17,226.00	Pending		
010	Renu: Lime CO1	9/13/24			9/16/24		9/16/24	9/16/24						\$18,951.58	Approved			
011	Renu: Fleetwood CO1	9/13/24			9/16/24		9/16/24	9/16/24						\$1,130.80	Approved			
012	Renu: Eldorado CO1	9/13/24			9/16/24		9/16/24	9/16/24						\$16,390.66	Approved			
013	Renu: Chestnut Deduct CO	9/13/24			9/16/24		9/16/24	9/16/24							Approved			

## Phase 3B – CIC Log – To Date

ORACLE Primavera Submittal Exchange

Project: East Ramapo Central School District - ARPA - Phase 3B - Door Replacement and Related Work Project Number



CIC's

View: **My Activity** | [All Activity](#)

[Download Multiple Files](#)

Sort By: **Category** | [Numeric](#)

Category: CICs | C1-GC-01

Category	CIC's #	Description	Posted		Remarks
			Date	File	
CICs	01 GC-006 LKES	Revision to door hardware set.	5/21/24	PDF	The following doors hardware set shall be revised ...
	01 GC-001-CRMS	DOOR FRAME TYPES	10/19/23	PDF	The "Door Frame Type" for all doors listed in the ...
	01 GC-001-EDES	Existing Door at Faculty Room 240	12/11/23	PDF	The existing door for Faculty Room 240 to be repla...
	01 GC-001-FES	Lead Testing Report - Fleetwood ES	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-001-GES	DOOR FRAME TYPES	12/11/23	PDF	The "Door Frame Type" for all doors listed in the ...
	01 GC-001-HES	Lead Testing Report - Hempstead ES	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-001-LKES	LKES - Doors at Stairs S101, S102, S201, and S202	12/19/23	PDF	Changes to the scope of work for doors at Stair Ro...
	01 GC-001-PMS	Lead Testing Report - Pomona MS	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-001-SPES	Lead Testing Report - Summit Park ES	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-002-CRMS	Lead Testing Report - Chestnut Ridge MS	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-002-CRMS REVISED	REVISED- Lead Testing Report CRMS	2/13/24	PDF	REVISED- Lead Testing Report for Chestnut Ridge Mi...
	01 GC-002-EDES	EDES - Doors at Stairs S101, S102, S201, and S202	12/19/23	PDF	Changes to the scope of work for doors at Stair Ro...
	01 GC-002-FES	FES - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-002-GES	Lead Testing Report - Grandview ES	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-002-HES	HES - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-002-LKES	Lead Testing Report - Lime Kiln ES	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-002-PMS	PMS - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-002-SPES	SPES - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-003-CRMS	Lead Safe Work Practices - CIC 01 GC-003-CRMS	1/2/24	PDF	Specification Section 028300 – Lead Safe Work Prac...
	01 GC-003-EDES	Lead Testing Report - Eldorado ES	12/11/23	PDF	The attached are lead testing results completed fo...
	01 GC-003-FES	FES revisions to Doors T003 and T004	5/1/24	PDF	Revisions to Doors T003 and T004 locksets.
	01 GC-003-GES	GES - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-003-LKES	LKES - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-003-PMS	01 GC-003-PMS- Additional Doors	4/10/24	PDF	Additional Doors because of reduction of ADA Phase...
	01 GC-004 PMS	Revision to door hardware set.	5/21/24	PDF	The following doors hardware set shall be revised ...
	01 GC-004-CRMS	CRMS - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-004-EDES	Lead Safe Work Practices - CIC 01 GC-004-EDES	1/3/24	PDF	Specification Section 028300 – Lead Safe Work Prac...
	01 GC-004-EDES REVISED	01 GC-004-EDES REVISED	2/13/24	PDF	REVISED Lead Safe Practices - Eldorado ES Lead-Ba...
	01 GC-004-FES	Additional Doors because of reduction of ADA Phase scope of ...	6/11/24	PDF	The following doors and associated hardware shall ...
	01 GC-004-GES	GES revisions to Doors T001 and T002	5/1/24	PDF	Revisions to Doors T001 and T002 locksets.
	01 GC-004-LKES	LKES - Doors at Stairs S101, S102, S201, and S202 (Updated f...	1/23/24	PDF	Updated changes to the scope of work for doors at ...
	01 GC-005-CRMS	CRMS - Additional Doors, Hardware Set Rvisions	5/31/24	PDF	Additional doors because of reduction of ADA Phase...
	01 GC-005-EDES	EDES - Paint Color for Door Frames	1/19/24	PDF	All door frames shall be painted with Sherwin Will...
	01 GC-005-GES	Additional Doors because of reduction of ADA Phase scope of ...	6/11/24	PDF	Additional Doors because of reduction of ADA Phase...
	01 GC-005-LKES	01 GC-005-LKES - Additional Doors	4/23/24	PDF	Additional Doors because of reduction of ADA Phase...
	01 GC-006-EDES	EDES - Doors at Stairs S101, S102, S201, and S202 (Updated f...	1/23/24	PDF	Updated changes to the scope of work for doors at ...
	01 GC-007-EDES	Security Door Cores	5/22/24	PDF	Eldorado Door C101A shall have a unique core from ...
	01 GC-007-LKES	Security Door Cores	5/22/24	PDF	Lime Kiln Door CL101 shall have a unique core from...
	01 GC-008-EDES	EDES - Additional Doors	5/31/24	PDF	Additional doors because of a reduction of ADA Pha...
C1-GC-01					

## Phase 3C – RFI Log – To Date

**ORACLE** Primavera Submittal Exchange

Project: East Ramapo CSD ARPA Phase 3C Project Number: 209-2107.02 & 209-2107.03

**JACOBS** RFI

View: [My Activity](#) | [All Activity](#) | [Download Multiple Files](#)

Sort By: [Category](#) | [Numeric](#)  
Category: 01- GC | 02 - MC | 03 - PC | 04 - EC

Category	RFI #	Description	From Subcontractor		From Contractor		From Construction Manager		Review by Consultant				Review by Architect		Returned to Contractor		Returned to Sub		Remarks
			Date	Type	Date	Type	Date	Type	Sent to Arch.	Sent to Consultant to Arch.	Returned	File	Returned to Construction Manager	File	Date	Type	Date	Type	
01- GC	001	Door Color Finishes	3/25/24		3/25/24		3/25/24		3/25/24	3/25/24			5/6/24		5/7/24		5/7/24		Contractor: Please confirm the finish colors for L...
	004	Paint Finishes	4/8/24		4/8/24		4/8/24		4/8/24	4/8/24			4/16/24		4/16/24		4/16/24		Arch.: See attached for response. Contractor: Plea...
	005	Fleetwood Room 120 - Wall Alignment Leng...	4/10/24		4/10/24		4/10/24		4/10/24	4/10/24			4/16/24		4/16/24		4/16/24		Arch.: See attached for response.
	006	Eldorado 108 Ceiling Height	4/23/24		4/23/24		4/23/24		4/23/24	4/23/24			4/23/24		4/24/24		4/24/24		Arch.: see attached for response.
	007	08 Ceiling - Eldorado	4/23/24		4/23/24		4/23/24		4/23/24	4/23/24			4/23/24		4/24/24		4/24/24		Arch.: See attached.
	008	Eldorado Room 108 - ADA Compliance & Plu...	4/25/24		4/26/24		4/26/24		4/26/24	4/26/24			5/6/24		5/6/24		5/6/24		Arch.: See attached for response.
	009	Fleetwood Room 120 - ADA Compliance, Mas...	4/25/24		4/26/24		4/26/24		4/26/24	4/26/24			5/7/24		5/7/24		5/7/24		Arch.: See attached for response.
	010	Summit Park Room 120 - ADA Compliance, M...	4/25/24		4/26/24		4/26/24		4/26/24	4/26/24			5/9/24		5/9/24		5/9/24		
	013	RFI #9 - Paint Codes to Match Existing	5/7/24		5/7/24		5/7/24		5/7/24	5/7/24			5/9/24		5/9/24		5/9/24		
	015	eldorado rm 108 -ADA compliance	5/14/24		5/14/24		5/14/24		5/14/24	5/14/24			5/15/24		5/17/24		5/17/24		Arch.: See attached.
	016	2nd Floor Pomona C201 Fountain Wall	5/17/24		5/17/24		5/20/24		5/20/24	5/20/24			5/20/24		5/20/24		5/20/24		Arch.: See attached.
	017	2nd Floor Pomona C201 Fountain Wall Thic...	5/17/24		5/17/24		5/20/24		5/20/24	5/20/24			5/20/24		5/20/24		5/20/24		Arch.: See attached.
	018	Summit Park 120 8A Framing	5/23/24		5/24/24		5/24/24		5/24/24	5/24/24			5/28/24		5/28/24		5/28/24		Arch.: See attached.
	019	Chestnut - C203 Masonry Wall	5/28/24		5/29/24		5/29/24		5/29/24	5/29/24			5/29/24		5/29/24		5/29/24		Arch.: See attached for response.
	020	Summer Locations - Epoxy	6/4/24		6/4/24		6/4/24		6/4/24	6/4/24			6/19/24		6/19/24		6/19/24		Arch.: See attached for response.
	021	Tile Wall Sheetrock	6/4/24		6/4/24		6/4/24		6/4/24	6/4/24			7/1/24		7/1/24		7/1/24		Arch.: See attached for response.
	021R1	Tile Wall Sheetrock - R1	6/4/24		6/4/24		6/4/24		6/4/24	6/4/24			7/1/24		7/1/24		7/1/24		Arch.: See attached for response.
	024	RFI #17 - Fleetwood 127 - CMU wall Demo	7/5/24		7/5/24		7/8/24		7/8/24	7/8/24			7/8/24		7/9/24		7/9/24		Arch.: See attached for response.
	026	Chestnut Corridor Ceilings	7/11/24		7/12/24		7/12/24		7/12/24	7/12/24			7/18/24		7/18/24		7/18/24		Arch.: See attached.
	027	Chestnut Gang Bathrooms -ADA	7/11/24		7/12/24		7/12/24		7/12/24	7/12/24			7/12/24		7/12/24		7/12/24		Arch.: See attached revised response.
	028	Hempstead Room 303 & Nurse's Room	7/12/24		7/14/24		7/15/24		7/15/24	7/15/24			7/22/24		7/22/24		7/22/24		Arch.: See attached for response.
	030	Hempstead Room 303 Additional Demo and ...	7/25/24		7/25/24		7/25/24		7/25/24	7/25/24			7/31/24		7/31/24		7/31/24		Arch.: See attached response.
	031	Chestnut Nurse's Door #109A Wall	8/14/24		8/14/24		8/14/24		8/14/24	8/14/24			8/14/24		8/14/24		8/14/24		
02 - MC	012	RFI-004-MC - Removed existent grills					5/3/24		5/3/24	5/3/24	5/6/24		5/6/24		5/7/24		5/7/24		Arch.: See Consultant Review
	029	Hempstead - Return Air	7/15/24		7/15/24		7/17/24		7/17/24	7/17/24			7/19/24		7/19/24		7/19/24		Arch.: See attached for response.
03 - PC	002	Clarification for model LAV-D	3/22/24		3/22/24		3/22/24		3/22/24	3/22/24	3/22/24		3/28/24		4/1/24		4/1/24		Arch.: See Consultant Review
	003	Water Cooler			3/25/24		3/25/24		3/25/24	3/25/24			3/28/24		4/1/24		4/1/24		Arch.: See attached response from consultant.
	011	Plumbing Rough-Ins			4/26/24		4/26/24		4/26/24	4/26/24			5/6/24		5/6/24		5/6/24		Arch.: The associated CIC's will be uploaded later...
	024	Electric Water Cooler					5/8/24		5/8/24	5/8/24			5/15/24		5/15/24		5/15/24		Arch.: See attached revised response.
	025	Grandview room 127B					7/3/24		7/3/24	7/3/24			7/11/24		7/11/24		7/11/24		Arch.: See attached for response.
	023	Summit Park Toilet 097A					7/3/24		7/3/24	7/3/24			7/11/24		7/11/24		7/11/24		Arch.: See attached for response.
04 - EC	025	Chestnut Ridge Plumbing Rough-Ins	7/11/24		7/11/24		7/11/24		7/11/24	7/11/24			7/12/24		7/12/24		7/12/24		Arch.: See attached for response.

## Phase 3C – Cost Proposal Log – To Date

**ORACLE** Primavera Submittal Exchange

Project: East Ramapo CSD ARPA Phase 3C Project Number: 209-2107.02 & 209-2107.03

**JACOBS** Cost Proposals

View: [My Activity](#) | [Download Multiple Files](#) | [Edit Expected Items](#)

Sort By: [Category](#) | [Numeric](#)  
Category: 01- GC | 02 - MC | 03 - PC | 04 - EC

Category	Cost Proposals #	Description	From Contractor		From Construction Manager		Review by Consultant			Review by Architect		Returned to Contr		Amount	Status	Action	Remarks	
			Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned to Arch.	File	Returned to Construction Manager	File	Date					Type
01- GC	001	↑ Epoxy Flooring - April Break Work Only	4/22/24		5/30/24		5/29/24	5/29/24			7/2/24		7/2/24	(\$2,440.00)	Approved		Arch.: See attached. Construction Manager: This is...	
	002	↑ T&M Ticket - Fleetwood	5/23/24		6/14/24		5/29/24	5/29/24			6/18/24		6/18/24	\$390.00	Approved		Arch.: Approved per Jacobs comments, apply toward...	
	002R1	EC-PH3C-CO-GC-002 T&M-Fleetwood	6/14/24		6/14/24		6/14/24	6/14/24			7/29/24		7/29/24	\$390.00	Approved		Arch.: Approved for \$390.00, bill towards allowanc...	
	003	↑ T&M Ticket - Hempstead	5/23/24		6/14/24		5/29/24	5/29/24			7/29/24		7/29/24		Rejected		Arch.: This is the same Cost Proposal as Cost Prop...	
	003R1	EC-PH3C-CO-GC-003 T&M-Hempstead	6/14/24		6/14/24		6/14/24	6/14/24			7/23/24		7/23/24	\$390.00	Approved		Arch.: Bill towards allowance, remove O&P Constru...	
	004	PMS Bathroom T221 and T211 RCP CIC	6/3/24		6/5/24		6/3/24	6/3/24			6/24/24		6/24/24	\$3,030.00	Approved		Arch.: See attached for details. Construction Mana...	
	005	PMS C203 Fountain Wall type change	6/3/24		6/5/24		6/3/24	6/3/24			6/13/24		6/14/24	\$2,238.00	Approved		Arch.: Review per comments. Construction Manager...	
	005R1	EC-PH3C-CO-GC-005-CIC 02-002 PMS-Ph3C-GC...	6/18/24		6/18/24		6/18/24	6/18/24			7/2/24		7/2/24	\$1,313.00	Approved		Arch.: See attached for comments. Construction Man...	
	006	EDES Toilet 108 and 109 Revisions	6/3/24		6/3/24		6/3/24	6/3/24			6/13/24		6/14/24	\$14,025.00	Approved		Arch.: Review per comments. Construction Manager...	
	006R1	EC-PH3C-CO-GC-006-CIC02-001R EDES-Ph3C R...	6/17/24		6/17/24		6/17/24	6/17/24			6/18/24		6/18/24	\$9,790.00	Approved		Arch.: See attached. Construction Manager: Approve...	
	007	FES Toilet Rm120 and 127 changes	6/3/24		6/3/24		6/3/24	6/3/24			6/13/24		6/14/24	\$6,435.00	Approved		Arch.: Review per comments. Construction Manager...	
	007R1	EC-PH3C-CO-GC-007-CIC 02-002R-FES-PH3C-G...	6/17/24		6/17/24		6/17/24	6/17/24			6/18/24		6/18/24	\$4,362.00	Approved		Arch.: See attached. Construction Manager: Approve...	
	008	SPES Toilet room 120 and 097A change	6/3/24		6/14/24		6/3/24	6/3/24			7/3/24		7/3/24	\$2,560.20	Approved		Arch.: Approved in the amount of \$2,560.20 See at...	
	009	EC-PH3C-CO-GC-009-CIC 02-003 PMS-Ph3C-GC...	6/23/24		6/23/24		6/23/24	6/23/24			7/2/24		7/3/24	\$30,998.00	Approved		Arch.: Bill towards allowance. Approved in the am...	
	011	EC-PH3C-CO-GC-010-CIC 02-001 LKES-Ph3C-G...	6/23/24		6/23/24		6/23/24	6/23/24			7/3/24		7/3/24	\$2,394.00	Approved		Arch.: Approved in the amount of \$2,394.00 See at...	
	012	EC-PH3C-CO-GC-011-CIC 02-001HES-Ph3C-GC...	6/23/24		6/23/24		6/23/24	6/23/24			7/3/24		7/3/24	\$13,462.00	Approved		Arch.: Approved in the amount of \$13,462.00. See ...	
	013	EC-PH3C-CO-GC-012-CIC 02-001 CRMS-Ph3C-G...	6/23/24		6/23/24		6/23/24	6/23/24			7/5/24		7/5/24	(\$7,828.00)	Approved		Arch.: Approved in the credit amount of (\$7,828.00...	
	014	EC-PH3C-CO-GC-013-CIC 03-001-GE5-Ph3C - ...	6/28/24		6/28/24		6/28/24	6/28/24			7/5/24		7/5/24	\$3,604.00	Approved		Arch.: Approved for \$3,604.00 (\$21,311.00 - \$17,70...	
	015	Remu - Water Fountain C201 - Pomona CIC...	7/5/24		7/5/24		7/5/24	7/5/24			7/23/24		7/23/24	\$1,037.00	Approved		Arch.: Approved for credit amount of (\$4,637.00), ...	
	016	EC-PH3C-CO-GC-014-CIC02_002SPES-Ph3C-GC...	7/9/24		7/9/24		7/9/24	7/9/24			8/2/24		8/5/24	\$2,160.00	Approved		Arch.: Approved for \$2,160.00, bill towards allowa...	
	017	EC-PH3C-CO-GC-015-CIC 02-003-FES-Ph3C-GC...	7/9/24		7/9/24		7/9/24	7/9/24			8/2/24		8/5/24		Approved		Arch.: Approved for a credit of (\$10,673.00) see L...	
	018	EC-PH3C-CO-GC-016-CIC02-002 EDES-Ph3C_nu...	7/14/24		7/14/24		7/14/24	7/14/24			7/29/24		7/30/24	\$5,503.00	Approved		Arch.: Approved for \$5,503.00, bill towards allowa...	
	019	EC-PH3C-CO-GC-017-FD 04_Add Abate-Pomona	7/15/24		7/15/24		7/15/24	7/15/24			8/13/24		8/13/24	\$3,600.00	Approved		Arch.: Approved for allowance disbursement for \$3...	
020	EC-PH3C-CO-GC-018-FD 04_Add Abate-Summit	7/15/24		7/15/24		7/15/24	7/15/24			9/10/24		9/10/24	\$3,600.00	Approved		Arch.: Approved to be \$3,600.00 applied towards al...		
021	EC-PH3C-CO-GC-019-FD-04_Add Abate-Hempst...	7/18/24		7/18/24		7/18/24	7/18/24			9/10/24		9/10/24	\$8,400.00	Approved		Arch.: Bill towards allowance, approved in the am...		
022	EC-PH3C-CO-GC-020-CIC 02-002 LKES-Ph3C-G...	7/21/24		7/21/24		7/21/24	7/21/24			8/5/24		8/5/24	\$568.00	Approved		Arch.: See attached. Construction Manager: Approv...		
023	EC-PH3C-CO-GC-021-CIC 02-004-FES-Ph3C-GC...	7/21/24		7/21/24		7/21/24	7/21/24			7/21/24		7/21/24	\$2,538.00	Approved		Arch.: Bill towards allowance, approved in the am...		
025	EC-PH3C-CO-GC-022-CIC 02-002HES-Ph3C-GC...	7/29/24		7/29/24		7/29/24	7/29/24			9/10/24		9/10/24	\$6,723.00	Approved		Arch.: Bill towards allowance, approved in the am...		
026	EC-PH3C-CO-GC-023-FD-04_Add Abate-Hemp 3...	8/6/24		8/6/24		8/6/24	8/6/24									Construction Manager: Jacobs Reviewed - Bill towar...		
027	EC-PH3C-CO-GC-025-HES Lintel CR206	9/23/24		9/23/24		9/23/24	9/23/24											
028	EC-PH3C-CO-GC-026-HES Lintel OF Corridor	9/23/24		9/23/24		9/23/24	9/23/24											
02- MC																		
03- PC																		
04- EC	009	EC-PH3C-CO-EC-001-CIC 05-001EDES-Ph3C	6/6/24		6/9/24		6/9/24	6/6/24			7/10/24		7/10/24	\$1,584.00			Arch.: Provide additional information and breakdow...	
	024	EC-PH3C-CO-EC-002-CIC 05-001 LKES-EC_in...	7/24/24		7/24/24		7/24/24	7/24/24			8/13/24		8/15/24	\$432.51	Approved		Arch.: Approved for \$432.51 to be applied to the a...	



## Phase 3C – CIC Log – To Date

**ORACLE** Primavera Submittal Exchange

Project: East Ramapo CSD ARPA Phase 3C Project Number: 209-2107.02 & 209-2107.03

**JACOBS** CIC's

View: **My Activity** | [All Activity](#) | [Download Multiple Files](#)

Sort By: **Category** | [Numeric](#)  
Category: 01- GC | 02 - MC | 03 - PC | 04 - EC

Category	CIC's #	Description	Posted		Remarks
			Date	File	
01- GC	02-001-CRMS-PH3C-GC	Revisions to Ceilings and Finishes	6/12/24		Ceiling and finishes for Rooms 109A, T131, and T13...
	02-001-GES-PH3C	Revisions to Toilet Room T005	6/19/24		Per direction from the district the Toilet Room in...
	02-001EDES-PH3C-GC	SUPERCEDED - Revisions to Classroom 108, Toilet Room 108B, H...	5/6/24		VOIDED - SUPERCEDED REFER TO REVISED CIC 02-001R E...
	02-001FES-PH3C-GC	02-001FES-PH3C-GC	4/16/24		Clarifications to Room 120 dimensions in response ...
	02-001HES-PH3C-GC	Revisions to Finishes	6/12/24		Finishes have been updated per the request of the ...
	02-001LKES-PH3C-GC	Revisions to Ceilings and Finishes	6/12/24		Ceilings and finishes have been updated per the re...
	02-001PMS-PH3C-GC	Revisions to RCP for Rooms T211 and T221	5/17/24		Revision to the ceiling material in Girls Toilet R...
	02-001R EDES-PH3C-GC	Revisions to Classroom 108, Toilet Room 108B, Health Room 10...	5/9/24		Revisions to Toilet Room 108B and Toilet Room 109T...
	02-001R SPES-PH3C-GC	REVISED REVISIONS TO TOILET ROOM 120A	5/9/24		Revisions to Toilet Room 120A. Revisions to finish...
	02-001SPES-PH3C-GC	SUPERCEDED - Revisions to Toilet Room 120A.	5/6/24		VOIDED -SUPERCEDED REFER TO REVISED CIC 02-001R SP...
	02-002 GES-PH3C - GC	Wall Finishes/ Door Frame Paint Color	8/1/24		All Door Frames in project scope shall be painted ...
	02-002 LKES-PH3C-GC	Revisions to dimensions at Nurse Room 110	7/19/24		Revisions to dimensions at Nurse Room 110, see att...
	02-002 PMS-PH3C-GC	Revisions to 2nd floor Drinking Fountain in Corridor C201.	5/17/24		REVISED COVER SHEET TO CIC. Revisions to 2nd floor...
	02-002 SPES-PH3C-GC	Finish Revisions	7/2/24		Based on discussions with the district and existin...
	02-002-CRMS-PH3C-GC	Updates to doors layout at Corridors C101 and C103	7/11/24		Based on newfound existing conditions, the layouts...
	02-002EDES- PH3C-GC	Revisions to Health Room 109	7/11/24		Revisions to Health Room 109 due to the unforeseen...
	02-002HES-PH3C-GC	Revisions to layout of Nurse's Toilet Room 014C	7/24/24		Based on unforeseen existing conditions the plan l...
	02-002R2-FES-PH3C-GC	Revisions to Room 120	5/7/24		REVISIONS TO TOILET ROOM 120A LAYOUT. Based on e...
	02-003 LKES-PH3C-GC	Wall Finishes/ Door Frame Paint Color / Soffit Paint Color	8/1/24		All Door Frames in project scope shall be painted ...
	02-003 SPES-PH3C-GC	Wall Finishes/ Door Frame Paint Color	8/1/24		All Door Frames in project scope shall be painted ...
	02-003-CRMS-PH3C-GC	Wall Finishes/ Door Frame Paint Color / Soffit Paint Color	8/1/24		All Door Frames in project scope shall be painted ...
	02-003EDES- PH3C-GC	Wall Finishes/ Door Frame Paint Color / Soffit Paint Color	8/1/24		All Door Frames in project scope shall be painted ...
	02-003FES-PH3C-GC	Revision to Finishes	7/3/24		Based on existing conditions and discussions with ...
	02-003HES-PH3C-GC	Wall Finishes/ Door Frame Paint Color	8/1/24		All Door Frames in project scope shall be painted ...
	02-003R PMS-PH3C-GC	REVISED Revision to Finishes	7/24/24		REVISED CIC ISSUED FOR DIMENSIONS OF URINAL PARTIT...
	02-004-CRMS-PH3C-GC	Section at Corridor CMU Wall Section at Toilet Room T131 and...	8/22/24		See the following pages for information at the wal...
	02-004HES-PH3C-GC	Revisions to Nurse's Office Sink	8/8/24		Based on existing conditions, the layout for the n...
	02-004-PMS-PH3C-GC	Girls Toilet T203 Design Layout	7/23/24		Based on newfound conditions caused by the contrac...
	02-004R-FES-PH3C-GC	REVISED BASED ON FIELD CONDITIONS Revised dimensions for Nur...	7/23/24		REVISED based on existing conditions Nurse Room 12...
	02-005FES-PH3C-GC	Wall Finishes/ Door Frame Paint Color	8/1/24		All Door Frames in project scope shall be painted ...
	02-005-PMS-PH3C-GC	Wall Finishes	8/1/24		All Door Frames in project scope shall be painted ...
	03-002PMS-PH3C-MC	Girls Toilet T203 Mechanical Design	7/23/24		Based on newfound conditions caused by the contrac...
	04-001PMS-PH3C-PC	Girls Toilet T203 Plumbing Design	7/23/24		Based on newfound conditions caused by the contrac...
	05-001HES-PH3C-EC	Electrical revisions to Nurse Toilet Room	7/24/24		Electrical revisions to the Nurse's Toilet Room 01...
	05-002 PMS-PH3C-EC	Girls Toilet T203 Electrical Design	7/23/24		Based on newfound conditions caused by the contrac...
	05-002EDES- PH3C-EC	Electrical revisions to Health Room 109	7/18/24		Provide power to the door operator for door 109 in...
02 - MC	02-002 LKES-PH3C-GC	Revisions to dimensions at Nurse Room 110	7/19/24		Revisions to dimensions at Nurse Room 110, see att...
	02-002HES-PH3C-GC	Revisions to layout of Nurse's Toilet Room 014C	7/24/24		Based on unforeseen existing conditions the plan l...
	02-004-PMS-PH3C-GC	Girls Toilet T203 Design Layout	7/23/24		Based on newfound conditions caused by the contrac...
	02-004R-FES-PH3C-GC	REVISED BASED ON FIELD CONDITIONS Revised dimensions for Nur...	7/23/24		REVISED based on existing conditions Nurse Room 12...
	03-001 PMS-PH3C-MC	Mechanical Revisions at Acoustical Ceiling Tile	6/12/24		Per the district request the ceiling material has ...
	03-001-CRMS-PH3C-MC	Mechanical Ceiling Revisions	6/12/24		Per the district request the ceiling material has ...
	03-001FES-PH3C-MC	Revisions to Toilet Room 120A	6/13/24		Mechanical revisions to Toilet Room 120A. FOR R...
	03-001-GES-PH3C	Revisions to Toilet Room T005	6/19/24		Per direction from the district the Toilet Room in...
	03-001EDES- PH3C-MC	Mechanical revisions to Toilet Room 108B and Bathroom 109T.	5/10/24		Mechanical revisions to Toilet Room 108B and Bathr...
	03-001HES-PH3C-MC	Mechanical revisions to Nurse Toilet Room	7/24/24		Mechanical revisions to the Nurse's Toilet Room 01...
	03-002PMS-PH3C-MC	Girls Toilet T203 Mechanical Design	7/23/24		Based on newfound conditions caused by the contrac...
03 - PC	04-001PMS-PH3C-PC	Girls Toilet T203 Plumbing Design	7/23/24		Based on newfound conditions caused by the contrac...
	05-002 PMS-PH3C-EC	Girls Toilet T203 Electrical Design	7/23/24		Based on newfound conditions caused by the contrac...
	02-002 LKES-PH3C-GC	Revisions to dimensions at Nurse Room 110	7/19/24		Revisions to dimensions at Nurse Room 110, see att...
	02-002HES-PH3C-GC	Revisions to layout of Nurse's Toilet Room 014C	7/24/24		Based on unforeseen existing conditions the plan l...
	02-004-PMS-PH3C-GC	Girls Toilet T203 Design Layout	7/23/24		Based on newfound conditions caused by the contrac...
	02-004R-FES-PH3C-GC	REVISED BASED ON FIELD CONDITIONS Revised dimensions for Nur...	7/23/24		REVISED based on existing conditions Nurse Room 12...
	03-002PMS-PH3C-MC	Girls Toilet T203 Mechanical Design	7/23/24		Based on newfound conditions caused by the contrac...
	03PC-001-CRMS	03 PC-001-CRMS	4/1/24		CRMS - Clarification to Electric Water Cooler moun...
	04-001 FES-Ph 3C PC	Revisions to Toilet Room 120A.	6/5/24		Based on existing conditions and discussions with ...
	04-001 LKES-PH3C-PC	Revisions to piping in Toilet Room 109B	8/1/24		Due to existing conditions piping in Toilet Room 1...
	04-001-GES-PH3C	Revisions to Toilet Room T005	6/19/24		Per direction from the district the Toilet Room in...
04 - EC	04-001EDES-PH3C-PC	Revisions to Toilet Room 108B, and Bathroom 109T.	5/10/24		Revisions to Toilet Room 108B, and Bathroom 109T.
	04-001HES-PH3C-PC	Plumbing Revisions to layout of Nurse's Toilet Room 014C	7/31/24		Based on unforeseen existing conditions the plan l...
	04-001PMS-PH3C-PC	Girls Toilet T203 Plumbing Design	7/23/24		Based on newfound conditions caused by the contrac...
	04-002PMS-PH3C-PC	Remove Hose Bibb From Nurse's Toilet Room G103E	7/23/24		REVISIONS TO DRAWING 3 ON SHEET PMS P602-C Hose B...
	05-002 PMS-PH3C-EC	Girls Toilet T203 Electrical Design	7/23/24		Based on newfound conditions caused by the contrac...
	02-002 LKES-PH3C-GC	Revisions to dimensions at Nurse Room 110	7/19/24		Revisions to dimensions at Nurse Room 110, see att...
	02-002HES-PH3C-GC	Revisions to layout of Nurse's Toilet Room 014C	7/24/24		Based on unforeseen existing conditions the plan l...
	02-004-PMS-PH3C-GC	Girls Toilet T203 Design Layout	7/23/24		Based on newfound conditions caused by the contrac...
	02-004R-FES-PH3C-GC	REVISED BASED ON FIELD CONDITIONS Revised dimensions for Nur...	7/23/24		REVISED based on existing conditions Nurse Room 12...
	03-002PMS-PH3C-MC	Girls Toilet T203 Mechanical Design	7/23/24		Based on newfound conditions caused by the contrac...
	04-001PMS-PH3C-PC	Girls Toilet T203 Plumbing Design	7/23/24		Based on newfound conditions caused by the contrac...



Phase 3D – RFI Log – To Date

ORACLE Primavera Submittal Exchange

Project: East Ramapo CSD ARPA Phase 3D #209-2107.02 & 209-2107.03 Project Number: 209-2107

JACOBS RFI

View: My Activity | All Activity | Download Multiple Files

Sort By: Category | Numeric

Category: 01- GC

Category	RFI #	Description	From Subcontractor		From Contractor		From Construction Manager		Review by Consultant				Review by Architect		Returned to Contractor	Returned to Sub	Remarks
			Date	Type	Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned to Arch.	File	Returned to Construction Manager	File	Date	Date	
01- GC	001	HES Second Floor Head Condition			3/4/24	PDF	3/11/24	PDF	3/11/24				3/11/24	PDF	3/12/24	3/12/24	Arch.: See attached response. Construction Manager...

Phase 3D – Cost Proposal Log – To Date

ORACLE Primavera Submittal Exchange

Project: East Ramapo CSD ARPA Phase 3D #209-2107.02 & 209-2107.03 Project Number: 209-2107

JACOBS Cost Proposals

View: My Activity | Download Multiple Files | Edit Expected Items

Sort By: Category | Numeric

Category: 01- GC

Category	Cost Proposals #	Description	From Contractor		From Construction Manager		Review by Consultant				Review by Architect		Returned to Contr		Amount	Status	Action	Remarks
			Date	Type	Date	Type	Sent to Arch.	Sent to Consultant	Returned to Arch.	File	Returned to Construction Manager	File	Date	Type				
01- GC	001	Chestnut Ridge Abatement Credit	7/29/24	PDF	7/30/24	PDF	7/30/24				9/12/24	PDF	9/12/24			Approved	9/8/2024	Arch.: See attached. Construction Manager: CM revi...
	002	Lime Kiln Abatement Credit	7/29/24	PDF	7/30/24	PDF	7/30/24				9/12/24	PDF	9/12/24			Approved	9/8/2024	Arch.: See attached. Construction Manager: CM rev...
	003	Hempstead Abatement Credit	7/29/24	PDF	7/30/24	PDF	7/30/24				9/12/24	PDF	9/12/24			Approved	9/6/2024	Arch.: See attached. Construction Manager: CM rev...
	004	El Dorado Abatement Credit	7/29/24	PDF	7/30/24	PDF	7/30/24				9/12/24	PDF	9/12/24			Approved	9/6/2024	Arch.: See attached. Construction Manager: CM rev...
	005	Fleetwood Roofing Proposal	8/20/24	PDF	9/10/24	PDF	9/10/24				9/13/24	PDF	9/13/24		\$9,950.00	Approved		Arch.: Approved as an allowance disbursement in th...
	006	Grandview Roof Proposal	8/20/24	PDF	9/10/24	PDF	9/10/24				9/13/24	PDF	9/13/24		\$9,950.00	Approved		Arch.: Approved as an allowance disbursement in th...

## Progress Photos



Chestnut Ridge Middle School – ADA & Water Fountain







**Eldorado Elementary School – Smoke Doors**



**Eldorado Elementary  
School – Water  
Fountain**



**Elmwood Elementary School – Flooring & MEP Upgrades**

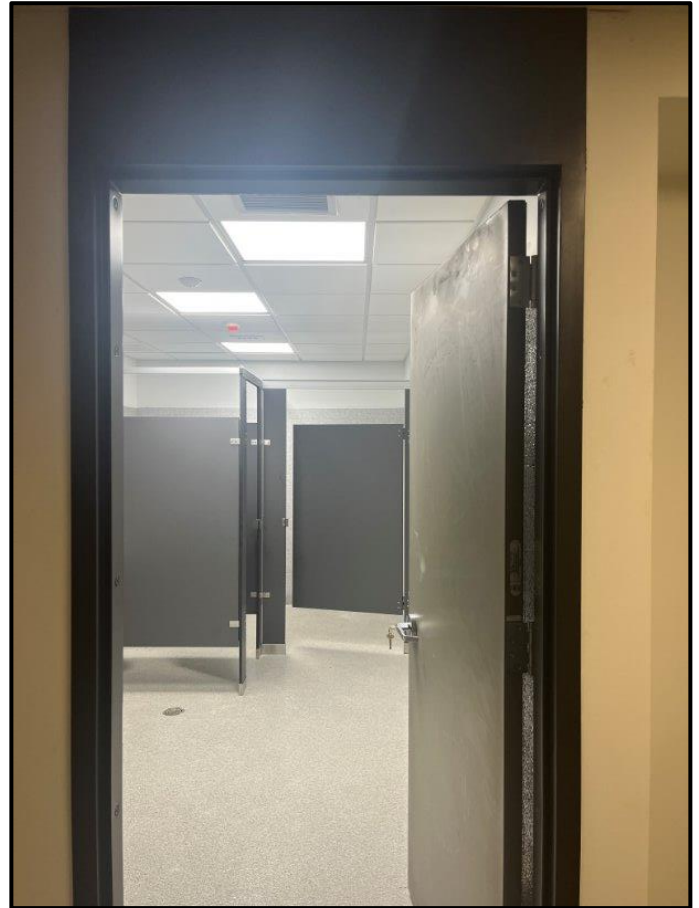

**Elmwood Elementary School – ADA**





Fleetwood Elementary School - ADA




Grandview Elementary School - Windows



Grandview Elementary School – ADA & Water Fountain





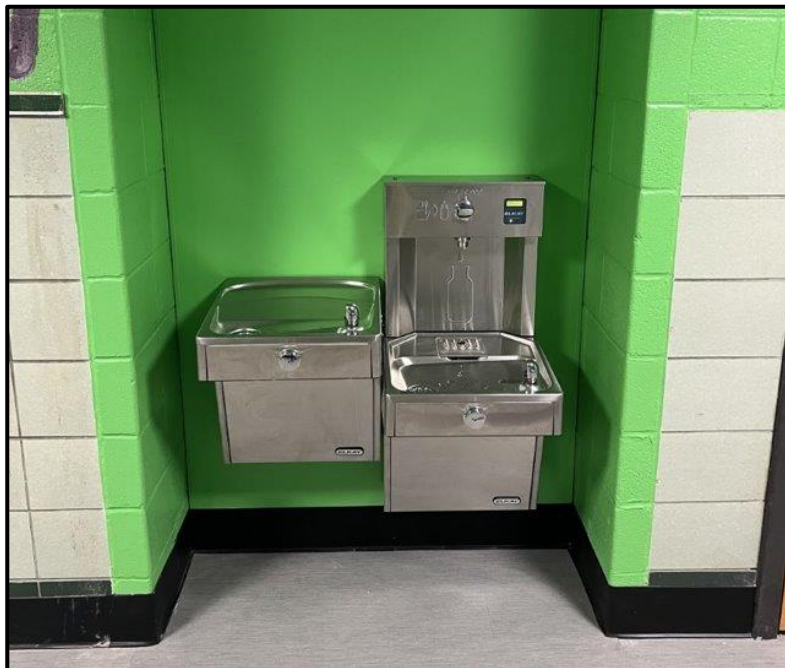


Hempstead Elementary School – Gymnasium Flooring & Water Fountain





Kakiat Elementary School – MEP Upgrades

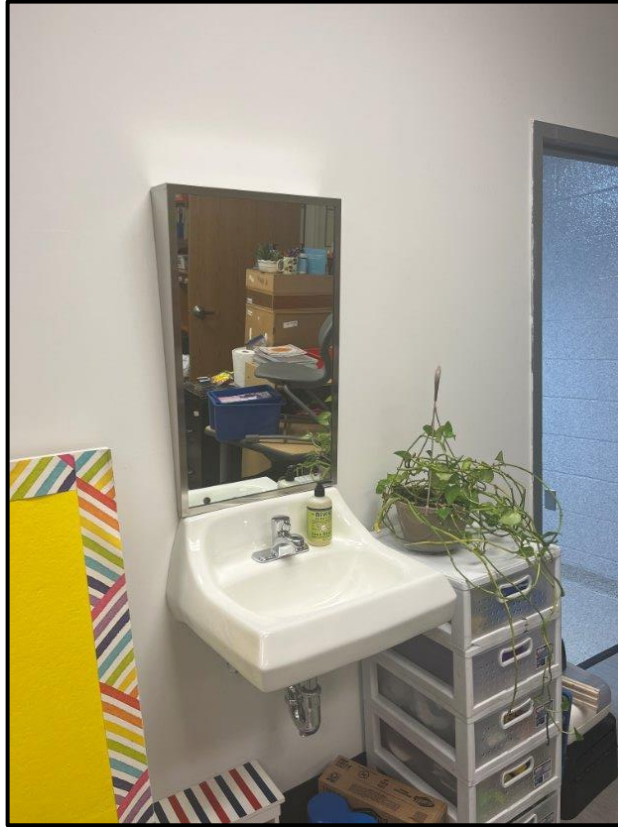


Kakiat Elementary School – ADA





Lime Kiln Elementary School – Doors & Windows



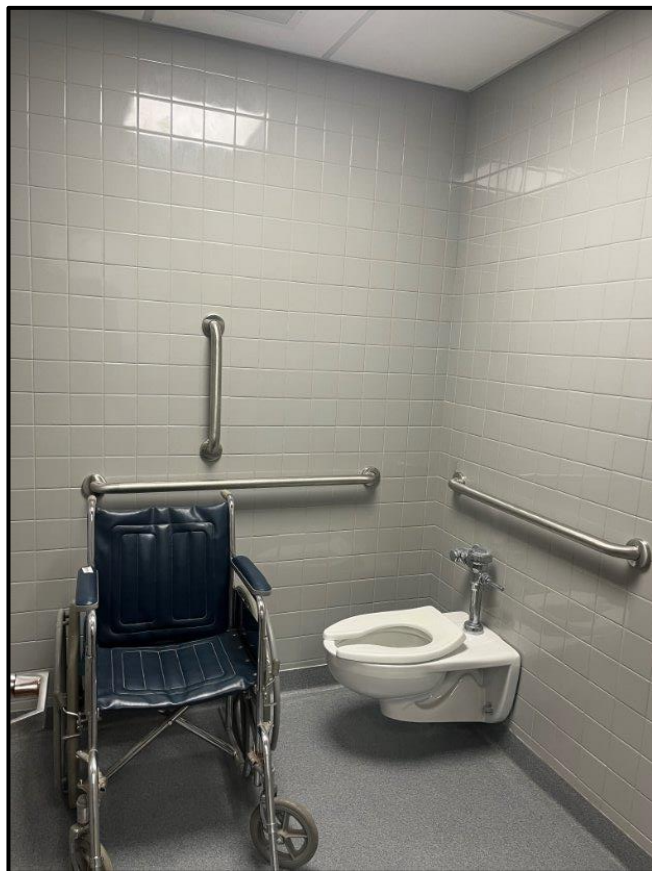

**Lime Kiln Elementary School – Water Fountain & ADA**




Margetts Elementary School – MEP Upgrades



Margetts Elementary School – Water Fountain





# Jacobs

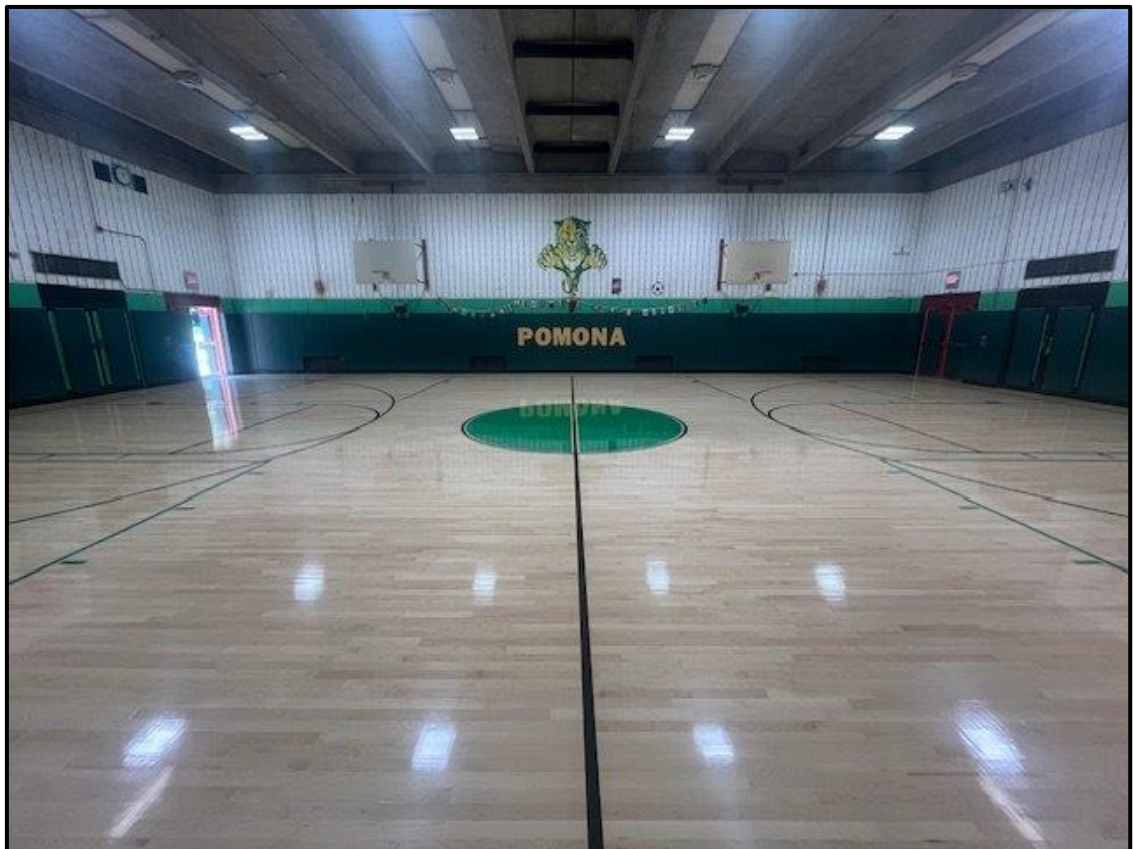

Pomona Middle School – Gymnasium Flooring



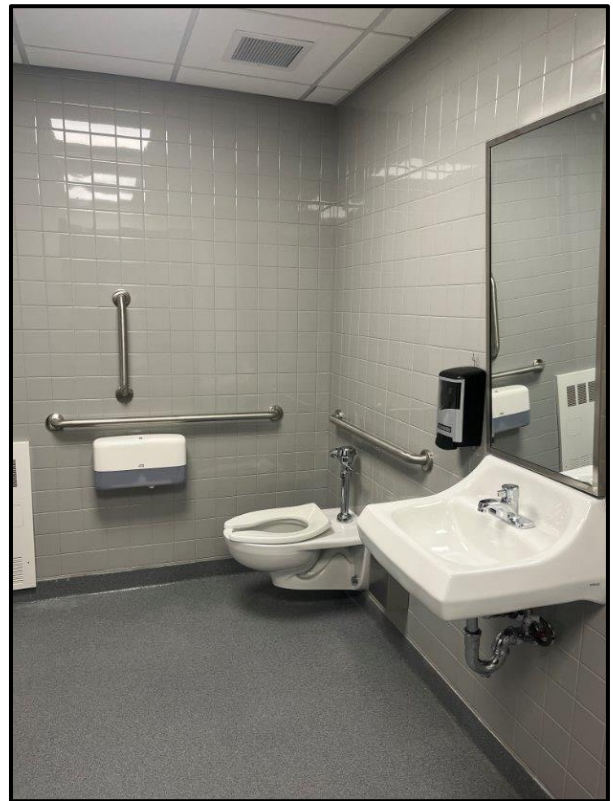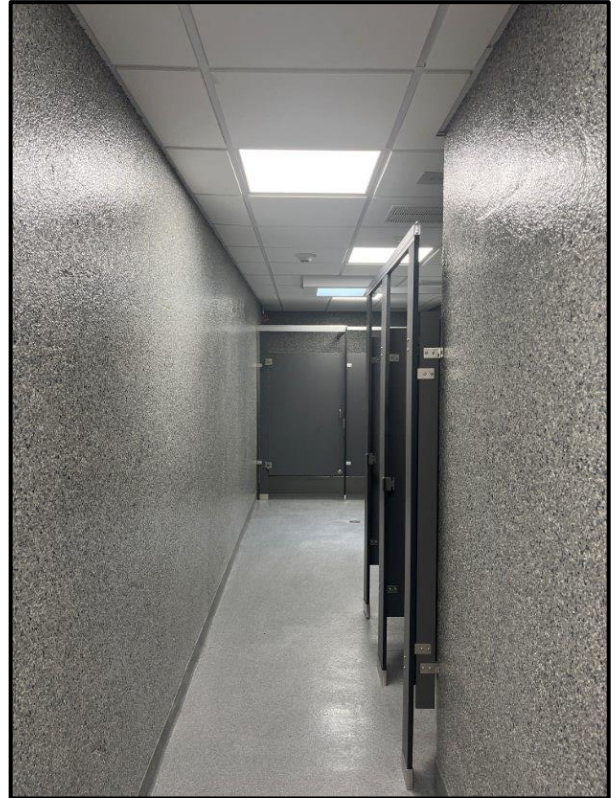

Pomona Middle School - ADA






Ramapo High School – Gymnasium Flooring





Ramapo High School – Door, Windows & ADA

# Jacobs

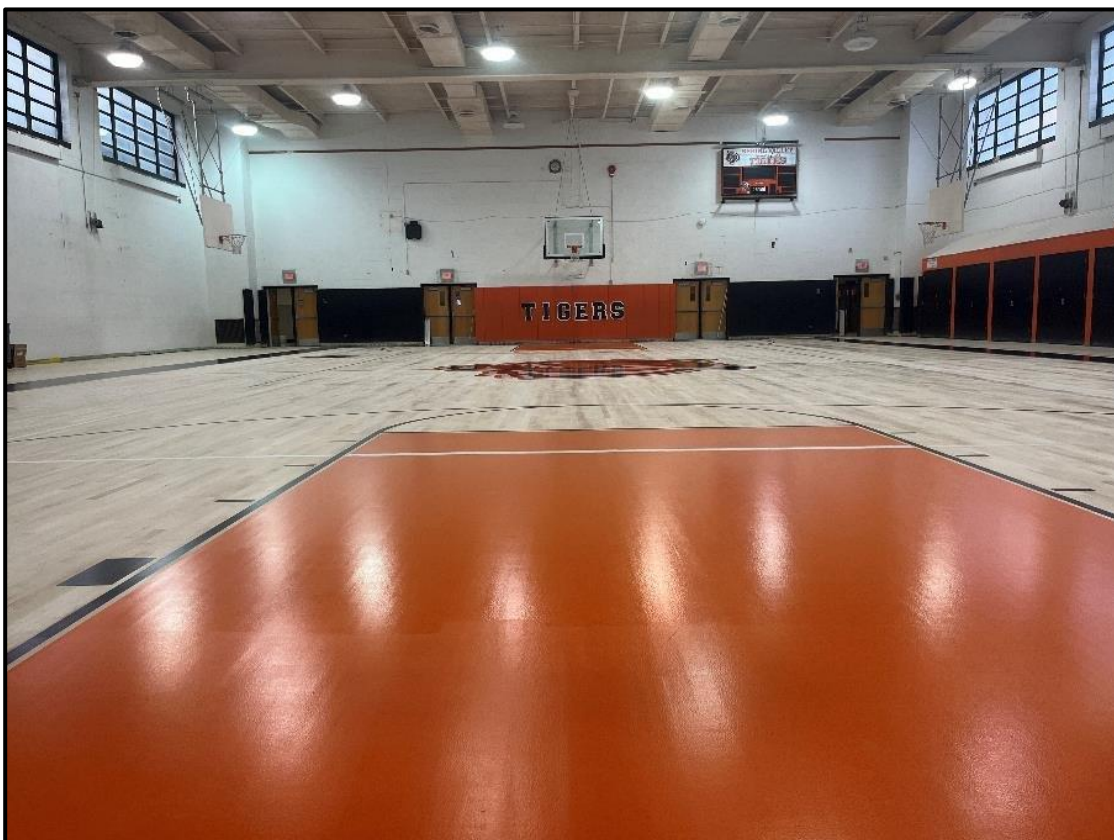



Spring Valley High School – Gymnasium Flooring





Spring Valley High School – ADA



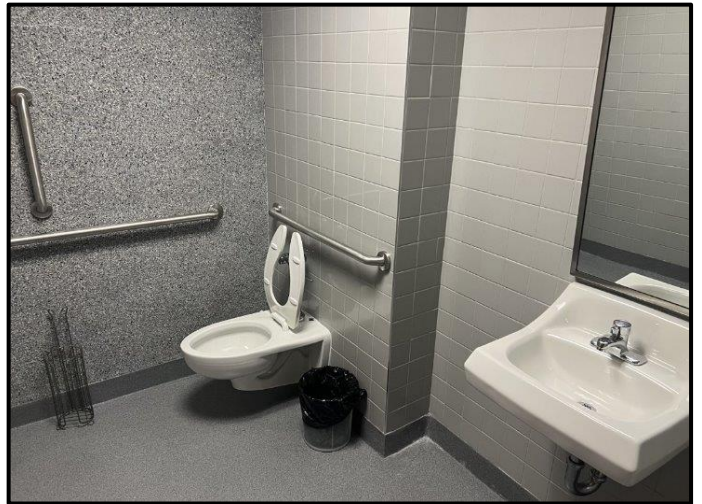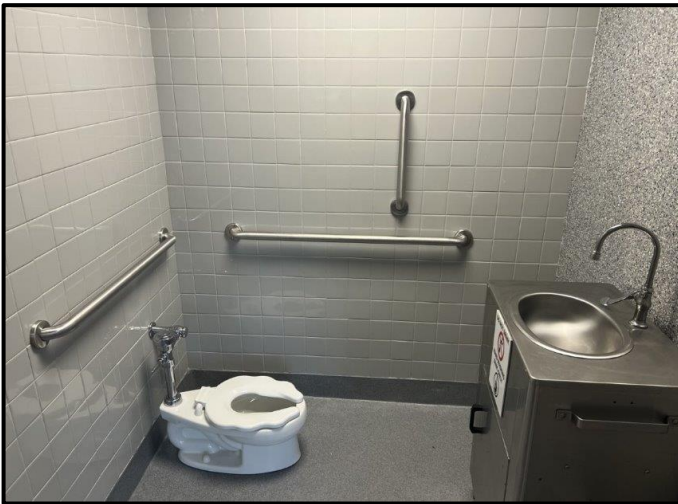

Summit Park Elementary School – Water Fountain & ADA

Construction Field Reports are available upon request per phase.

**END OF REPORT**
