



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 21th, 2024



Last 5 Days:

- Segment F Classroom Addition: Underground Plumbing Completed
- Segment F Classroom Addition: Prep for Slab-on-Grade and SOG Pour Completed
- Segment D B&G Club Admin Area Flooring Install
- Segment D B&G Club Admin Area Finishes – Casework
- Segment D Admin Area – Ceiling Grid Installation.
- MEPs continued working on overhead rough ins in the Segment D Administrative Area
- Taping continued into the School District Administrative Area.
- Interior Painting in Administrative Area
- Ceiling Cloud and MEPS Finishes in the Common's Area Continued.
- Aluminum Curtain Wall glazing at the Radius Entryway
- Radius Entryway Roofing In-Progress.
- GYM 194 Overhead work Continued.
- Segment D Corridor 158 Flooring Install Continued throughout the week.
- Segment E&G Punchlist Items In-Progress
- Exterior Landscaping on North and East Site.
- Shoring in Existing Art Room for Mechanical Equipment Install. Start of Phase 3A.

Next 5 Days:

- Segment D Admin Area: Casework, Doors and Hardware.
- Segment F Canopy Overhang Exterior Concrete.
- Interior Finishes in the Radius Entryway
- Interior Painting – Segment D Administrative Area.
- Taping to continue into the School District Administrative Area.
- Painting to Continue in the Administrative Office Area.
- Exterior Canopy Roofing and Soffit Installation Continued.
- GYM 194 Overhead Work to be completed.
- ID Room Buildout In-Progress.
- Radius entryway exterior paving.
- M&J Pre-Punchlist in Segment B and Exterior Site.

Key Factors:

- GYM 194 Wood Floor Install to Begin 11/04/2024
- Start of Phase 3A – Future Band and Multi-Purpose Room



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 21th, 2024



Segment A Existing Art Room – Shoring for Mechanical Equipment Install



North Exterior Site – Landscaping in Progress



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 21th, 2024



Segment F Classroom Addition – Slab-on-Grade Prep and Pour



Segment F Classroom Addition – Overhang Canopy Exterior Site Concrete Poured




WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 21th, 2024



Segment B – Overhead Gym Equipment Install

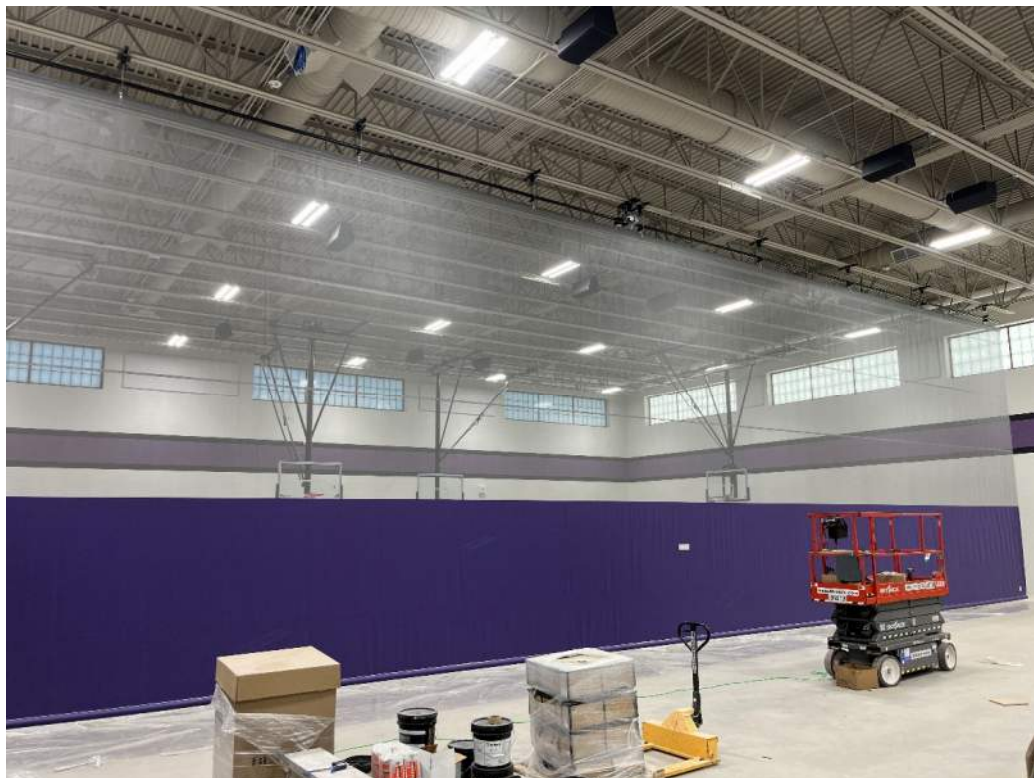

GYM 194 Divider Curtain Installed



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 21th, 2024



Segment D – Corridor 158 Flooring Installation In-Progress



Segment D – B&G Club Flooring Install & Finishes Ongoing



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 21th, 2024



Segment D – B&G Club Admin Area Bathroom Tile Installed



Segment D – School District Admin Area Interior Painting In-Progress
