

# Citizens' Oversight Committee

September 23, 2024




**FREMONT UNION  
HIGH SCHOOL DISTRICT**



# Agenda

1. Big Ten Projects and Bond Project Schedule
2. FHS New Field House and Athletic Complex
3. MVHS Music Building F4 Modernization
4. LHS New Voyager Building
5. LHS Buildings 000, 100, and 300 Classroom Modernizations and Utility Upgrades
6. District Office Solar and Parking Lot Improvements
7. District Robotics Center at CHS
8. District Wide Athletic Fields Replacements
9. Sunnyvale Lakewood Library

# FUHSD Bond Projects

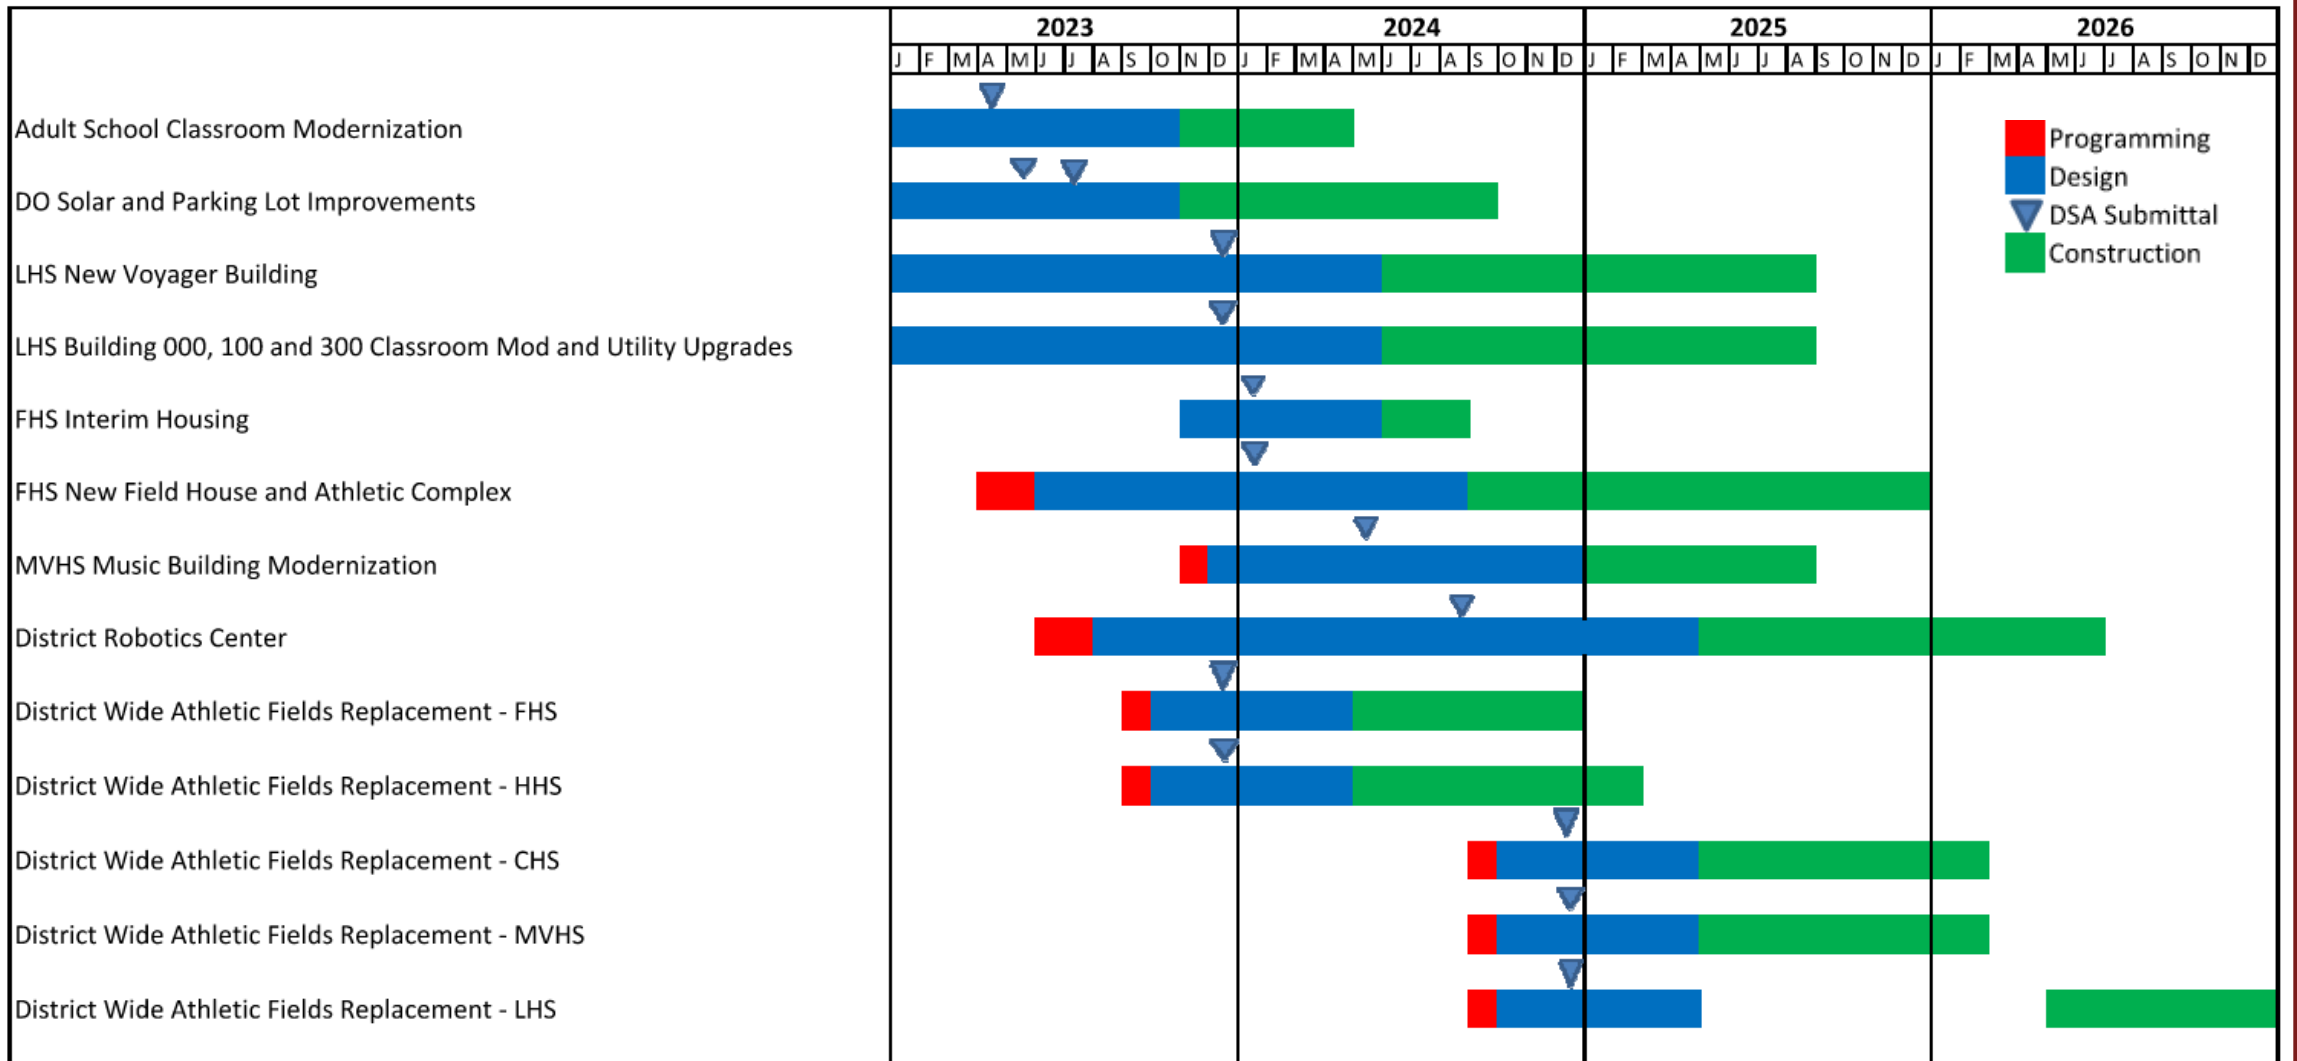

# Fremont High School





**FREMONT UNION  
HIGH SCHOOL DISTRICT**



# FHS New Field House and Athletic Complex

- **Designer:** Aedis Architects
- **Design Status:**
  - **New Building:** DSA Approved
  - Schematic Design Approved: July 18, 2023 Board Meeting
- **Construction Schedule:**
  - **Interim Housing:** Summer 2024 - Complete
  - **New Building:** September 2024 – December 2025
- **Contractor:** Lathrop Construction Associates

# FHS New Field House Interim Housing

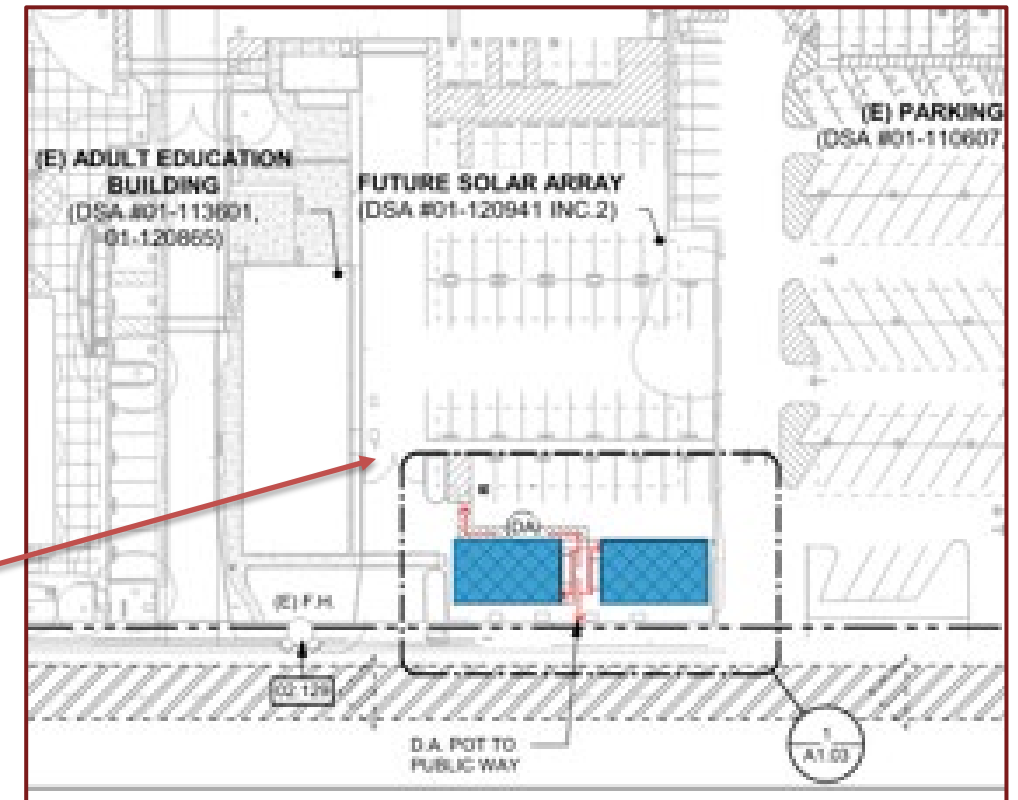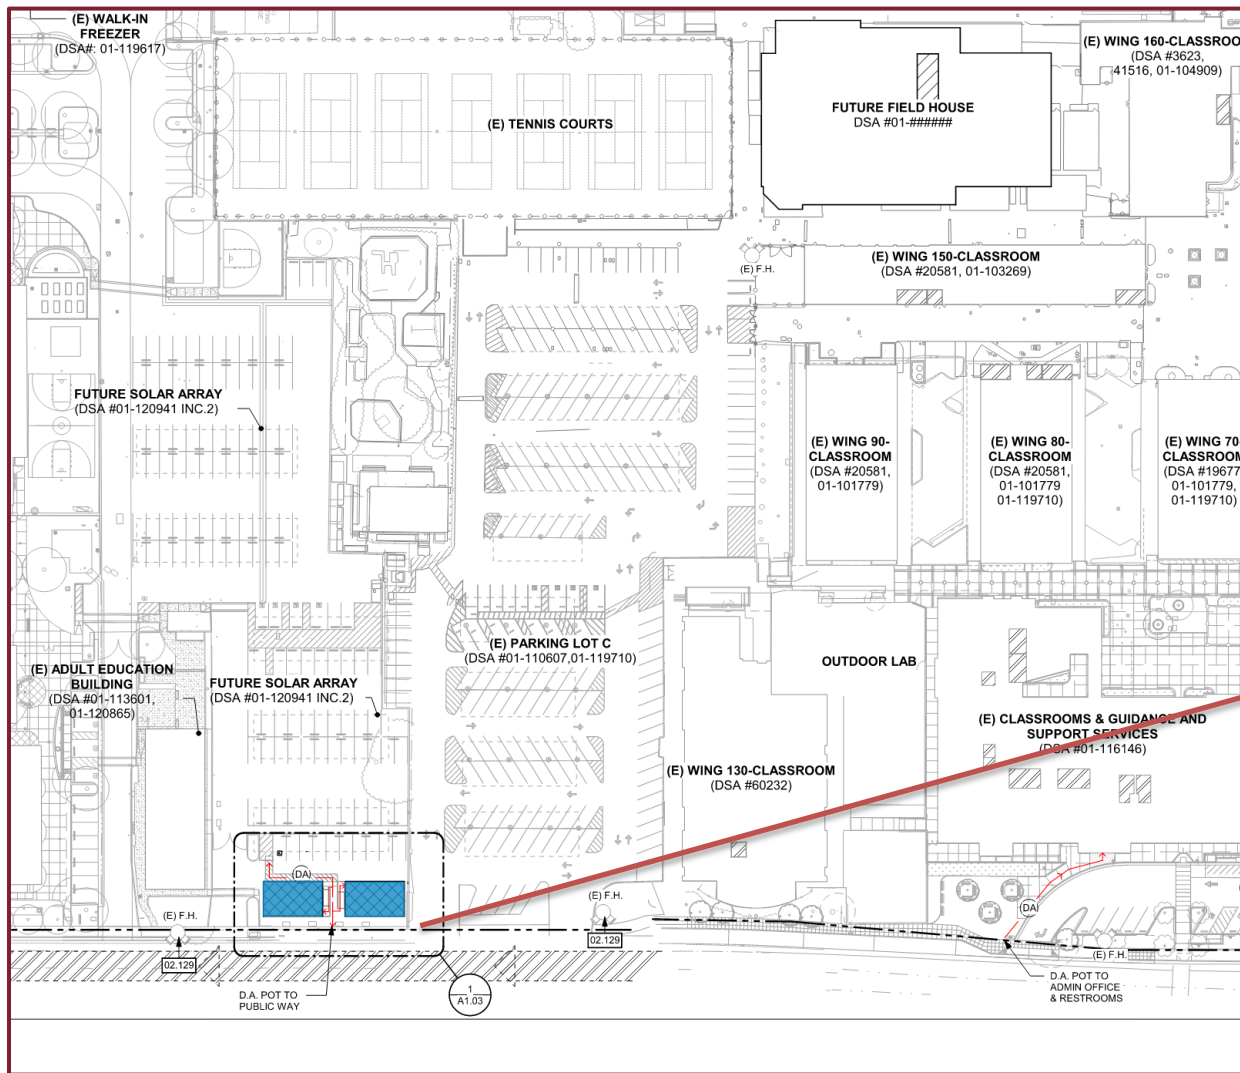

## FHS Interim Housing – Relocating Portables




# FREMONT HIGH SCHOOL FIELD HOUSE

## FREMONT UNION HIGH SCHOOL DISTRICT




# FHS New Field House & Athletic Complex

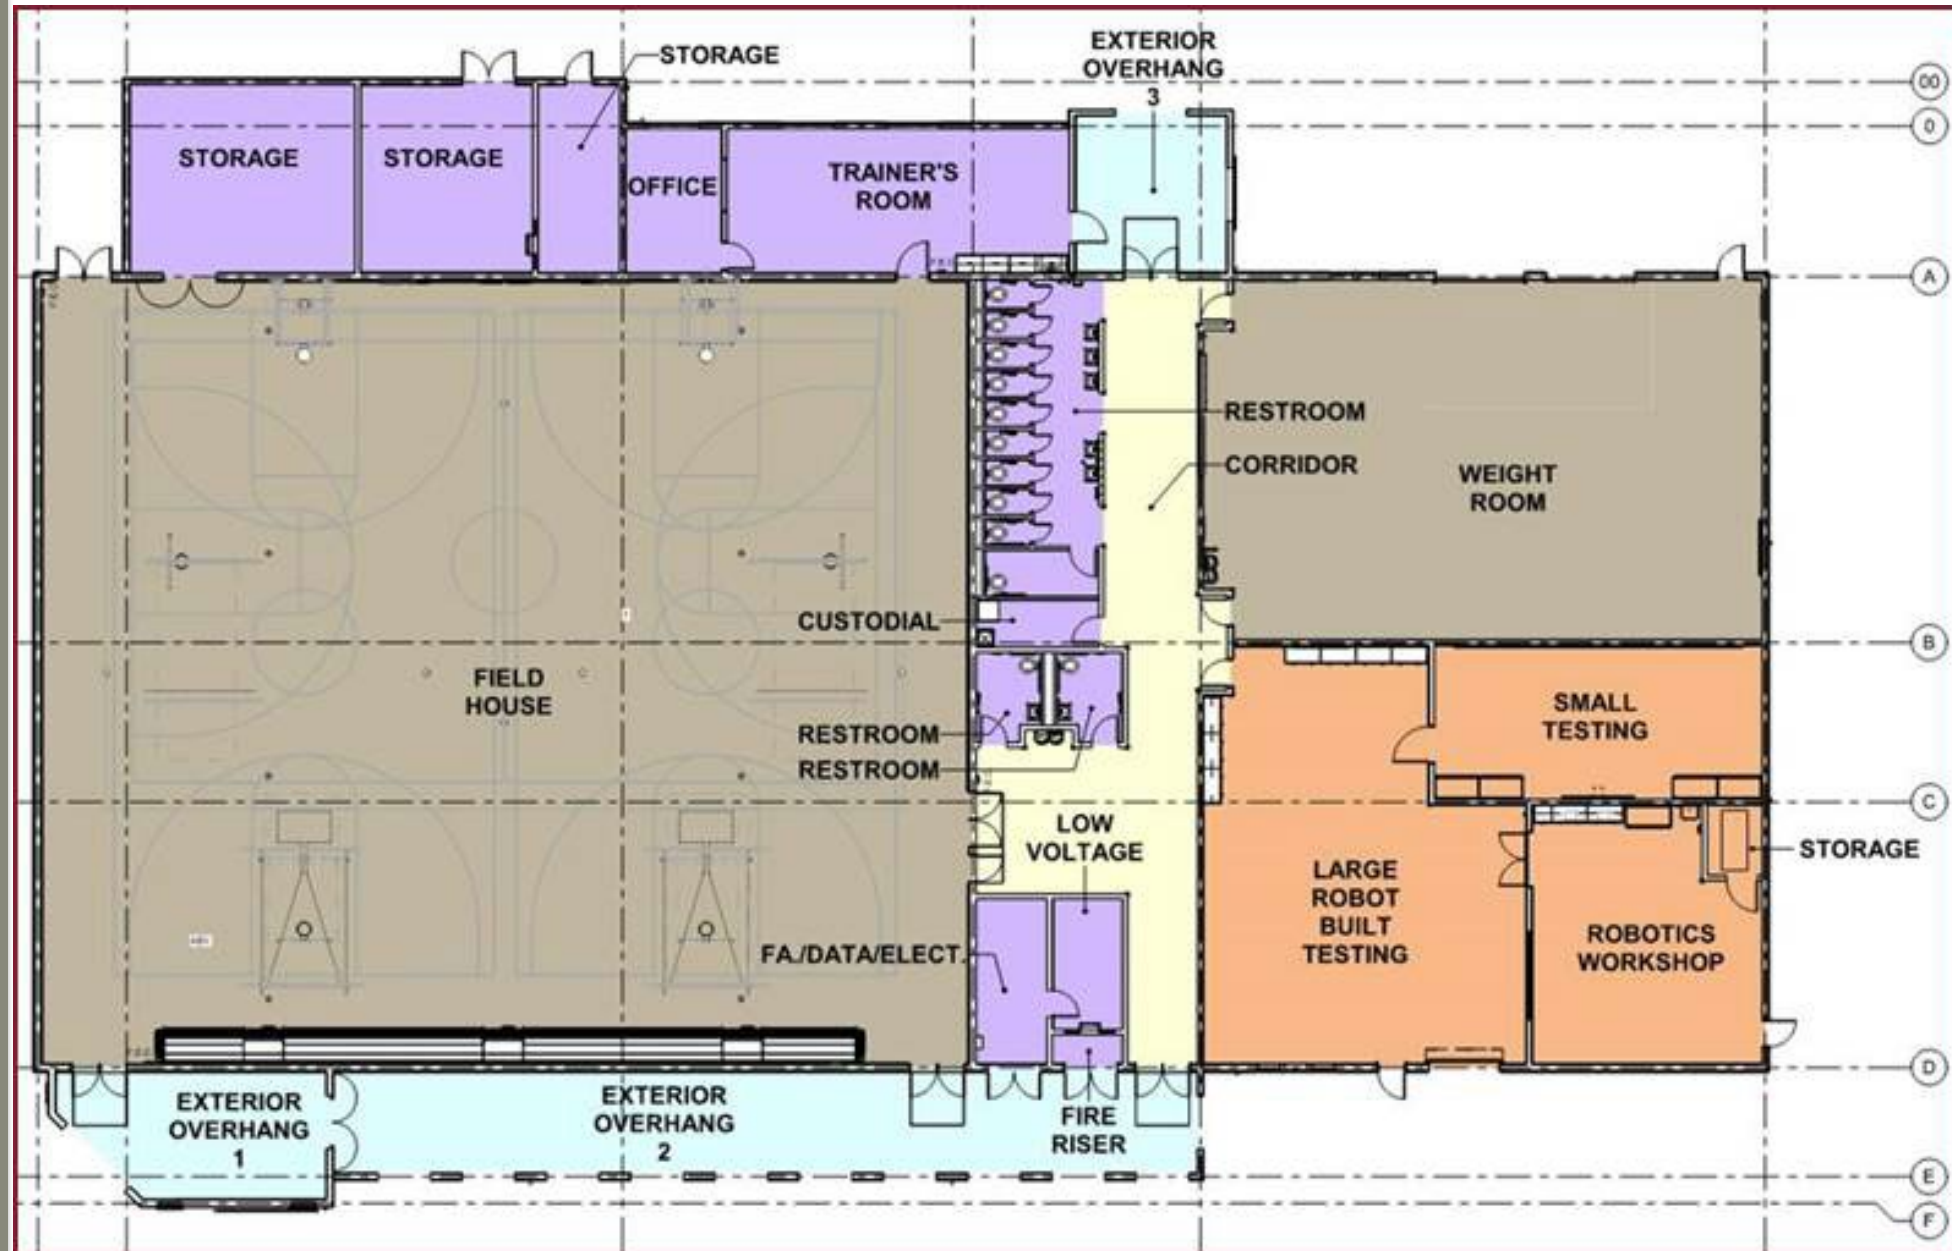



FHS  
Demolition  
of Weight  
Room



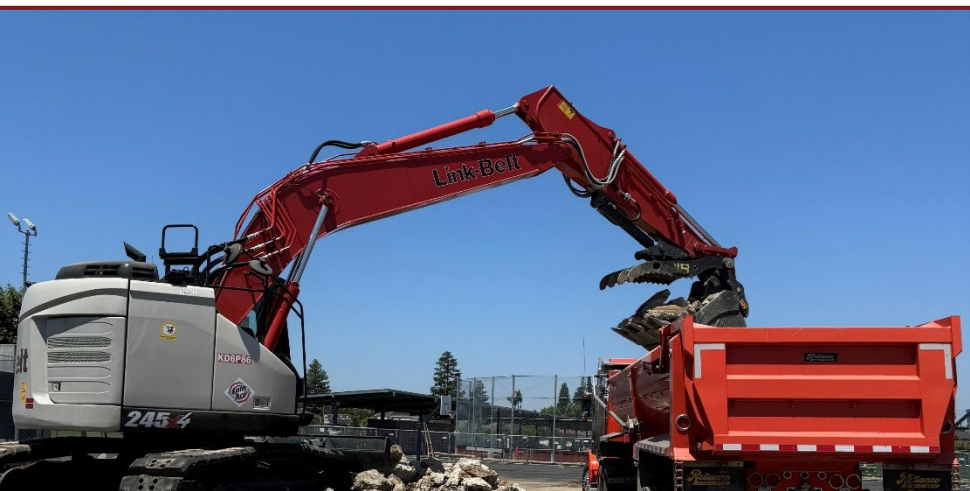

# Monta Vista High School




**FREMONT UNION  
HIGH SCHOOL DISTRICT**

# MVHS Building Music Building (F4) Modernization

- **Designer:** Derivi Castellanos Architects (DCA)
- **Design Status:** DSA Review
- **Construction Schedule:** January 2025 – August 2025
- **Contractor:** SC Builders



# MVHS Music Building (F4)

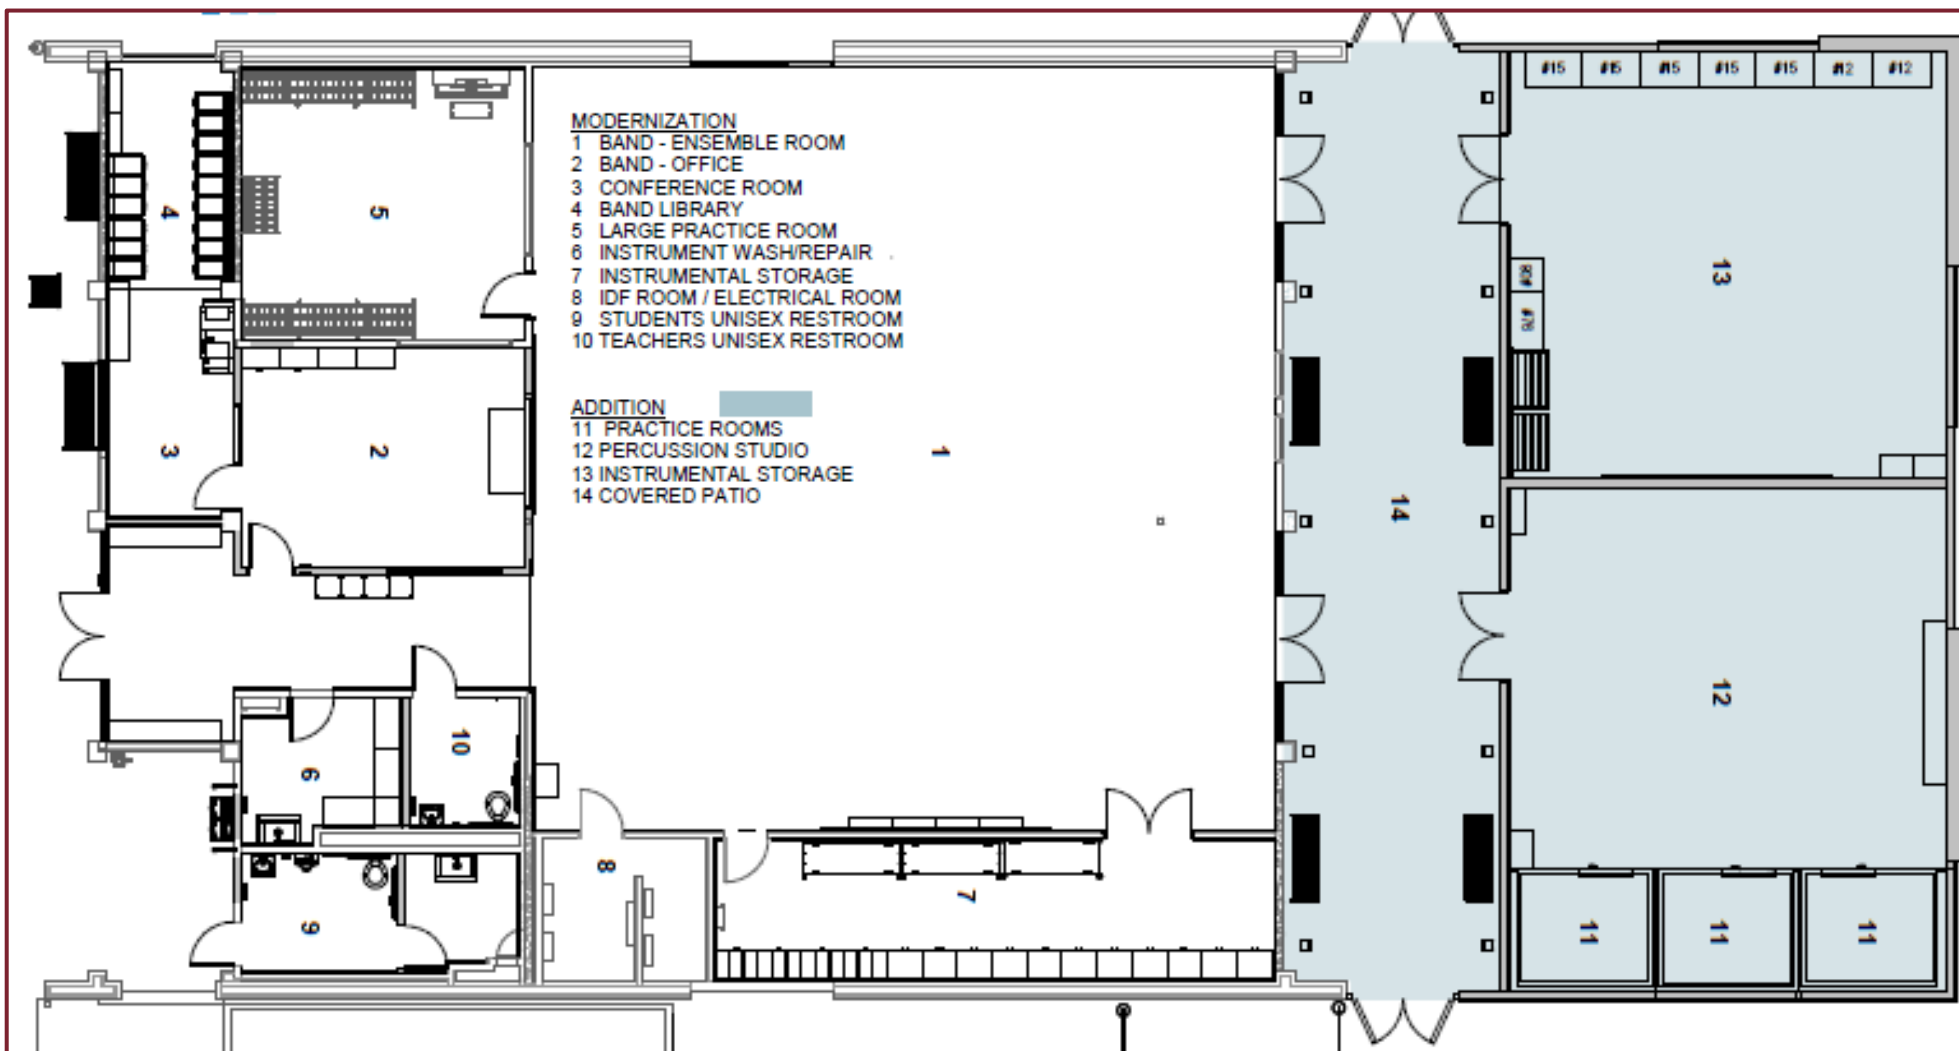

# Lynbrook High School



**FREMONT UNION  
HIGH SCHOOL DISTRICT**

# LHS New Voyager Building

- **Designer:**  
Quattrocchi Kwok Architects (QKA)
- **Construction Status:**  
Footing Installation
- **Construction Schedule:** June 2024  
– August 2025
- **Contractor:** Blach Construction Company



LHS New  
Voyager  
Building





# LHS Buildings 000, 100, and 300 Classroom Modernizations and Utility Upgrades

- **Designer:** Quattrocchi Kwok Architects (QKA)
- **Construction Status:**
  - **Site Work:** Underground utility work complete. Site concrete and temp AC placed in preparation for start of school.
  - **Bldg. 300:** Demolition complete. Framing and rough-in of MEP in progress
- **Anticipated Construction Schedule:** Summer 2024 – Summer 2025
  - **Underground Utility Upgrades** – Summer 2024
  - **Bldg. 300:** June 2024 – November 2024
  - **Bldg. 000:** November 2024 – March 2025
  - **Bldg. 100:** March 2025 – August 2025
- **Contractor:** Blach Construction Company



LHS Utility Upgrades



LHS Flatwork



LHS Building 300



LHS Building 300

# District Office Site and District Wide



**FREMONT UNION  
HIGH SCHOOL DISTRICT**



# District Office Solar and Parking Lot Improvements

- **Designer:** Quattrocchi Kwok Architects (QKA)
- **Construction Status:** Parking lot and solar panel installation complete. Testing waiting area patio and shade structure in progress.
- **Construction Schedule:**
  - **Inc. 1:** November 2023 – January 2024 (Complete)
  - **Inc. 2:** February 2024 – September 2024
- **Contractor:** Blach Construction Company



District Office Solar and Parking Lot Improvements


# District Robotics Center at CHS

- **Designer:** Quattrocchi Kwok Architects (QKA)
- **Design Status:** Construction Documents
  - Schematic Design Approved: April 23, 2024 Board Meeting
- **Anticipated Construction Schedule:** May 2025 – June 2026
- **Contractor:** Landmark Constructors




# District Robotics Center at CHS


## Campus Site Plan

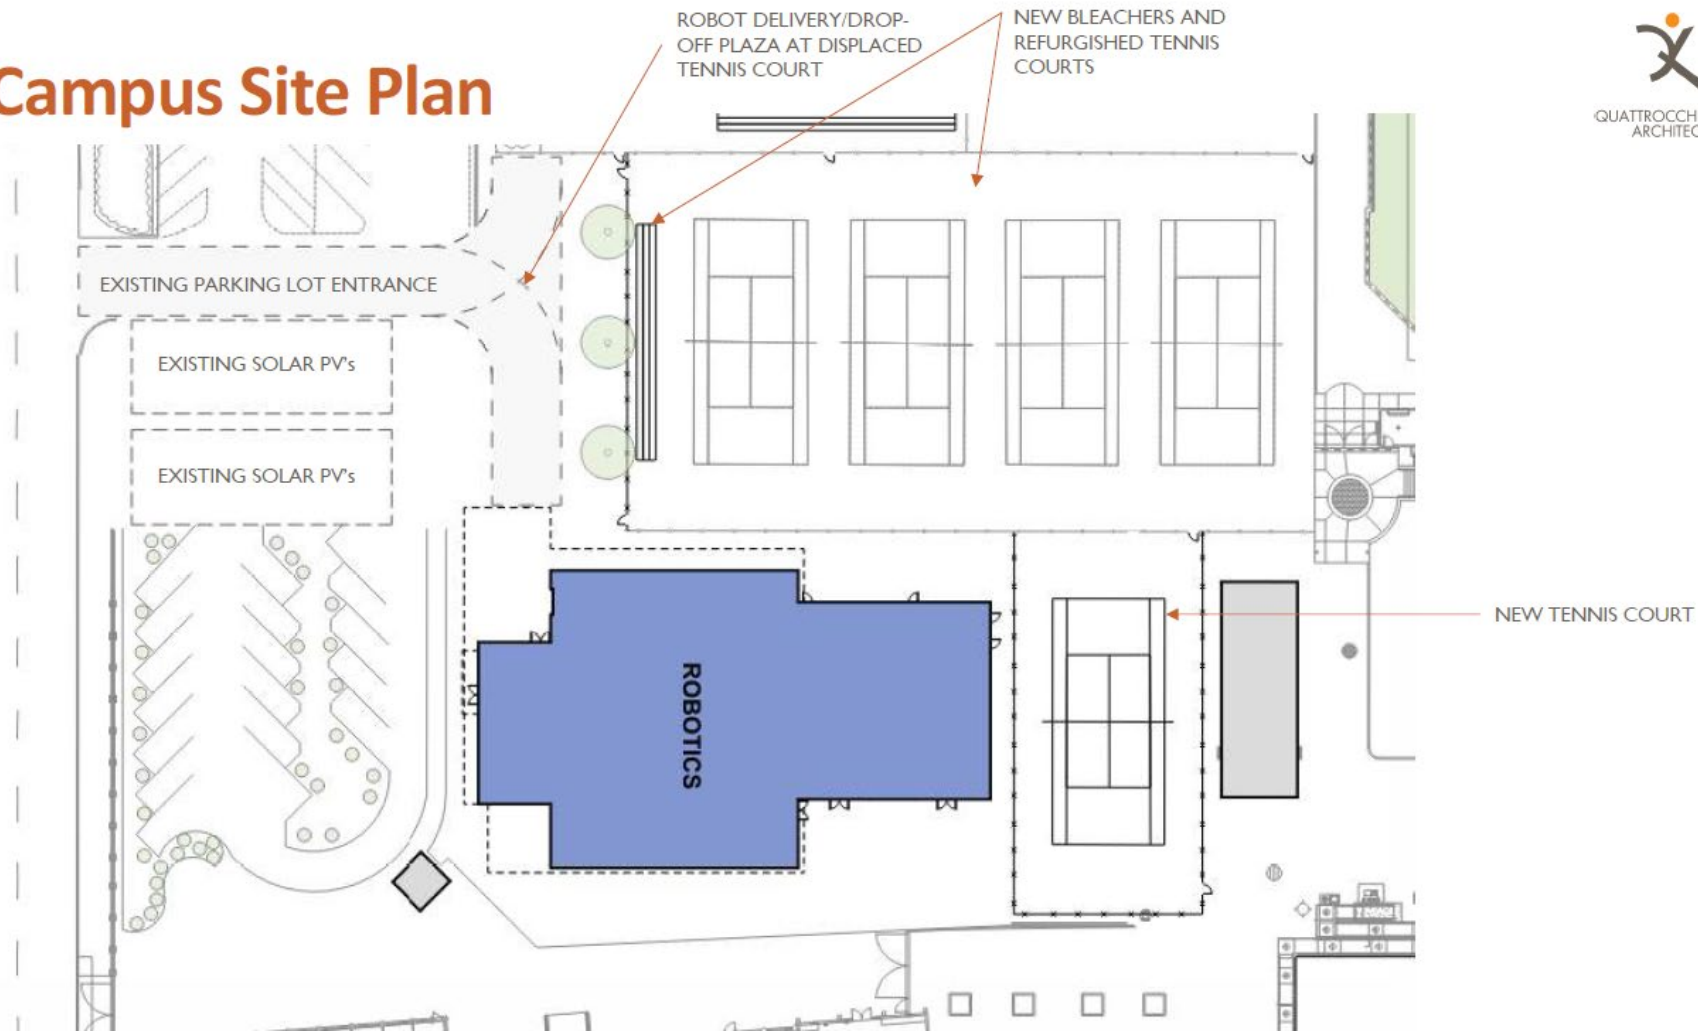

## First Floor Plan

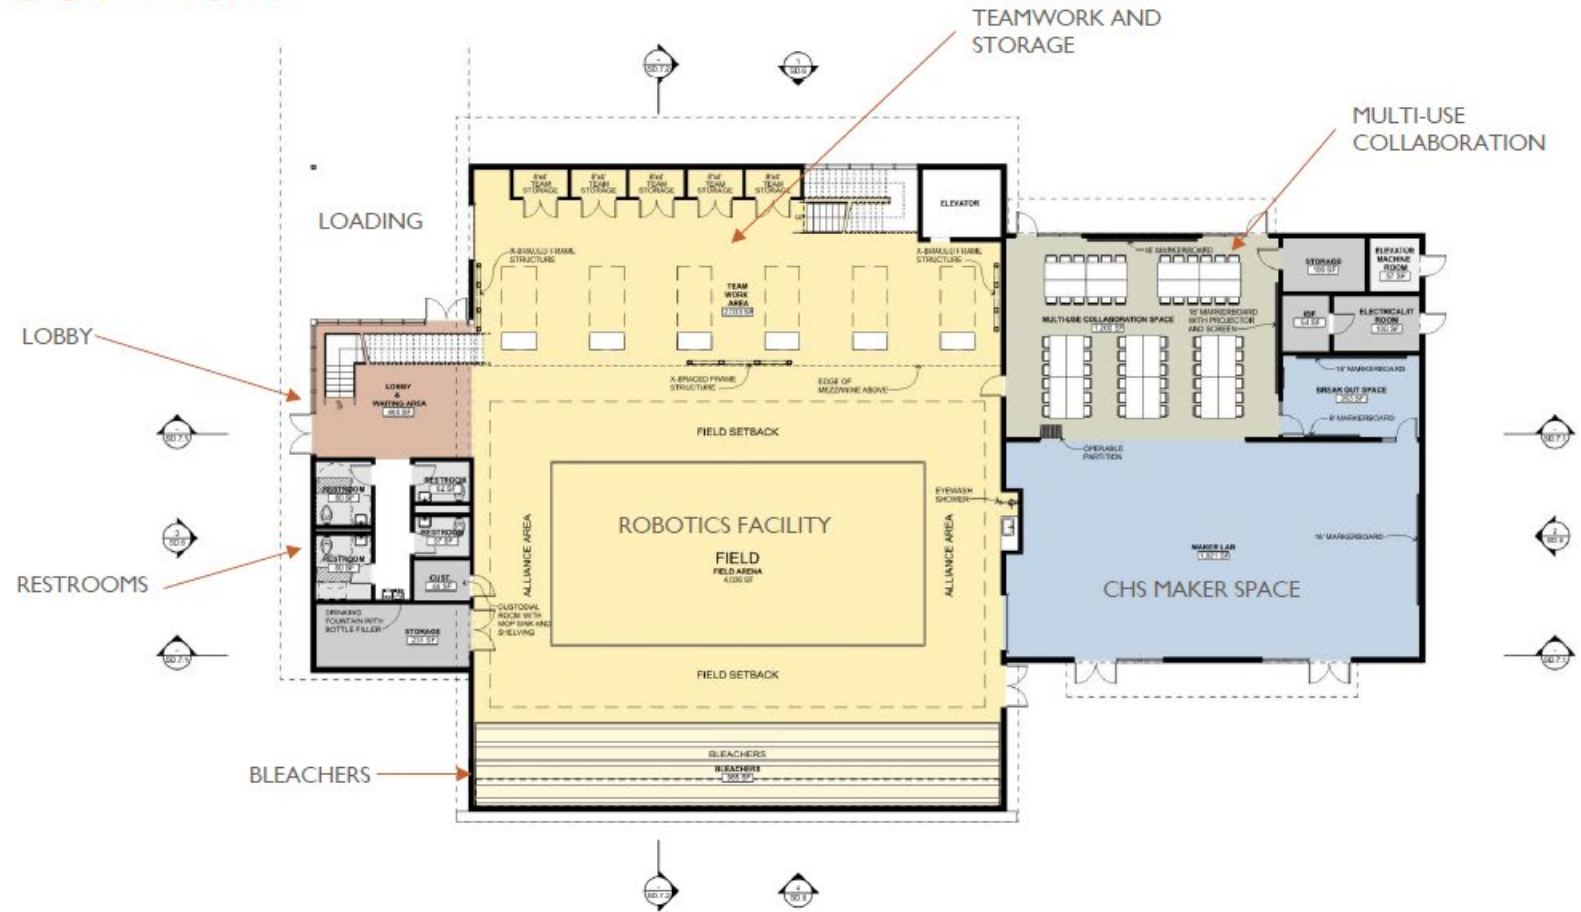

# Mezzanine Floor Plan

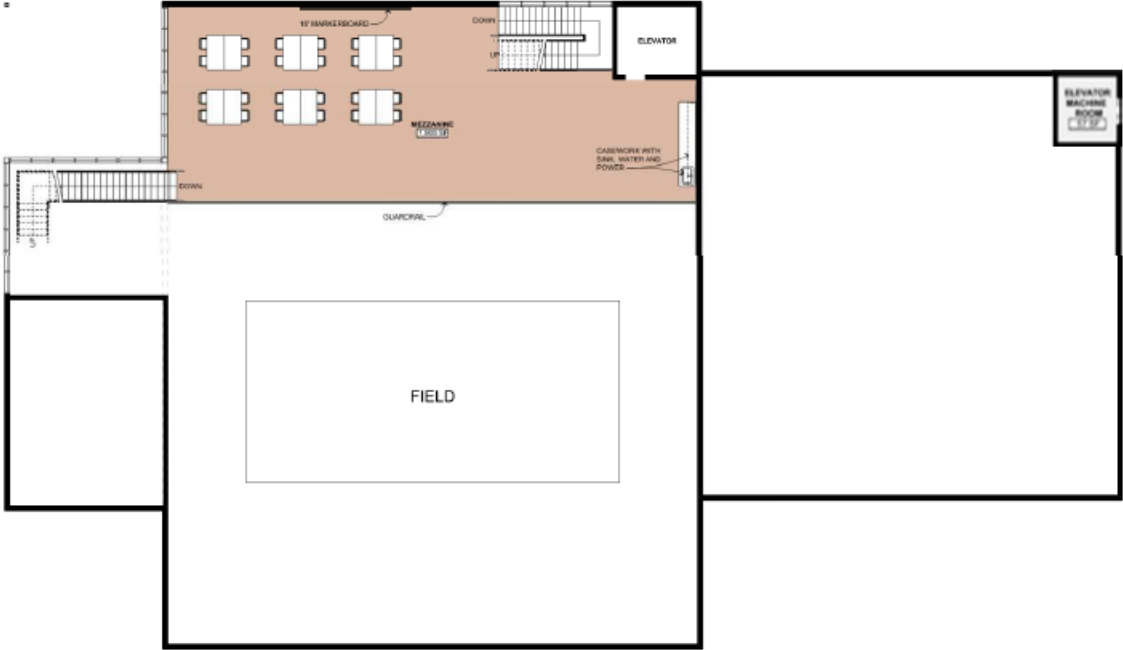




# District Wide Athletic Fields Replacements

- **Designer:** Verde Design
- **Construction Status:**
  - **Fremont HS:**
    - Soccer Field – Complete
    - Football Field – Turf installation near completion
    - Track – Resurfacing in progress
    - Baseball field – Grading in Progress
  - **Homestead HS:**
    - Softball/Multi-Use Field – Turf Installation in Progress
    - Football Field – Complete
    - Track – Resurfacing in progress
    - Baseball/Multi-Use Field – To begin 9/13
- **Anticipated Construction Schedule:**
  - Fremont HS: May 2024 – December 2024
  - Homestead HS: May 2024 – February 2025
- **Contractor:** Robert A. Bothman Construction


# Fremont High School Phasing Plan

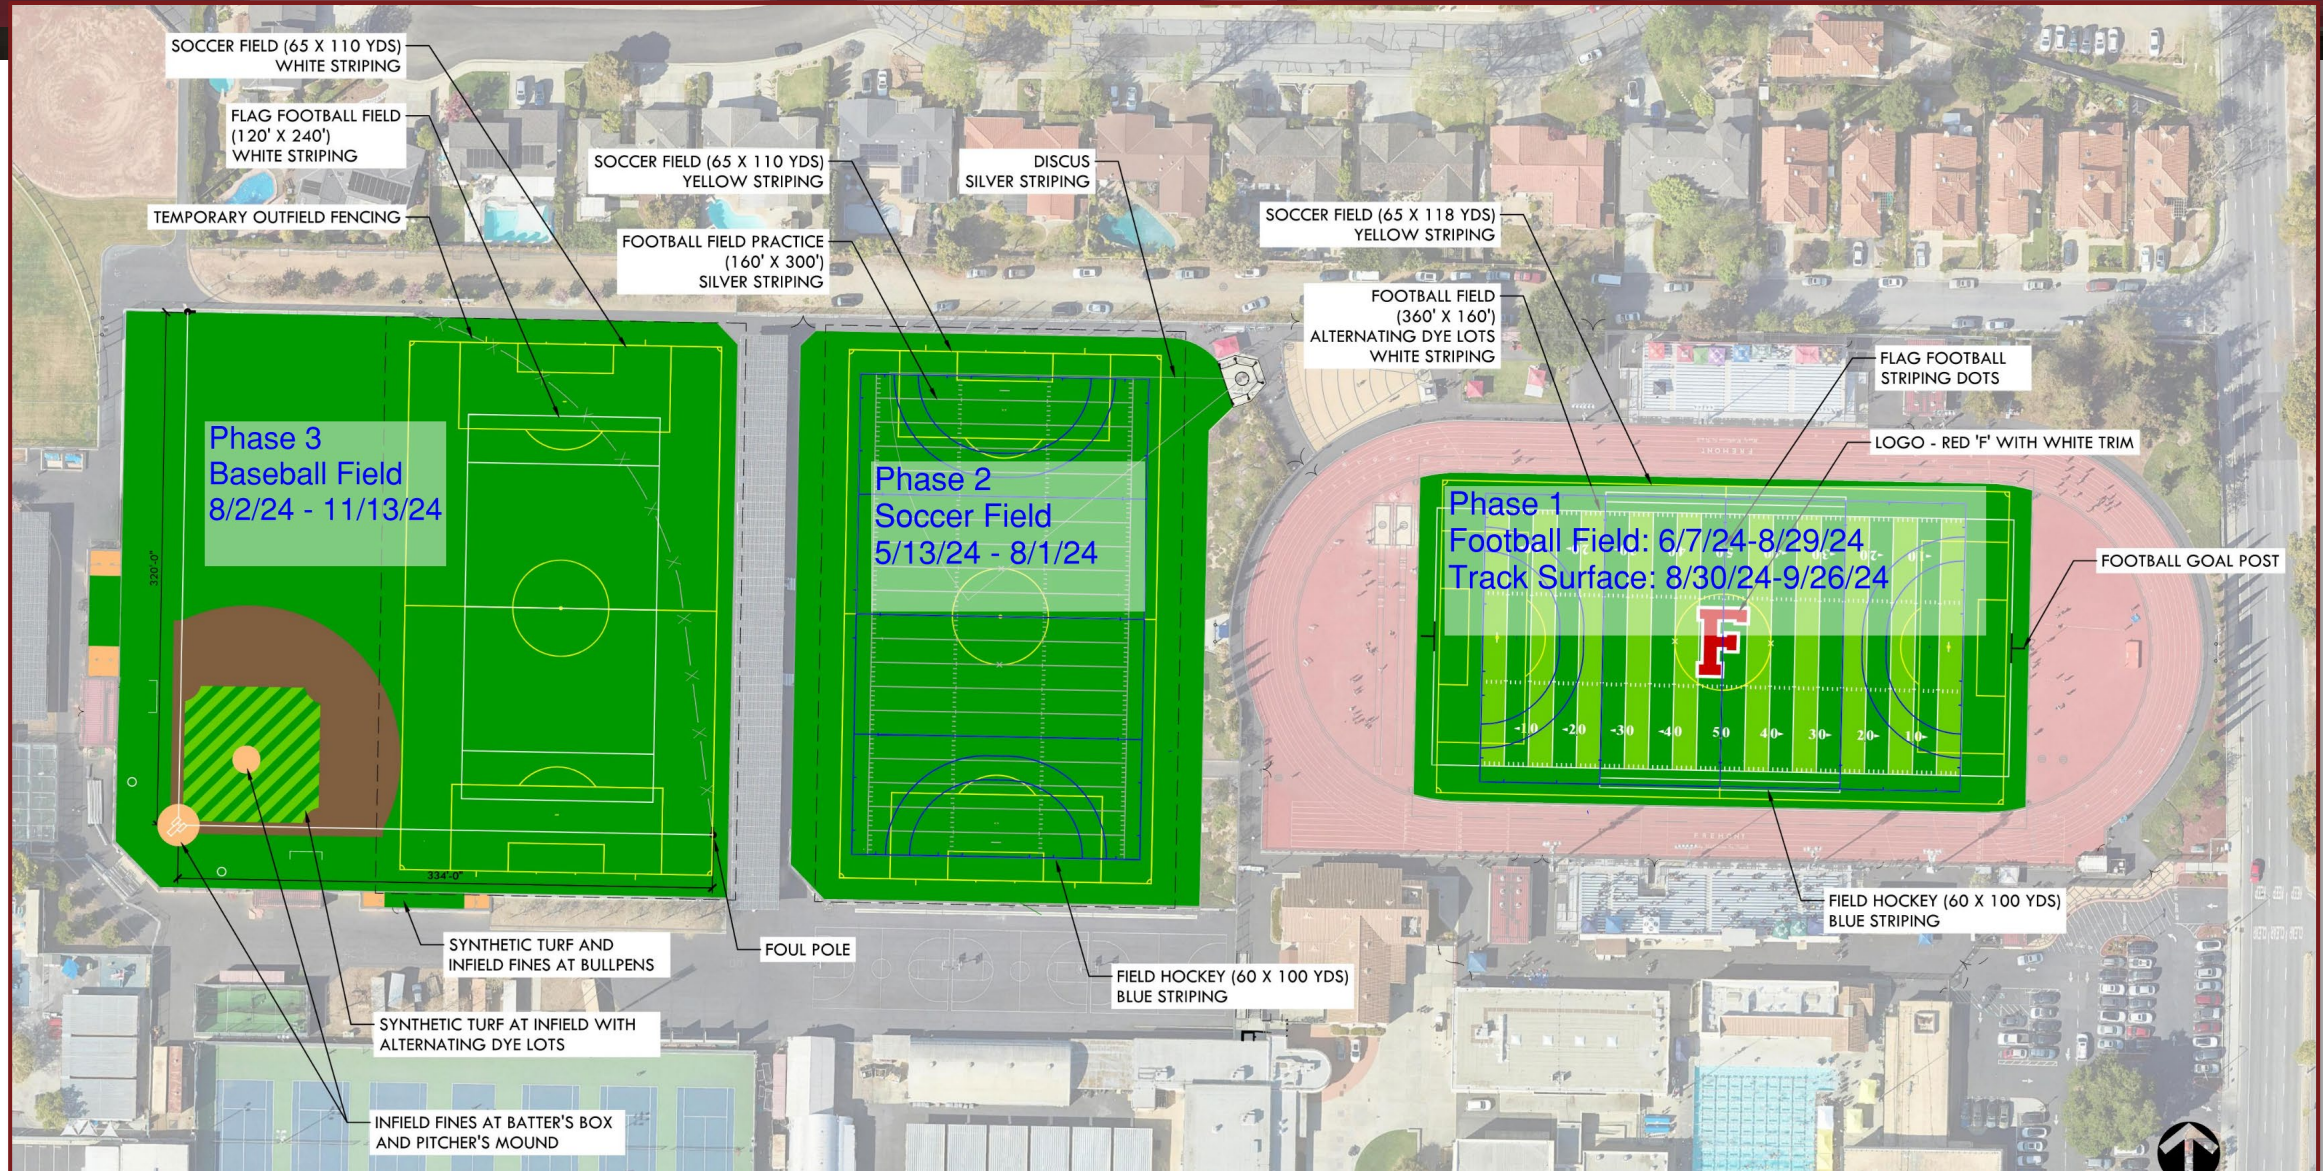


## Fremont HS Soccer and Football Fields



# Homestead High School Phasing Plan

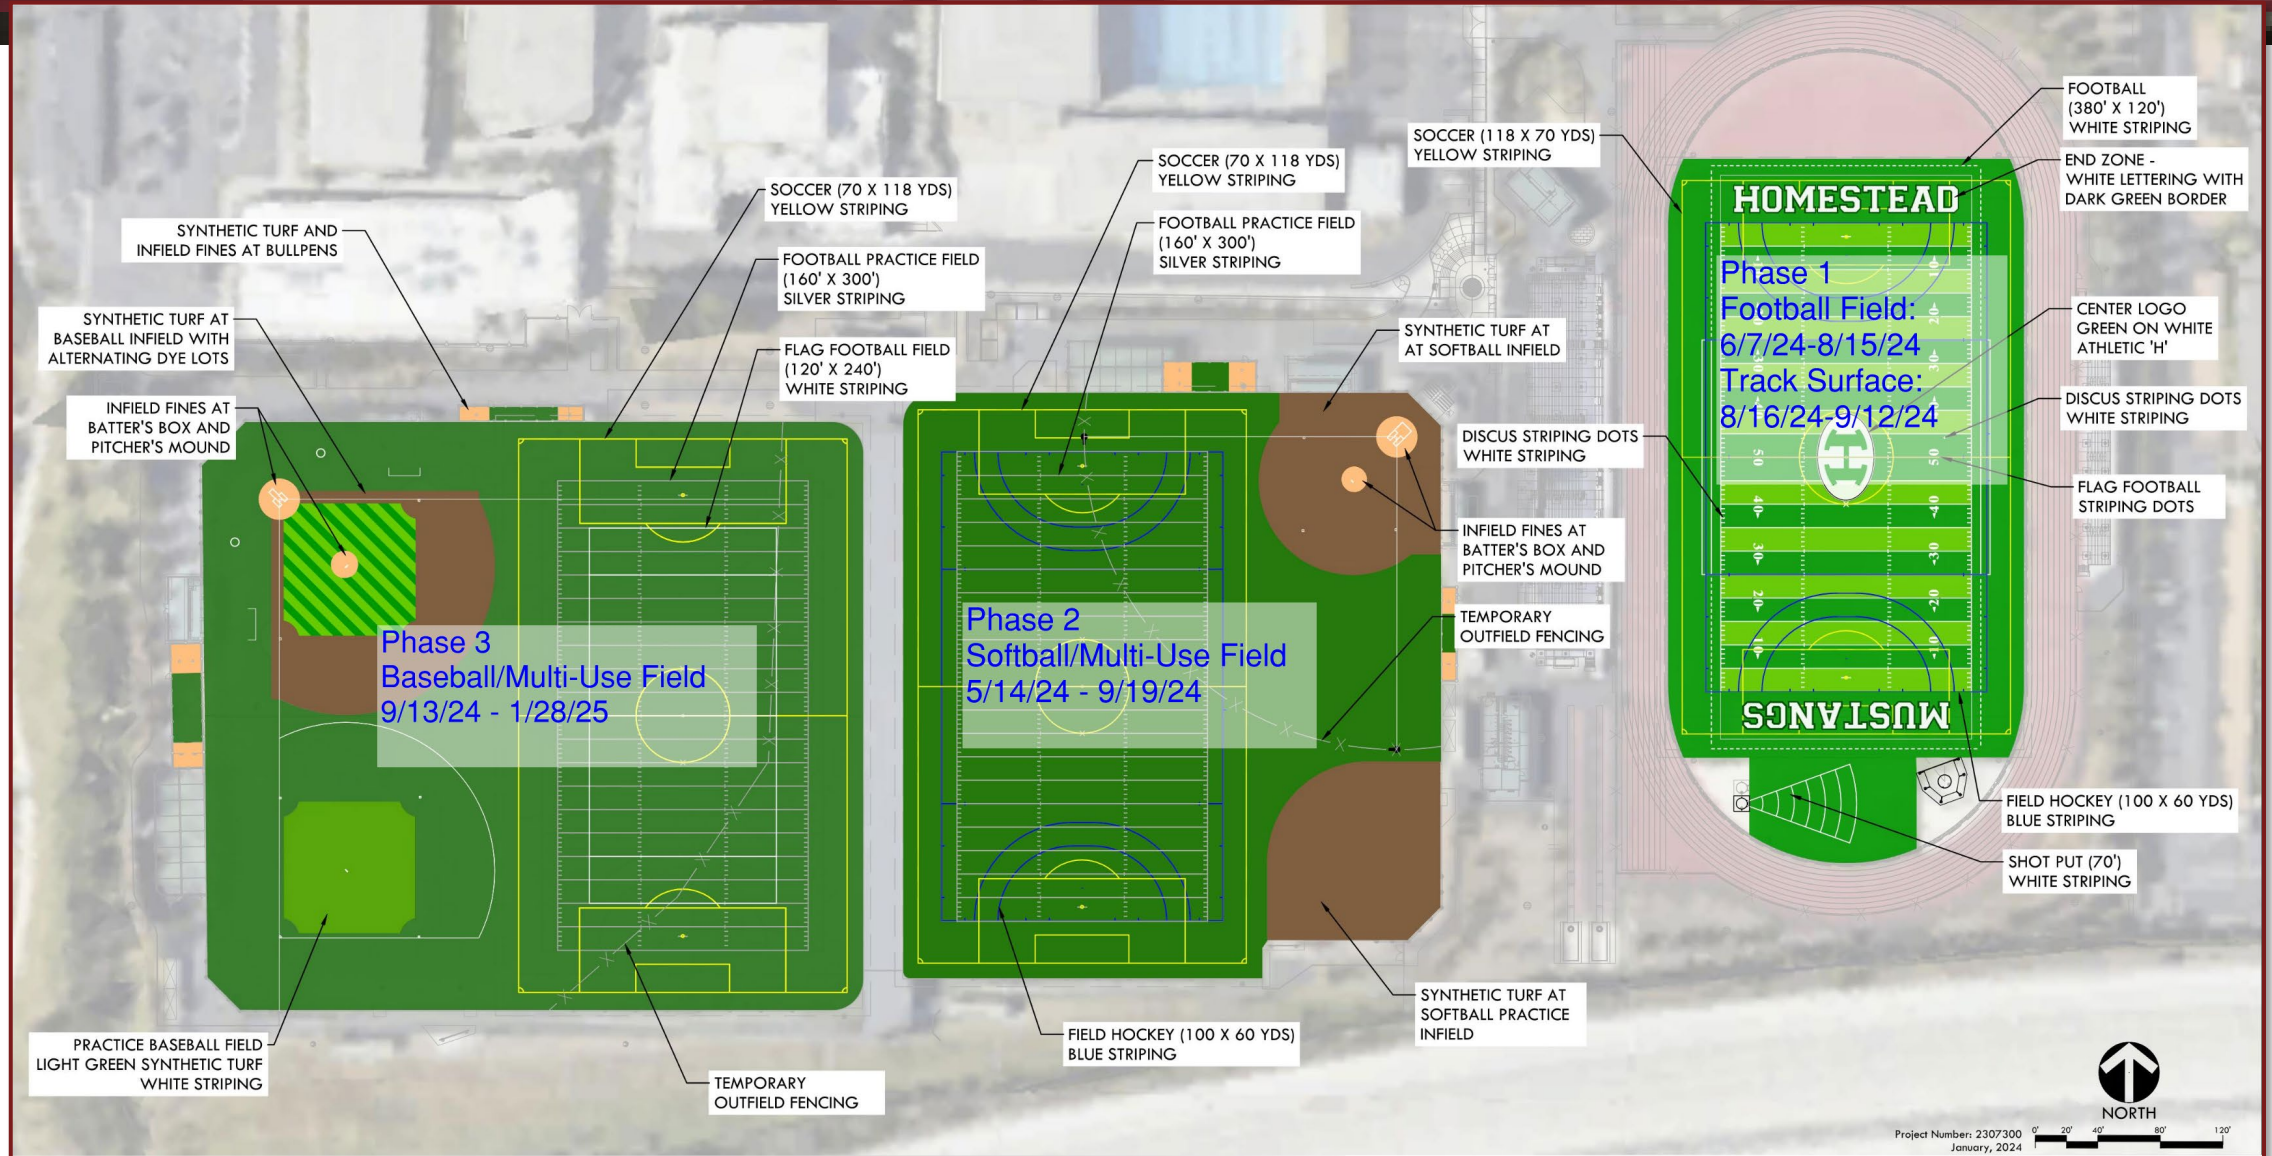

# Homestead HS Softball and Football Fields

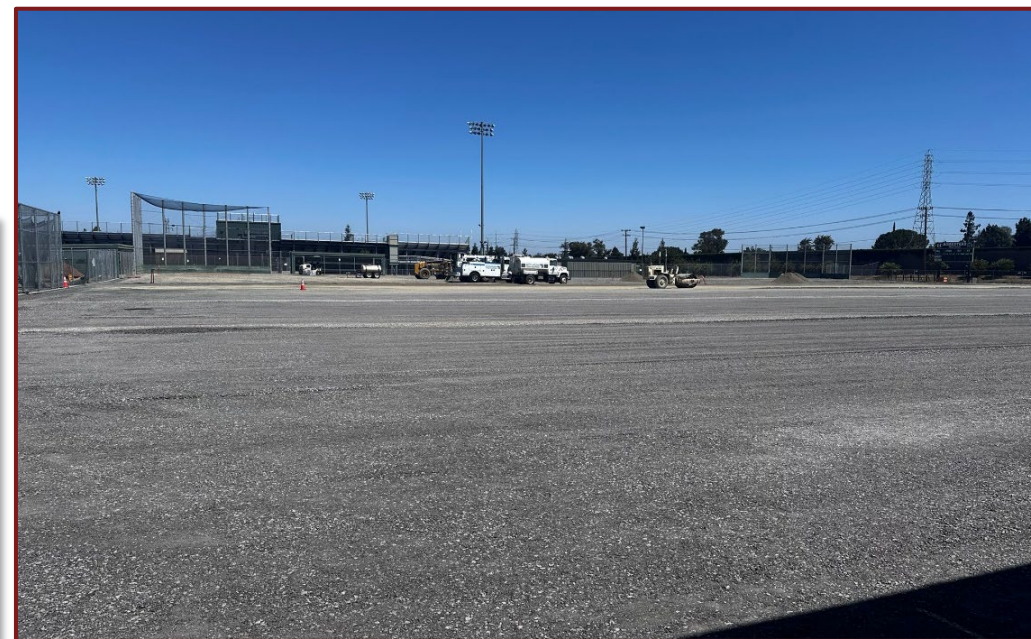

# District Wide Athletic Fields Replacements

| CURRENT PLAN - Measure K |                  |                |
|--------------------------|------------------|----------------|
| SITE                     | Number of Fields | Square Footage |
| Cupertino High School    | 2 Fields         | 217,328        |
| Fremont High School      | 3 Fields         | 169,904        |
| Homestead High School    | 3 Fields         | 419,088        |
| Lynbrook High School     | 2 Fields         | 170,172        |
| Monta Vista High School  | 2 Fields         | 290,055        |

| RECOMMENDED - Measure K |                  |                |
|-------------------------|------------------|----------------|
| SITE                    | Number of Fields | Square Footage |
| Cupertino High School   | 2 Fields         | 217,328        |
| Fremont High School     | 3 Fields         | 169,904        |
| Homestead High School   | 3 Fields         | 419,088        |


| RECOMMENDED - Measure CC |                  |                |
|--------------------------|------------------|----------------|
| SITE                     | Number of Fields | Square Footage |
| Lynbrook High School     | 2 Fields         | 170,172        |
| Monta Vista High School  | 2 Fields         | 290,055        |

# Sunnyvale Lakewood Library



**FREMONT UNION  
HIGH SCHOOL DISTRICT**

# Sunnyvale Lakewood Library Project

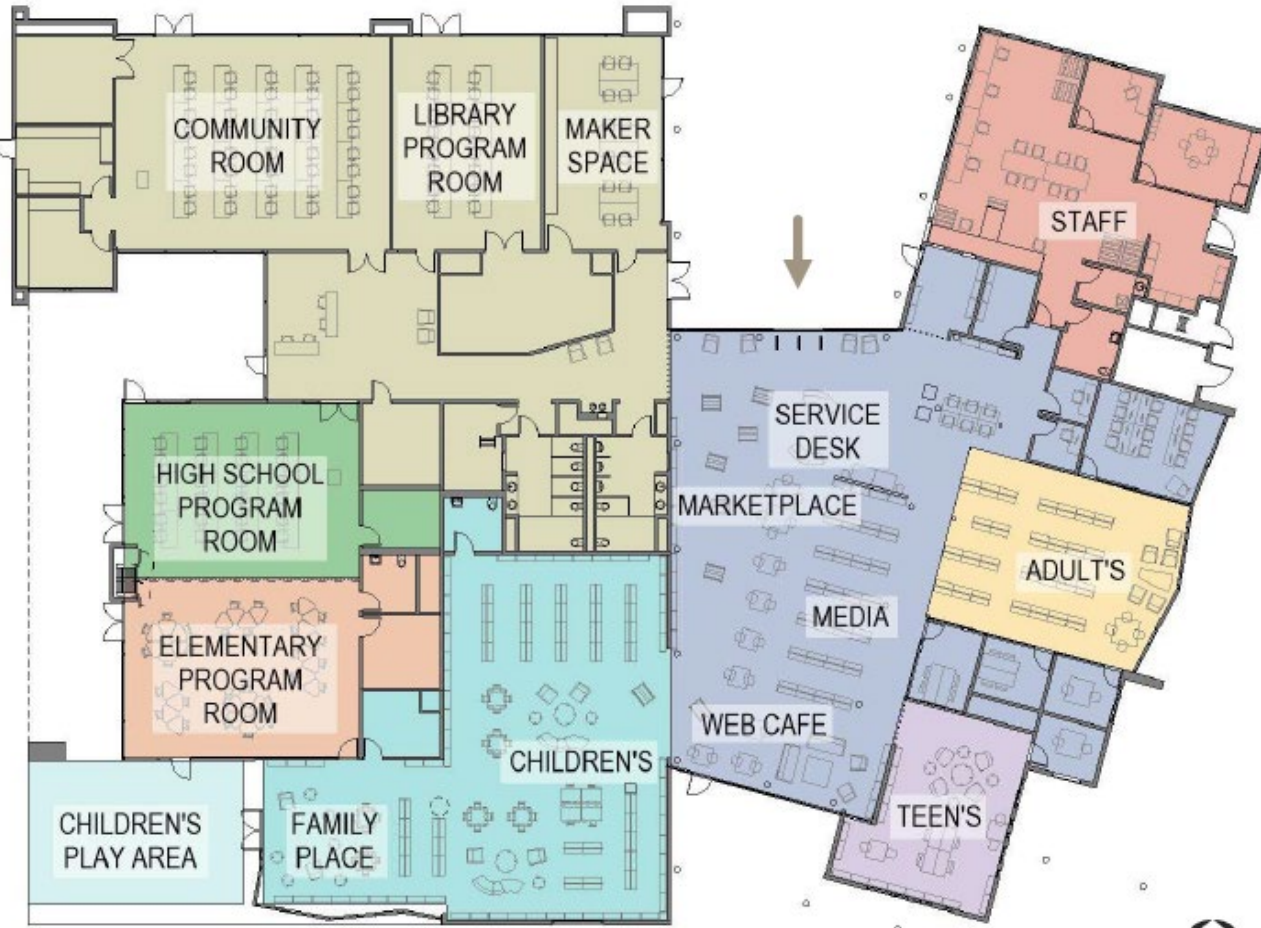

## Schedule

- Joint MOU Approved (3 Party) Winter 2020
  - City of Sunnyvale
  - Fremont Union High School District
  - Sunnyvale School District
- Schematic Design Approval November 2020
- DSA Submittal October 2022
- DSA Approval Fall 2023
- Bidding March 2024
- Construction Start Summer 2024
- Completion End of 2025
- **Groundbreaking September 5<sup>th</sup>, 2024**
