

Crown Point Community School Corporation Construction Projects

Board Report October 28, 2024



Crown Point Community School Corporation Construction Projects

Table of Contents

Board Report
October 28, 2024

- **High School Additions & Renovations**
- **Solon Robinson Elementary Additions & Renovations**
- **Winfield Elementary Additions & Renovations**
- **Lake Street Elementary Additions & Renovations**






Progress Photographs



PLTW Classroom

New Satellite Kitchen

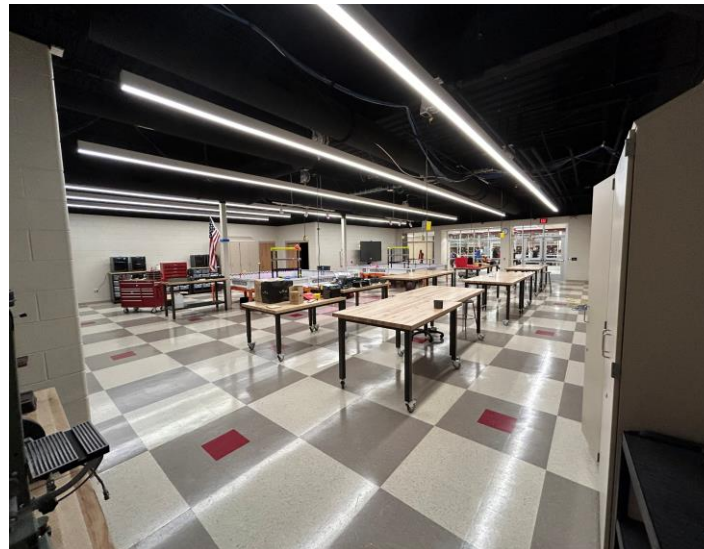

High School Additions & Renovations:

- Completed the seeding to the restoration areas in the Athletic Fields
- Completed the copper metal fascia to the ticket booths
- Continued punch list items for Athletic Fields and High School
- Installed Cobi-ovens
- Continued to install new pool pump equipment

Next Four Weeks

- Complete door replacement for the TV Studio (Christmas Break)
- Complete concrete replacement at kitchen patio area
- Complete punch list items



Progress Photographs



New Playground Equipment

Gymnasium Progress



Solon Robinson Elementary School

Additions & Renovations:

- Finished installing playground equipment
- Finished painting, installing ceiling grid and installing flooring in cafeteria
- Finished gym and cafeteria restrooms
- Finished painting kitchen
- Finished Unit A addition mechanical piping and roofing
- Continued reroofing existing building
- Began installing new floor, athletic equipment, and bleachers in gymnasium



Progress Photographs



Solon Robinson Elementary School Additions & Renovations:

Next Four Weeks

- Finish installing athletic equipment, flooring and bleachers in gymnasium
- Finish installing cooler/freezer
- Finish drywall and taping in Units A/B classrooms/corridor
- Begin painting Unit A addition
- Begin casework in Unit B classrooms
- Begin casework in Unit A addition



Completed Cafeteria



Progress Photographs



Roofing Coping Progress



Winfield Elementary School

Additions & Renovations:

- Started coping on the roof
- Completed most of the punch list items over fall break
- Installed permanent glazing in the classroom doors

Next Four Weeks

- Continue working on changing the louvers
- Complete the outside and inside signage
- Finish remaining punch list items



Progress Photographs



Clerestory Interior Completion



Lake Street Elementary School Additions & Renovations:

- Continued completing open task items
- Completed wheelchair lift state inspection and owner training
- Completed stage lighting programming and owner training
- Completed clerestory and turned it over to the school
- All trades have demobilized from the job site



Progress Photographs



Lake Street Elementary School

Additions & Renovations:

Next Four Weeks

- Complete corner guards
- Complete roof ladders
- Complete cafeteria/stage/gymnasium sound system owner training
- Complete clerestory acoustical sound panels
- Complete east elevation building fascia metal, metal panels and roof edge metal
- Complete exterior building signage and dedication plaque installations
- Complete entire building EIFS
- Complete open punch list items



New Clerestory/Roofing Progress
