

### GREENPORT SCHOOL PROJECT-A, B & C

#### Renu GC:

- Completed foundation walls, soil re-grading and soil compaction
- Completed New ceilings in New Pre-K rooms
- Currently working on spackling and framing rooms 106, 106A, and 105
- Currently working on erecting steel for the new addition

#### Bana Electrical:

- Completed new lights in 2 New pre-k rooms
- Completed electrical work accommodating for the new steel in the basement
- Working on completing electrical conduit for the new gym

#### D & S Mechanical:

- Working on connecting new equipment with DDC controls

#### WHM Plumbing:

- Completed plumbing work accommodating for the new steel in the basement
- Working on plumbing elements at the addition

#### Belfor:


- Work is complete

### **Work in room 106/ 106A:**



GREENPORT SCHOOL PROJECT-A, B & C

**Work in room 106A Bathroom:**

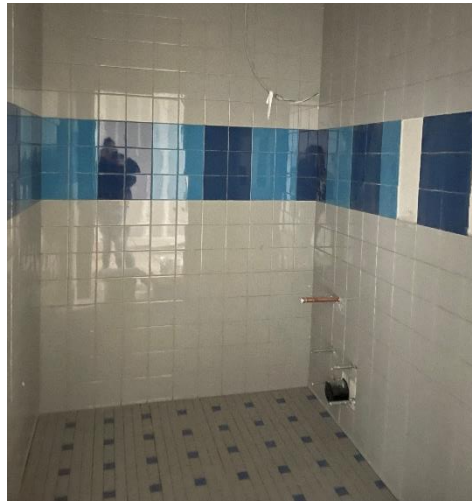

**Work in room CR-19 CR-20 New pre-k rooms:**



**GREENPORT SCHOOL PROJECT-A, B & C**  
**Work at New Gym addition:**



GREENPORT UNION FREE SCHOOL DISTRICT

DATES: 11/3/2022-1/12/2023

## GREENPORT SCHOOL PROJECT-A, B & C

