




2023 BOND

MAJOR PROJECTS UPDATE

DECEMBER 2024



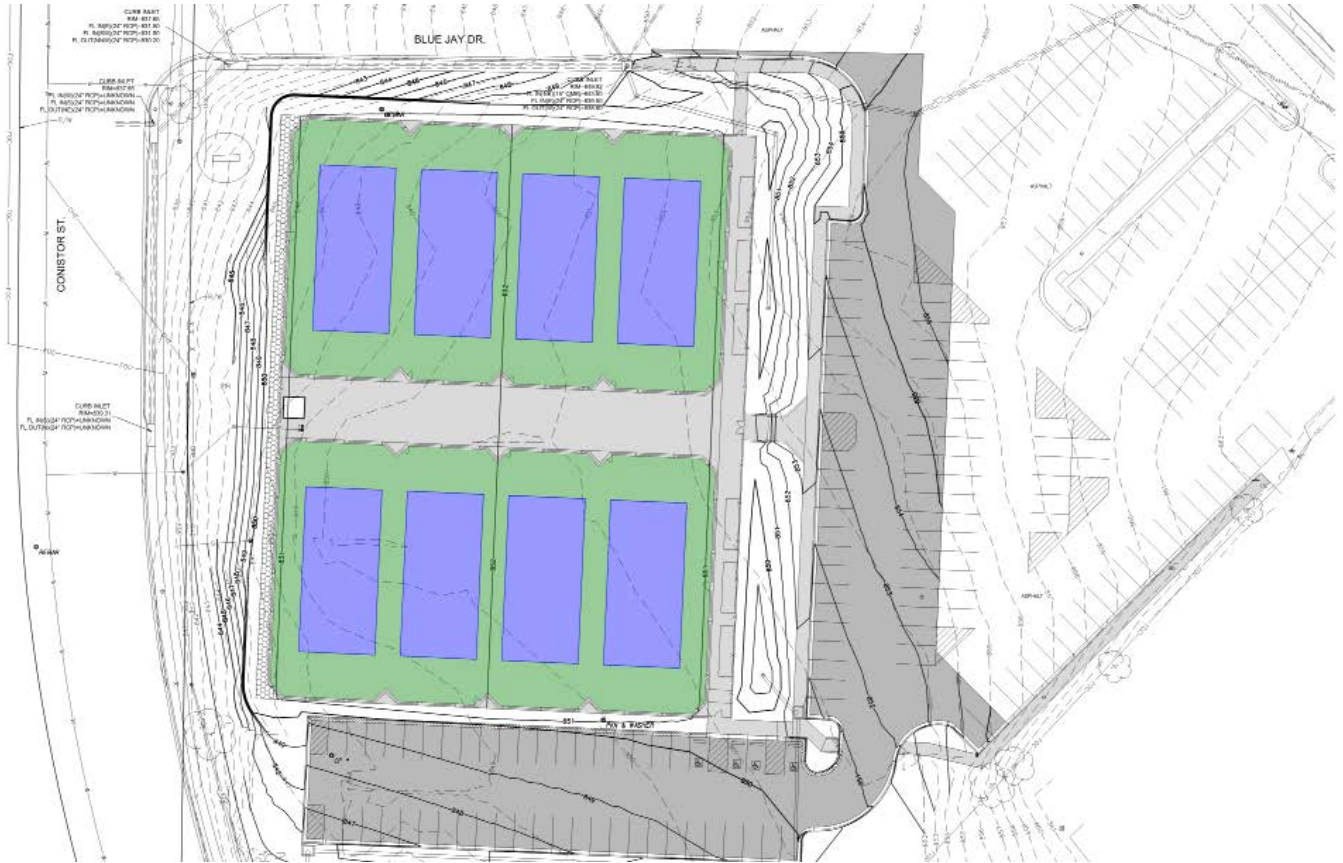

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

UPCOMING

Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North


WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

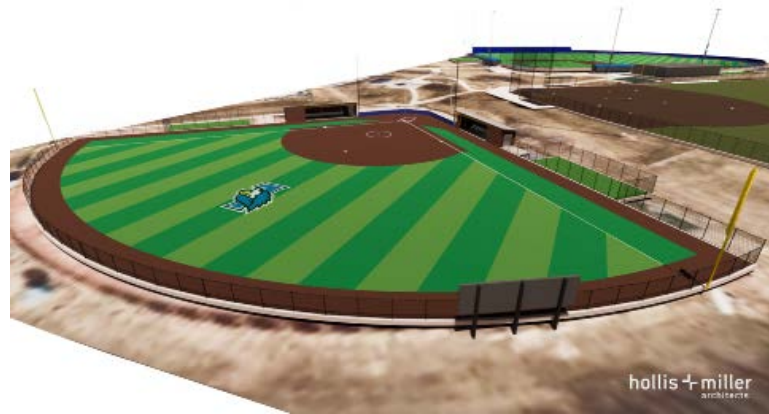

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024



Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

**WEEKLY
PROGRESS
REPORT**

LPS Ball Fields 08/09/2024

Liberty Public Schools



PROJECT STATUS

- LNHS
- Punch List Completion
 - Final Inspection Passed

- LHS
- Punch List Completion
 - Retaining Wall Ongoing
 - Final Sod Ongoing

UPCOMING

- LHS
- City Inspection

Project Completion
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

PROJECT STATUS

South Valley MS - Upgrades Complete
Discovery MS - Upgrades Complete
EPiC Elementary - Upgrades Complete
Liberty North High School - Upgrades Ongoing

UPCOMING

Energy Inspections - All Four Schools
Emergency LED Fixtures

Project Completion
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

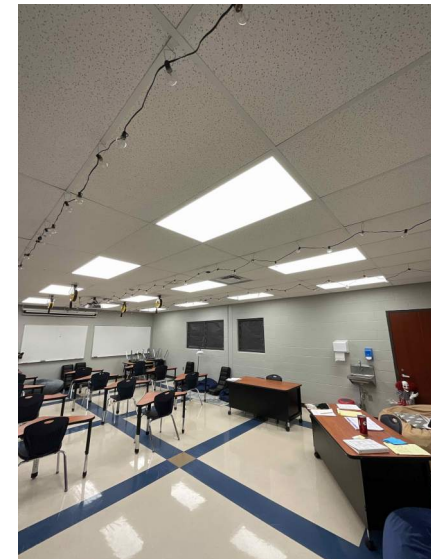

Liberty North HS

PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


UPCOMING

Energy Inspections All Four Schools
Emergency LED Fixtures

Project Completion
December 2023

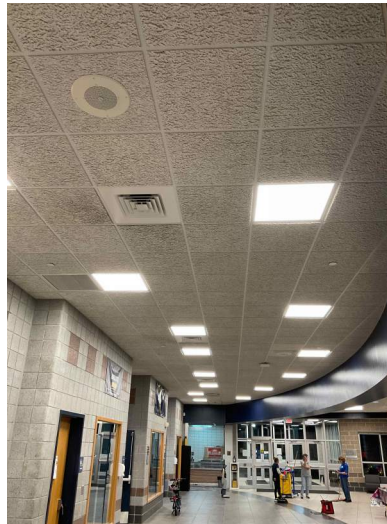


South Valley Middle School

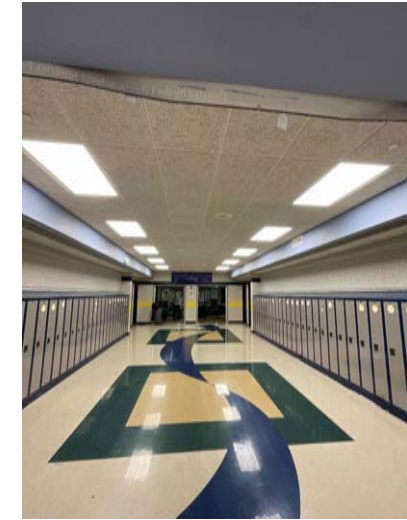

South Valley Middle School



Discovery Middle School

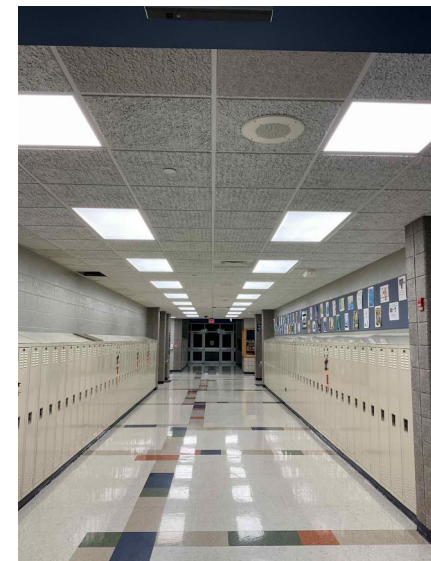

Discovery Middle School

WEEKLY PROGRESS REPORT



Epic Elementary



Epic Elementary



Liberty North High School




Liberty North High School



EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

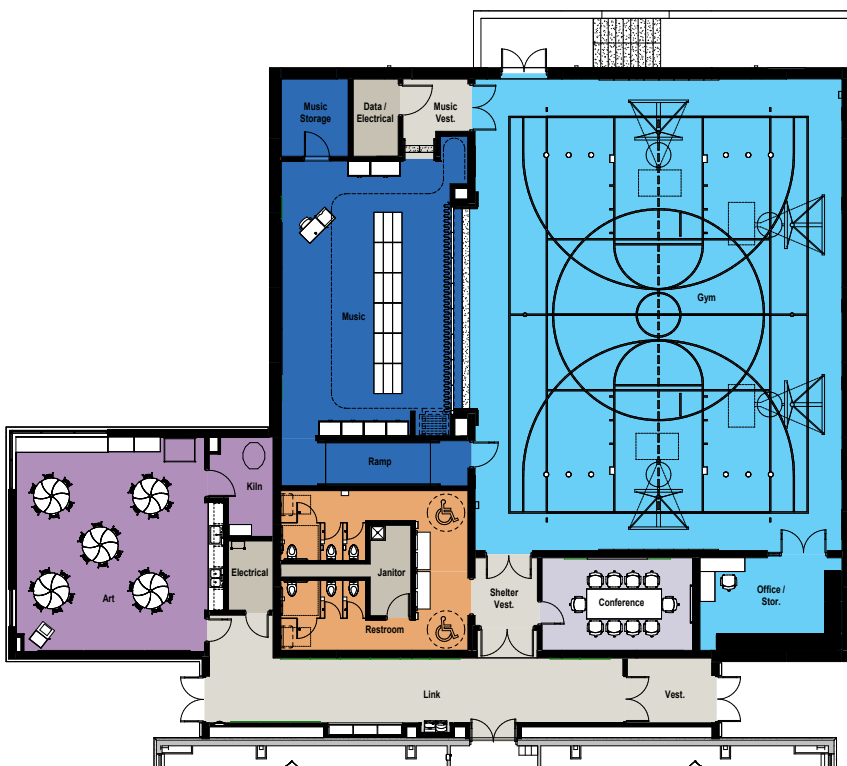

▲ Addition



▲ Renovation Area

PROJECT STATUS

- EPiC Elementary
- Metal Panels
 - Pre-cast joint sealants
 - Ceiling/Wall tectum panels complete
 - North gym retaining wall complete
 - Art room sheet rock complete
 - RTU hook up complete
 - Art room windows and exterior doors complete
 - Stage curtain rigging ongoing
 - Painting ongoing

UPCOMING

- EPiC Elementary
- All epoxy flooring
 - Dryfall gym ceiling
 - Art room ceiling grid
 - Casework/Marker boards/Solid surface
 - Install of gym equipment
 - MEP OH finish fixtures

Project Completion
EPiC February 2025




EPiC Elementary - Metal Panels



EPiC Elementary - N. Retaining Wall



EPiC Elementary

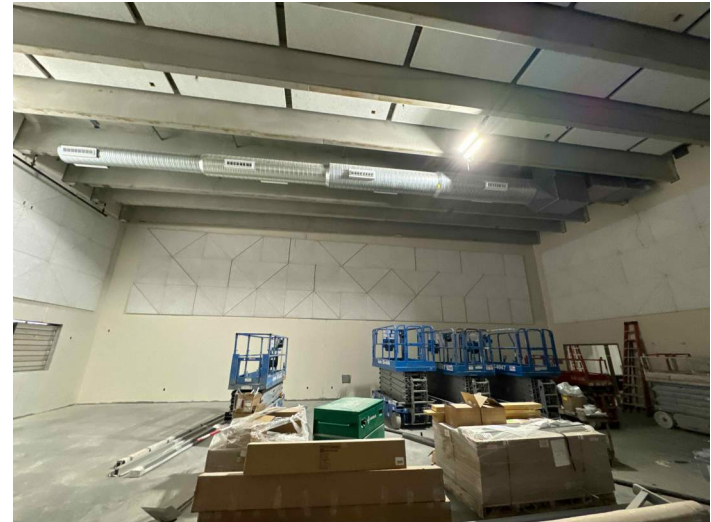



EPiC Elementary - Gym Tectum



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

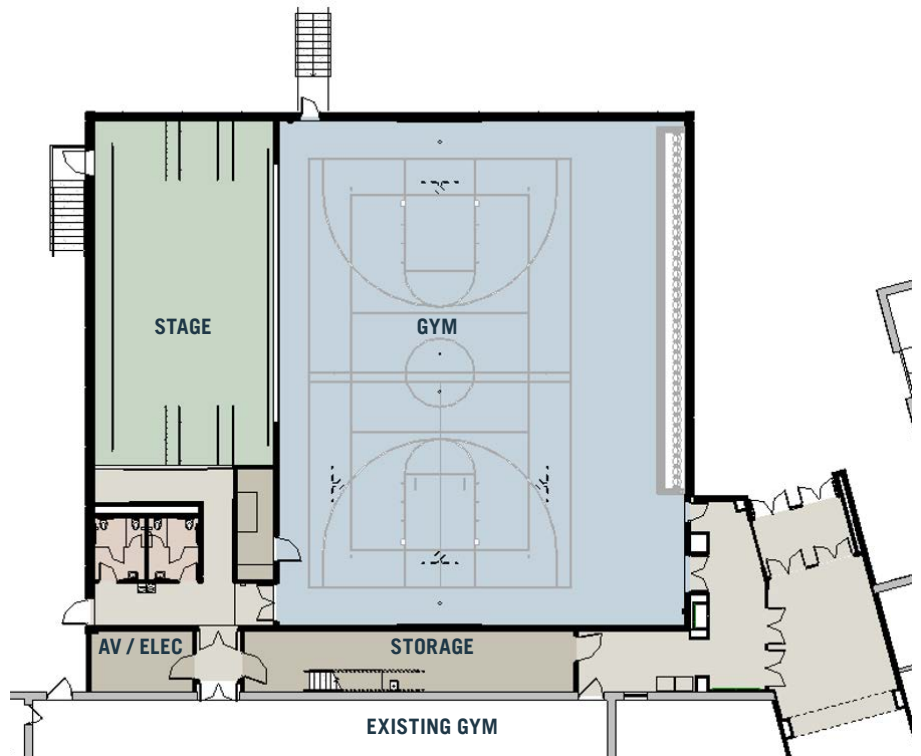

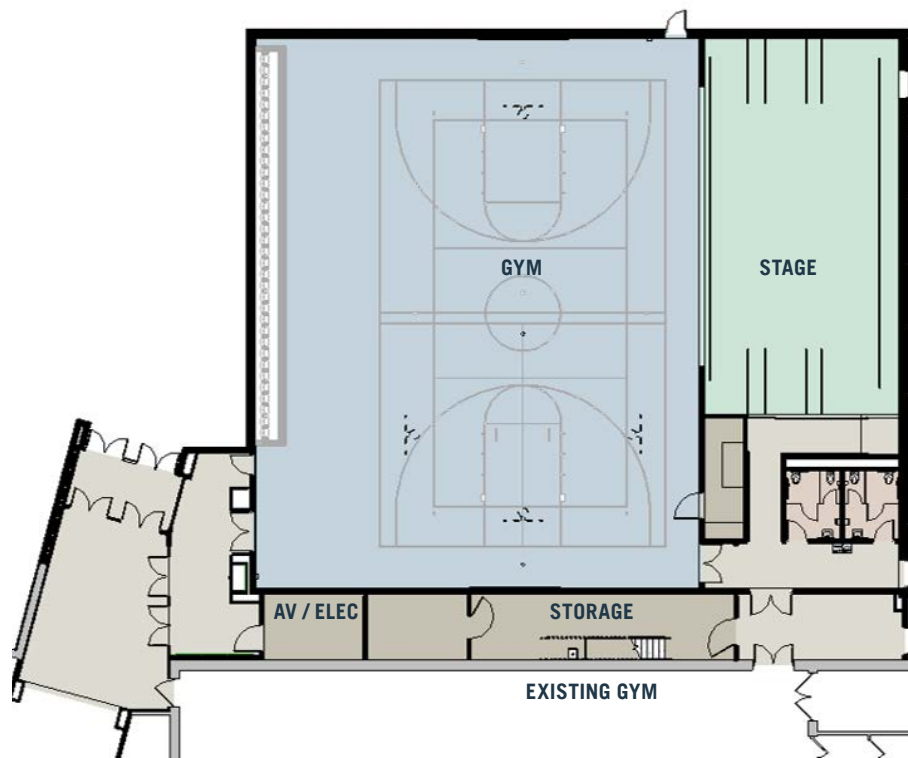

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

PROJECT STATUS

SVMS and DMS

- Interior CMU on-going
- SVMS roofing on-going
- Waterproofing ongoing
- Theater SOG ongoing
- Pre-cast leave out panels complete
- Soffit framing complete

UPCOMING

SVMS and DMS

- Bathroom ceiling framing
- Windows and exterior doors
- Metal Panels
- DMS roofing
- Hang MDF board

Project Completion

DMS&SVMS June 2025



SVMS - Pre-cast panel leave out install



SVMS - Gym Roofing



DMS - Pre-cast leave out panels installed



Theater SOG Prep



hollis + miller



hollis + miller



hollis + miller



hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



WEEKLY
PROGRESS
REPORT

Distribution Center 12/6/24

Liberty Public Schools



12/6/24

PROJECT STATUS

- Garage door complete
- Window installation ongoing
- Drywall ongoing
- Paint ongoing
- Freezer detailing ongoing
- Generator Set
- East lot curb completed

UPCOMING

- Trash enclosure railing
- Dock levelers
- Canopy west framing
- East lot paving
- Tile

Project Completion
June 2025



East Lot/Generator Set



East Lot Construction



Overall Site




Garage Doors



Dry Storage



Break Room

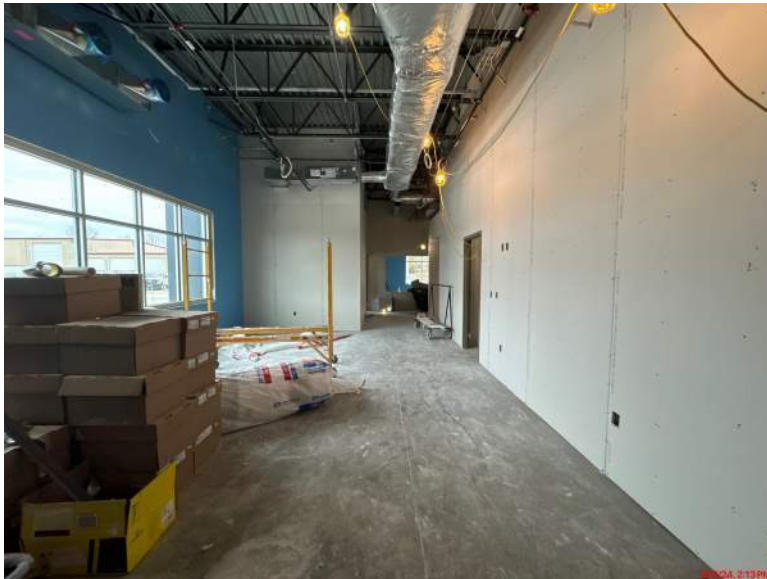

Workstation



Mezzanine

**WEEKLY
PROGRESS
REPORT**

District Tech Center 7/12/24

Liberty Public Schools



7/12/24

PROJECT STATUS

- District Technology Center:
- Completed Communications Install
 - Completed Interior Paint
 - Completed All Exterior Paint
 - Completed Floor Install
 - Completed Data Pod Install
 - Completed HVAC Equipment Install
 - Completed Landscaping/Fence Install
 - Completed Generator Install
 - Certificate of Occupancy - Received July 9th

UPCOMING

- District Technology Center:
- Complete Punchlist Work
 - Complete Furniture Move In
 - Server Switchover July 13th
 - Staff Move in July 16th

Project Completion July 2024



IT Reception



Exterior



Kid's Zone Open Office



Fine Arts Open Office



Fine Arts Workshop



Restrooms



Breakroom



Data Pod Install



Exterior



Medium Conference Room



Kid's Zone Storage



IT Open Office



LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
 - Integrated SPED resources
 - Renovated cafeteria & scramble
 - Restroom renovations
- Exterior masonry repair & window replacement
 - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

**WEEKLY
PROGRESS
REPORT**

Heritage Middle School

Liberty Public Schools



12/6/24

PROJECT STATUS

Heritage Middle School
1964 Wing:

- Completed Drywall Install/Finish
- Completed Casework Install
- Completed Paint
- Completed Exterior Window Install
- Completed Ceiling Grid and Tile
- Completed Tile
- Continued Floor Install
- Continued MEP Trimout
- Began Specialty Finish Install

UPCOMING

Heritage Middle School
1964 Wing:

- Complete Flooring Install
- Complete MEP Trimout
- Complete Wheelchair Lift Install
- Complete Specialty Finish Install
- Complete Final Inspections
- Begin Punchlist Work
- Begin Owner Move In

Projected Completion: December 2024



1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress




1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress

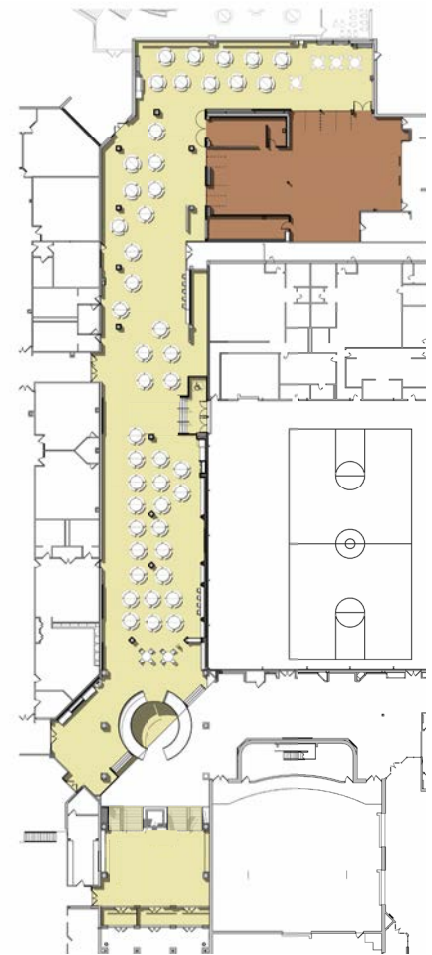

PHASE 2

Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025



PHASE 1

12/6/24

PROJECT STATUS

Liberty High School:

- Completed Paint
- Completed Casework Install
- Completed Tile Install
- Completed Flooring Install
- Completed Door and Hardware Install
- Completed Glazing Install
- Installed Specialty Finishes
- Completed Partial TCO
- Began Punchlist
- Began Owner Move In

UPCOMING

Liberty High School:

- Complete Punchlist
- Complete Owner Move In
- Final FACS Classroom Inspections

Project Completion: December 2024



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing




Progress 100's Wing



Shop Building

- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

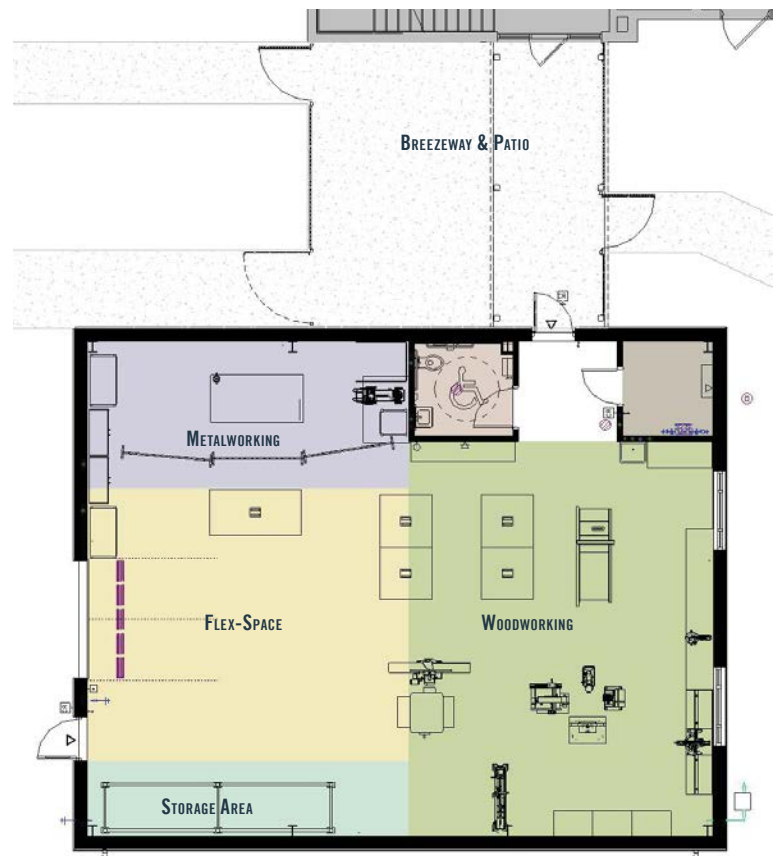

▲ Floor Plan

12/6/24

PROJECT STATUS

- PEMB ongoing
- Utilities complete
- PR04 East storm drains complete

UPCOMING

- IMP delivery 12/23
- Metal panel install
- Roofing
- Skirt wall framing
- Masonry

Project Completion
June 2025



PEMB



PEMB




PR04 Storm Drains




PR04 Storm Drains

Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:
Spring 2024–Spring 2025

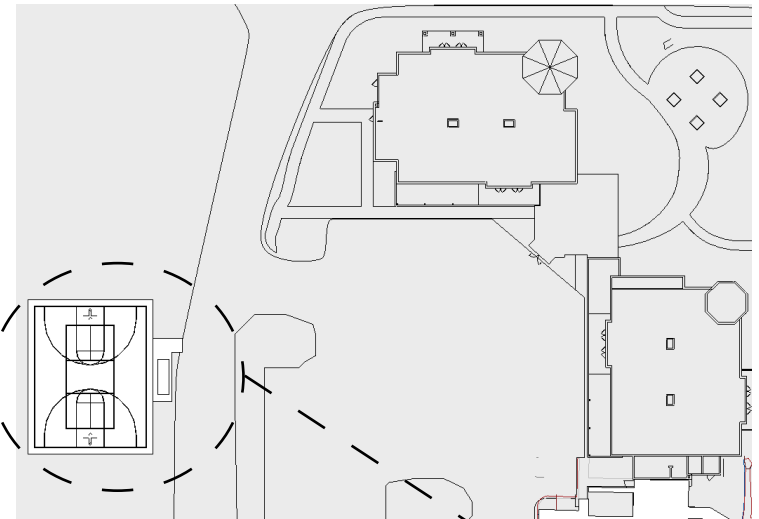


Overall Site Plan

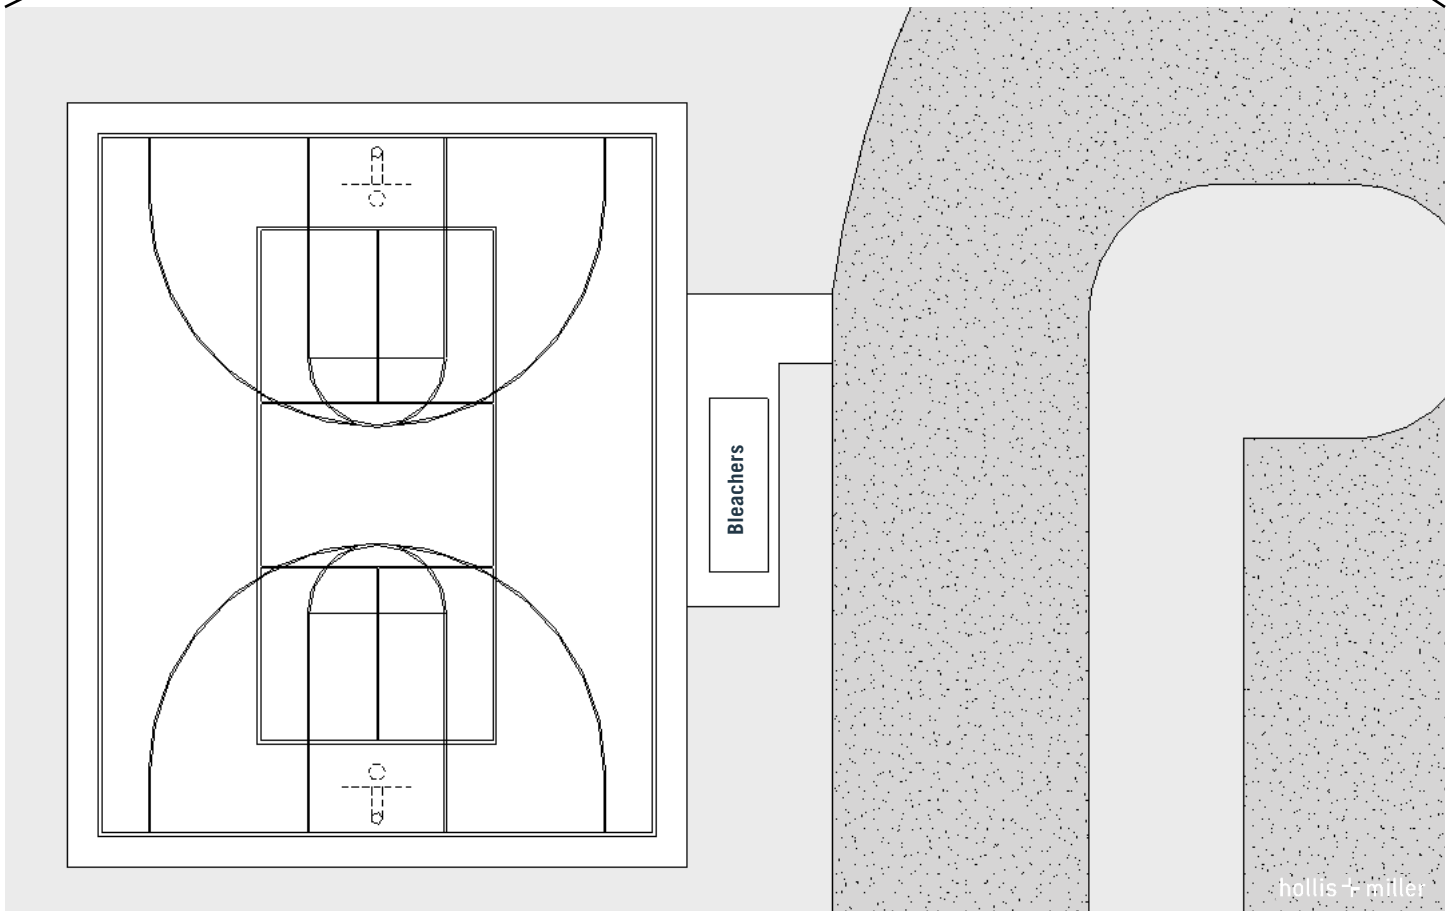

Enlarged Site Plan

Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:
May 2024 - August 2025

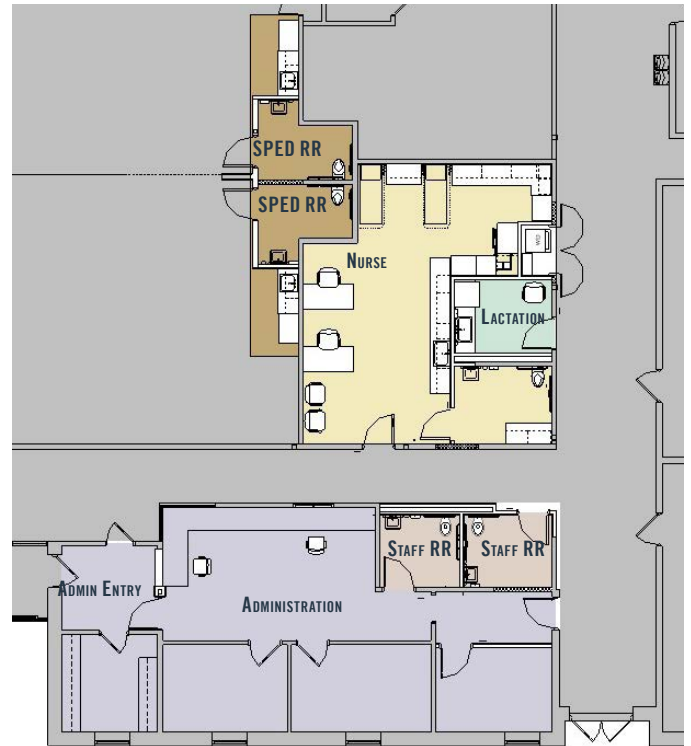

▲ Enlarged Floor Plan




▲ Overall Floor Plan

Interior Renovation

- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:
May 2024 - August 2025



Administration

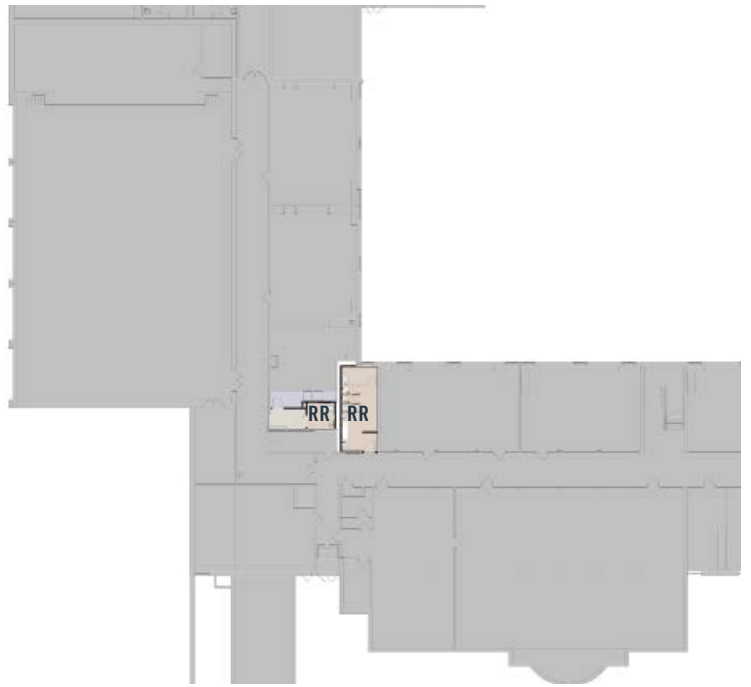

Partial First Level Floor Plan




Overall Second Level Floor Plan

Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule: May 2024 - August 2025



Administration

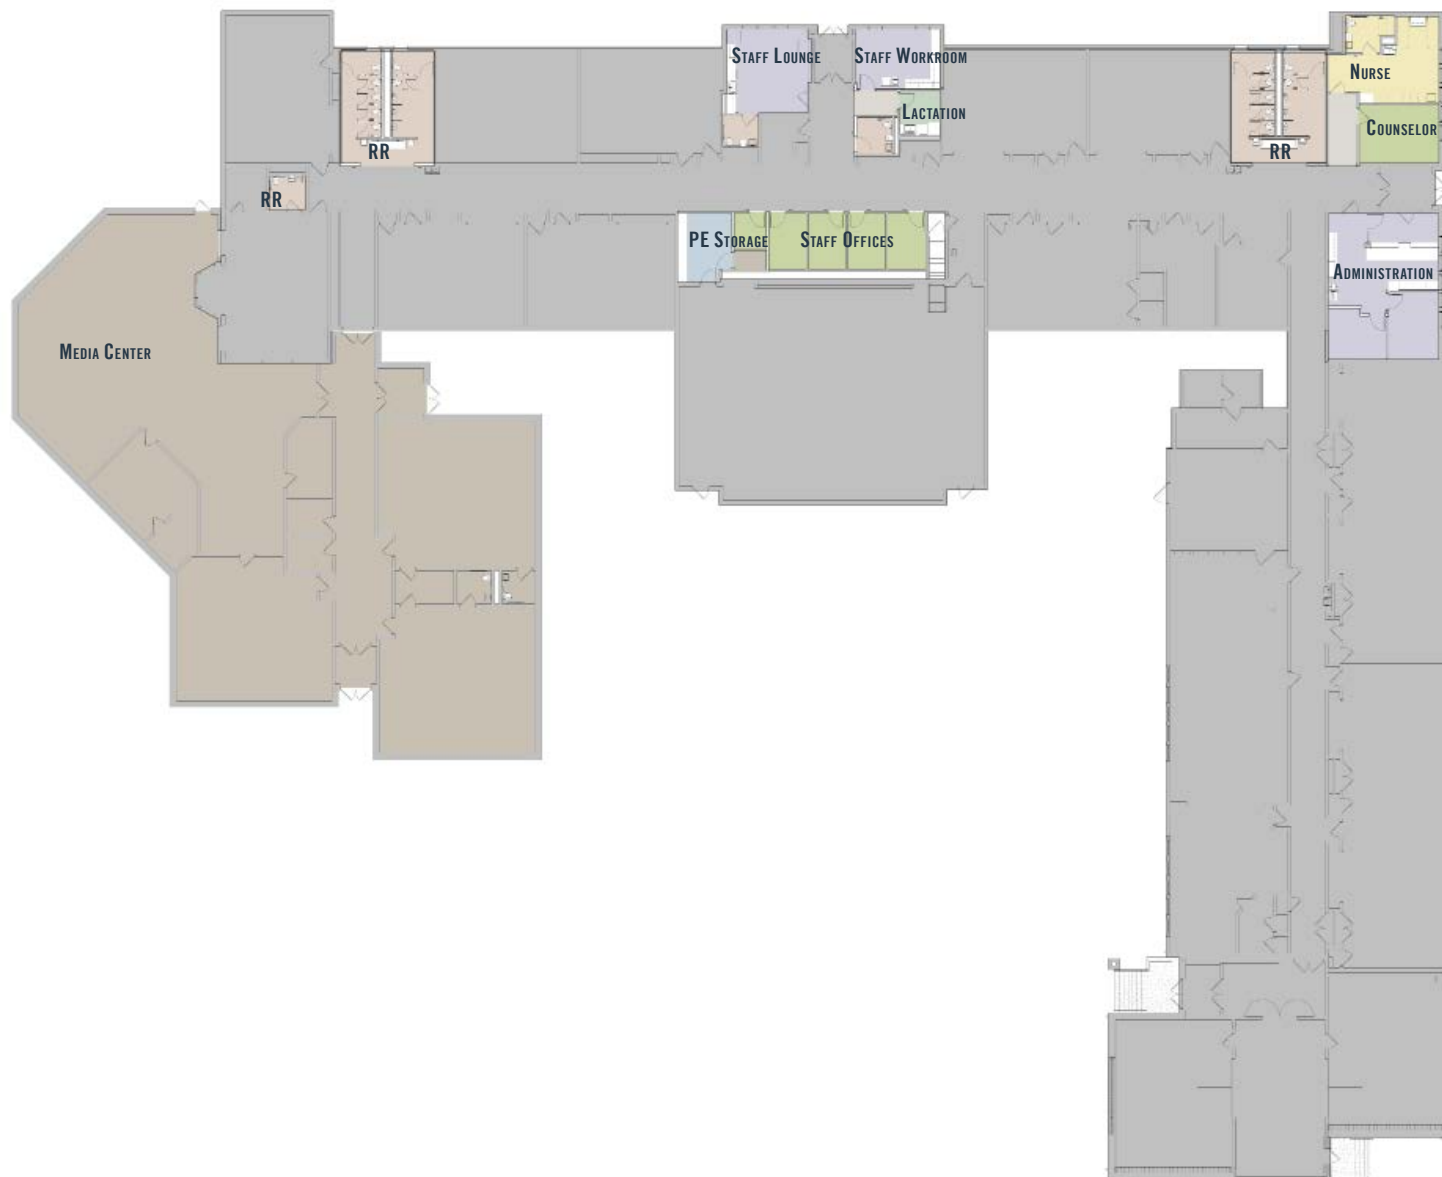

Overall Floor Plan

**WEEKLY
PROGRESS
REPORT**

**Doniphan, Franklin, and Ridgeview
Summer Renovation Projects
Liberty Public Schools**



8/9/24

PROJECT STATUS

- Doniphan, Franklin, and Ridgeview:
- Completed MEP Install
 - Completed Drywall Install
 - Completed Ceiling Grid Install
 - Completed Paint
 - Completed Tile
 - Completed Casework Install
 - Completed Flooring Install
 - Completed Epoxy Install
 - Completed Specialties Install
 - Began Punch List Work

UPCOMING

- Doniphan, Franklin, and Ridgeview:
- Complete Punch List Work
 - Complete Final Inspections
 - Furniture Move-In

Project Completion: August 2024



Franklin - Main Office



Franklin - Restrooms



Franklin - Workroom



Ridgeview - Level 2 Restroom



Ridgeview - Main Office



Doniphan - Main Office



Doniphan - Assistant Principal Office



Doniphan - Teacher's Lounge
