

Building Capacity | Sustaining Success

Operations Board Report

January 14, 2025



East Lake Elementary School

OCSD – East Lake Elementary

WEEK OF January 3rd , 2025



SAFETY

Incidents to Date	1
First Aids to Date	2



SCHEDULE MILESTONES



WEATHER

Working Days	4
Weather Days	0
Activities Delayed	0



MANPOWER

Number of Trades	8
Average Workers (per day)	49

TOP ACTIVITIES THIS WEEK

- OSF Inspection
- Installation of Clouds in the Rotunda
- Completed Furniture Install
- Continued Final Paint
- Continued Final Cleaning
- Continued Punch List
- Ribbon Cutting Ceremony

UPCOMING ACTIVITIES

East Lake Elementary School

OCSD – East Lake Elementary

WEEK OF December 20th , 2024



SAFETY

Incidents to Date	1
First Aids to Date	2



SCHEDULE MILESTONES



WEATHER

Working Days	5
Weather Days	0
Activities Delayed	0



MANPOWER

Number of Trades	8
Average Workers (per day)	65

TOP ACTIVITIES THIS WEEK

- Continue Furniture Install
- Finish Flooring
- Continue Final Paint
- Continue Striping, and Signage
- Continue Punch List
- Fire Marshall Inspection
- Continued Irrigation


UPCOMING ACTIVITIES

- Continue Furniture Install
- Finish Flooring
- Continue Final Paint
- Continue Striping, and Signage
- Continue Punch List

East Lake Elementary School

OCSD – East Lake Elementary

WEEK OF December 27th , 2024

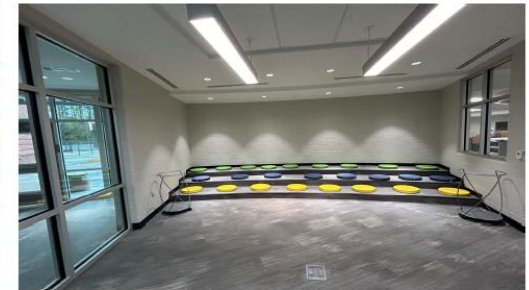

SAFETY

Incidents to Date	1
First Aids to Date	2



SCHEDULE MILESTONES



WEATHER

Working Days	4
Weather Days	2
Activities Delayed	0



MANPOWER

Number of Trades	8
Average Workers (per day)	49

TOP ACTIVITIES THIS WEEK

- Continued Furniture Install
- Continued Final Paint
- Continued Punch List
- Install flooring in Gym/ Rotunda Area
- Elevator Inspection

UPCOMING ACTIVITIES

- Continue Punch List
- Elevator Inspection

Orangeburg-Wilkinson High School

SAFETY

Incidents to Date	#0
First Aids to Date	#0

WEATHER

Working Days	#160
Weather Days	#29
Activities Delayed	#2

MANPOWER

Number of Trades	#7
Average Workers	#110


SCHEDULE MILESTONES

Top Activities This Week

- Masonry walls in the gym continue.
- The segmented retaining wall by the practice fields is roughly 80% complete.
- Electrical and plumbing underground in area A1 and D continues.
- SOG at E1 and B was poured.
- The main plumbing line for the field house was installed.
- Site work continues.
- Backfill at areas C and A2 continues.

Upcoming Activities

- SOG in C and A2 will be poured
- Foundations for the field house will begin.
- Front parking lot curb/gutter will start.
- Masonry in the cafeteria and build B will start.

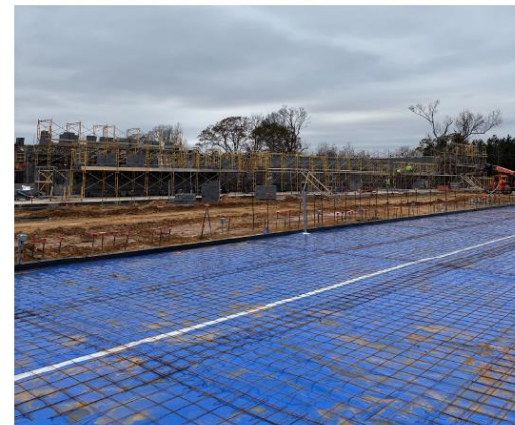

Orangeburg-Wilkinson High School

SAFETY

Incidents to Date	#0
First Aids to Date	#0

WEATHER

Working Days	#167
Weather Days	#29
Activities Delayed	#2

MANPOWER

Number of Trades	#6
Average Workers	#76

SCHEDULE MILESTONES

Top Activities This Week

- Masonry walls in the cafeteria and area B began.
- The segmented retaining wall by the practice fields is nearly complete.
- Underground plumbing in D was completed.
- SOG at A1 & A2 was poured.
- Cleaning of detention ponds and site grading continues.
- Electrical, HVAC and plumbing in-wall rough in continues with masonry.

Upcoming Activities

- SOG in C and A1 will be poured.
- Foundations for the field house will begin.
- Front parking lot curb/gutter will start.
- Box culverts at the rear entrance will be installed.

