



Facilities Referendum Progress Update

School District of Jefferson

August 26, 2024 | Board Meeting

Framing our future facilities

Agenda

- 1 Construction Progress Updates
- 2 What's Coming Up?
- 3 Questions


01

Construction Progress Updates

Framing our future facilities.

Schedule

We are here

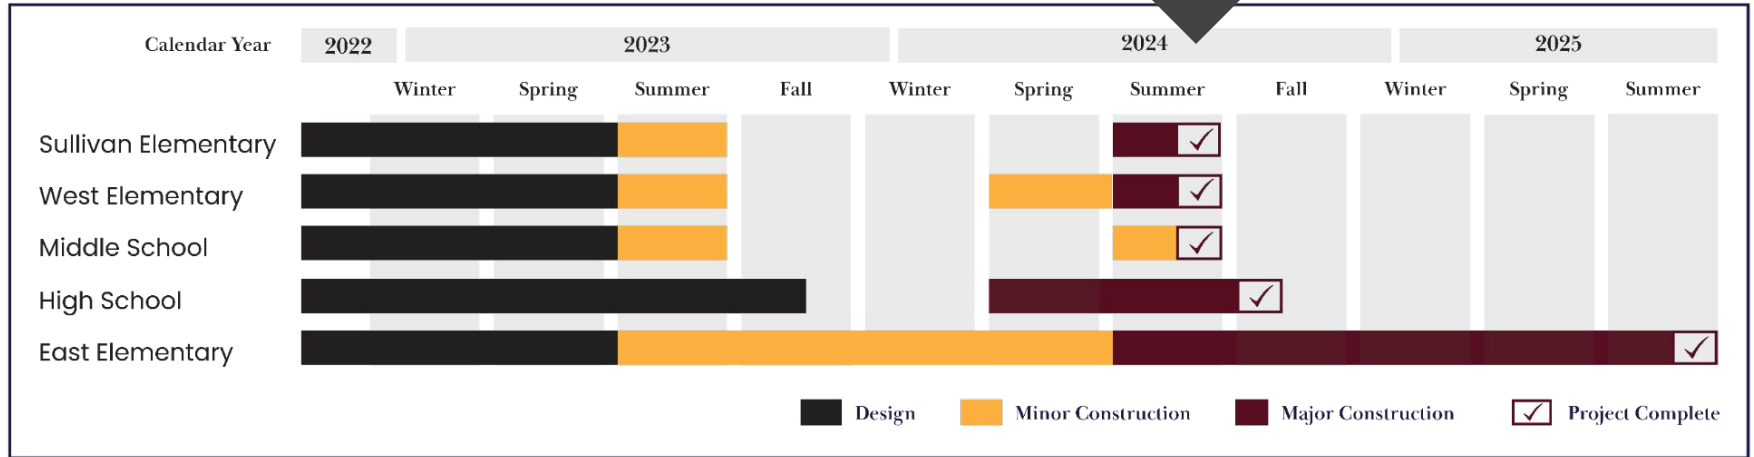


Progress Update | Sullivan Elementary

- Work completed:
 - Secure entry reconfiguration and renovations
 - Main office and reception reconfiguration and renovations
 - Main restroom renovations
- Construction at Sullivan is complete!



Progress Update | Sullivan Elementary

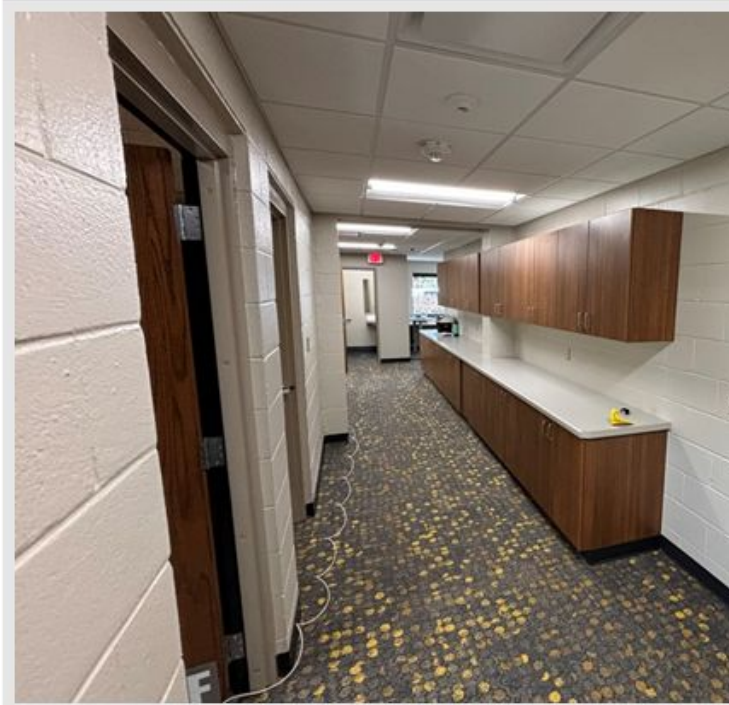

Progress Update | West Elementary


- Work completed:
 - Restroom renovations
 - Library renovations
 - Classroom ceiling and casework replacement in west wing classrooms
 - Flooring abatement and replacement in south and west wing classrooms and corridors
- Construction complete August 30, 2024
- Summer 2025
 - Additional flooring abatement and replacement added scope



Progress Update | West Elementary



Progress Update | West Elementary

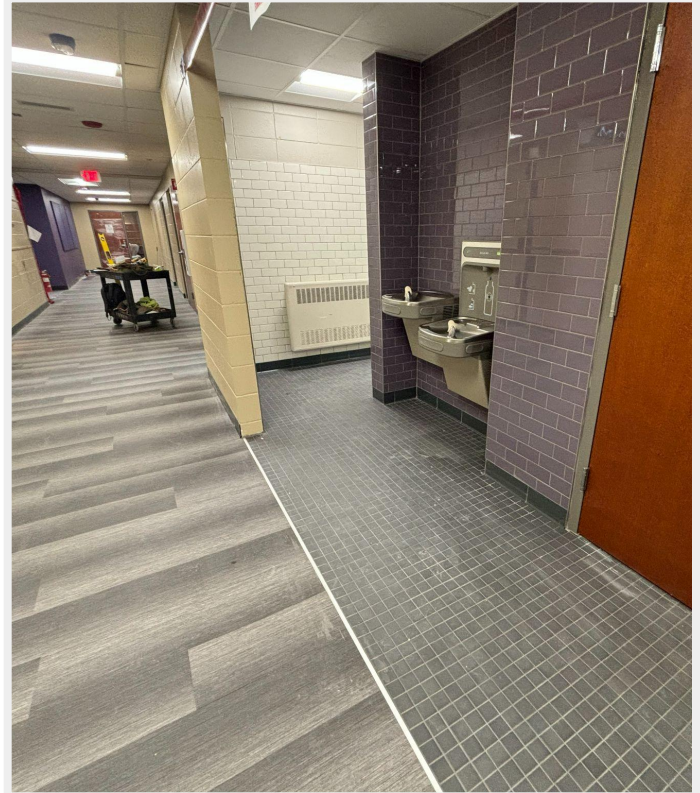

Progress Update | West Elementary





Jefferson High School

Phasing Plan: March 2024 – October 2024

PHASING SUMMARY

MAR 2024 - OCT 2024

MAR 2024 - OCT 2024

MAR 2024 - AUG 2024

JUN 2024 - AUG 2024



JUN 2024 - OCT 2024



PAC HVAC
Renovations:
BEGIN JUN 2024
COMPLETE AUG 2024

Progress Update | High School


- Work completed:
 - Classroom, Food Lab and Ag Shop renovations complete!
 - PAC air handling units installed and operational
- Upcoming work:
 - Equipment move-in and MEPF connections in Auto/Metal/Wood Shops & Test Kitchen beginning 8/26
 - Skills Lab painting and finishes
- Construction complete October 11, 2024

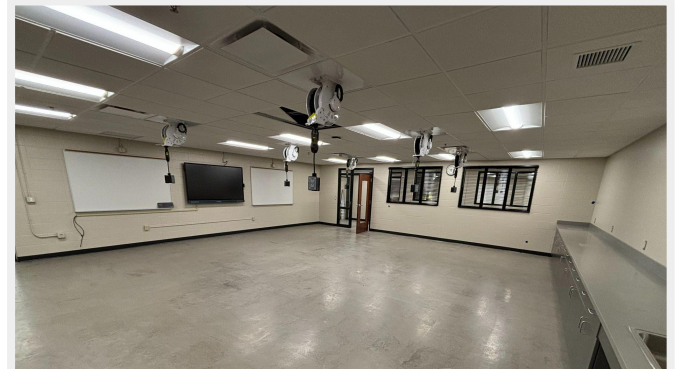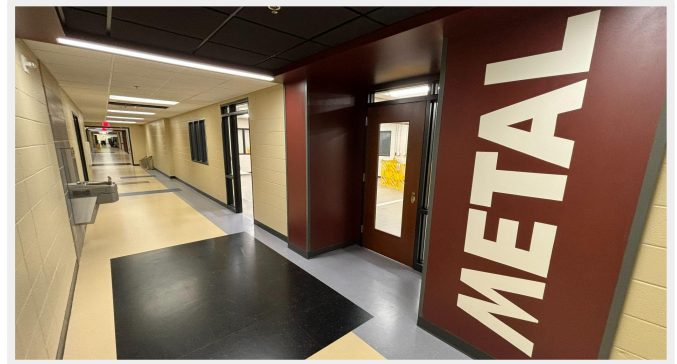

Progress Update | High School



Progress Update | High School

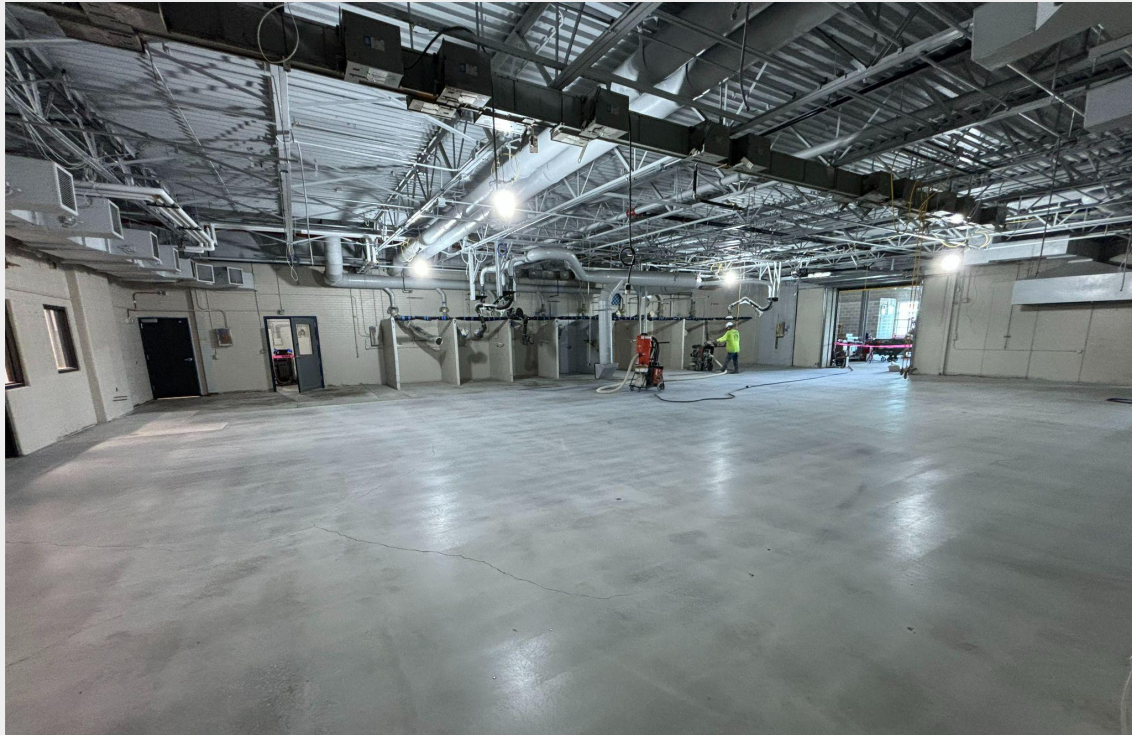

Progress Update | High School





Jefferson East Elementary

Phasing Plan: June 2024 – January 2025 additional phases begin Jan 2025

PHASING SUMMARY

1



JUN 2024 - AUG 2024

2

JUL 2024 - OCT 2024

3

OCT 2024 - JAN 2025

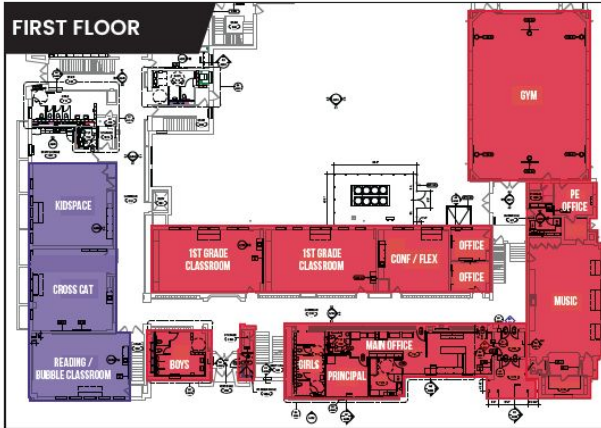

FEB 2024 - AUG 2025

Construction materials
and equipment area

Beginning
March 2024,
the entire building,
regardless of phase,
will not have ceilings.

Progress Update | East Elementary

- Work completed:
 - Phase 1 classroom renovations
 - Main office & secure entry re-configuration and renovations
 - Phase 1 restroom renovations
 - Gym ceiling
- Upcoming work:
 - Phase 2 classroom renovations
 - Phase 3 classroom renovations
 - Additional renovation phases
- Construction complete September 2025

Progress Update | East Elementary – Interior



Progress Update | East Elementary – Interior



Progress Update | East Elementary – Interior



Progress Update | East Elementary – Exterior



02

What's Coming Up?

Framing our future facilities.

Upcoming Dates

- **September 5, 2024:**
Elementary School Project Celebrations
5:00 p.m. - East Elementary (phase 1)
5:45 p.m. - West Elementary
6:45 p.m. - Sullivan Elementary
- **October 24, 2024:**
High School Project Celebration



Questions?

Framing our future facilities.
