

Measure BB Bond

21st Century Classroom Improvements
February 27, 2025




CUMMING
GROUP

//////////////////// BUILDING VALUE THROUGH EXPERTISE



HLPUSD MEASURE BB - SUMMARY

SCHOOLS IN PROGRESS



IN PROGRESS CONSTRUCTION

- California ES
- Baldwin ES
- Los Molinos ES
- Grazide ES (Pending)

OUT TO BID 2-11-2025

- Kwis ES
- Fairgrove K-8
- Lassalette ES
- Sierra Vista MS

AT DSA FOR REVIEW

- Palm ES
- Valinda ES
- Sparks ES
- Wing Lane ES
- Valley Alternative

IN DESIGN

- Orange Grove MS




COMPLETED

- Nelson ES
- Los Altos ES
- Workman ES
- Mesa Robles K-8
- Cedarlane K-8
- Sparks MS
- Grandview MS
- Newton MS
- Stimson EC
- Workman HS
- La Puente HS
- Wilson HS
- Los Altos HS

PHASE B PROGRESS

	PROJECT STARTS	CONSTRUCTION DOCUMENTS TO DSA	DSA PLAN REVIEWS COMPLETED	PROJECTS BID	CONSTRUCTION STARTS (COMPLETED*)
La Puente HS Refresh	●	NA	NA	●	●*
Los Altos HS Refresh	●	NA	NA	●	●*
Wilson HS Refresh	●	NA	NA	●	●*
Workman HS Refresh	●	NA	NA	●	●*
Stimson LC Refresh	●	NA	NA	●	●*
Baldwin ES	●	●	●	●	●
California ES	●	●	●	●	●
Grazide ES	●	●	●	●	·
Los Molinos	●	●	●	●	●
Kwis ES	●	●	●	●	·
Lassalette ES	●	●	●	●	·
Fairgrove Academy	●	●	●	●	·
Sierra Vista MS	●	●	●	●	·
Sparks ES	●	●	·	·	·
Palm ES	●	●	●	·	·
Valinda ES	●	●	●	·	·
Wing Lane ES	●	●	·	·	·
Valley Alternative School	●	●	·	·	·
Orange Grove	●	·	·	·	·


HIGH SCHOOL REFRESH GROUP 2

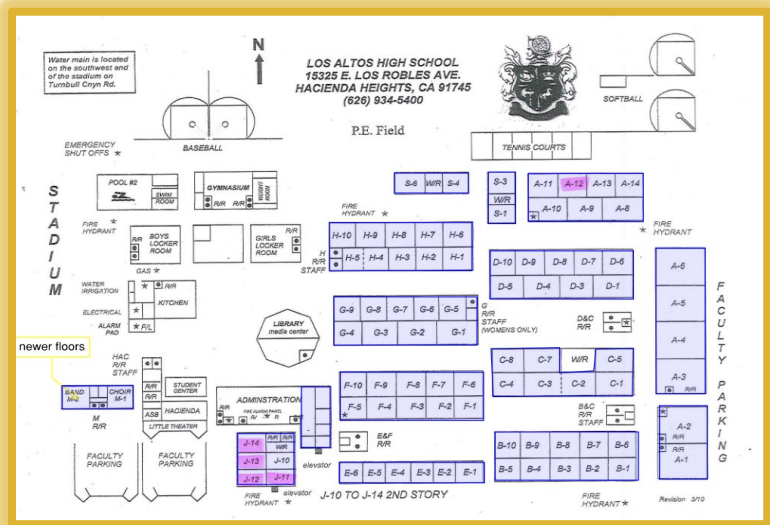

LOS ALTOS HIGH SCHOOL 69 CLASSROOMS

SCHOOL	START DATE	ANTICIPATED COMPLETION DATE
WILSON HS	3/4/2024	Completed 48 days Ahead of Schedule
LOS ALTOS HS	3/4/2024	Completed 65 Days Ahead of Schedule

Measure BB 21st Century
Classroom Improvements
Baldwin Academy Phase 1

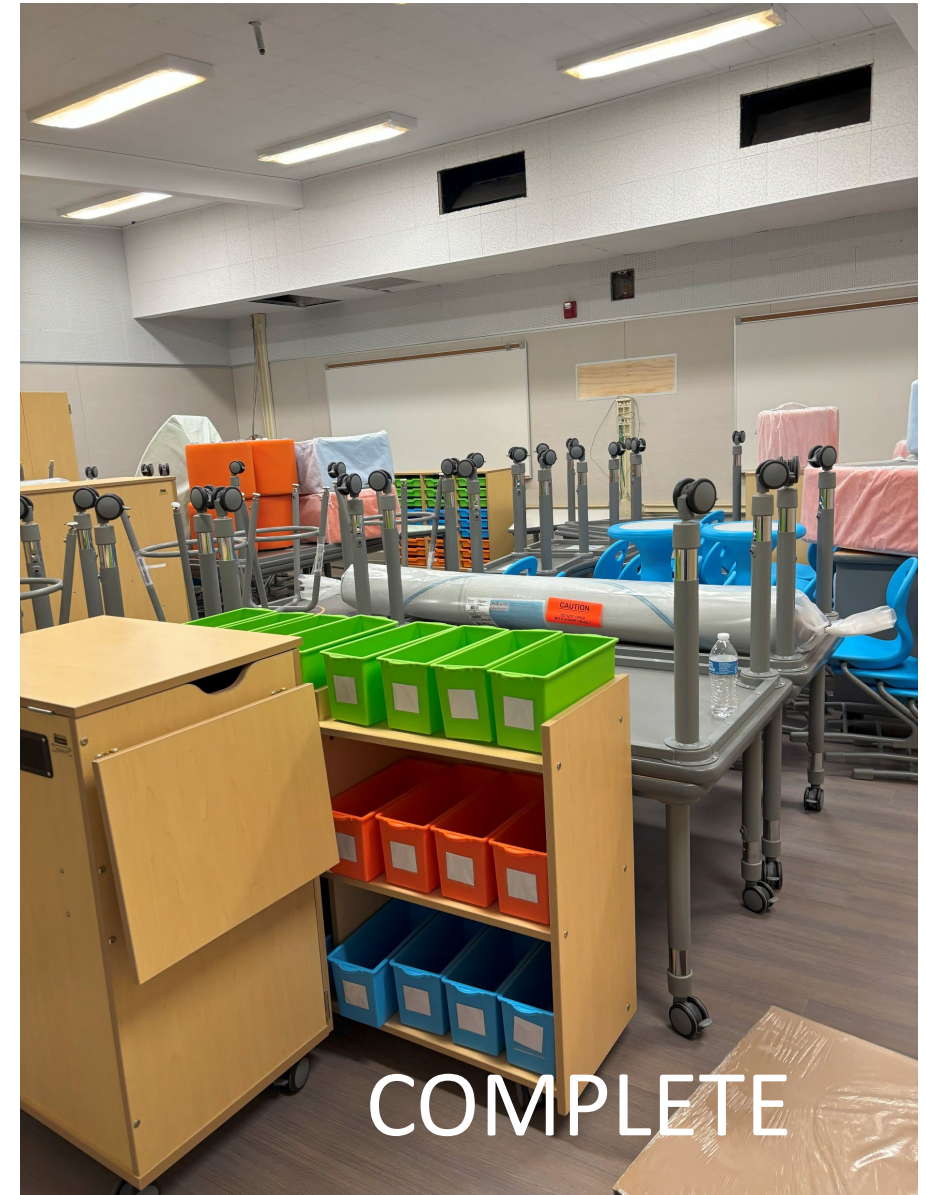

Measure BB 21st Century
Classroom Improvements
California Elementary School
Phase 1



COMPLETE



FURNITURE DELIVERY

Measure BB 21st Century
Classroom Improvements
Los Molinos Elementary Phase 1





QUESTIONS
