




Update on FCPS Construction / Renovation Projects

March 24, 2025

Mary E. Britton Middle School

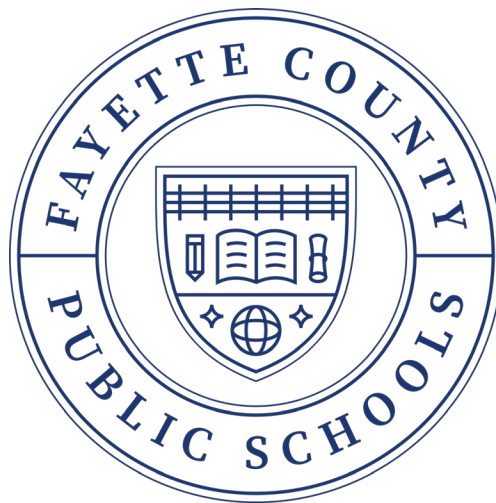

Mary E. Britton Middle School



➤ Architect:

JRA Architects

➤ General Contractor:

Rising Sun Developing Co.

➤ GC Contract Sum:

\$69,964,000.00

➤ Total Project Cost:

\$82,680,000.00

➤ Change Orders to Date (9):

\$126,716.97

Mary E. Britton Middle School




➤ **Completed/Work in Progress:**

- Finished glass on entries at Areas B, C, E/F, Cafeteria (excluding doors) Area A completed.
- All terrazzo poured except logos and few makeups in entry ways.
- Finished Kitchen lighting.
- Overhead electrical inspection complete in Media Center.
- Finished vertical panel to MCM panel connections.
- Finished metal studs Cafeteria. (All sheetrock complete besides center soffit).
- Kitchen equipment install (98%). Awaiting a couple stainless chases.
- Gym floor wood complete. Continuing work on finish.
- Finished Gym pad install. (Some removed for completion of cutouts).
- Installation of all interior handrails complete. Finish work continued.

➤ **Upcoming Work/Look Ahead:**

- Complete exterior louver install.
- Rough grading at entrance.
- Finish unit start-ups throughout.
- Start building clean in Area A.
- Finish sod.
- Small Canopy Panels when available.
- Install Solid Surface sills.
- Complete casework install and building lettering.

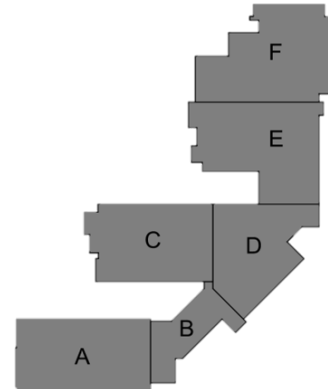

Mary E. Britton Middle School



Site – Sod Continues Around Building



Week Ending March 14, 2025

Mary E. Britton Middle School



Site – Art Courtyard



Mary E. Britton Middle School



Building Signage has Started



Mary E. Britton Middle School



Area A – Window Sills Installed



Mary E. Britton Middle School



Area D – Wood Ceiling Installed



Week Ending March 14, 2025

Mary E. Britton Middle School



Area A – Cafeteria Window Glass



Mary E. Britton Middle School



Area E – Music Room Ceiling Grid



Mary E. Britton Middle School



Area F – Gym Wall Pads



The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



- Architect:
EOP Architects
- General Contractor:
D.W. Wilburn Inc.
- GC Contract Sum:
\$50,700,288.00
- Total Project Cost:
\$64,712,240.00
- Change Orders to Date (13):
\$1,417,561.62

The Hub for Innovative Learning & Leadership (The HILL)



➤ **Completed Work:**

- All concrete curbs, all fence posts, and 60% of fence installed.
- Canopy - metal roof panels continued.
- Metal stud and drywall is 99% complete.
- Doors and hardware – continued punch list.
- Kitchen hoods certified.

➤ **Upcoming Work/Look Ahead:**

- Site landscaping to continue, concrete and fencing to complete
- Canopy – to complete pending weather
- Doors and hardware – continue punch list work
- Kitchen – continue punch list work
- Mech/Elec/Plumb – obtain final certificates and perform testing.

The Hub for Innovative Learning & Leadership (The HILL)



Walk Off Carpet at West Entry



Week Ending March 14, 2025

The Hub for Innovative Learning & Leadership (The HILL)



Building Plaque



The Hub for Innovative Learning & Leadership (The HILL)



Automotive Lifts on Site



The Hub for Innovative Learning & Leadership (The HILL)



Exterior Railing Installation getting ready to start



Week Ending March 14, 2025

The Hub for Innovative Learning & Leadership (The HILL)



Metal Panels for Column Surrounds on Site



Week Ending March 14, 2025

The Hub for Innovative Learning & Leadership (The HILL)



Stone being Installed in Site Elements



Week Ending March 14, 2025

The Hub for Innovative Learning & Leadership (The HILL)



Grading at Planters Progressing



Week Ending March 14, 2025

The Hub for Innovative Learning & Leadership (The HILL)



Overall Shot of Level 2 at Multi Purpose / Elevator



Week Ending March 14, 2025

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



- Architect:
Ross Tarrant Architects
- General Contractor:
Momentum Construction
- GC Contract Sum:
\$3,998,400.00
- Total Project Cost:
\$4,886,547.24
- Change Orders to Date (3):
\$255,645.39

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



➤ **Completed Work:**

- First coat of paint applied.
- Fire caulking in progress.
- Exterior ceiling installation started.

➤ **Upcoming Work/Look Ahead:**

- Ceiling framing installation.
- Metal panel mockup installation.
- Continue remaining spray foam application.
- Continue painting.

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Paint Work in Progress



Week Ending March 14, 2025

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Paint Work in Progress



Week Ending March 14, 2025

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Fire Caulking in Progress



Week Ending March 14, 2025

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Exterior Ceilings in Progress



Rise STEM Academy for Girls



Rise STEM Academy for Girls



- Architect:
Ross Tarrant Architects
- General Contractor:
D.W. Wilburn, Inc.
- GC Contract Sum:
\$48,800,100.00
- Total Project Cost:
\$58,460,689.35
- Change Orders to Date (0):
\$0

Rise STEM Academy for Girls



➤ **Completed Work:**

- Continued storm system work.
- Continued slab prep and placement
- Continued ICF and masonry work.
- Continued geothermal drilling.
- Continued with underground MEP work.
- Continued kitchen and storm shelter works.
- Commencement of steel structure installation.

➤ **Upcoming Work/Look Ahead:**

- Excavation for site utilities will continue.
- Storm system work will continue.
- Slab prep and placement will continue.
- ICF work will continue.
- Masonry work will continue; base course masonry will begin.
- Geothermal drilling will continue.
- Kitchen and storm shelter works will continue.
- Steel structure installation will continue.

Rise STEM Academy for Girls



Geothermal Drilling in Progress



Week Ending March 14, 2025

Rise STEM Academy for Girls



Storm Shelter



Rise STEM Academy for Girls



Concrete Slab Work



Rise STEM Academy for Girls



CMU and Joist Work




Rise STEM Academy for Girls



Steel Structure Installation



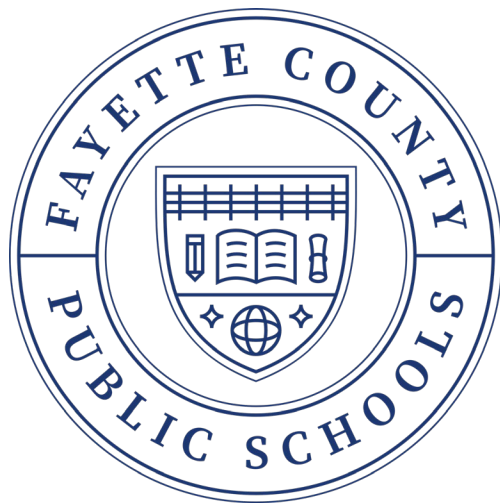

Thank you!
