




Quarterly Executive Summary Daisy Elementary Auditorium Renovations Q4 2024

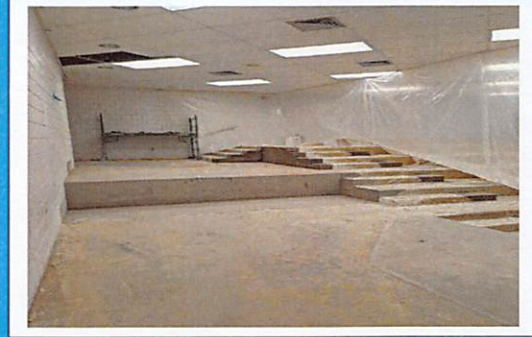

HCS Project Managers: Tricia Lemeur

Principal: Josh Todd

Design: SGA | NW, a design Company

Contractor: FBi Construction

Project Scope: Includes the addition of ADA seating, the replacement of all exterior and interior handrails, the installation of a new wheelchair lift, the upgrade of existing lighting and the renovation of two existing bathrooms, to include fixtures and finishes.

Current Status: All interior pours are complete, and upper seats have been cut back. Exterior hardscape work to be completed over the holiday break.

Budget: Original Budget: **\$1,500,000.00** Board Approval Date: March 11, 2024

Budget Issues: None.

Schedule: Office of School Facilities did not finalize review and issue permits until July 12, 2024. Working with construction team and school to determine best timing and currently estimating an April completion date.

Schedule Issues: None.

Achievements: All demo complete and new interior concrete poured to include the ADA ramps and location of ADA lift.
