




ORANGEBURG COUNTY SCHOOL DISTRICT BOARD MEETING





ORANGEBURG
COUNTY SCHOOL DISTRICT
We Are **One**

OPERATIONS UPDATE

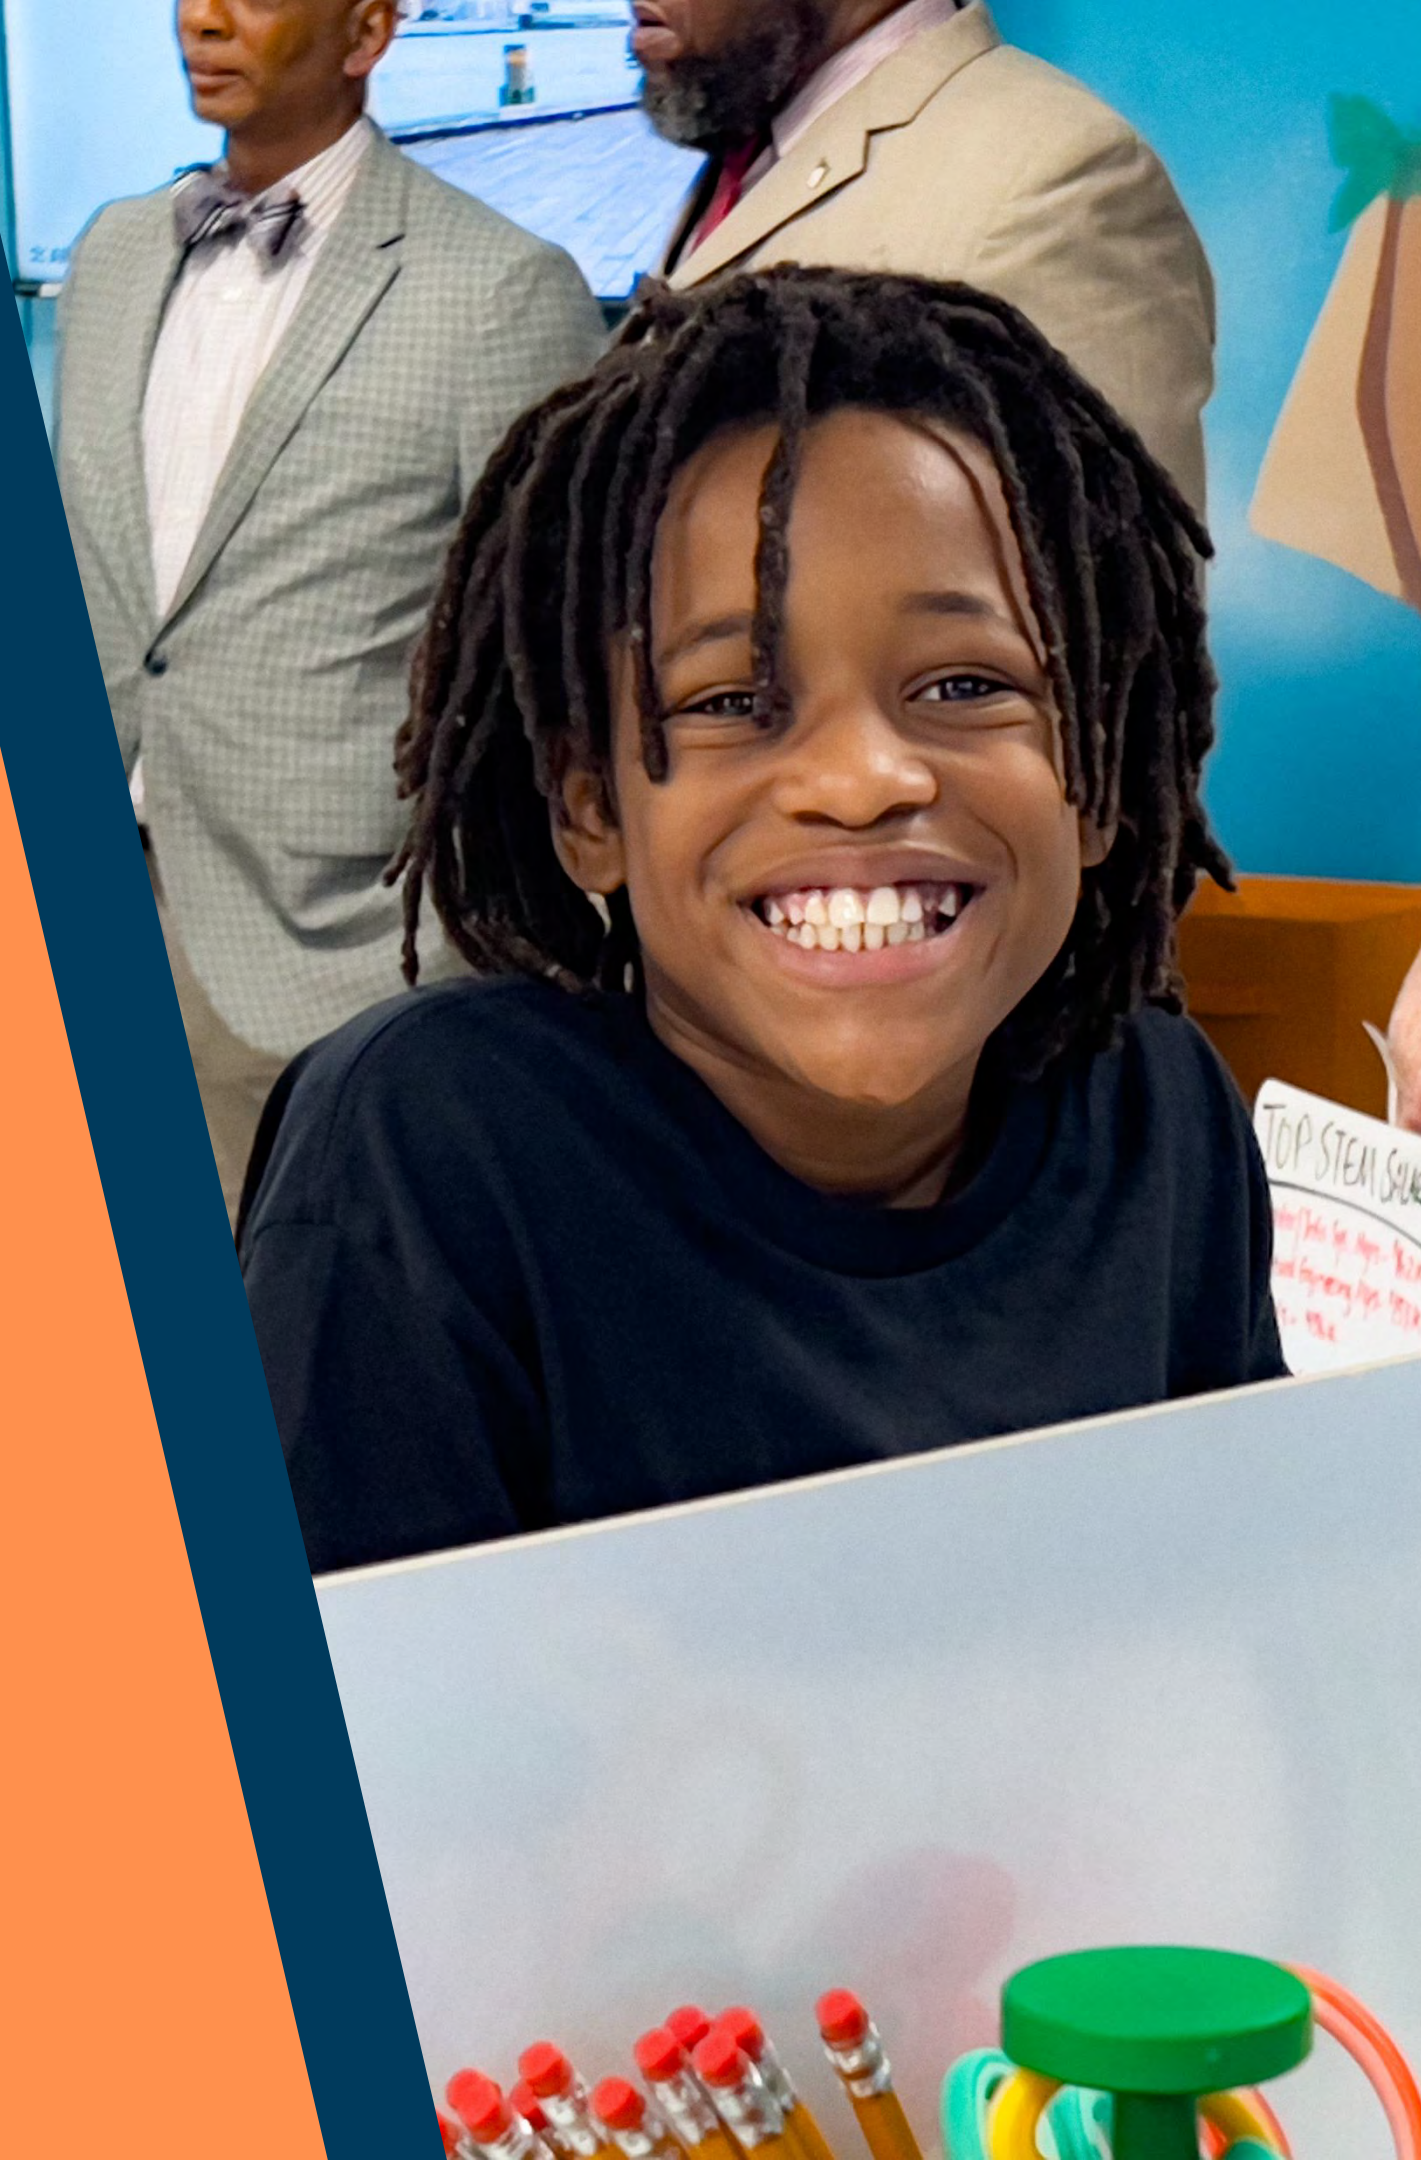

Orangeburg-Wilkinson High School

SAFETY

Incidents to Date	1
First Aids to Date	0

WEATHER

Working Days	233
Weather Days	40
Activities Delayed	2

MANPOWER

Number of Trades	8
Average Workers <i>(per day)</i>	121

SCHEDULE MILESTONES

Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continues.
- Steel erection in E1 continues.
- Masonry work at the 2nd floor of the gym and area B continues.
- Segmented walls near Bruin Dr. continue.
- Baseball/Softball foundation block began.
- The slab on grade at the field house was poured.
- Site roads are being rocked and curb and gutter is being installed near the athletic buildings.

Upcoming Activities

- Masonry work will continue in area F1 and connecting corridors.
- The field house masonry walls will begin.
- Steel erection in C will begin.
- Underground rough-in at the baseball/softball area will begin.
- Field house masonry work will begin.



Orangeburg-Wilkinson High School

SAFETY

Incidents to Date	1
First Aids to Date	0

WEATHER

Working Days	243
Weather Days	40
Activities Delayed	2

MANPOWER

Number of Trades	8
Average Workers (per day)	133

SCHEDULE MILESTONES

Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continues.
- Steel in area C was completed. Joists in the cafeteria begun.
- Masonry work at the 2nd floor of the gym and area B continues. The gym masonry was topped out.
- Segmented walls near Bruin Dr. are complete.
- Baseball/Softball MEP underground was completed.
- Masonry wall as at the field house continue.
- Road work continues.

Upcoming Activities

- Masonry work will continue in areas B, the chase walls and the field house.
- Baseball/softball SOG will be poured.
- Steel erection A1 will begin.



Orangeburg-Wilkinson High School

SAFETY

Incidents to Date	1
First Aids to Date	0

WEATHER

Working Days	248
Weather Days	40
Activities Delayed	2

MANPOWER

Number of Trades	8
Average Workers (per day)	137

SCHEDULE MILESTONES

Job Start	5/6/2024
Contract Completion	11/5/2026

Top Activities This Week

- MEP rough-in building wide continues.
- Fire sprinkler piping began in area F1.
- Steel joist/decking installed in area E2; steel beams in area A1 began.
- Masonry work at the 2nd floor of the gym and area B continues. Masonry in E1 connectors continues.
- The media center stairs were framed.
- Baseball/Softball MEP SOG was backfilled and prepared for concrete.
- Masonry walls as at the field house continue.
- Road base with curb & gutter is being installed near the athletic fields.

Upcoming Activities

- Masonry work will continue in areas E1 and start in area C.
- Baseball/softball SOG will be poured.
- Steel erection in the main lobby will begin.





EAST LAKE ELEMENTARY SCHOOL



EAST LAKE ELEMENTARY SCHOOL

HOWARD ELEMENTARY SCHOOL

- Planning session to prepare for site demolition
- Construction trailer will be on site May 12
- Site prep work will take place around the football field over to the basketball court first
- HVAC Units removal will begin May 27
- Community Walkthrough will be May 28, 6-8pm
- Teacher materials will be moved beginning May 30
