




Update on FCPS Construction / Renovation Projects

June 23, 2025

Mary E. Britton Middle School



Mary E. Britton Middle School



Mary E. Britton Middle School



➤ Architect:

JRA Architects

➤ General Contractor:

Rising Sun Developing Co.

➤ GC Contract Sum:

\$69,964,000.00

➤ Total Project Cost:

\$82,680,000.00

➤ Change Orders to Date (10):

\$168,134,25

Mary E. Britton Middle School



Mary E. Britton Middle School



Mary E. Britton Middle School



Mary E. Britton Middle School



Mary E. Britton Middle School



Mary E. Britton Middle School



The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



- Architect:
EOP Architects
- General Contractor:
D.W. Wilburn Inc.
- GC Contract Sum:
\$50,700,288.00
- Total Project Cost:
\$64,712,240.00
- Change Orders to Date (13):
\$1,417,561.62

The Hub for Innovative Learning & Leadership (The HILL)




The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)

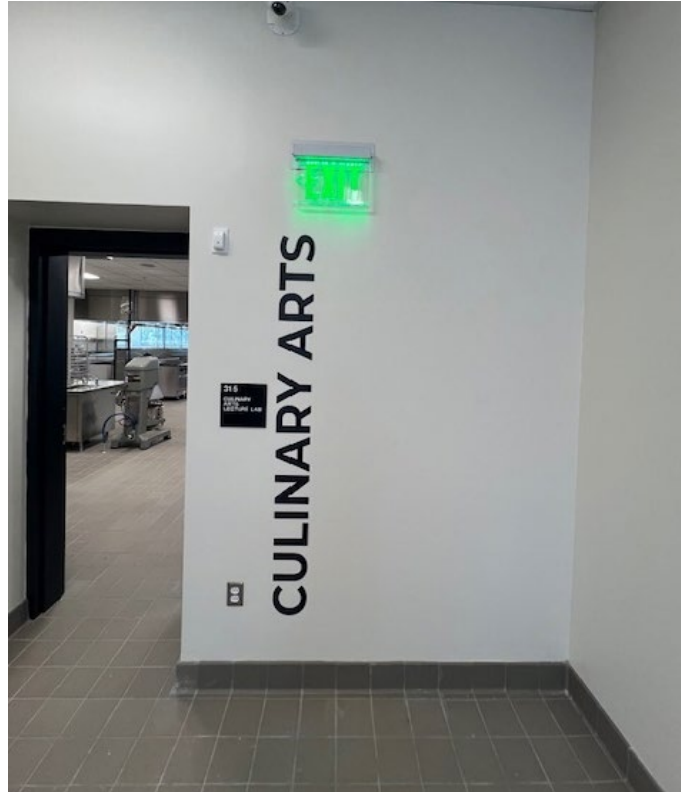

The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



The Hub for Innovative Learning & Leadership (The HILL)



Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



- Architect:
Ross Tarrant Architects
- General Contractor:
Momentum Construction
- GC Contract Sum:
\$3,998,400.00
- Total Project Cost:
\$4,886,547.24
- Change Orders to Date (3):
\$255,645.39

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



➤ **Completed Work:**

- Final coats of paint.
- Remaining door hardware.
- Exterior expansion assemblies.
- Continued site concrete.
- VFD installation.
- Toilet accessories installation.


➤ **Upcoming Work/Look Ahead:**

- Plumbing fixtures installation will start.
- 1st floor heat pumps replacement.
- Existing wall access to school/stairwell demolition.
- Site concrete will continue.

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Wall Paint Work in Progress

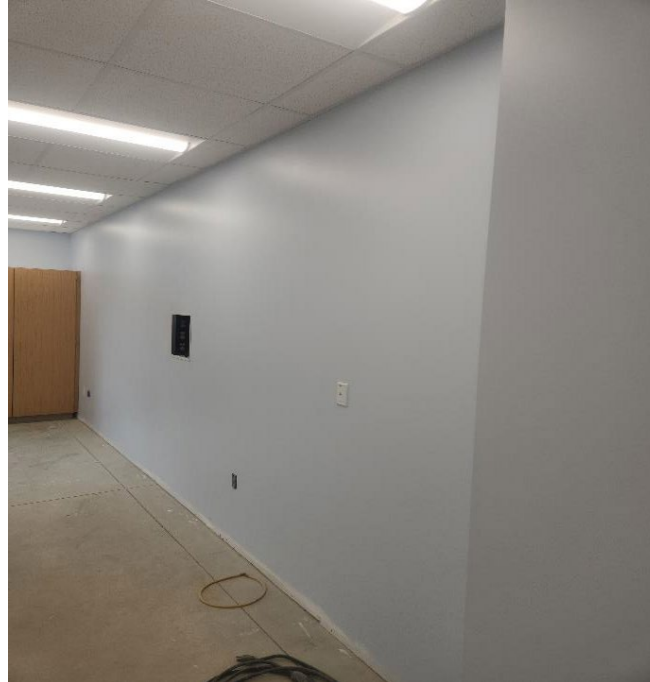

Week Ending June 6, 2025

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Toilet Accessories Installation in Progress



Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Casework Installation In Progress



Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Exterior Concrete Works In Progress



Week Ending June 6, 2025

Harrison Elem - Preschool Classrooms Addition & HVAC Upgrades



Exterior Concrete Work In Progress



Week Ending June 6, 2025

Rise STEM Academy for Girls



Rise STEM Academy for Girls



- Architect:
Ross Tarrant Architects
- General Contractor:
D.W. Wilburn, Inc.
- GC Contract Sum:
\$48,800,100.00
- Total Project Cost:
\$58,460,689.35
- Change Orders to Date (1):
\$300,018.90

Rise STEM Academy for Girls



➤ **Completed Work:**

- Geothermal drilling is completed.
- Continued storm system work.
- Continued ICF and masonry work.
- Continued slab preparation and placement
- Continued rough-in electrical work.
- Continued roofing installation
- Brick veneer installation started.

➤ **Upcoming Work/Look Ahead:**

- Geothermal field loops will start.
- Storm system work will continue.
- Slab preparation and placement will continue.
- ICF and masonry work will continue.
- Rough-in electrical work will continue.
- Brick veneer installation will continue.

Rise STEM Academy for Girls



Geothermal Work in Progress



Rise STEM Academy for Girls



Door Frame Installation and Masonry Work in Progress



Week Ending June 6, 2025

Rise STEM Academy for Girls



Above Ceiling Work in Progress



Week Ending June 6, 2025

Rise STEM Academy for Girls



Stud Frame Installation in Progress



Week Ending June 6, 2025

Rise STEM Academy for Girls



Steel Joist Work in Progress



Week Ending June 6, 2025

Rise STEM Academy for Girls



Brick Installation in Progress



Week Ending June 6, 2025

Rise STEM Academy for Girls



MEP Work in Progress



Week Ending June 6, 2025

Rise STEM Academy for Girls



Underground Electrical Conduit Installation in Progress



Week Ending June 6, 2025

Stay tuned, there's more to come in July




Henry Clay High School (New)



New Elementary on Greendale Road





Thank you!
