
WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- M&J completed demolition of walls & ceilings.
- M&J completed carpet & LVT demolition.
- M&J installed shoring.
- M&J started metal soffit framing.
- Subs completed MEP demolition.
- Cutting Edge completed saw cuts.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- M&J carpenters to continue soffit framing & start metal stud walls.
- M&J masons to start CMU opening rework.
- Subs to start MEP rough ins.

Priority RFI's

- RFI #12: Electrical Demolition Coordination
- RFI #13: Electrical Floor Boxes
- RFI #15: Floor Box Discrepancies


Priority Submittals

- #08 87 34-2 - Decorative Window Film
- #28 31 10-1 - Fire Alarm System (Existing)

Weekly Photos





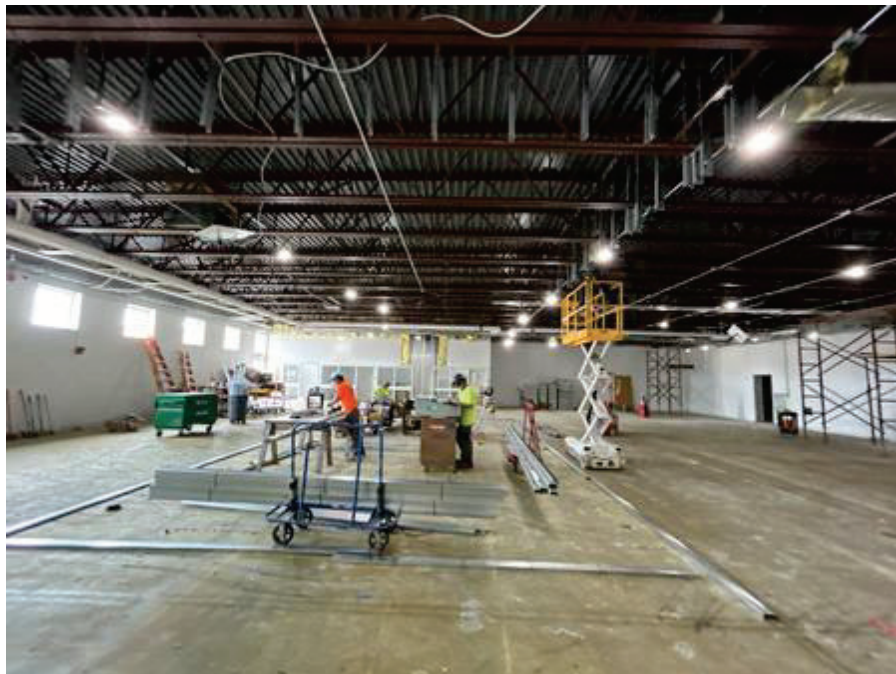



**Market &
Johnson**

Adding Value to Everything We Do

ECASD Memorial HS Additions & Alterations

33

Week of: 6/16/2025

WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- Band Addition/Remodel
 - Ford Metro installed A-8 aluminum frame & glazing.
- Auditorium Remodel
 - Subs continued MEP rough-ins.
 - ICS continued ceiling cloud framing.
 - ICS continued side catwalk structure install.
 - ICS started catwalk handrails & detailing.
 - RJP continued dryfall painting structure.
 - Tweet Garot continued chiller replacement work.
 - Rhom started installing ceiling cloud drywall.
- Commons Addition/Remodel
 - Ford Metro started aluminum entry frame installation.
 - Rhom started to rework new wall openings.
 - Rhom started floor demo in corridor.
- Little Theater
 - Rhom completed seating & AWP demo.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- Auditorium Remodel
 - Subs to continue MEP & AV-Low Voltage rough-ins.
 - RJP to continue dryfall painting structure.
 - ICS to continue ceiling cloud framing.
 - ICS to continue side catwalk structure install.
 - Tweet Garot to complete chiller replacement work.
 - Rhom to continue installing ceiling cloud drywall.
- Commons Addition/Remodel
 - Ford Metro to continue aluminum entry frame installation.
 - Rhom to demo walls.

Project Manager: Jordan Lieftring

(715) 579-0176

jlieftring@market-johnson.com

Superintendent: Josh Snyder

(715) 450-4508

jsnyder@market-johnson.com



**Market
&
Johnson**

ECASD Memorial HS Additions & Alterations

33

Week of: 6/16/2025

Adding Value to Everything We Do

- Rhom to rework new wall openings.
- Subs to start MEP rough ins.
- Little Theater
 - Rhom to start floor demo.
 - TJ Electric to start theater light demo.

Priority RFI's

- RFI #107: PR 16

Project Manager: Jordan Lieffring

(715) 579-0176


jlieffring@market-johnson.com

Superintendent: Josh Snyder

(715) 450-4508

jsnyder@market-johnson.com

Weekly Photos

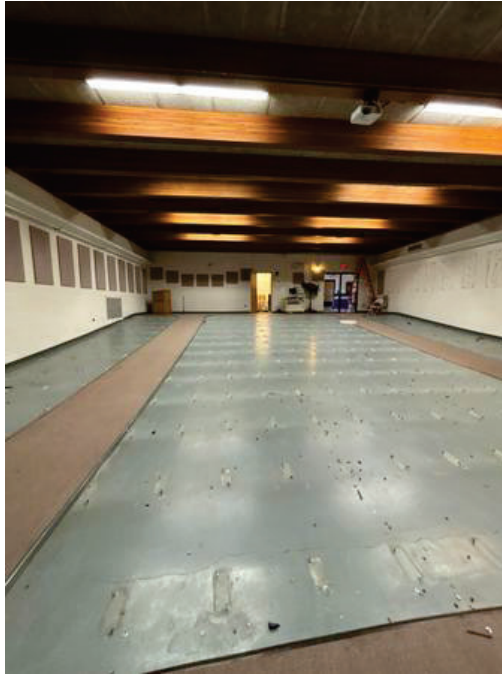




**Market &
Johnson**

Adding Value to Everything We Do

ECASD Memorial HS Additions & Alterations

33

Week of: 6/16/2025

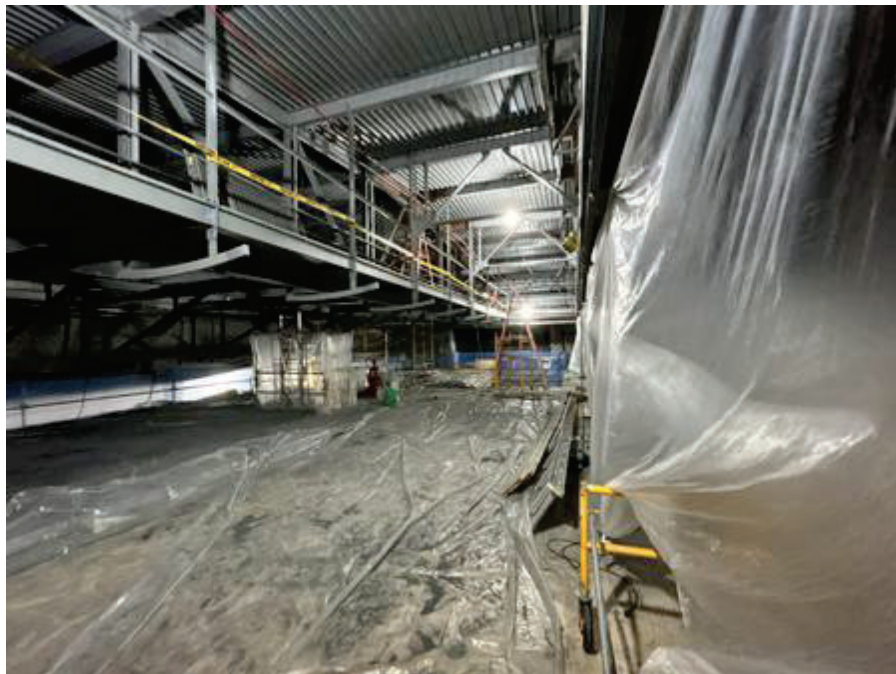





**Market &
Johnson**

Adding Value to Everything We Do

ECASD Memorial HS Additions & Alterations

33

Week of: 6/16/2025

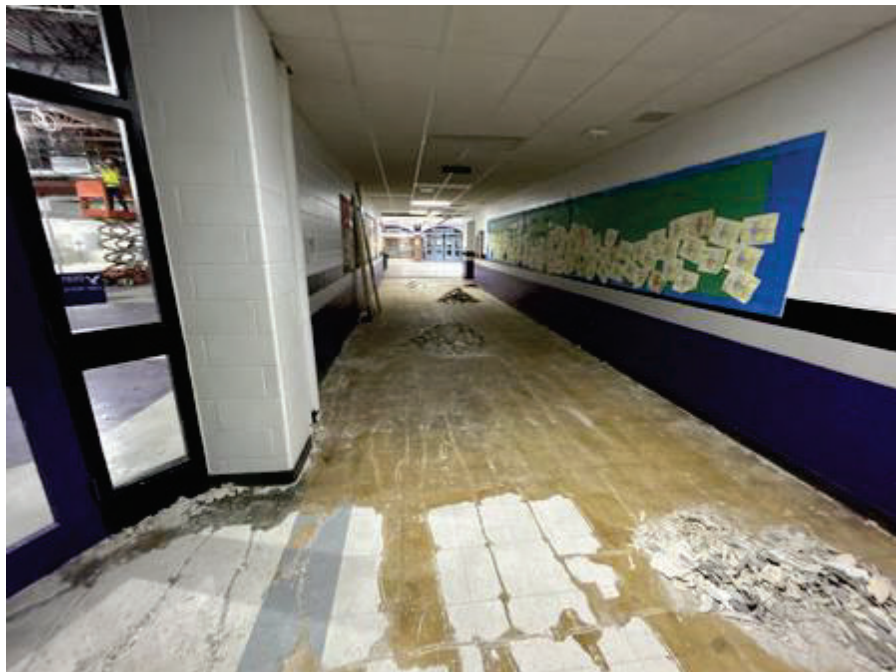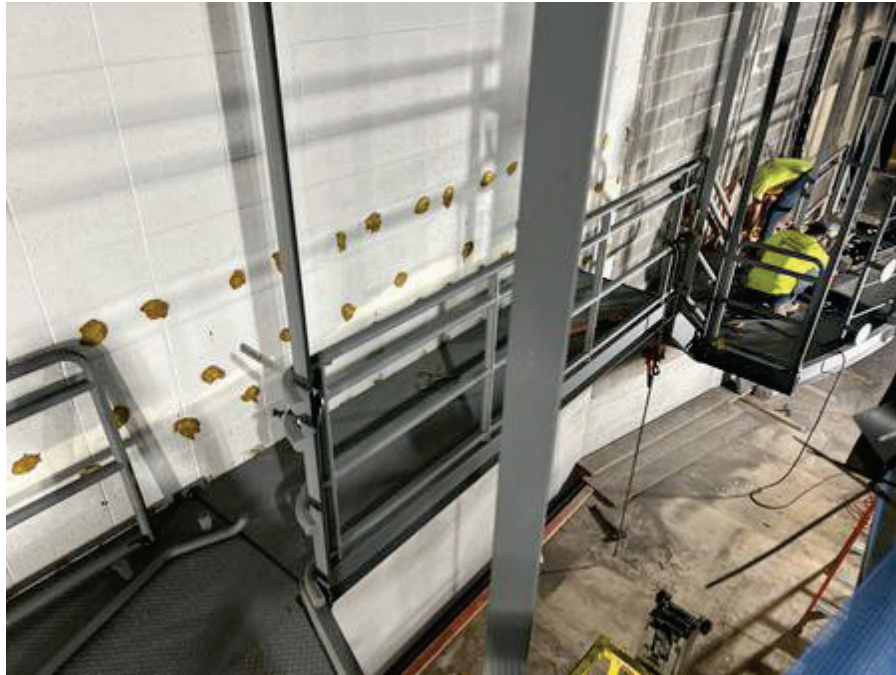



**Market &
Johnson**

Adding Value to Everything We Do

ECASD Memorial HS Additions & Alterations

33

Week of: 6/16/2025

