

New London_Spicer – 2025 Ventilation Improvement Project

Weekly Executive Summary: Ending June 13th 2025

Ongoing/ Completed:

- Footings for Chiller Screen commenced at the MS/HS
- Duct Cleaners mobilized and commenced at MS/HS
- Finished Duct Install in Area A of MS/HS
- Installing VAVs in Upper Area B and C – MS/HS
- Installing roof curbs and adapters – weather dependent – MS/HS
- Piping the VAVs in Area A – MS/MS
- Abatement re-mobilized for ACM in Lower B (Old Kitchen Area) – MS/HS
- Abatement re-mobilized for Rooms 118 and 118A – MS/HS
- Existing AHUs have been removed - PWES
- Ceiling Demo has been completed - PWES
- Valves on Fin Tube Radiators are being replaced - PWES
- Boilers Delivered for PWES
- Domestic Water Main Lines have been removed - PWES
- EC is running the Grounding Lines for the Chillers - PWES
- All lights that are being re-used re now suspended in the plenum - PWES
- VAVs are currently being wired - PWES
- RTUs have been de-energized - PWES
- Conduit being Installed to serve the RTUs - P MEC
- Ceiling Demo has been Completed - P MEC
- Interior Demo is 90% Complete - P MEC


2-Week Look Ahead:

- Roofers to Commence for Curbing Reinforcement – MS/HS
- Likely Commencement of Concrete pour for Chiller Screen – MS/HS

Issues/Concerns/Other:

- Water Infiltration at new roof curb locations (5) – to be resolved week of 6/13
- Parent Parking is an ongoing issue in the construction area – now roped off

PWES Boiler Pad Replcement

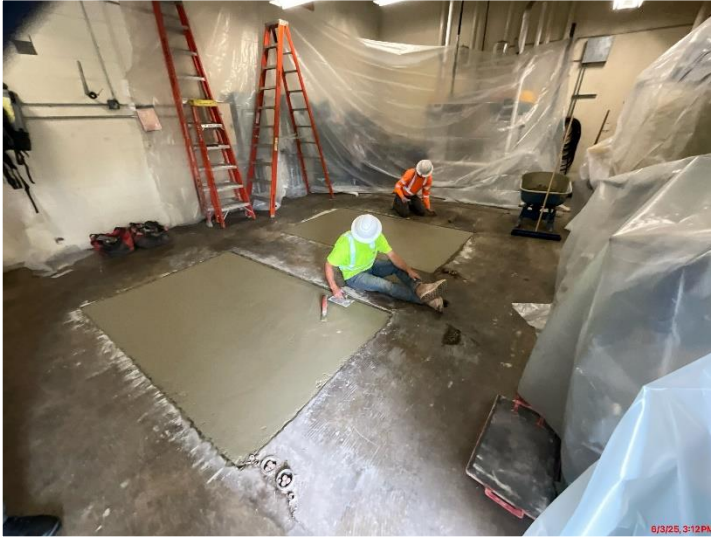

**MS/HS - Area A - Duct
Cleaning In Progress**

PWES Piping Plan Coordination



**MS/HS - Area A - EC
Performing Rough-Ins**



sitealogiq

**Nick Kurtzweg and
Ryan Mattson**

Site Superintendents

Anthony Heimkes

Project Manager
