




Quarterly Executive Summary Daisy Elementary Renovations Q2 2025

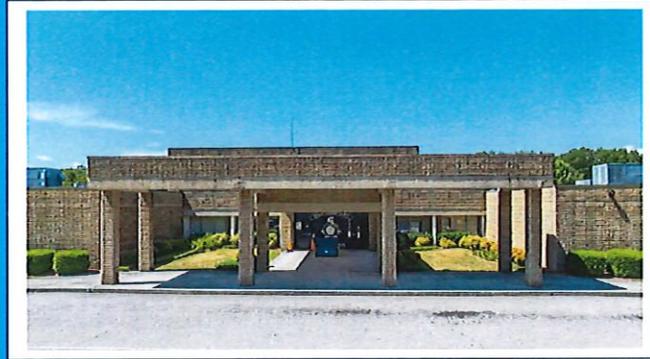

HCS Project Managers: Tricia Lemeur

Principal: Josh Todd/Ashley Arthur

Design: SMHa, Inc

Contractor: FBI Construction

Project Scope:

Critical Systems that are in the scope include: investigate and remediate electrical services and distributions (if needed), upgrade fire alarm, upgrade low voltage wiring, kitchen/servery renovations, metal roof remediation, investigate and remediate plumbing (if needed), improve exterior envelope. Refresh items that could be addressed, funding permitting, include ceiling grid and tile, lighting/flooring/painting, minor interior space adjustments, interior doors, cabinets/counters/lockers, and other such renovations.

Current Status:

Phase I to investigate exterior structure, tuck point repairs, canopy and caissons, soffits clad cover up and interior lighting for Summer 2025.

Budget:

Original Budget: \$ 15,000,000.00 Board Approved Date: May 1, 2023

Budget Issues:

None.

Schedule:

Design:	Winter 2024/Spring 2025
Construction Start:	Summer 2025
Final Completion:	TBD

Schedule Issues:

None.

Achievements:

Design underway for Phase II. GMP #1 issued for the Summer 2025 work.
