




Monthly Progress Report

August 2025

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **August 2025**

Section III – Work Projected for **September 2025**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

August 2025

Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
 - Staircase railings upgrades.
 - Classroom wall upgrades per code.
 - Install eye wash stations.
 - Install new exhaust fans.
 - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
 - Remove old asphalt tennis grounds.
 - Install new tennis courts with bleachers.
 - Install a bridge for students to access the tennis courts.
- **Hempstead UFSD – Window replacement at McNeil and Paterson elementary school – In Progress**
 - Removal of caulking under abatement.
 - Removal of existing windows.
 - Installation of new windows and new caulking.



Section II - Work Progress August 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Completed installation of new fire rated walls to ceiling decking in rooms 105 and 106.
 - Completed all wall painting and partial ceiling grid install.
 - Completed new floor tiles.
 - Completed new double doors in hallway and new door into classroom 104.
 - Completed small area of terrazzo floor.
 - Completed interior ramp.
 - Completed all punch list items.
- Locust Valley:
 - Completed all electrical work in classroom 105 and 106.
 - Completed magnet install for the hallway double doors.
 - Completed installation of wall strobes for fire alarm.
- IMC:
 - BMS controls punch list completed.
 - HVAC balancing completed.

Hempstead UFSD – HS Tennis Courts

- United Paving
 - Completed final layer of asphalt.
 - Completed tennis courts painting.
 - Completed asphalt walkway to stadium bleachers.
 - Completed bleacher installation.
 - Completed all fence installation.



Section II - Work Progress August 2025

Hempstead UFSD – Window replacement

- Arrow Steel Windows
 - Completed abatement for all window caulking at Paterson elementary school.



Section III - Work Planned September 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Complete handi-lift work.

Hempstead UFSD – HS Tennis Courts

- United Paving
 - Complete remaining punch list items.
 - Complete bridge install.

Hempstead UFSD – Window replacement

- Arrow steel windows
 - Wait on window delivery. Expected mid-October.



Section IV – Progress Photos



Hempstead HS – Interior Ramp



Section IV – Progress Photos



Hempstead HS – C Building Classrooms




Section IV – Progress Photos



Hempstead HS – C Building Classrooms



Section IV – Progress Photos

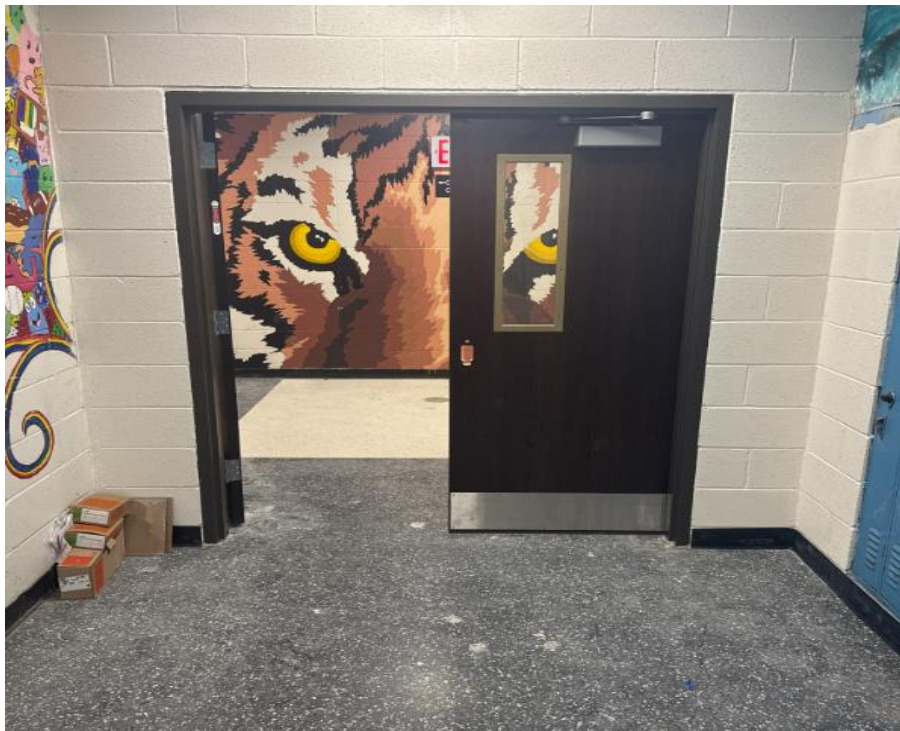

Hempstead HS – C Building Classrooms



Section IV – Progress Photos



Hempstead HS – Tennis Courts



Section IV – Progress Photos



Hempstead HS – Tennis Courts



Section IV – Progress Photos



Hempstead HS – Window Caulking Abatement




Section V – Workforce Summary – Company/Hours

August 2025

Manpower Chart

MANPOWER GRAPH

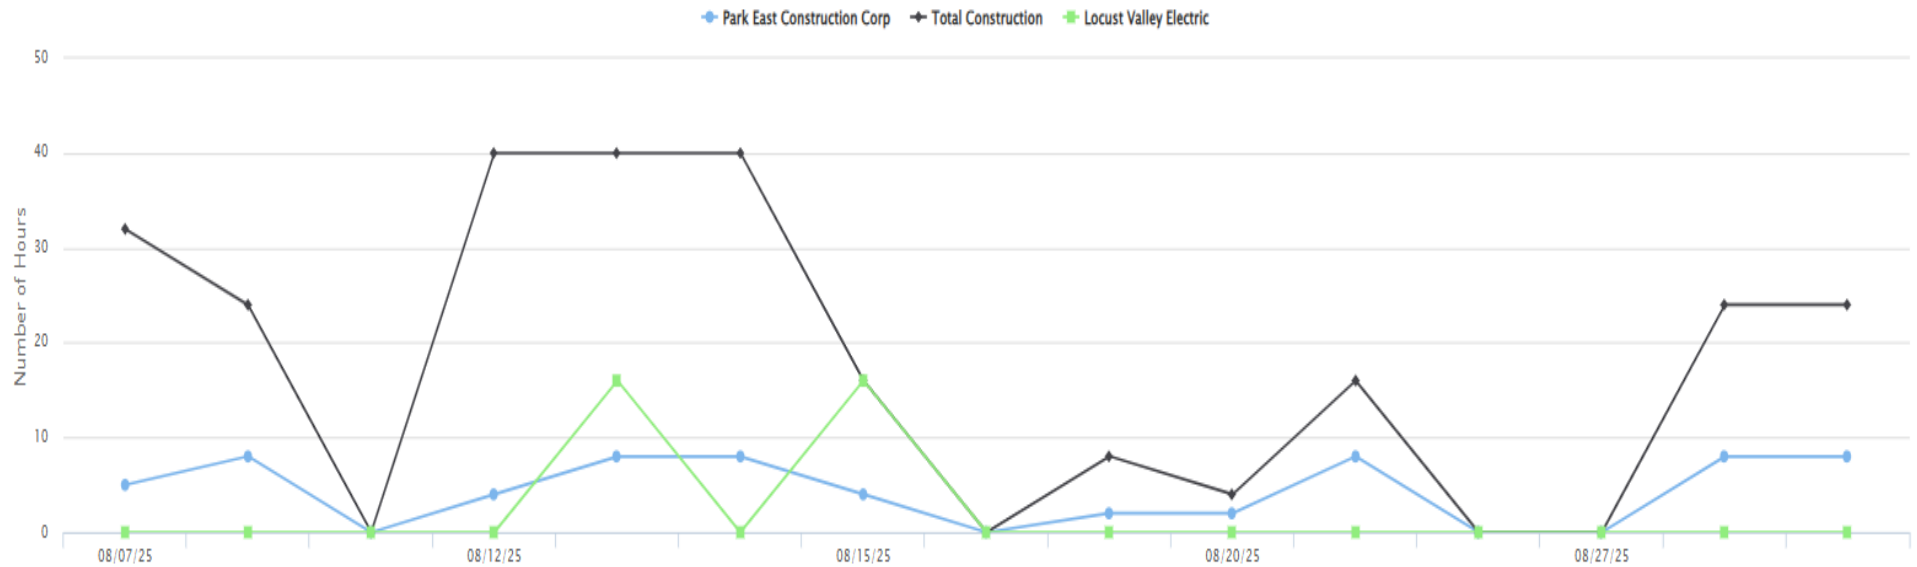


Hempstead HS – Infrastructure



Section V – Workforce Summary – Company/Hours

August 2025

MANPOWER GRAPH

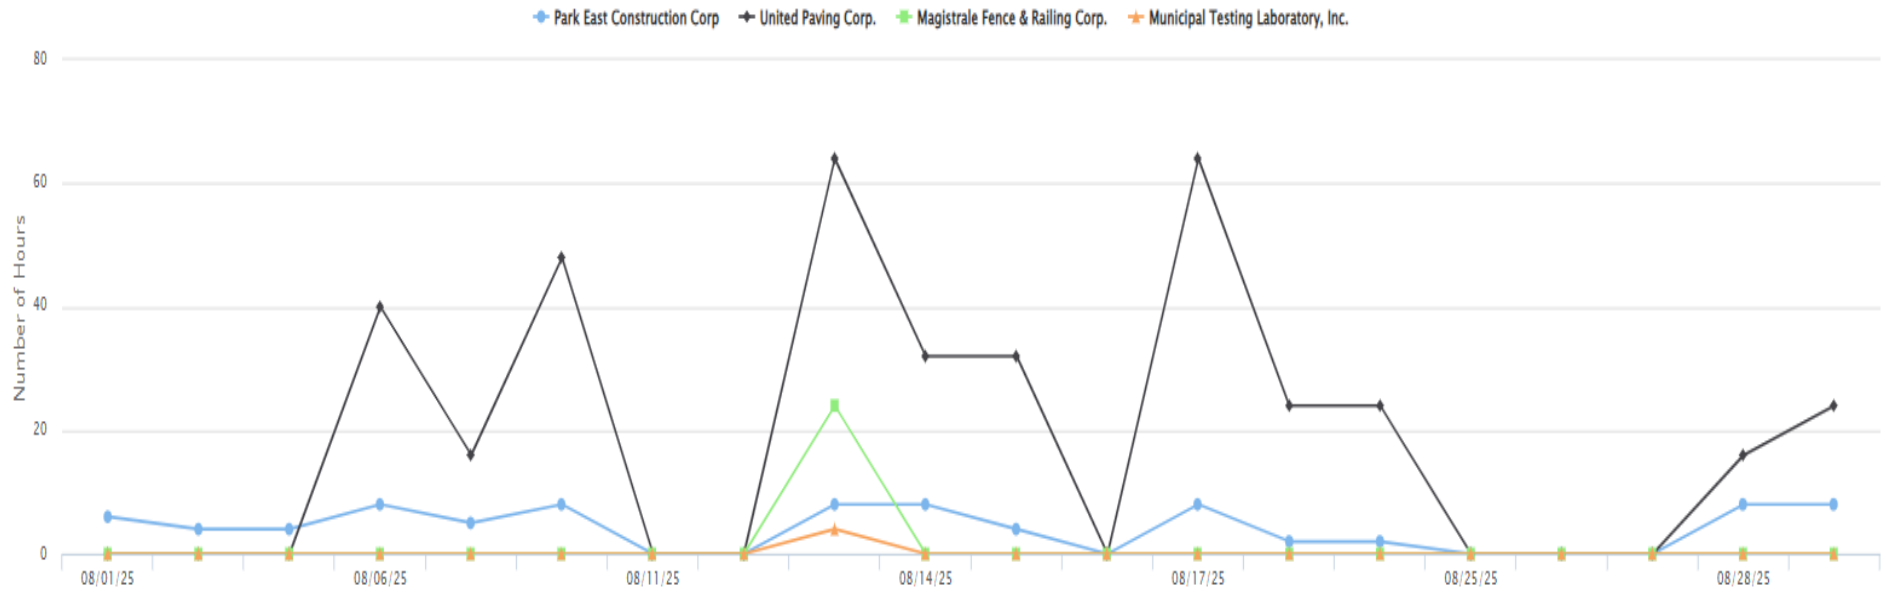


Hempstead HS – Tennis Courts



Section V – Workforce Summary – Company/Hours

August 2025

▼ MANPOWER GRAPH

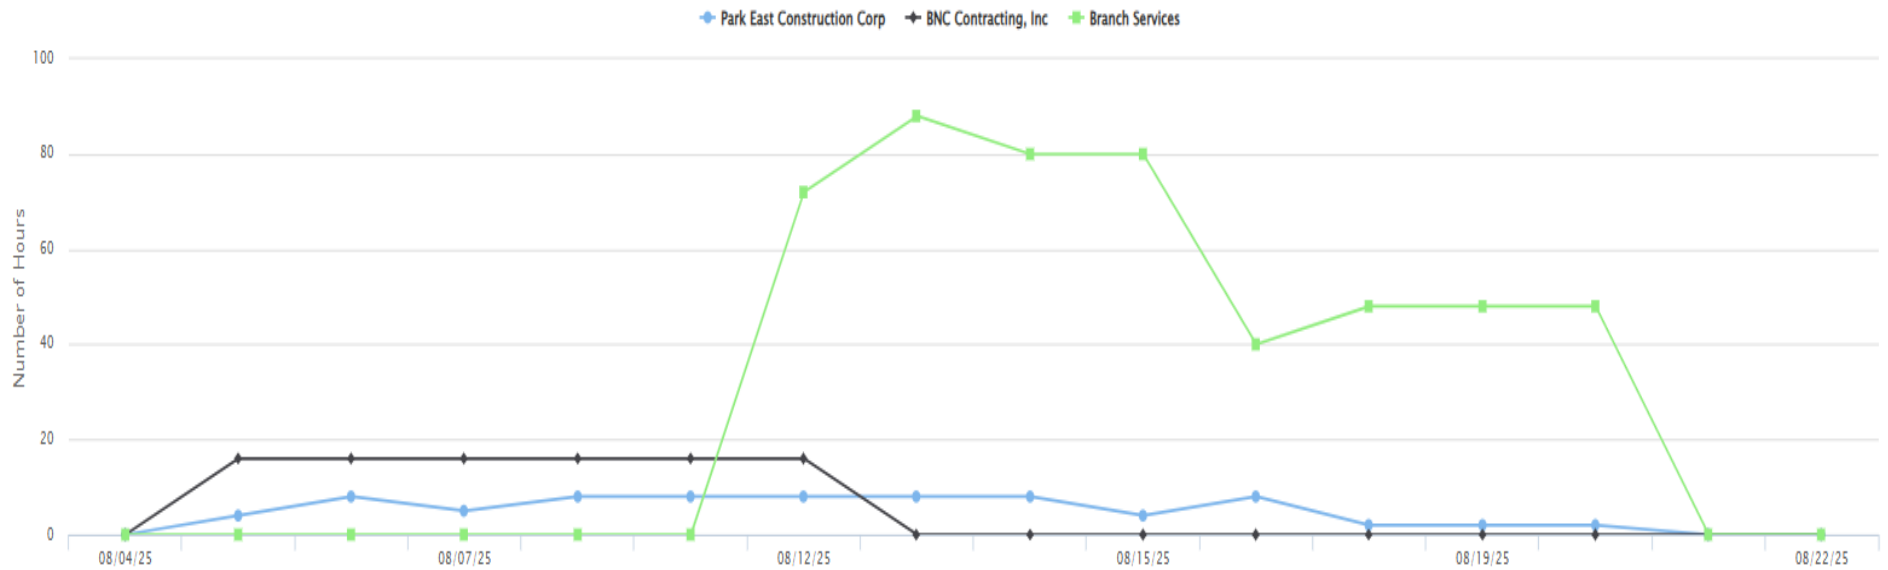

Hempstead HS – Window replacement



Hempstead Union Free School District

August 2025

End of Progress Report
