



**BOND PROJECT UPDATES
AS OF: OCTOBER 13, 2025**

PHIL DANAHER STADIUM PROJECTS

Project List:

- Phil Danaher Stadium - Press Box Replacement
- Phil Danaher Stadium - Stadium Renovation
- Phil Danaher Stadium - Score Board Replacement

Project Updates:

Phil Danaher Stadium – Press Box Replacement and Stadium Renovation

Administration released the formal procurement for this project on September 26, 2025. Responses are due back on October 15, 2025, and the top ranked proposal will be presented for Board approval at the November 10, 2025 Board meeting. The project will commence, after procurement and contractor selections, in January 2026 and be completed by July 31, 2026.

PHIL DANAHER STADIUM – SCORE BOARD REPLACEMENT

Contracts Awarded to:

Independent Design Representative:	Stridde, Callins & Associates, Inc. Wilkerson & Sanders, Inc.
Contractor:	Nevco Sports, LLC

Project Timelines:

Board Approved Contracts/Purchases:	July 14, 2025
Contracts Awarded & Purchase Orders Issued:	August 5, 2025
Estimated Project Start Date:	January 1, 2025
Estimated Project Completion Date:	July 31, 2026

Project Updates:

The board approved the contractor selections and contract with Nevco Sports, LLC on July 14, 2025. The Administration met with the Engineer, Athletic Department, Band, and Multimedia Production Specialist to approve the final proof on August 20, 2025. The scoreboard is now

moving into the production phase. The project will commence in January 2026 and be completed by July 31, 2026.

Final Approve Proof:

CALALLEN HIGH SCHOOL, CORPUS CHRISTI, TX PROOF #69807G-PR



PROOF INCLUDES:

- **Full Color LED Video Display**
25.2'H x 47.24'W 10mm
(768 x 1440 pixel matrix)
*Shown with virtual scoring
- **Full Color LED Video Display**
(2) 6.3'H x 12.6'W 10mm
(192 x 384 pixel matrix)
- **SP-2000EV Stadium Pro 2000EV**
22.04'W x 6.3'H x 42"D
Scrim Size: 254.48'W x 65.6'H
Printable Scrim Area: 247.98'W x 59.1'H
Scrim Color: 199 Maroon
Imprint Color: White/Black/Maroon
- **FT-24-T14 LED Field Timer 24" Digits with Game Time 14" Digits (Set of 2)**
5'W x 4'H x 8"D
Color: 199 Maroon
Game Time Digit Color: Red
Play Clock Digit Color: White
- **Decorative Arch Truss**
47.24'W x 4'H
- **Decorative Arch Truss Illuminated Letters**
(18) 36" Letters



SIGNATURE OF APPROVAL _____ DATE _____

This rendering is for conceptual purposes only. It may not be to exact scale or specifications and should not be used for installation purposes. Every effort has been made to make it as accurate as possible. Beams and or pillars are for illustration only. Engineering specifications may require changes in the quantity, size and/or shape of beams and pillars to meet installation requirements. Nevco assumes no obligations or liability regarding the viability of applicability of existing structures. THIS DRAWING IS THE PROPERTY OF NEVCO INC. AND SHALL NOT BE REPRODUCED, COPIED, SHARED or DISTRIBUTED WITH ANYONE OTHER THAN THE INTENDED STAFF OR CLIENT OF THE PROPOSED PROJECT WITHOUT THE EXPRESSED PERMISSION OF NEVCO INC.

BASEBALL & SOFTBALL FIELD TURF & FENCING

Contracts Awarded to:

Independent Design Representative:	CEI Engineering, Inc.
Contractor:	Paragon Sports Constructors, LLC

Project Timelines:

Board Approved Contracts/Purchases:	June 24, 2024
Contracts Awarded & Purchase Orders Issued:	July 24, 2024
Estimated Project Completion Date:	February 28, 2025


Project Updates:


Administration continues to work with the contractor and independent design representative to complete the outstanding punch list items on both fields. Estimated acceptance, final completion, and issuance of final payment is October 2025.

Project Photos:





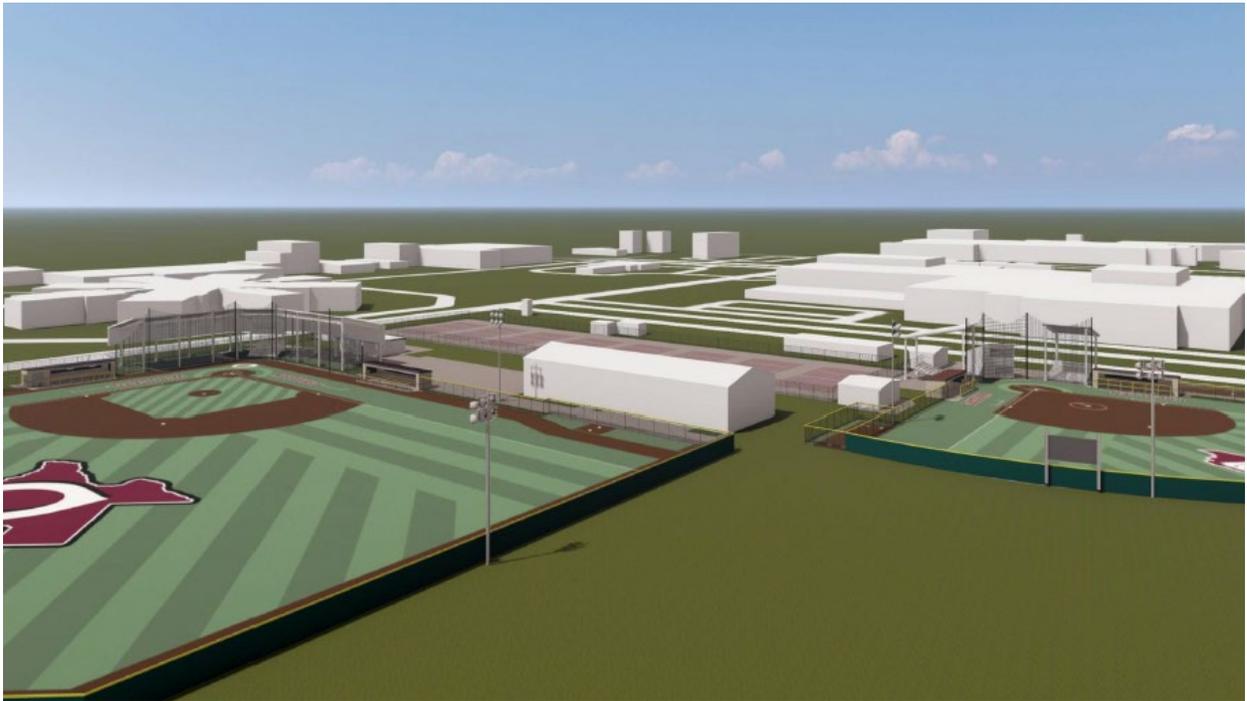

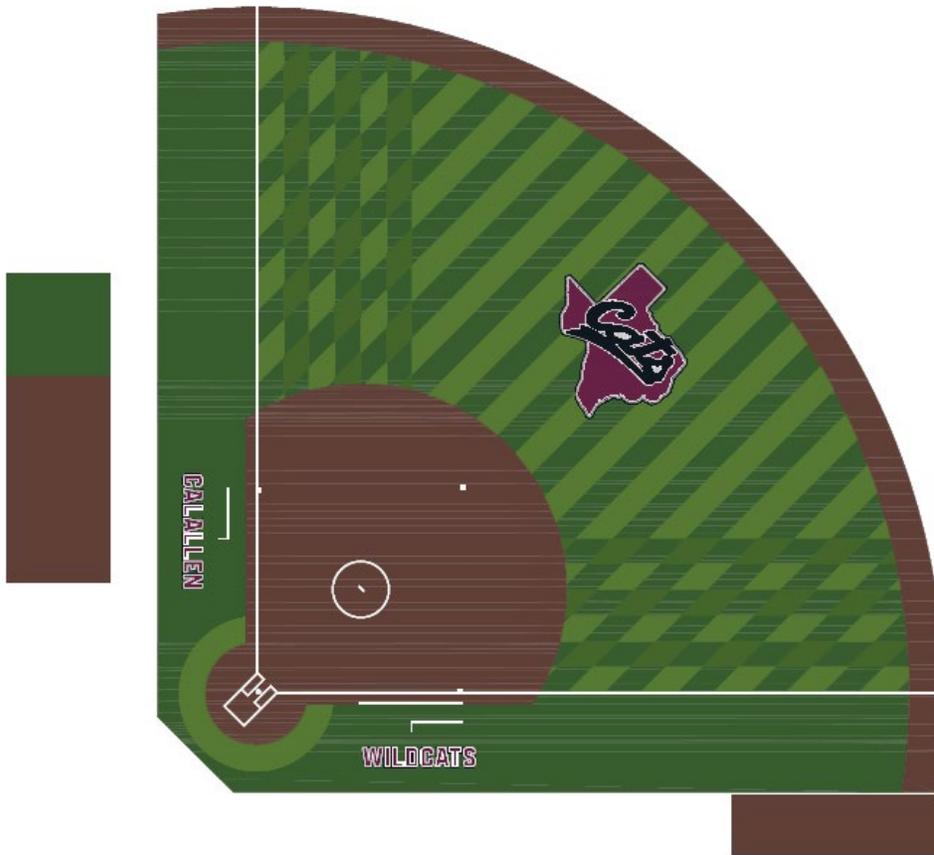

GENERAL PLANNING COSTS

All Bond 2024 Projects

Legal Services:

Walsh Gallegos

Estimated expenditures \$20,000

Administration continues to work closely with legal counsel to negotiate and finalize contracts for the Bond 2024 program. Utilizing the assistance of legal counsel ensures that the Bond 2024 program is compliant with all applicable laws during every phase.

Architect Services:

Rawley McCoy and Associates, PLLC

Rawley McCoy and Associates' (RMA) contract was awarded at the May 13, 2024 Board Meeting. Future updates on RMA's progress can be found on the specific projects updates above.

Civil Engineering Services:

York Engineering

Estimated expenditures \$40,000

Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

MEP Engineering Services:

Stridde, Callins & Associates, Inc.

Estimated expenditures \$75,000

Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

Structural Engineering Services:

Wilkerson & Sanders, Inc

Estimated expenditures \$25,000

Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

Geotechnical Engineering and Construction Material Testing Services:

Intertek PSI

Estimated expenditures \$25,000

Bond 2024 contracts were awarded at the June 24, 2024 Board Meeting. Administration will begin scheduling these services as needed throughout project design and implementation.
