




Monthly Progress Report

October 2025

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **October 2025**

Section III – Work Projected for **November 2025**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

October 2025

Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
 - Staircase railings upgrades.
 - Classroom wall upgrades per code.
 - Install eye wash stations.
 - Install new exhaust fans.
 - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
 - Remove old asphalt tennis grounds.
 - Install new tennis courts with bleachers.
 - Install a bridge for students to access the tennis courts.
- **Hempstead UFSD – Window replacement at McNeil and Paterson elementary school – In Progress**
 - Removal of caulking under abatement.
 - Removal of existing windows.
 - Installation of new windows and new caulking.
- **Hempstead UFSD – Boiler replacement at McNeil elementary school – In Progress**
 - Boiler and piping replacement.
- **Hempstead UFSD – IAQ at Various School – In Progress**
 - Indoor air quality and mechanical upgrades.
 - Electrical upgrades.



Section II - Work Progress October 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Waiting for 11/17 to complete Handi-lift

Hempstead UFSD – HS Tennis Courts

- United Paving:
 - Preparing to start bridge footings.

Hempstead UFSD – Window replacement

- Arrow Steel Windows:
 - Started replacing windows at McNeil ES.
 - Completed rooms, 12, 15, 19, 27, 28, 29, 30, and 31.

Hempstead UFSD – Boiler replacement

- Thermotech:
 - Removed existing boiler and associated piping in its entirety.
 - Installed new boiler pad, and expansion tank pads.
 - Installed piping to keep existing system operational.

Hempstead UFSD – IAQ at Various Schools

- Reliance:
 - Started condensate piping at Prospect ES.
 - Started installing split units and refrigerant piping at McNeil ES.
 - Started installing split units and refrigerant piping at Paterson ES.
- Eldor:
 - Started roughing in ceiling at Paterson ES.



Section III - Work Planned November 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Complete Handi-lift work.

Hempstead UFSD – HS Tennis Courts

- United Paving
 - Complete remaining punch list items.
 - Complete bridge footings.

Hempstead UFSD – Window replacement

- Arrow steel windows
 - Continue replacing windows at McNeil ES.

Hempstead UFSD – Boiler replacement

- Thermotech:
 - Complete boiler installation.
 - Complete prefabrication of piping and installation of piping.
 - Complete electrical lighting and power to boiler and associated equipment.

Hempstead UFSD – IAQ at Various Schools

- Reliance:
 - Complete condensate piping at Prospect ES and start chilled water piping roughing.
 - Complete refrigerant piping at Paterson ES.
- Eldor:
 - Continue to rough in ceilings at Paterson ES and McNeil ES.



Section IV – Progress Photos



Hempstead McNeil ES – Window Replacement



Section IV – Progress Photos



Hempstead McNeil ES – Window Replacement



Section IV – Progress Photos



Hempstead McNeil ES – Boiler Replacement



Section IV – Progress Photos



Hempstead McNeil ES – Boiler Replacement



Section IV – Progress Photos



Hempstead McNeil ES – IAQ



Section IV – Progress Photos




Hempstead Paterson ES – IAQ



Section V – Workforce Summary – Company/Hours

October 2025

▼ MANPOWER GRAPH

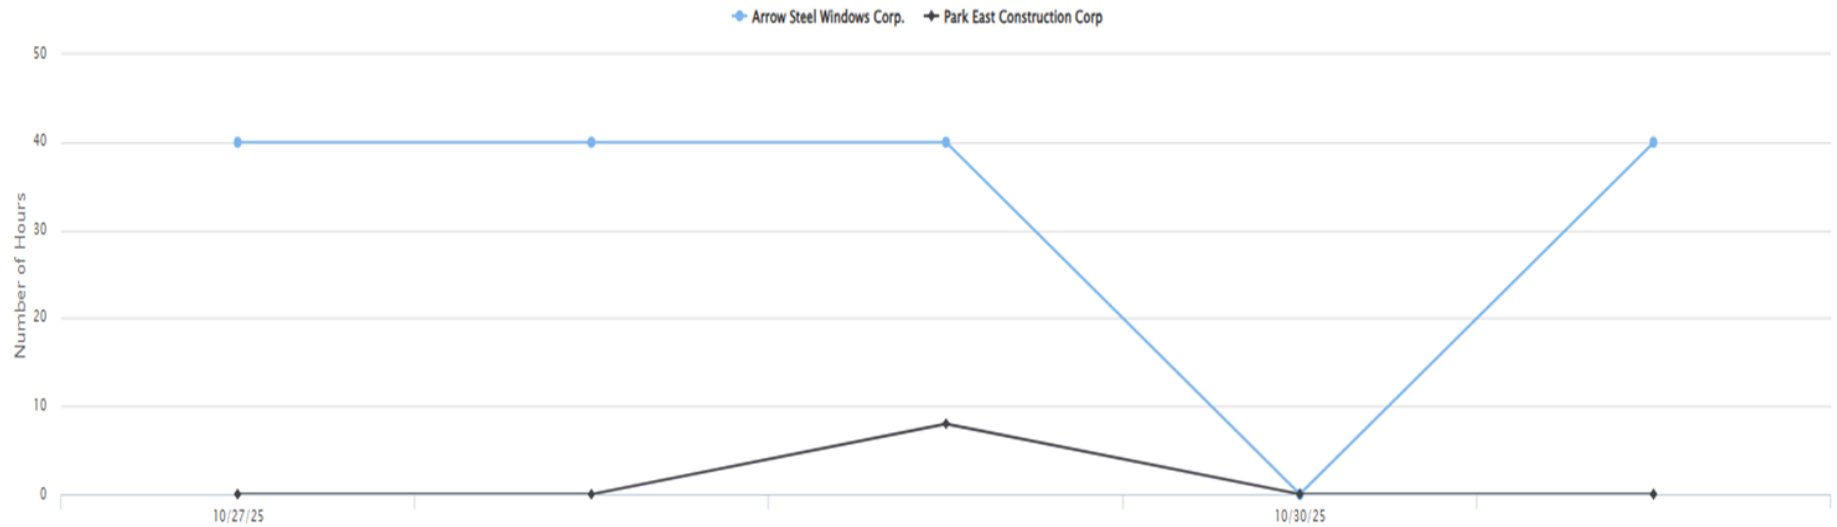


Hempstead UFSD – Window Replacement



Section V – Workforce Summary – Company/Hours

October 2025

MANPOWER GRAPH

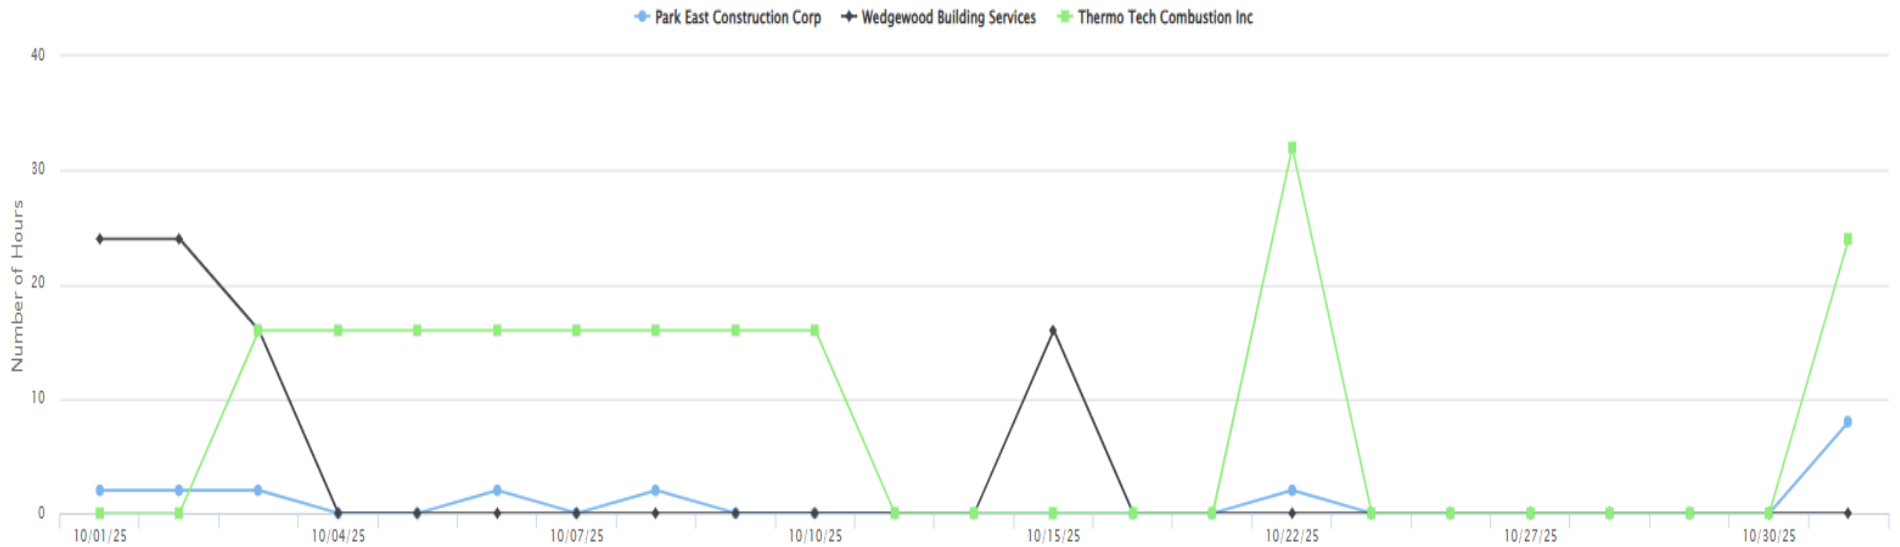


Hempstead McNeil – Boiler Replacement



Section V – Workforce Summary – Company/Hours

October 2025

MANPOWER GRAPH

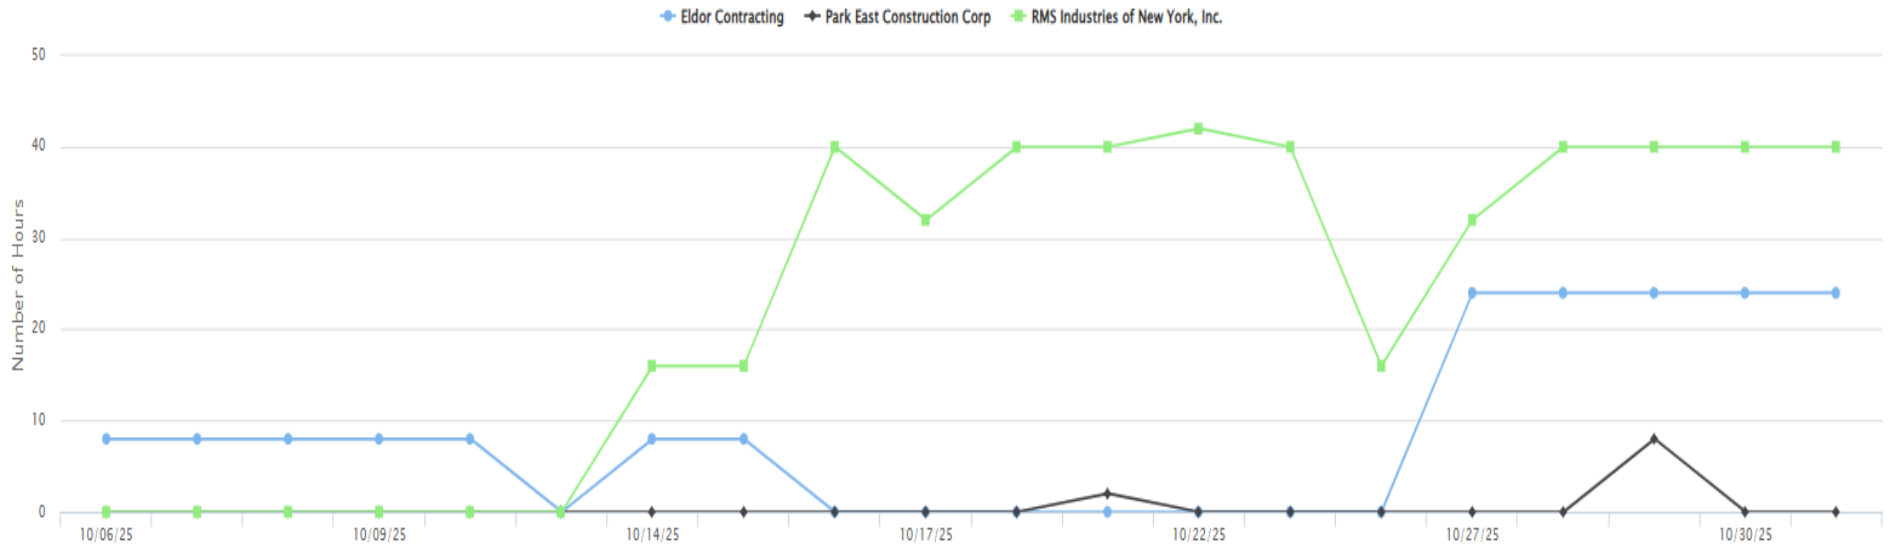

Hempstead UFSD – IAQ at Various Schools



Hempstead Union Free School District
October 2025

End of Progress Report
