




Monthly Progress Report

October 2025

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **October 2025**

Section III – Work Projected for **November 2025**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

October 2025

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress October 2025

Hempstead UFSD – ABGS MS

- VRD:
 - Delivered job trailers to the site.
 - Started installing drainage pools throughout the site.
 - Removed excess soil from site.
 - Surveyor marked out transformer island.
 - Surveyor marked out corners of new addition.
 - Installed temp smoke doors on 2nd floor.
 - Installed temp partitions to block off exit doors in the boy's gym.
- Relle:
 - Continued the rough-in for girl's locker room and boiler room.
 - Excavated for underground feed from boiler room to Henry Street.
 - Installed underground conduits from Henry Street to transformer island.
 - Installed conduits from transformer island to electric vault.
- Reliance:
 - Abated existing boiler.
 - Removed existing boiler from boiler room.



Section III - Work Planned November 2025

Hempstead UFSD – ABGS MS

- VRD:
 - Start excavation for footings.
 - Start demo on the bridge platforms.
 - Continue installing drainage pools.
- Relle:
 - Continue roughing for girl's locker room and boiler room.
 - Install temp power to trailers.
 - Pull primary feeds to transformer island and vault.
 - Disconnect exterior exit staircase building.
- Hirsch:
 - Mobilize to site.
 - Start gas piping in boiler room.
 - Install underground piping.



Section IV – Progress Photos



Hempstead ABGS MS – Drainage Pools



Section IV – Progress Photos



Hempstead ABGS MS – Drainage Pools



Section IV – Progress Photos



Hempstead ABGS MS – Drainage Pools



Section IV – Progress Photos



Hempstead ABGS MS – Drainage Pools



Section IV – Progress Photos



Hempstead ABGS MS – Temp Smoke Doors/Partitions



Section IV – Progress Photos



Hempstead ABGS MS – Transformer Island



Section IV – Progress Photos



Hempstead ABGS MS – Underground Feeds



Section IV – Progress Photos




Hempstead ABGS MS – Boiler Abatement/Demo



Section V – Workforce Summary – Company/Hours

October 2025

MANPOWER GRAPH

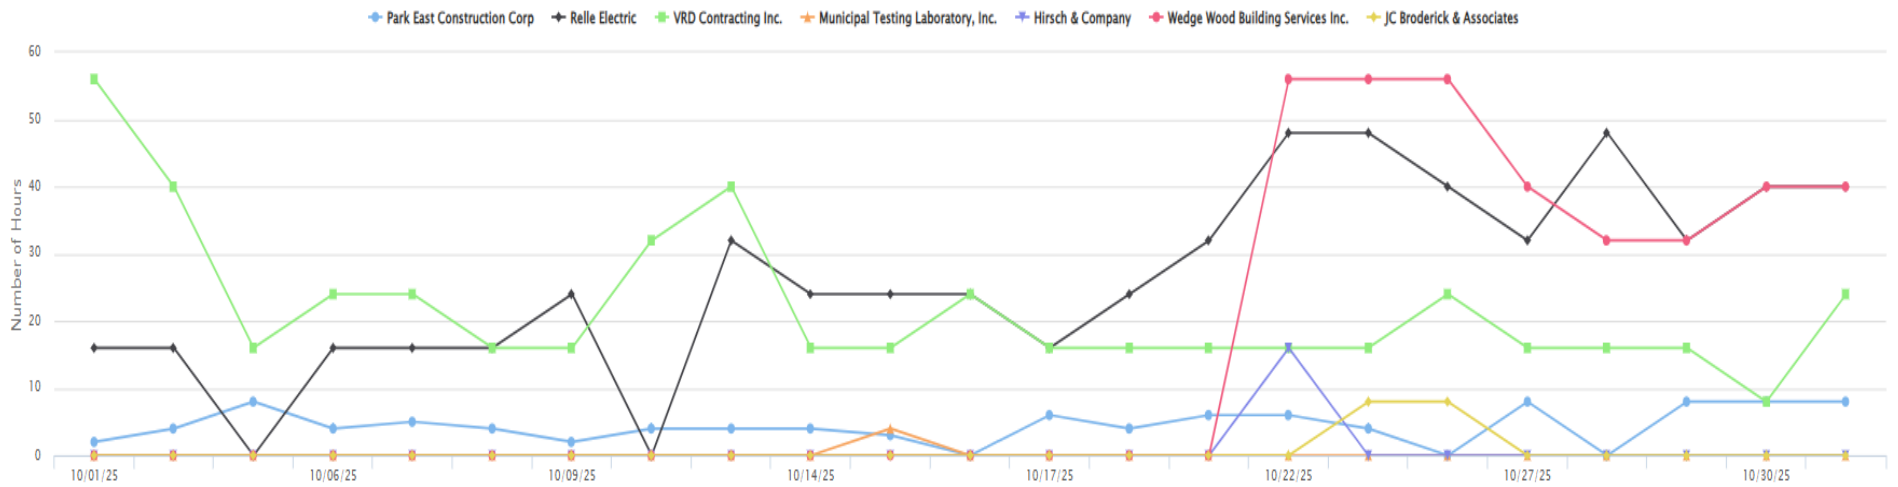

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

October 2025

End of Progress Report
