




# Monthly Progress Report

November 2025

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





# Table of Contents

**Section I** – Program Summary

**Section II** – Work Progress **November 2025**

**Section III** – Work Projected for **December 2025**

**Section IV** – Progress Photos

**Section V** – Monthly Workforce Summary



## Section I – Program Summary November 2025

- **Hempstead UFSD – ABGS MS**
  - New addition to the existing building.
  - Abatement work throughout the existing building.
  - Classroom upgrades in the existing building.
  - New boilers installation in the existing building.
  - MEP upgrades throughout the existing building.



## Section II - Work Progress November 2025

### Hempstead UFSD – ABGS MS

- **VRD:**
  - Continued installing drainage pools throughout site.
  - Removed existing exterior staircase building.
  - Started excavating for footings - 50% complete.
  - Started installing footings formwork and rebar.
  - Core drilled openings for plumber's gas piping.
- **Relle:**
  - Continued the rough-in for existing classrooms and the boiler room.
  - Excavated for underground feed from transformer island to new addition.
  - Pulled wire for new primary feed into boiler room vault.
- **Hirsch:**
  - Started installing new gas main feed in the boiler room.
  - Started installing new domestic water feed in the boiler room.



## Section III - Work Planned December 2025

### Hempstead UFSD – ABGS MS

- VRD:
  - Continue excavation for footings.
  - Continue installing form work and rebar for footings.
  - Start foundation walls formwork.
- Relle:
  - Continue roughing for existing building and boiler room.
  - Install new transformer on island.
  - Switchover to new primary transformer.
- Hirsch:
  - Continue gas piping in the boiler room.
  - Install hot water heater.



## Section IV – Progress Photos



Hempstead ABGS MS – Drainage Pools



## Section IV – Progress Photos



Hempstead ABGS MS – Transformer Island



## Section IV – Progress Photos



Hempstead ABGS MS – New Gas Feed



## Section IV – Progress Photos



### Hempstead ABGS MS – Exterior Staircase



## Section IV – Progress Photos



Hempstead ABGS MS – Underground Electrical feeds



## Section IV – Progress Photos



## Hempstead ABGS MS – Footings



## Section IV – Progress Photos



Hempstead ABGS MS – Footings



## Section IV – Progress Photos




Hempstead ABGS MS – Footings



## Section V – Workforce Summary – Company/Hours

### November 2025

MANPOWER GRAPH

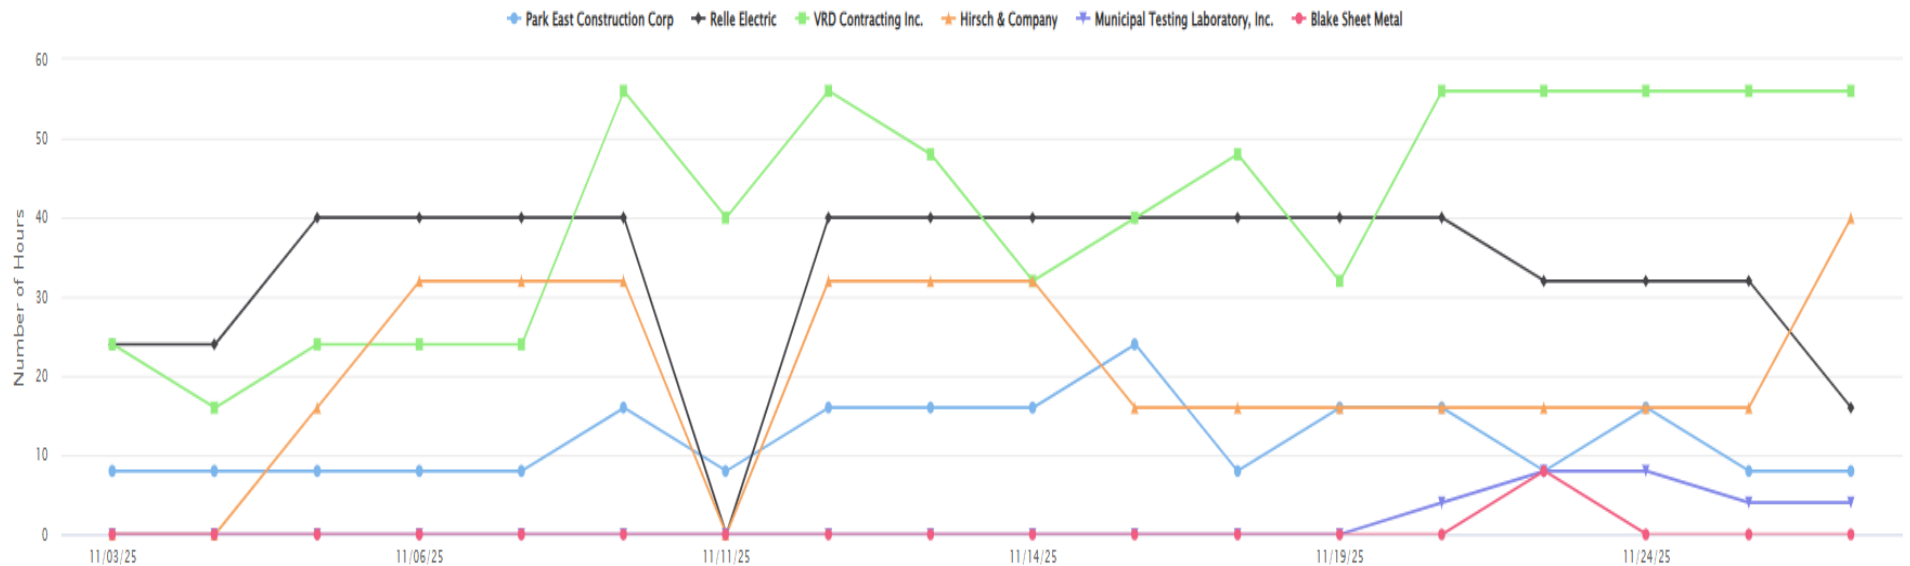

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)  
November 2025

**End of Progress Report**
