


New Henry Clay High School

➤ Completed/Work in Progress:

- Geothermal well field drilling at the south end of the site is complete.
- KAWC installation of main waterline is complete.
- ICF and CIP formwork placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Area A & B Level 2 steel erection is nearly complete.
- Area G foundations are in progress.
- Area D ICF walls, IFAs, CMU, and hollowcore are underway.
- Area A Level 1 ductwork and cable tray installation is in progress.

➤ Upcoming Look Ahead:


- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue pouring ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs and hollow metal frames.
- Continue with ICF walls in Area D and foundations in Area G.
- Continue with steel erection for Level 2.
- Continue with ductwork and cable tray installation at Area A Lvl 1.

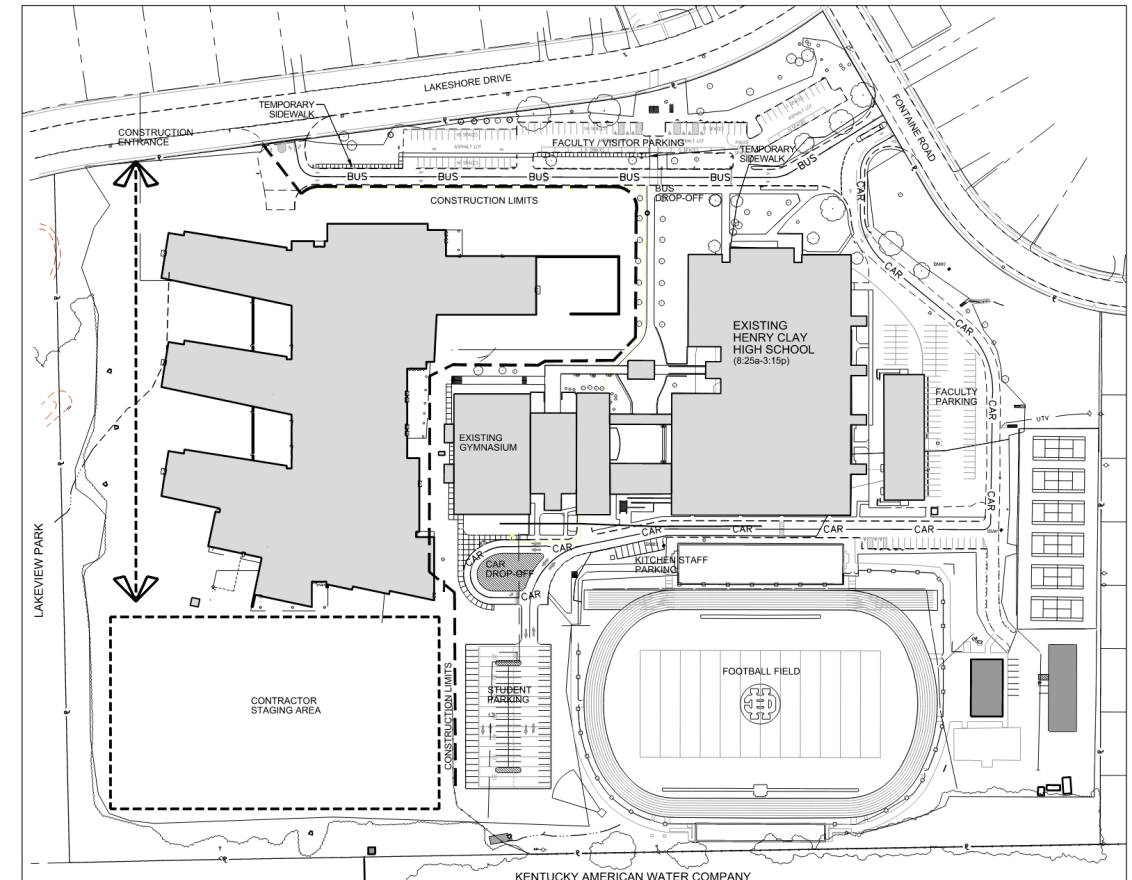

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School


Area A - Level 2 CMU Walls, ICF & IFA Frame Installation in Progress

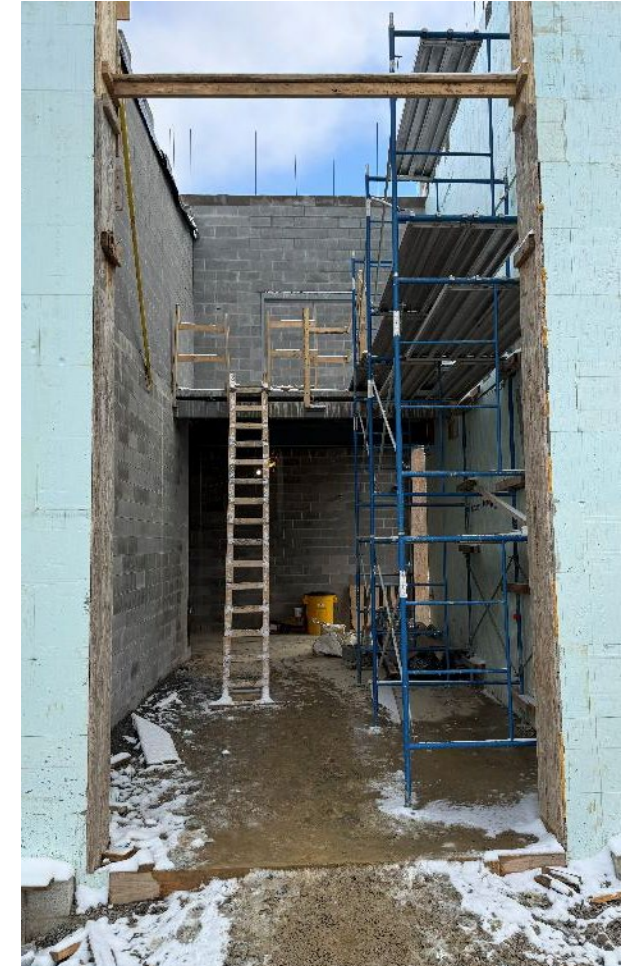

Week Ending December 05, 2025

New Henry Clay High School

Area A – Level 1: Installation of Ductwork, Cable Tray & Pipe Hangers

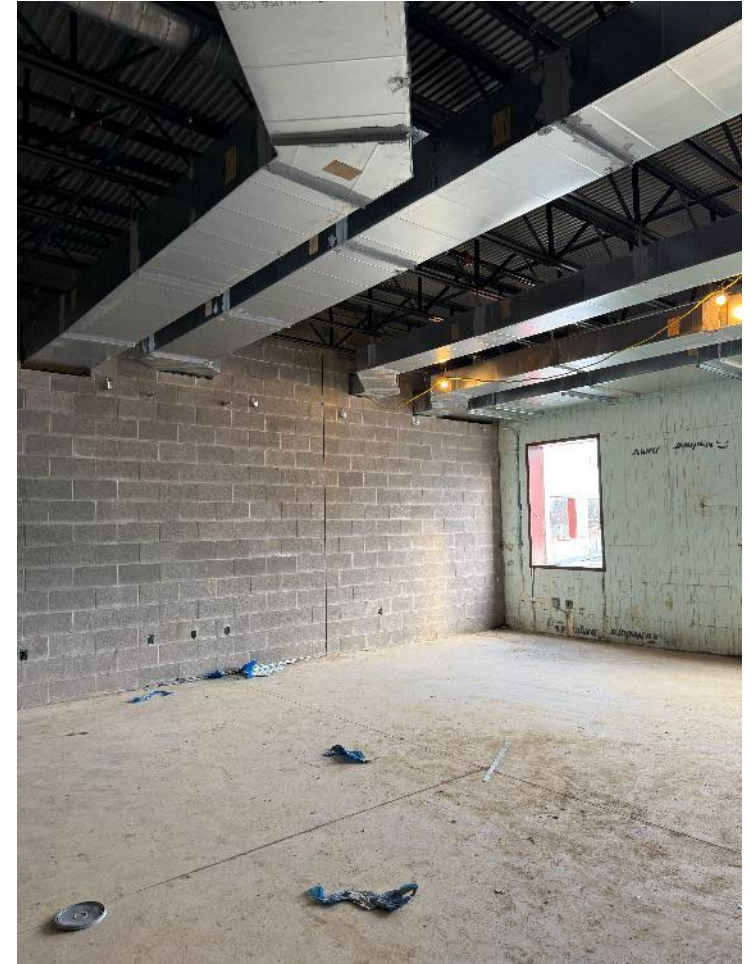

Week Ending December 05, 2025

New Henry Clay High School



Area D / Storm Shelter – ICF / IFA Installation and Laying CMU



Week Ending December 05, 2025

New Henry Clay High School

Area D / Storm Shelter – Installation of Hollow Core Concrete Floor Planks

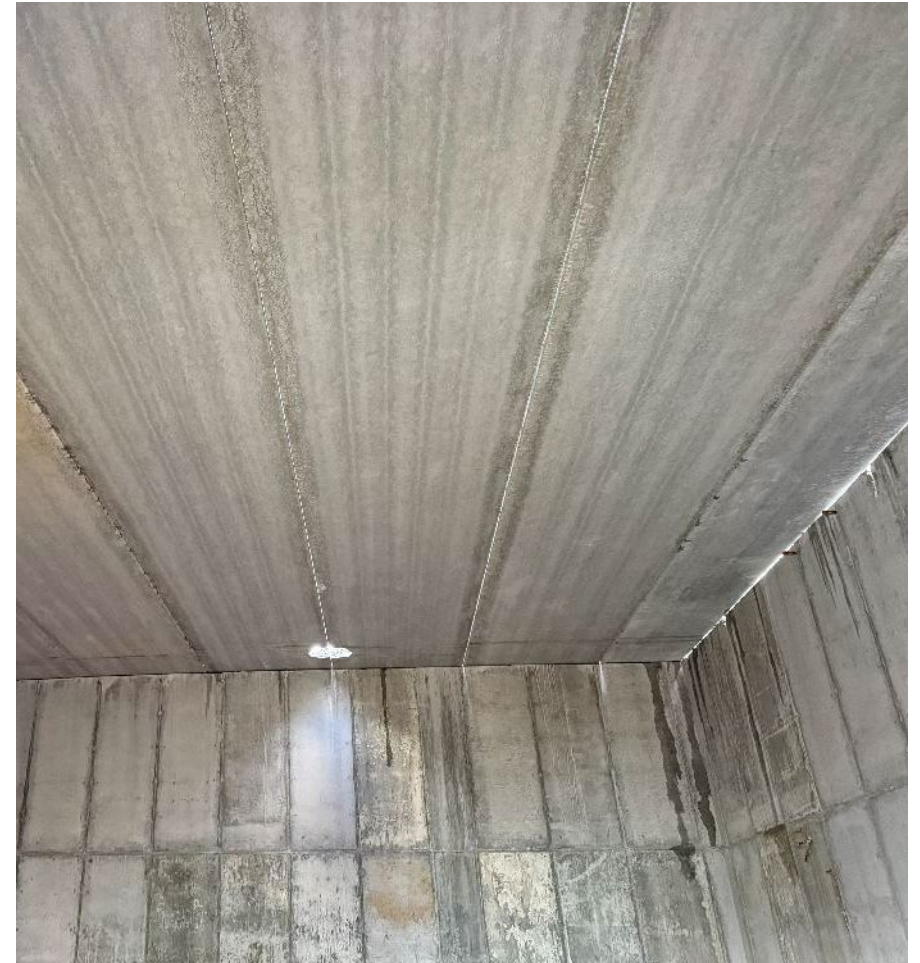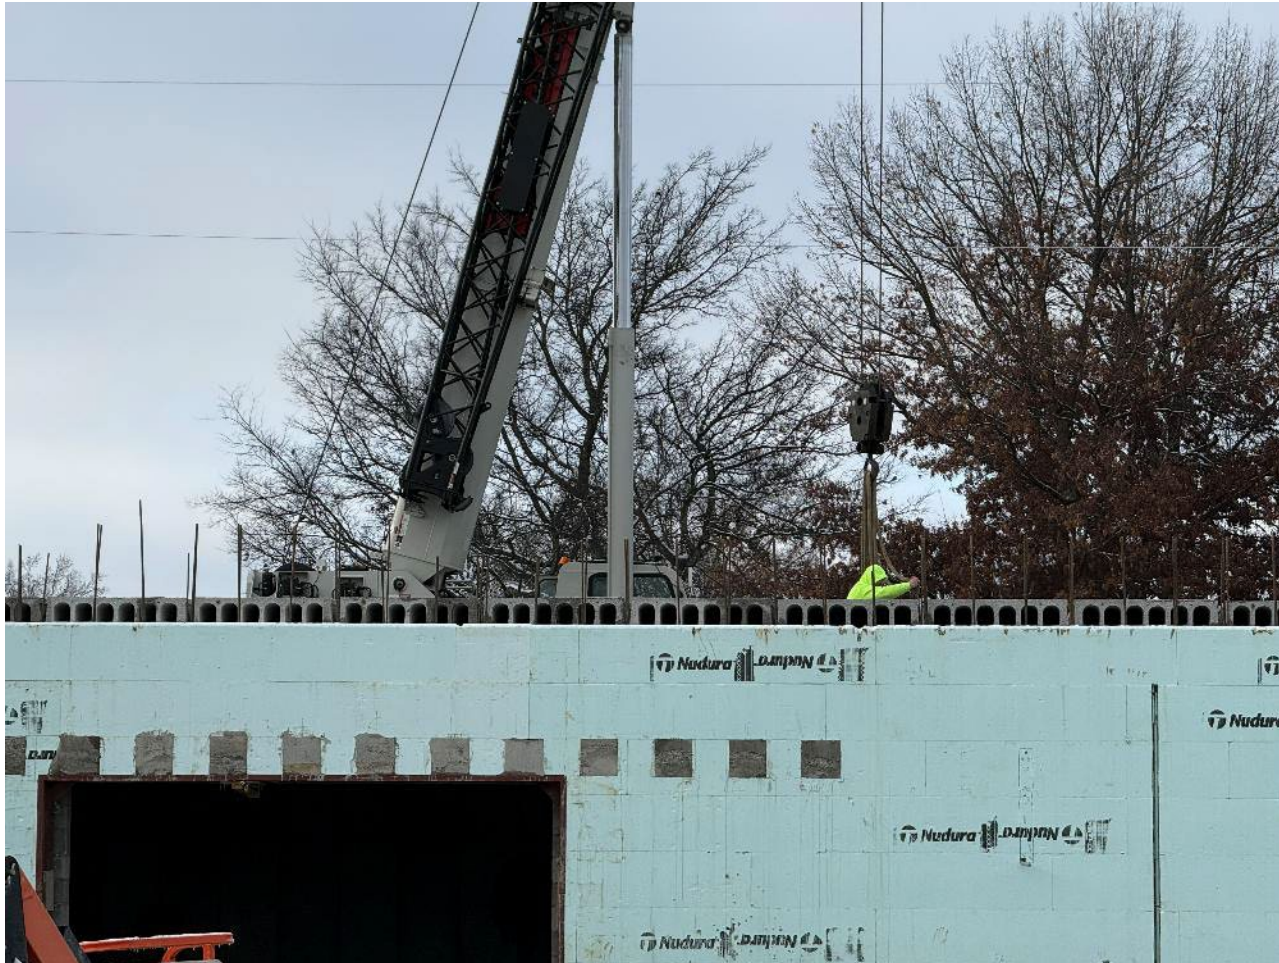

Week Ending December 05, 2025

New Henry Clay High School

Area B – Steel Erection – Installing Floor Joists



Week Ending December 05, 2025

New Henry Clay High School

Area B – ICF & IFA Installation, Framing Openings for Curtain Walls, Storefront, and Erecting Steel



Week Ending December 05, 2025
