



Projects in Construction

Cherokee HS Replacement

Replacement Facility

Carroll Daniel Construction

Substantial Completion: 12.2025



Anticipated Occupancy: 08.2026

- ADA and life safety inspections are being conducted in conjunction with fire alarm testing in the main academic building. Completion of punch list items on the first floor is underway and identification of similar items on the second and third floors is in development.
- Completion of punch list items in the CTAE building is in the final stages. ADA and life safety inspections are ongoing. Final inspections have been scheduled.
- The auditorium fixed seating and stage curtain installations have begun.
- Kitchen equipment and the casework installation are complete in the cafeteria. Kitchen hood inspections are underway.
- Above ceiling inspections continue in the main gym. The gym railing and locker installations are complete. The wood floor has been installed and is ready to be painted and sealed. The bleacher installation is progressing.
- Work at all fields continues for synthetic turf. Installation of the baseball and softball scoreboards is complete. Preparation for the track surfacing has commenced.
- Installation of the sidewalks continues, as well as sodding and tree installation for the entire campus. The courtyard concrete and parking lot striping continue. Campus signage installation has begun.



Capital Outlay Report

Work Session | 12.11.2025

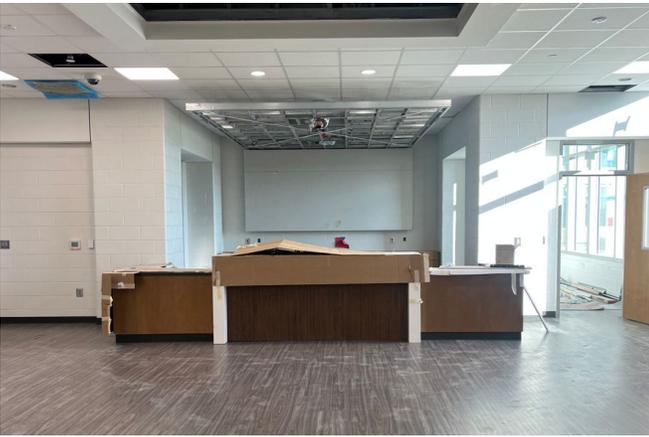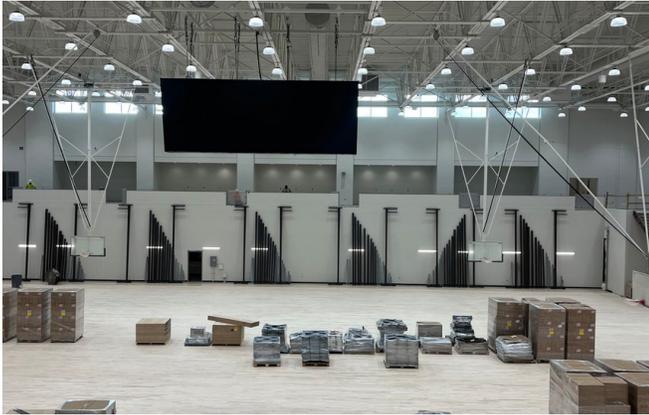



River Ridge HS



Auxiliary Gymnasium

SmithBuilt Construction Group

Substantial Completion: 04.2026

Anticipated Occupancy: 08.2026

- Installation of the roofing TPO is complete.
- Exterior brick installation is nearing completion.
- Overhead MEP, ductwork, and interior ceiling grid installation are ongoing.

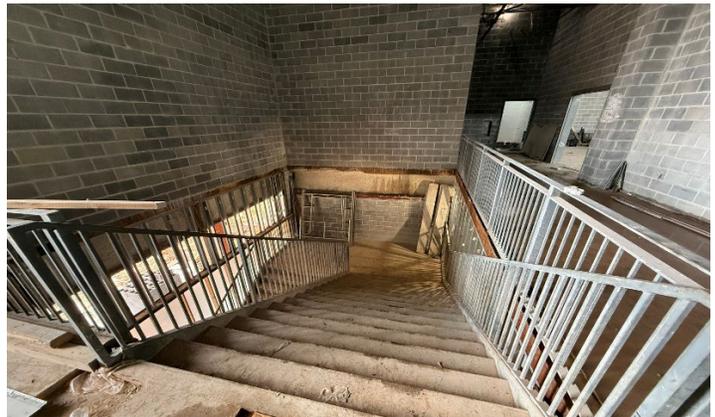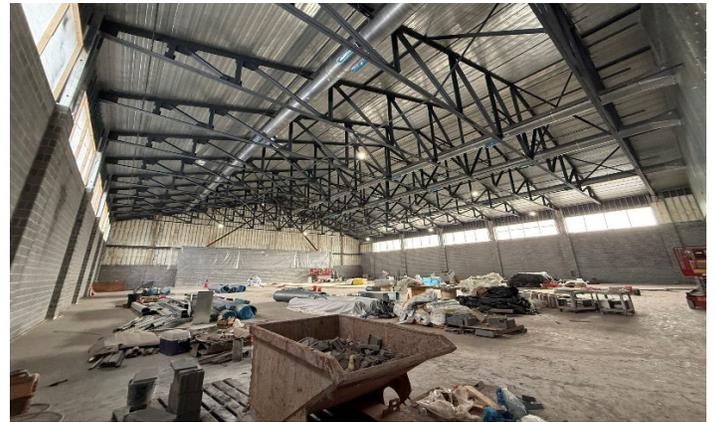



Sequoyah HS

Auxiliary Gym and Facility Improvements

(Press Box & Field House)

Carroll Daniel Construction

Substantial Completion: 11.2026

Anticipated Occupancy: 01.2027

- Steel erection is complete at the auxiliary gym. Roof decking and electrical service installation are underway. Placement of the exterior masonry walls has been scheduled.
- Re-route of the sanitary sewer and the scoreboard fiber and power at the home concessions is ongoing.
- The foundation wall pour is complete, and the forms have been removed. Underground MEP activities have begun, along with the slab preparation.
- Layback and grading at the home field house are complete. Placement of the foundation is scheduled to begin.



Capital Outlay Report

Work Session | 12.11.2025



Woodstock HS

Classroom Addition

SmithBuilt Construction Group

Substantial Completion: 01.2026

Anticipated Occupancy: 08.2026

- Final state and county inspections have been scheduled for the first two weeks in December.
- Completion of punch list items is wrapping up.
- Furniture has been ordered and is scheduled for delivery and installation in late February.
- Project is on schedule for student occupancy in August 2026.

