




Monthly Progress Report

December 2025

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **December 2025**

Section III – Work Projected for **January 2026**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary December 2025

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress December 2025

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continued installing drainage pools throughout site.
 - Completed 75% of footings and poured concrete.
 - Started installing foundation walls formwork and rebar. About 30% completed.
- **Relle:**
 - Continued the rough-in for existing classrooms and the boiler room.
 - Excavated for underground feed from the new transformer to new addition.
- **Hirsch:**
 - Continued installing new gas main feed in the boiler room.
 - Continued installing new domestic water feed in the boiler room.
 - Installed partial sleeves in foundation walls.



Section III - Work Planned January 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue installing form work and rebar for foundation walls.
 - Pour concrete as needed for foundation walls.
 - Start interior building footings and foundation walls.
- **Relle:**
 - Continue roughing for existing building and boiler room.
 - Continue to install underground feeds for new addition.
- **Hirsch:**
 - Continue gas piping in the boiler room.
 - Install hot water heater in the boiler room.



Section IV – Progress Photos



Hempstead ABGS MS – New Gas Feed



Section IV – Progress Photos



Hempstead ABGS MS – New Domestic Water



Section IV – Progress Photos



Hempstead ABGS MS – Footings & Foundation wall Rebar



Section IV – Progress Photos



Hempstead ABGS MS – Footings & Foundation wall Rebar



Section IV – Progress Photos



Hempstead ABGS MS – Concrete Pours



Section IV – Progress Photos




Hempstead ABGS MS – Concrete Pours



Section V – Workforce Summary – Company/Hours

December 2025

MANPOWER GRAPH

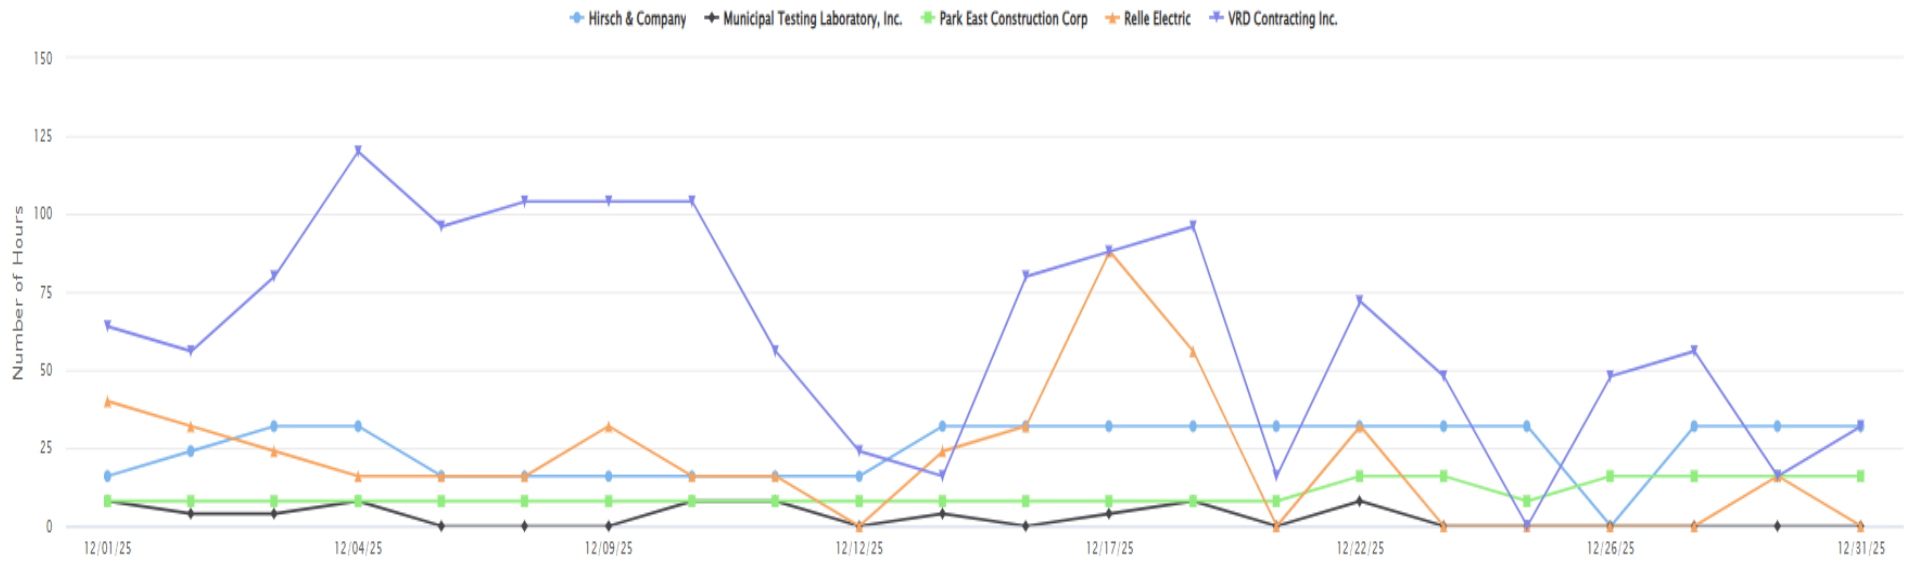

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)
December 2025

End of Progress Report
