




Monthly Progress Report

January 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **January 2026**

Section III – Work Projected for **February 2026**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary January 2026

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress January 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continued installing drainage pools throughout site.
 - Completed installation of Foundation walls formwork and rebar. About 70% completed.
- **Relle:**
 - Continued the rough-in for existing classrooms and the boiler room.
 - Excavated for underground feeds throughout new addition.
- **Hirsch:**
 - Continued installing new gas main feed in the boiler room. Completed 90%.
 - Continued installing new domestic water feed in the boiler room. Completed 90%.
 - Installed partial sleeves in foundation walls.
 - Started domestic water piping in the crawl space of existing building.



Section III - Work Planned February 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue installing form work and rebar for foundation walls. Complete all walls.
 - Pour concrete as needed for foundation walls.
 - Start interior building footings and column piers.
- **Relle:**
 - Continue roughing for existing building and boiler room.
 - Continue to install underground feeds for new addition as needed.
- **Hirsch:**
 - Continue crawl space domestic water piping.




Section IV – Progress Photos



Hempstead ABGS MS – New Gas Feed



Section IV – Progress Photos

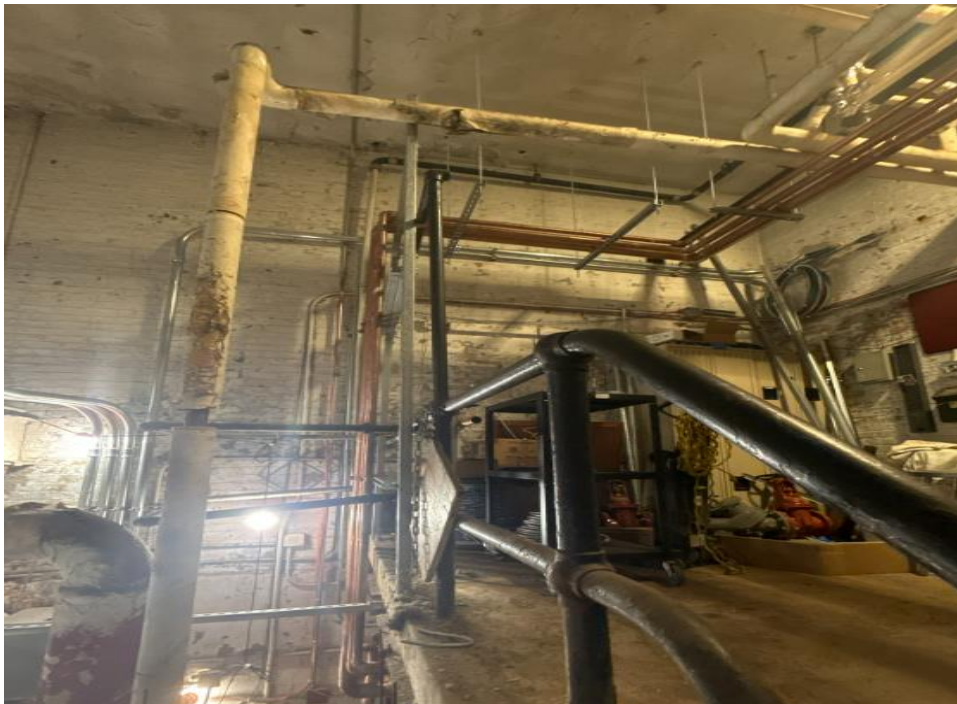

Hempstead ABGS MS – New Domestic Water



Section IV – Progress Photos



Hempstead ABGS MS – Foundation wall Forms/Rebar



Section IV – Progress Photos



Hempstead ABGS MS – Foundation wall Forms/Rebar



Section IV – Progress Photos



Hempstead ABGS MS – Foundation wall Forms/Rebar



Section IV – Progress Photos




Hempstead ABGS MS – Concrete Pours



Section V – Workforce Summary – Company/Hours

January 2026

MANPOWER GRAPH

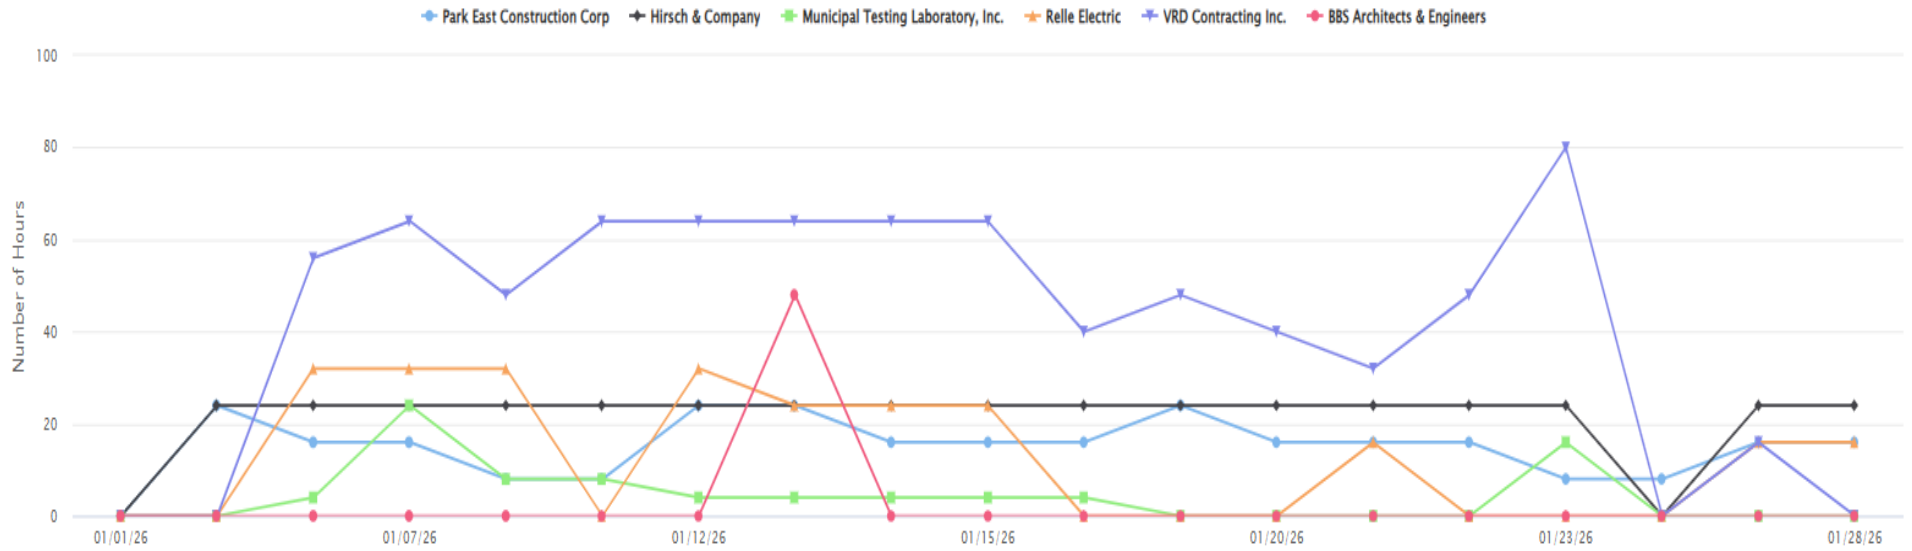

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

January 2026

End of Progress Report
