



JANUARY 2026 BOND OVERSIGHT COMMITTEE MEETING



AGENDA

- Welcome and Introductions
- 2024 Bond Projects – General Information
- 2024 Bond Projects – Project-by-Project Update
- Committee Business
- What's Ahead
- Wrap Up
- Adjourn

WELCOME

- Opening Remarks
- Introductions
- What are you hearing about the bond projects?

3

2024 Bond Projects General Information

4

2024 Bond Projects – General Information

- Overall 2024 Bond Projects Budget

2024 Bond Projects - Schedules and Cash Flow

Bond Sales		\$175m	\$150m	\$275m	\$132m					\$732m
Projects	Budget	2024/2025	2025/2026	2026/2027	2027/2028	2028/2029	2029/2030	2030/2031	2031/2032	Totals
BLHS Classroom Addition & Intersection	\$76.9m	\$2.0m	\$6.0m	\$40.0m	\$28.9m					\$76.9m
Sumner HS Phase 2 West Building	\$114.0m	\$2.0m	\$6.0m	\$40.0m	\$40.0m	\$26.0m				\$114.0m
New Middle School at Tehaleh	\$200.0m	\$2.0m	\$6.0m	\$20.0m	\$88.0m	\$84.0m				\$200.0m
Liberty Ridge Elementary Improvements	\$2.9m		\$0.8m	\$1.4m	\$0.6m					\$2.9m
Crestwood Elementary Improvements	\$2.9m		\$0.8m	\$1.4m	\$0.6m					\$2.9m
Tehaleh Heights Elementary Expansion	\$19.0m		\$1.0m	\$3.0m	\$15.0m					\$19.0m
Donald Eismann Ele. Queueing, Parking & Field	\$7.8m		\$1.0m	\$6.8m						\$7.8m
Daffodil Valley Ele. Field Improvements	\$6.0m			\$6.0m						\$6.0m
Sumner HS (Master Plan Build Out)	\$298.2m				\$2.0m	\$54.0m	\$116.2m	\$92.0m	\$34.0m	\$298.2m
Energy Efficiency Improvements*	\$4.0m	\$0.3m	\$0.8m	\$1.0m	\$0.5m	\$1.0m	\$0.5m			\$4.0m
Totals		\$6.3m	\$22.4m	\$119.7m	\$175.7m	\$165.0m	\$116.8m	\$92.0m	\$34.0m	\$731.8m
Ending Balance		\$168.8m	\$146.4m	\$26.7m	\$1.0m	\$111.0m	\$126.2m	\$34.2m	\$0.2m	
Actual Totals		\$4.2m								
Actual Ending Balance		\$170.8m								

2024 Bond Projects – Risks & Opportunities

- Risks**
 - Economy, including tariffs and inflation
 - Permit process timing
- Opportunities**
 - Early bid packages
 - Outreach to local, small and women/minority owned businesses

2024 BOND PROJECT UPDATES

7

Bonney Lake HS Expansion

PROJECT TEAM

Architect: BCRA, Inc.

GC/CM Contractor: Korsmo Construction

Structural Engineer: PCS Structural Solutions

Mechanical/Electrical Engineer: GFT

Civil Engineer: Sitts & Hill Engineers


Landscape Architect: Fora Landscape Architects

8

Bonney Lake HS Expansion

- Schematic Design (SD) and Value Engineering presented to School Board on January 20.
- Exterior and interior material and color palettes finalized.
- Design Development Phase underway.

9

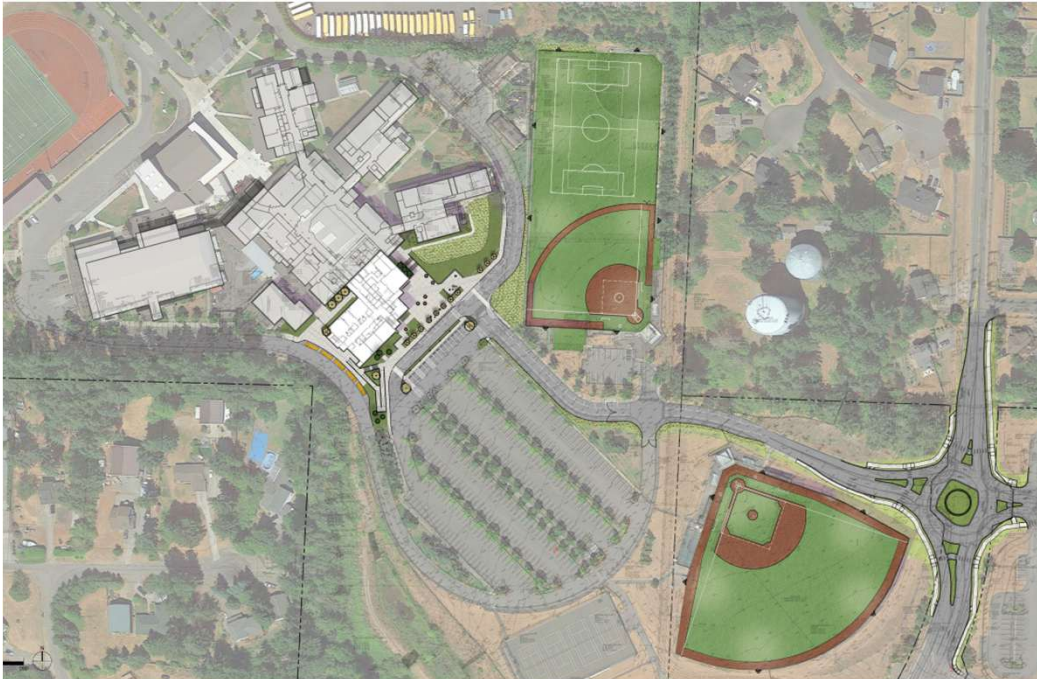

10

Exterior Materials - Options

ARCHITECTURE



OPTION 1 FROM MAIN ENTRY



OPTION 2 FROM MAIN ENTRY

Exterior EGD

OPTION 1




ILLUMINATED RECESSED LETTERING



WINDOW GRAPHICS



WELCOME CENTER

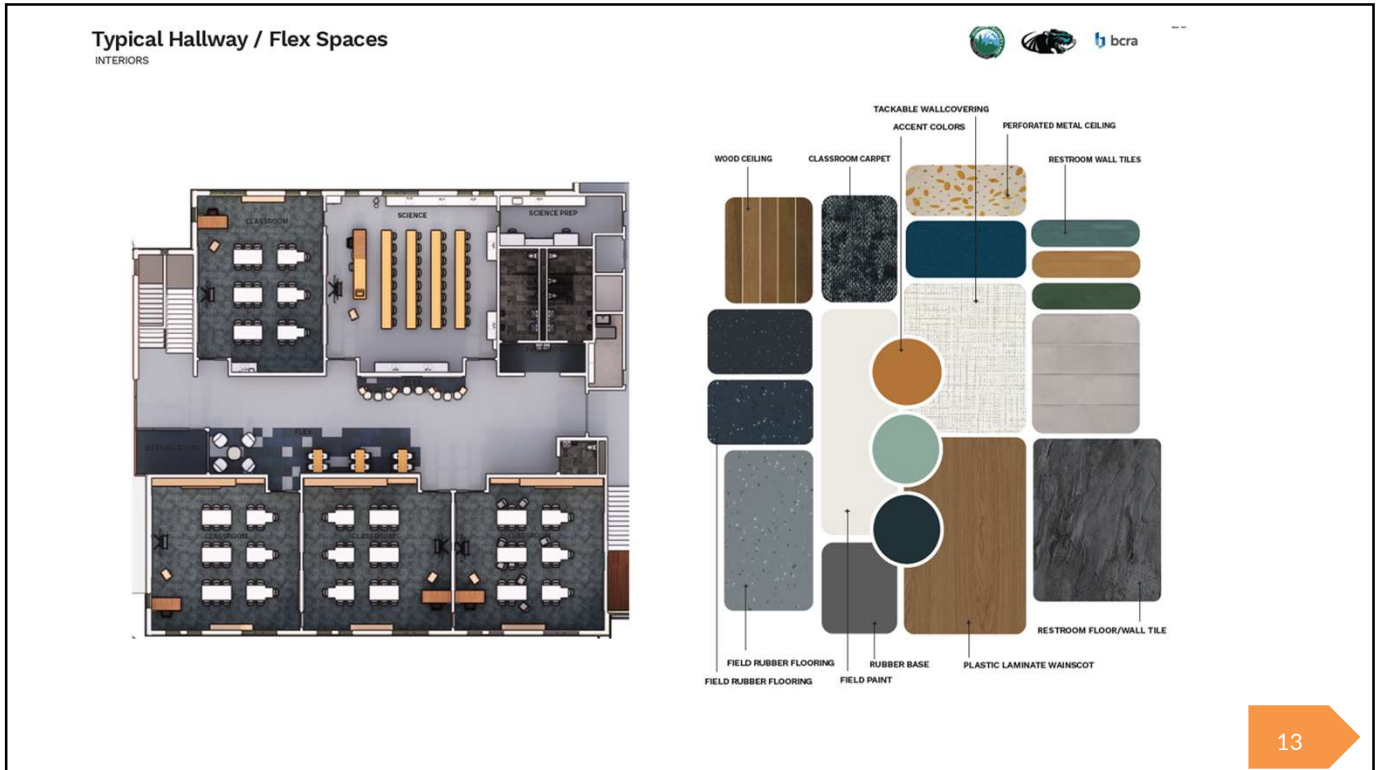

Bonney Lake HS Intersection

PROJECT TEAM

Prime Designer: Sitts & Hill Engineer

Traffic Engineer: Transpo


Landscape Architect: Fora Landscape Architects

Bonney Lake HS Intersection

- Initial comments on turning movement analysis received from City of Bonney Lake
- Traffic Impact Analysis submitted to City and first comment received
- Civil design underway.

15

Bonney Lake HS Intersection

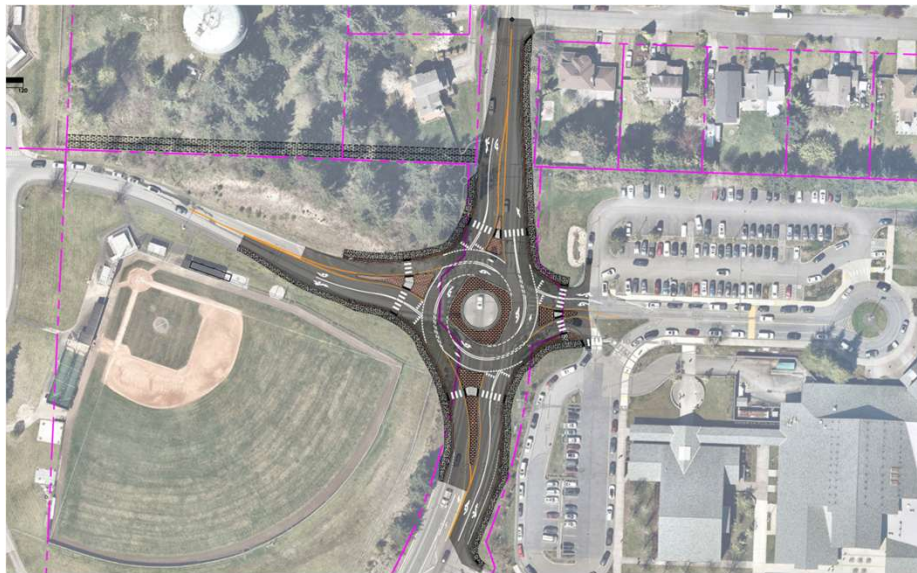

16

Bonney Lake HS Expansion & Intersection


Budget Status		
Project Budget (includes all contingencies)		\$ 76,882,286
Costs to Date		\$ 1,863,247
Percent Spent		2.4%
Project Contingencies		
Construction		\$ 4,934,054
Support Costs		\$ 1,520,548
Program		\$ 1,537,645
Contingency Accessed to Date		\$ 0

17

Bonney Lake HS Expansion & Intersection

- Schedule

BLHS	958 days	Mon 2/3/25	Wed 10/4/28	14%	
BLHS Expansion	958 days	Mon 2/3/25	Wed 10/4/28	13%	
Edspec	75 days	Mon 2/3/25	Fri 5/16/25	100%	2
Schematic Design	79 days	Tue 5/13/25	Fri 8/29/25	90%	18FS-4 days
Design Development	90 days	Mon 9/1/25	Fri 1/2/26	0%	19
Construction Drawings	150 days	Mon 1/5/26	Fri 7/31/26	0%	20
Permit	150 days	Mon 1/5/26	Fri 7/31/26	0%	20
Bid	20 days	Mon 8/3/26	Fri 8/28/26	0%	21
Construct	523 days	Mon 8/31/26	Wed 8/30/28	0%	23
Occupy	25 days	Thu 8/31/28	Wed 10/4/28	0%	24
BLHS Intersection	555 days	Wed 2/5/25	Tue 3/23/27	14%	
Develop Civil & LS Drawings	160 days	Wed 2/5/25	Tue 9/16/25	50%	2
Permit	150 days	Wed 9/17/25	Tue 4/14/26	0%	27
Bid	45 days	Wed 4/15/26	Tue 6/16/26	0%	28
Construct	180 days	Wed 6/17/26	Tue 2/23/27	0%	29
City Acceptance	20 days	Wed 2/24/27	Tue 3/23/27	0%	30

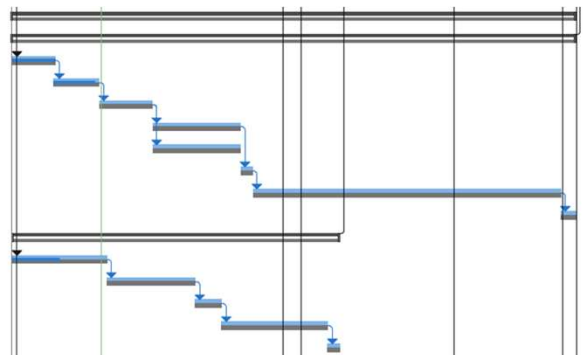

18

Sumner High School Master Plan

PROJECT TEAM

Architect: Hutteball + Oremus Architecture, Inc.

GC/CM Contractor: Skanska USA Building

Structural Engineer: PCS Structural Solutions

Mechanical Engineer: Metrix Engineers

Electrical Engineer: Hargis Engineers

Civil Engineer: Jacobsen Consulting Engineers

Landscape Architect: For a Landscape Architects


19

Sumner High School Master Plan

- GC/CM chosen and under contract.
- Construction Documents underway.
- Exterior and interior material and color palettes under review.
- Value Engineering presented to the School Board at the December 16 board meeting.

20


Sumner HS Phase II

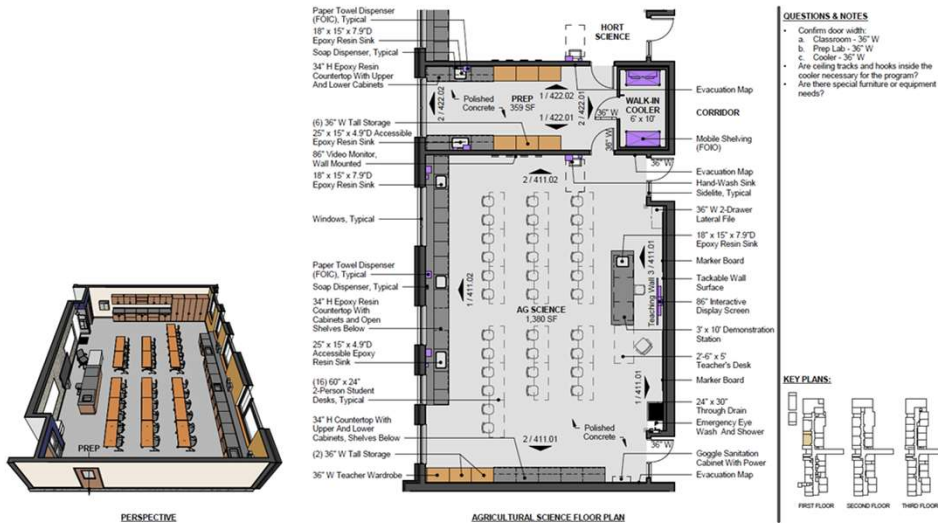

HUTTEBALL + OREMUS
4010 LAKE WASHINGTON BLVD NE, SUITE 320, KIRKLAND, WA 98033
P 425.828.8948 W | HDMARCH.COM

300/400 - CAREER & TECHNICAL EDUCATION // AGRICULTURAL SCIENCE LAB
SUMNER HIGH SCHOOL ADDITION - PHASE II
SUMNER-BONNEY LAKE SCHOOL DISTRICT
411.00

Sumner HS Phase II

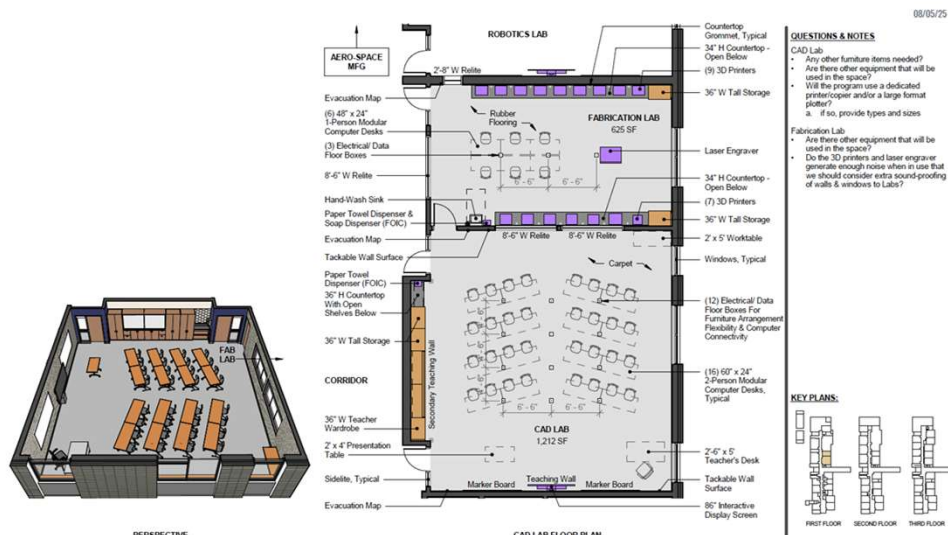

HUTTEBALL + OREMUS
4010 LAKE WASHINGTON BLVD NE, SUITE 320, KIRKLAND, WA 98033
P 425.828.8948 W | HDMARCH.COM

300/400 - CAREER & TECHNICAL EDUCATION // CAD LABS & FABRICATION LAB
SUMNER HIGH SCHOOL ADDITION - PHASE II
SUMNER-BONNEY LAKE SCHOOL DISTRICT
351.00

Sumner HS Phase II



23

Sumner High School Master Plan – West Building


Budget Status		
Project Budget (includes all contingencies)		\$113,540,360
Costs to Date		\$ 3,551,314
Percent Spent		3.1%
Project Contingencies		
Construction		\$ 7,947,825
Support Costs		\$ 3,000,000
Program		\$ 2,000,000
Contingency Accessed to Date		\$ 0

24

Sumner High School Master Plan

- Schedule

SHS Phase 2 - West Building	950 days	Wed 2/5/25	Tue 9/26/28	13%	
EdSpec	80 days	Wed 2/5/25	Tue 5/27/25	100%	2
Schematic Design	75 days	Wed 4/30/25	Tue 8/12/25	80%	33FS-20 days
Design Development	110 days	Wed 8/13/25	Tue 1/13/26	0%	34
Construction Drawings	150 days	Wed 1/14/26	Tue 8/11/26	0%	35
Permit	150 days	Wed 1/14/26	Tue 8/11/26	0%	35
Bid	30 days	Wed 8/12/26	Tue 9/22/26	0%	36
Construct	500 days	Wed 9/23/26	Tue 8/22/28	0%	38,37
Occupy	25 days	Wed 8/23/28	Tue 9/26/28	0%	39



25

New Middle School @ Tehaleh

PROJECT TEAM

Architect: McGranahanPBK

Structural Engineer: PCS Structural Solutions

Mechanical/Electrical Engineer: Hargis Engineers

Civil Engineer: Sitts & Hill Engineers

Landscape Architect: Fora Landscape Architects


26

New Middle School @ Tehaleh


- Schematic Design presented to the School Board at the December 16 board meeting.
- Test wells for ground-source heat pumps underway.
- Design Development underway.

27

New

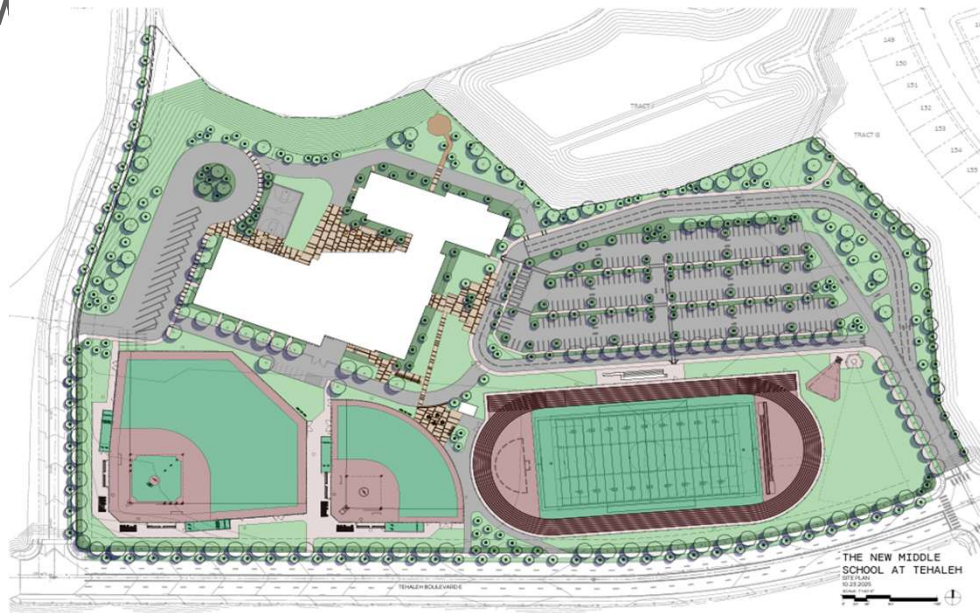

28

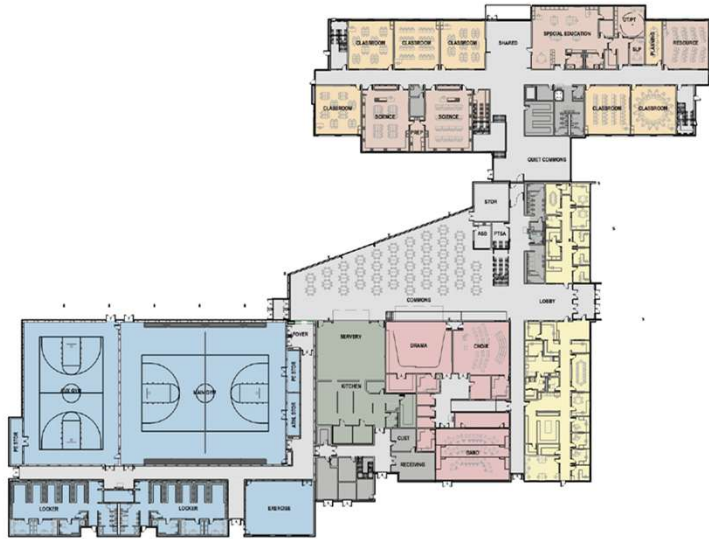

- ADMINISTRATION
- ADMINISTRATION - STUDENT SERVICES
- BLDG SUPPORT - CIRCULATION
- BLDG SUPPORT - MECH, TOILETS, STORAGE
- COMMON AREAS - COMMONS
- CORE INSTRUCTION - GENERAL
- CORE INSTRUCTION - LAB
- SPECIALIZED INSTRUCTION
- SPECIALTIES - ART, MUSIC
- SPECIALTIES - PE, GYM
- STUDENT DINING / FOOD SERVICE
- STUDENT SUPPORT - SHARED LEARNING



First Floor Plan

New Middle School at Totalin



Main Entrance Aerial



Main Entrance

31



Commons

32


New Middle School @ Tehaleh

Budget Status		
Project Budget (includes all contingencies)		\$200,000,000
Costs to Date		\$ 1,728,822
Percent Spent		0.86%
Project Contingencies		
Construction		\$ 9,280,592
Support Costs		\$ 8,000,000
Program		\$ 3,000,000
Contingency Accessed to Date		\$ 0

New Middle School @ Tehaleh

- Schedule

Tehaleh Middle School	1035 days	Wed 2/5/25	Tue 1/23/29	10%	
EdSpec	100 days	Wed 2/5/25	Tue 6/24/25	100%	2
Schematic Design	100 days	Wed 6/25/25	Tue 11/11/25	20%	42
Design Development	120 days	Wed 11/12/25	Tue 4/28/26	0%	43
Construction Drawings	160 days	Wed 4/29/26	Tue 12/8/26	0%	44
Permit	180 days	Wed 4/29/26	Tue 1/5/27	0%	44
Bid	30 days	Wed 12/9/26	Tue 1/19/27	0%	45
Construct	500 days	Wed 1/20/27	Tue 12/19/28	0%	46,47
Occupy	25 days	Wed 12/20/28	Tue 1/23/29	0%	48



Daffodil Valley Elementary Field Improvements

PROJECT TEAM

Landscape Architect: Second Nature Consulting

Civil Engineer: Momentum Civil

Architecture: Zervas Group

Structural Engineer: Kingworks

Mechanical/Electrical Engineer: Hultz BHU

35

Daffodil Valley Elementary Field Improvements

- Plans submitted to the City of Sumner for review and approval.
- Developing field lighting.
- Outdoor learning concept approved.

36


Daffodil Valley Elementary Field Improvements

Budget Status		
Project Budget (includes all contingencies)		\$ 6,022,014
Costs to Date		\$ 125,548
Percent Spent		2%
Project Contingencies		
Construction		\$ 281,000
Support Costs		\$ 480,000
Program		\$ 120,000
Contingency Accessed to Date		\$ 0

Daffodil Valley Elementary Field Improvements

- Schedule

Daffodil Valley Field	400 days	Mon 6/2/25	Fri 12/11/26	7%	
EdSpec	20 days	Mon 6/2/25	Fri 6/27/25	100%	
Schematic Design	30 days	Mon 9/29/25	Fri 11/7/25	20%	89
Design Development	40 days	Mon 11/10/25	Fri 1/2/26	0%	90
Construction Drawings	60 days	Mon 1/5/26	Fri 3/27/26	0%	91
Permit	120 days	Mon 1/5/26	Fri 6/19/26	0%	91
Bid	30 days	Mon 6/22/26	Fri 7/31/26	0%	93
Construct	90 days	Mon 8/3/26	Fri 12/4/26	0%	94
Occupy	5 days	Mon 12/7/26	Fri 12/11/26	0%	95



Donald Eismann Elementary Parking, Queuing and Field Improvements

PROJECT TEAM

Civil Engineer: Ethos Civil

Landscape Architect: KG Designs

Electrical Engineer: Tres West Engineers


41

Donald Eismann Elementary Parking, Queuing and Field Improvements

- Received approval from the Tehaleh Architectural Review Committee.
- Plans submitted to Pierce County for review and approval.

42

Donald Eismann Elementary Parking, Queuing and Field Improvements

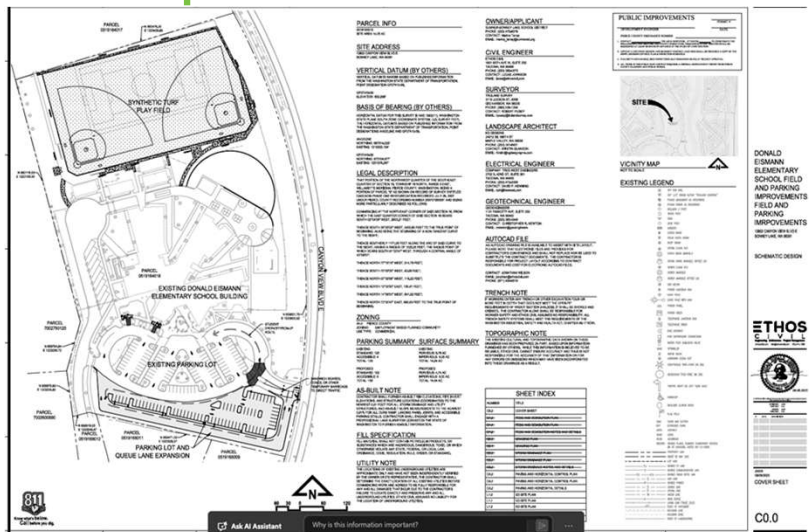


Donald Eismann Elementary Parking, Queuing and Field Improvements

Budget Status		
Project Budget (includes all contingencies)		\$ 7,806,605
Costs to Date		\$ 168,136
Percent Spent		2.2%
Project Contingencies		
Construction		\$ 364,308
Support Costs		\$ 624,528
Program		\$ 156,132
Contingency Accessed to Date		\$ 0

Donald Eismann Elementary Parking, Queuing and Field Improvements

- Schedule**

Donald Eisman Queueing & Field	370 days	Mon 6/2/25	Fri 10/30/26	8%	
EdSpec	20 days	Mon 6/2/25	Fri 6/27/25	100%	
Schematic Design	75 days	Mon 6/30/25	Fri 10/10/25	20%	80
Design Development	30 days	Mon 10/13/25	Fri 11/21/25	0%	81
Construction Drawings	45 days	Mon 11/24/25	Fri 1/23/26	0%	82
Permit	120 days	Mon 11/24/25	Fri 5/8/26	0%	82
Bid	30 days	Mon 5/11/26	Fri 6/19/26	0%	84
Construct	90 days	Mon 6/22/26	Fri 10/23/26	0%	85
Occupy	5 days	Mon 10/26/26	Fri 10/30/26	0%	86



45

Crestwood Elementary Improvements

PROJECT TEAM

Architect: Studio Meng Strazzara

Mechanical/Electrical Engineer: Hargis

46

Crestwood Elementary Improvements

- Scoping of project underway.
- Design concepts for security vestibule and front office in development.

47

Crestwood Elementary Improvements


Budget Status		048
Project Budget (includes all contingencies)		\$ 2,885,048
Costs to Date		\$ 21,015
Percent Spent		0.73%
Project Contingencies		
Construction		\$ 134,636
Support Costs		\$ 44,689
Program		\$ 223,751
Contingency Accessed to Date		\$ 0

48

Crestwood Elementary Improvements

- Schedule

Crestwood Improvements	640 days	Fri 6/27/25	Thu 12/9/27	8%	
Architect Selection	60 days	Fri 6/27/25	Thu 9/18/25	100%	
EdSpec	30 days	Fri 9/19/25	Thu 10/30/25	0%	61
Schematic Design	40 days	Fri 10/31/25	Thu 12/25/25	0%	62
Design Development	60 days	Fri 12/26/25	Thu 3/19/26	0%	63
Construction Drawings	90 days	Fri 3/20/26	Thu 7/23/26	0%	64
Permit	120 days	Fri 3/20/26	Thu 9/3/26	0%	64
Bid	30 days	Fri 7/24/26	Thu 9/3/26	0%	65
Construct	320 days	Fri 9/4/26	Thu 11/25/27	0%	67
Occupy	10 days	Fri 11/26/27	Thu 12/9/27	0%	68



Liberty Ridge Elementary Improvements

PROJECT TEAM

Architect: fi Archecture


Mechanical/Electrical Engineer: TBD

Liberty Ridge Elementary Improvements

- Scoping of project underway.
- Design concepts for security vestibule and front office in development.

51

Liberty Ridge Elementary Improvements

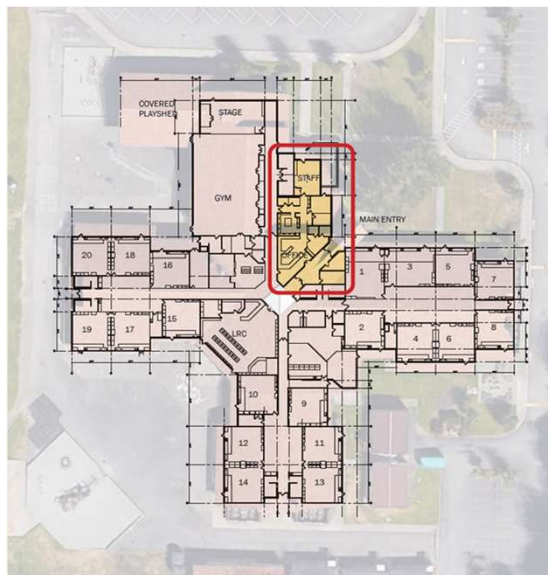

SCOPE OF WORK


Front Office Modernization

- Vestibule
- Reception Area
- Offices
- Staff Lounge
- Workroom
- Keep original bell out front



52

Liberty Ridge Elementary Improvements

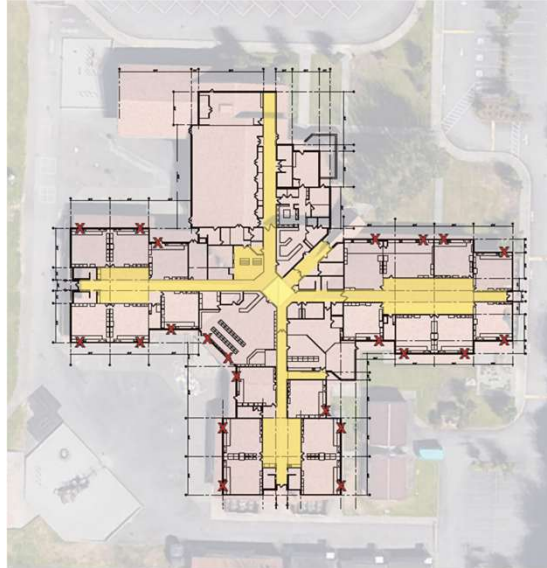


SCOPE OF WORK

Exterior Classroom Doors

- Remove and infill openings
- Improved access controls
- Revised exiting pathways



Liberty Ridge Elementary Improvements

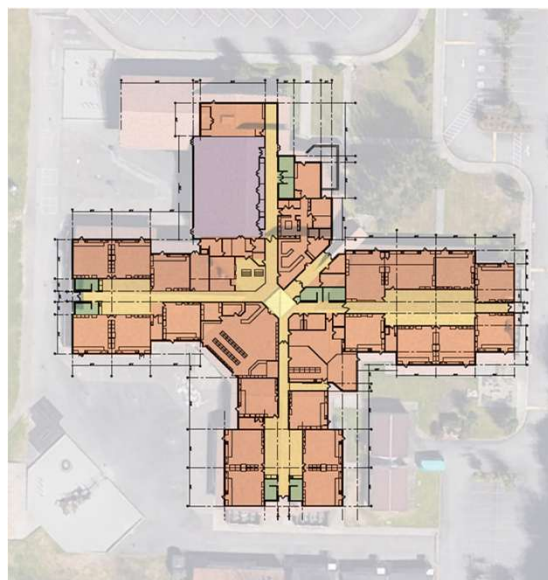

SCOPE OF WORK

New Interior Finishes

- New wood gym floor
- New flooring throughout
 - Classrooms
 - Corridors
 - Support spaces
- Paint walls throughout



Liberty Ridge Elementary Improvements


Budget Status		048
Project Budget (includes all contingencies)		\$ 2,885,048
Costs to Date		\$ 15,998
Percent Spent		0.55%
Project Contingencies		
Construction		\$ 134,636
Support Costs		\$ 44,689
Program		\$ 223,751
Contingency Accessed to Date		\$ 0

55

Liberty Ridge Elementary Improvements

- Schedule**

LRE Improvements	640 days	Fri 6/27/25	Thu 12/9/27	8%	
Architect Selection	60 days	Fri 6/27/25	Thu 9/18/25	100%	
EdSpec	30 days	Fri 9/19/25	Thu 10/30/25	0%	51
Schematic Design	40 days	Fri 10/31/25	Thu 12/25/25	0%	52
Design Development	60 days	Fri 12/26/25	Thu 3/19/26	0%	53
Construction Drawings	90 days	Fri 3/20/26	Thu 7/23/26	0%	54
Permit	120 days	Fri 3/20/26	Thu 9/3/26	0%	54
Bid	30 days	Fri 7/24/26	Thu 9/3/26	0%	55
Construct	320 days	Fri 9/4/26	Thu 11/25/27	0%	57
Occupy	10 days	Fri 11/26/27	Thu 12/9/27	0%	58



56

Tehaleh Heights Elementary Expansion

- **PROJECT TEAM**
- **Architecture:** McGranahanPBK
- **Mechanical/Electrical Engineer:** Hargis
- **Structural Engineer:** PCS Structural Solutions
- **Landscape Architect:** Fora Landscape Architects
- **Civil Engineer:** Sitts & Hill

57

Tehaleh Heights Elementary Expansion

- Received Project Review Committee approval for GC/CM on December 5
- Advertised for Statements of Qualification December 8th.
- Interactive meetings with GC/CM candidates on January 28.
- Selection to the School Board on February 19.

58

Tehaleh Heights Elementary Expansion



59

Tehaleh Heights Elementary Expansion



60

Tehaleh Heights Elementary Expansion


Budget Status		
Project Budget (includes all contingencies)		\$19,019,250
Costs to Date		\$ 9,632
Percent Spent		0.05%
Project Contingencies		
Construction		\$ 1,318,985
Support Costs		\$ 237,016
Program		\$ 16,500
Contingency Accessed to Date		\$ 0

61

Tehaleh Heights Elementary Expansion

- Schedule

Tehaleh Heights Elementary	763 days	Mon 9/22/25	Wed 8/23/28	0%	
EdSpec	53 days	Mon 9/22/25	Wed 12/3/25	0%	
Schematic Design	60 days	Thu 12/4/25	Wed 2/25/26	0%	71
Design Development	110 days	Thu 2/26/26	Wed 7/29/26	0%	72
Construction Drawings	150 days	Thu 7/30/26	Wed 2/24/27	0%	73
Permit	120 days	Thu 7/30/26	Wed 1/13/27	0%	73
Bid	50 days	Thu 1/14/27	Wed 3/24/27	0%	75
Construct	350 days	Thu 3/25/27	Wed 7/26/28	0%	76
Occupy	20 days	Thu 7/27/28	Wed 8/23/28	0%	77



62

COMMITTEE BUSINESS

63

COMMITTEE BUSINESS

- **BOC Meeting #3 requests**
- **Draft outline of Annual Community/School Board Report**
- **Committee Discussion**

64

Questions / Requests from September BOC Meeting

Asked

1. Input on what to include in annual report

Response

1. All included in detailed outline

65

65



Annual Report

- I. Introduction & executive summary
- II. BOC makeup and activities
- III. Bond funding overview
- IV. BOC's work
- V. BOC's findings
- VI. BOC's recommendations
- VII. Next year's forecast
- VIII. Any proposed changes to project schedules, sequences or finances

66

BOC Key Findings, Recommendations, and Proposed Changes

- Are funds being spent appropriately and in compliance with the bond measure?
- Any risks and opportunities to address?
- Are projects progressing according to the Master Schedule?
- Is communication between the District, Project Managers, and the BOC effective?
- Anything else you want to add to this section?

67

Conclusion and Appreciation

- What do you want to say?

68

BOC Meeting Outcomes

We learned about:

- .

Key messages:

- .

WHAT'S
AHEAD

WHAT'S AHEAD

- Preview of Meeting #4, January 26, 2026 (inclement weather – virtual option)
- Annual Report review and revise as needed - seeking consensus
- Questions for BOC Discussion at January meeting

71

WRAP UP

72

WRAP UP

- **Key messages**
 - **What were the key outcomes of this meeting?**
- **Evaluation**
- **Process**
 - **Content**
 - **Discussions**
- **Gratitude and adjournment**

73



THANK YOU

74
