




Monthly Progress Report

February 2026

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress February 2026

Section III – Work Projected for March 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

February 2026

Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
 - Staircase railings upgrades.
 - Classroom wall upgrades per code.
 - Install eye wash stations.
 - Install new exhaust fans.
 - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
 - Remove old asphalt tennis grounds.
 - Install new tennis courts with bleachers.
 - Install a bridge for students to access the tennis courts.
- **Hempstead UFSD – Window replacement at McNeil and Paterson elementary school – In Progress**
 - Removal of caulking under abatement.
 - Removal of existing windows.
 - Installation of new windows and new caulking.
- **Hempstead UFSD – Boiler replacement at McNeil elementary school – In Progress**
 - Boiler and piping replacement.
- **Hempstead UFSD – IAQ at Various School – In Progress**
 - Indoor air quality and mechanical upgrades.
 - Electrical upgrades.
- **Hempstead UFSD – 2022 Bond Phase 3 – In Progress**

Infrastructure upgrades throughout all schools.



Section II - Work Progress February 2026

Hempstead UFSD – HS Priority Infrastructure Upgrades

- **Total:**
 - Completed Handi-lift installation.

Hempstead UFSD – HS Tennis Courts

- **United Paving:**
 - Installed bridge.

Hempstead UFSD – Window replacement

- **Arrow Steel Windows:**
 - Started replacing windows. About 75% complete.

Hempstead UFSD – Boiler replacement

- **Thermotech:**
 - Received punch list from BBS.

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Continuing of low voltage wiring at McNeil and Paterson.
 - Working on BMS for McNeil and Paterson.
- **Eldor:**
 - Continued roughing in ceilings and on walls at Paterson ES and McNeil ES.
 - Installed transformer pad at Paterson.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Completed abatement at Obama ES.
 - Completed openings for HVAC work.
- **IPS:**
 - Installed eye wash stations, sinks, bubblers, and drinking fountains.



Section III - Work Planned March 2026

Hempstead UFSD – HS Priority Infrastructure Upgrades

- **Total:**
 - Complete Handi-lift training to staff.

Hempstead UFSD – HS Tennis Courts

- **United Paving**
 - Complete remaining asphalt walkways and punch list items.

Hempstead UFSD – Window replacement

- **Arrow steel windows**
 - Continue replacing windows at Paterson ES.

Hempstead UFSD – Boiler replacement

- **Thermotech:**
 - Closeout process.

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Install chiller pad and bollards at Prospect ES.
 - Continue chilled water piping.
 - Continue low voltage roughing.
- **Eldor:**
 - Continue to rough in at Paterson ES, McNeil ES, and Prospect ES.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Continue making openings for HVAC work and install lintels as needed.




Section IV – Progress Photos



Hempstead IAQ – Paterson Transformer Pad



Section IV – Progress Photos

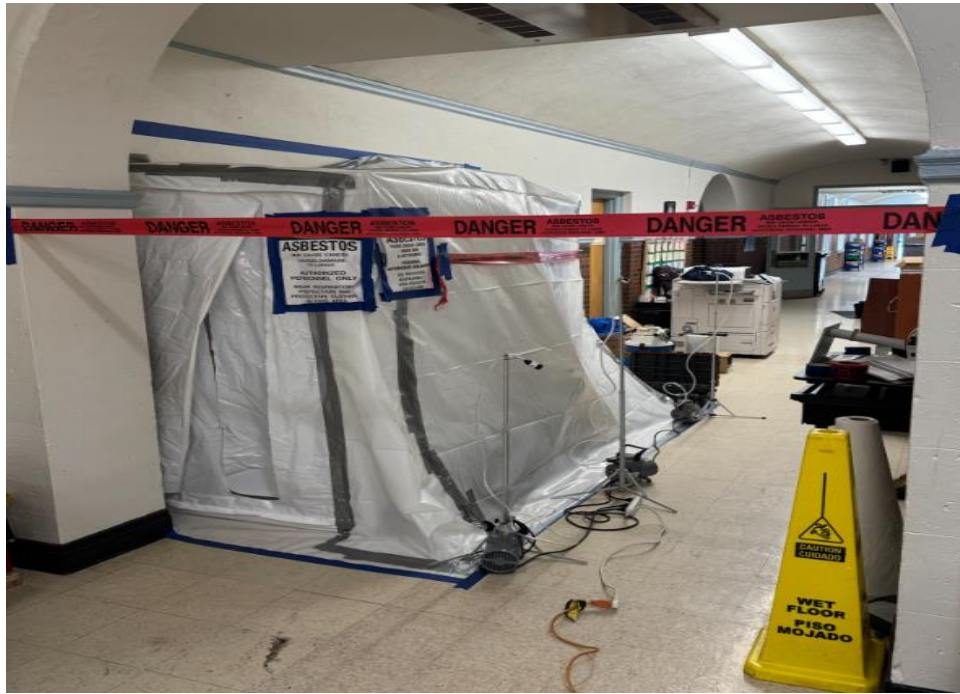

Hempstead 2022 Ph. 3 – Abatement and Openings



Section IV – Progress Photos



Hempstead UFSD – 2022 Bond Ph. 3



Section IV – Progress Photos




Hempstead UFSD – Window Replacements



Section V – Workforce Summary – Company/Hours

February 2026

▼ MANPOWER GRAPH

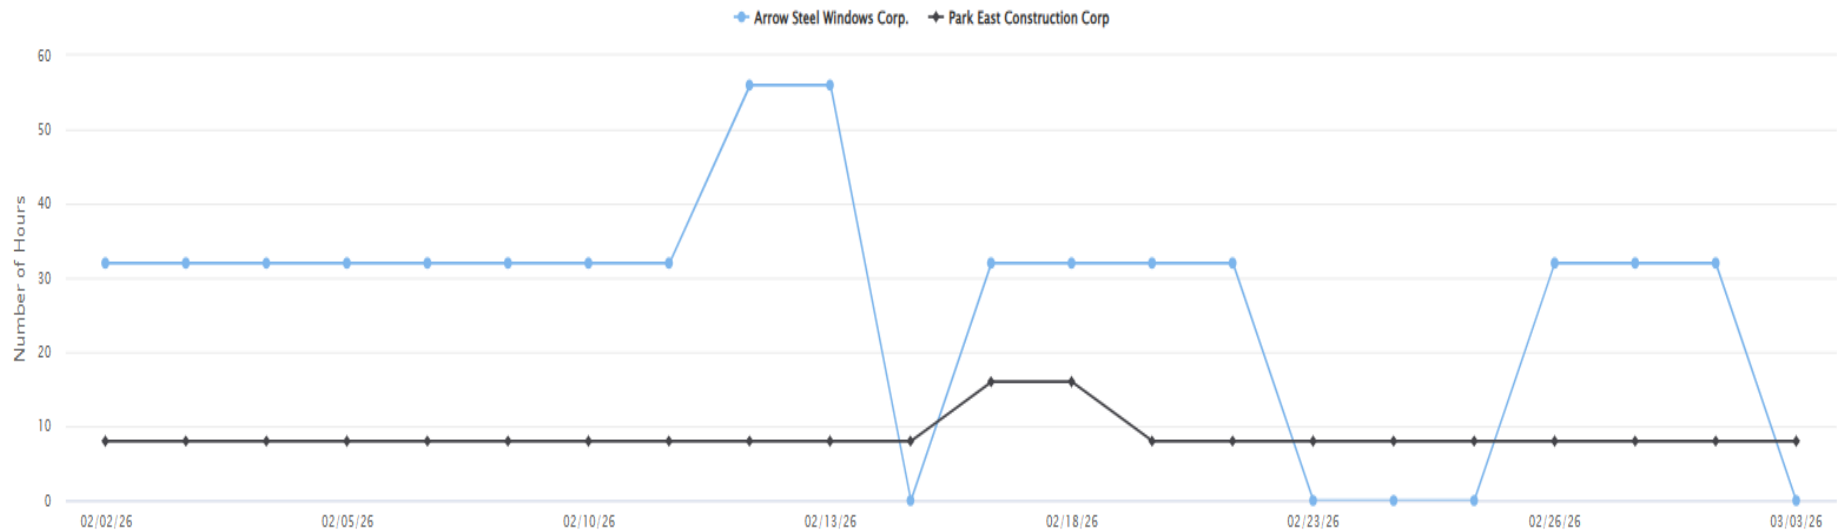


Hempstead UFSD – Window Replacement



Section V – Workforce Summary – Company/Hours

February 2026

MANPOWER GRAPH

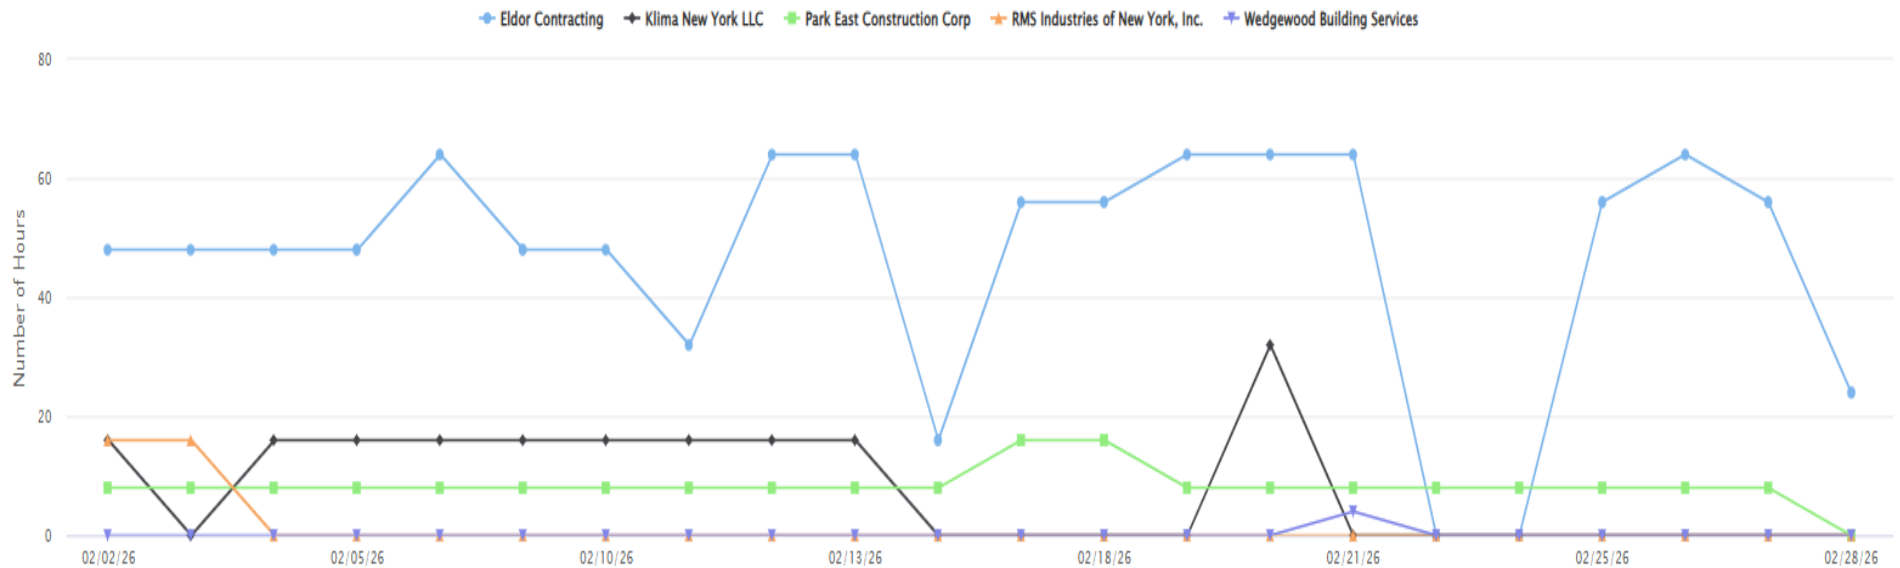


Hempstead UFSD – IAQ at Various Schools



Section V – Workforce Summary – Company/Hours

February 2026

MANPOWER GRAPH

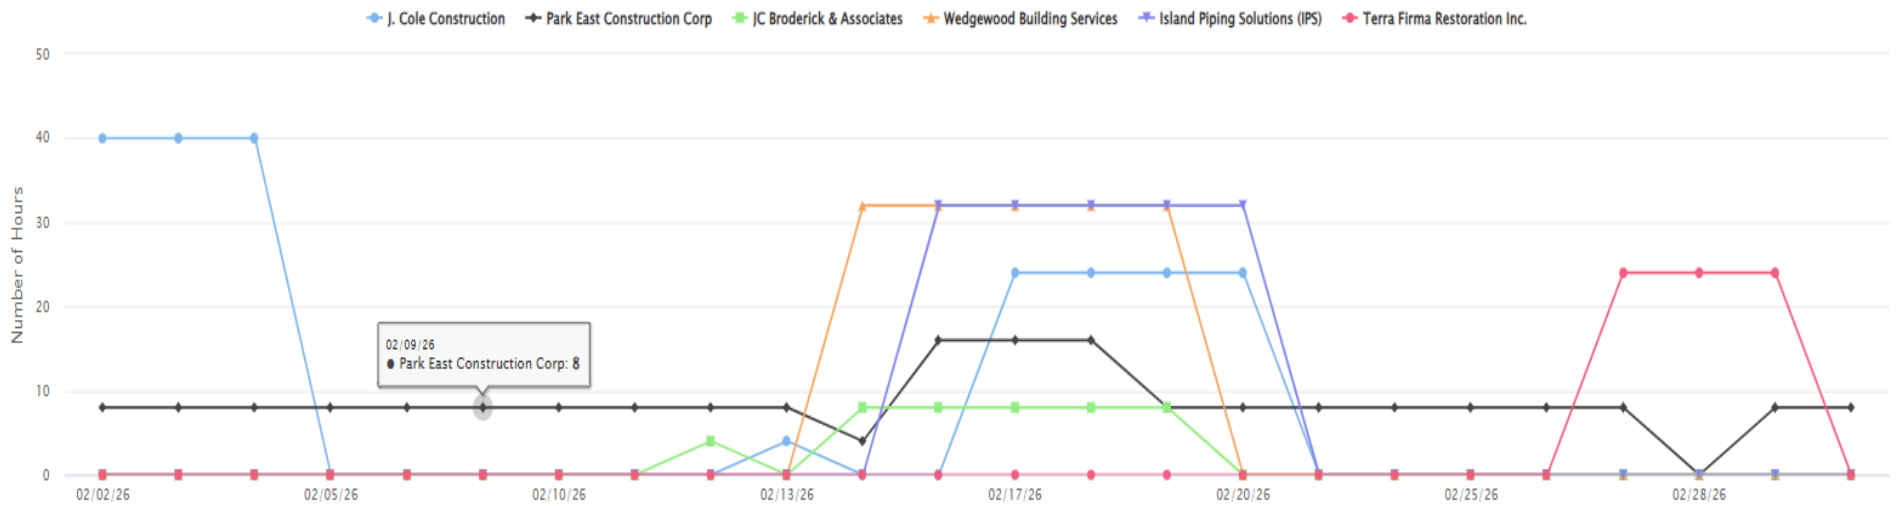

Hempstead UFSD – 2022 Bond Phase 3



Hempstead Union Free School District
February 2026

End of Progress Report
