



Citizen-Led Oversight Committee (CLOC) 2023 Bond Referendum

Twenty-Fourth Meeting
(Okatie Elementary School - Media Center and Via Zoom)
March 11, 2026

Pledge of Allegiance





CLOC's Mission

Independently monitor all building projects, schedules, budgets, and expenditures from the Beaufort County School District's Nov. 2023 Bond Referendum, thereby ensuring proper use of Beaufort County taxpayer funds and superior facilities for Beaufort County students.

PRESENTATION AGENDA



1. Pledge of Allegiance
2. Public Comments
3. Approval of Draft CLOC Meeting Minutes from January 14, 2026 & February 11, 2026
4. Glossary of Acronyms
5. February 2026 Master Schedule Updates
6. 2023 Bond Referendum Project Updates
7. 2023 Bond Referendum Financial Reports and Summary
 - A. Financial Summary Report
 - B. Project Level Financial Reports
 - C. Contingency Use Log
 - D. Financial Update

PRESENTATION

AGENDA



8. 2023 Bond Referendum Cash Flow Projections vs Actual Expenditures
9. 2023 Bond Referendum Community Outreach
10. 2023 Bond Referendum CLOC Sub-Committee Reports/Updates
11. 2023 Bond Referendum Forward Looking Items and Events
12. 2023 Bond Referendum Next Meeting April 8, 2026 (Location TBD)

4. Glossary of Acronyms



Glossary of Acronyms

A/E – Architect/Engineer

ADA – American with Disabilities Act

AHJ – Authority Having Jurisdiction

ATP – Authorization To Proceed

CATE – Career And Technology Education

CD – Construction Documents

CLOC – Citizen-Led Oversight Committee

CM – Construction Manager

CMU – Concrete Masonry Unit

CMAR – Construction Manager At Risk

CTE – Career and Technical Education

DD – Design Development

DOR – Designer Of Record

GMP – Guaranteed Maximum Price

IT – Information Technology

JCS – Jumper Carter Sease Architects

HCM – Hord Coplan Macht

HVAC – Heating, Ventilation and Air Conditioning

LDAC – Little Diversified Architectural Consulting

LGIP – Local Government Investment Pool

LULL – Mfg. of Const. Equipment (combo forklift & tractor)

MBK – M.B. Kahn Construction Co., Inc.

MCT – Marmoleum Composition Tile

MEP – Mechanical Electrical Plumbing

MOA – Memorandum Of Agreement

MOU – Memorandum Of Understanding



Glossary of Acronyms

- MWBE – Minority Women-owned Business Enterprises
- NTP – Notice To Proceed
- OSF – Office of School Facilities, SC Dept. of Education
- QAP – Quackenbush Architects and Planners
- RFI – Request For Information
- RFP – Request For Proposals
- RFQ – Request For Qualifications
- SD – Schematic Design
- TTC – Thompson Turner Construction
- VCT – Vinyl Composition Tile



School Acronyms

BCHS – Battery Creek High School

BES – Beaufort Elementary School

BHS – Beaufort High School

BLECC – Bluffton Early Childhood Center

BLES – Bluffton Elementary School

BLHS – Bluffton High School

BLMS – Bluffton Middle School

BMS – Beaufort Middle School

BRES – Broad River Elementary School

CES – Coosa Elementary School

DESC – District Educational Support Center

DIES – Daufuskie Island Elementary School

HEMMS – H.E. McCracken Middle School

HHIECC – Hilton Head Island Early Childhood Center

HHIES – Hilton Head Island Elementary School

HHIHS – Hilton Head Island High School

HHIMS – Hilton Head Island Middle School

HHISCA – Hilton Head Island School for The Creative Arts

JJDELCC – James J. Davis Early Learning Center

JSES – Joseph S. Shanklin Elementary School

LIES – Lady's Island Elementary School

LIMS – Lady's Island Middle School

MCRECC – M.C. Riley Early Childhood Center

MCRES – M.C. Riley Elementary School

MOES – Mossy Oaks Elementary School

MRES – May River Elementary School



School Acronyms

MRHS – May River High School
OES – Okatie Elementary School
PRES – Port Royal Elementary School
PVES – Pritchardville Elementary School
RCES – Red Cedar Elementary School
RRA – River Ridge Academy
RSLA – Robert Smalls Leadership Academy
RVCS – Riverview Charter School
SHELCH – St. Helena Early Learning Center
SHES – St. Helena Elementary School
WBECHS – Whale Branch Early College High School
WBES – Whale Branch Elementary School
WBMS – Whale Branch Middle School

5. February 2026 Master Schedule Updates



6. 2023 Bond Referendum Project Updates



May River Elementary School (Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
77 - May River Elementary School (AM)	New PreK-5 Elementary School	● 1	●

Status Flag Comments:

- 1 ● See 2023 Referendum Project Contingency Log for details



May River Elementary School (Quackenbush Architects and Planners/TTC)




- Area "A" (Front Office Area, Multipurpose Room and Media Center) Slab is complete; ICF is 50% complete
- Area "B" (Pre-K wing Kindergarten, ECSE Wing) – Foundations are complete; 1st floor ICF is 100% complete; Steel erection is scheduled to begin in March 2026
- Area "C" (kitchen, and 1st grade) ICF walls are in place in the classroom wing; Steel erection for the 2nd floor is complete; Concrete slab is scheduled to be in place in March 2026; Kitchen slab placement is complete; Masonry is scheduled to begin in March 2026
- Underground rough in for the building is complete
- Site utilities – Water line service is 40% complete; Storm Water is 60% complete
- Other Item(s) To Note: TTC Amendment No 08 for the Structural and Non-Structural Soil Import was executed in February 2026



May River Elementary School (Quackenbush Architects and Planners/TTC)



Phase 1 - February 2026 Progress Photos

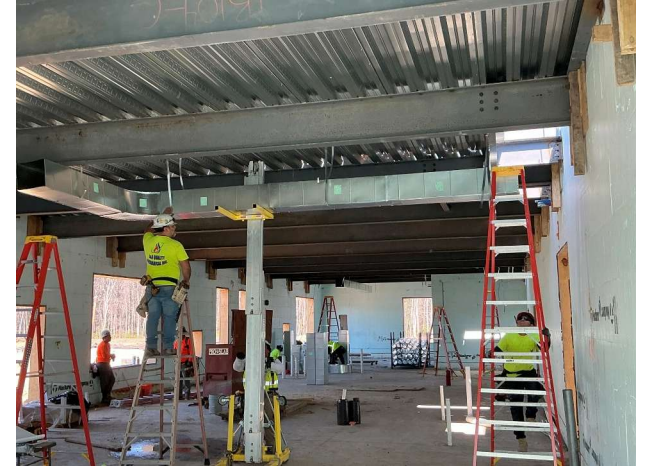

May River High School (Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
97 - May River High School (AM)	CTE/JROTC Addition and CTE Partial Renovations	●	●

- Auto lift has been installed; Plumber's scope is progressing
- Final testing is scheduled to occur the week of March 2, 2026, pending the arrival of the HVAC fire dampers; Final inspections are being coordinated to occur after the final testing is complete
- Other Item(s) To Note: Plumbing line repairs are scheduled to occur in Spring Break 2026

New Early Learning Center (Hord Coplan Macht/McKnight Construction Co., Inc.)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
79 - New Early Learning Center (AM)	New Early Learning Center Construction (RRA Campus)	●	●

- 50% DD's are have been received and comments will be issued in early March 2026;
100% DD's are scheduled to be received in March 2026
- Other Item(s) To Note: DD's cost estimate will take place once the 100% DD's have been received

Safety/Security Improvements – Bluffton Campus

M.B. Khan Construction



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
70 – Bluffton Early Childhood Center (TS)	Cameras at Parking Lots & Playgrounds, Access Controls, Intrusion Alarm	●	●
70 – Bluffton Elementary School (TS)	Cameras at Parking Lots, Playgrounds & Athletic Fields, Access Controls, Intrusion Alarm	●	●
88 – H.E. McCracken Middle School (TS)	Cameras at Parking Lots & Athletic Fields, Access Controls, Intrusion Alarm	●	●
98 – Bluffton High School (TS)	Cameras at Parking Lots & Athletic Fields, Access Controls, Intrusion Alarm	●	●

- BLECC: Pole installations are complete; Camera installations has begun
- BLES: Pole installations are complete; Camera installations has begun
- HEMMS: Pole installations are 95% complete; Camera installations will begin in March 2026
- BLHS: Pole base installations are complete; Pole installations are 60% complete; Camera installations will begin in March 2026
- Other Item(s) To Note: None at this time

Bluffton High School

(Jumper Carter Sease Architects/MBK)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
98 - Bluffton High School (TS)	CTE Addition	●	●

- CD's are scheduled for completion in March 2026; GMP Pricing is scheduled to be received May 2026
- Other Item(s) To Note: None at this time

Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
96 - Hilton Head Island High School (TS)	New Construction, Renovations and Demolition	●	●

Status Flag Comments:

- 1 ● See 2023 Referendum Project Contingency Log for details



Hilton Head Island High School

(Little Diversified Architectural Consulting, Inc./MBK)




Phase 1: Contractual Substantial Completion date is June 19, 2026

- Site Work: Scope is proceeding on schedule
- Phase 1A: Scope includes construction of a 3-story classroom addition (approximately 144,000 SF) and a mechanical support building; 3rd floor overhead inspection occurred on January 12, 2026; Data cabling terminations are ongoing; testing will begin in March 2026; Metal panel installation is complete; Casework is 60% complete; Flooring is 75% complete; Terrazzo flooring is scheduled for installation in March 2026; PA/Intercom installation is scheduled to begin in February 2026; Front entrance pavers are scheduled to begin in February 2026
- Phase 1B: Scope includes selective demolition and initial renovations of the "D" wing (Music & Art), group restroom improvements, and modifications of corridor walls and finishes; Full scope of work will be addressed once Phase 1A is complete
- Other Item(s) To Note: None at this time

Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)





Phase 1 - February 2026 Progress Photos

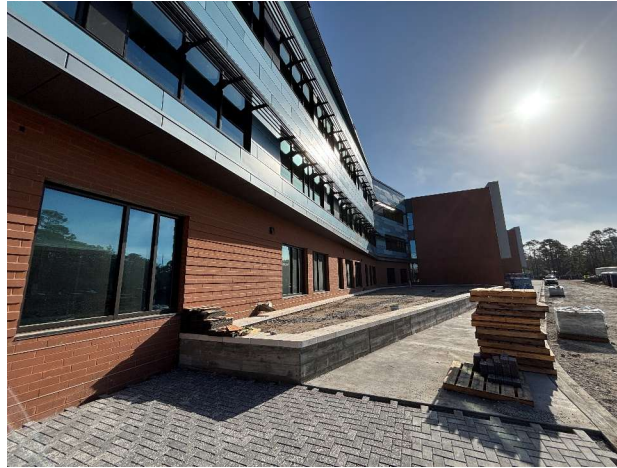

Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



Phase 1 - February 2026 Progress Photos

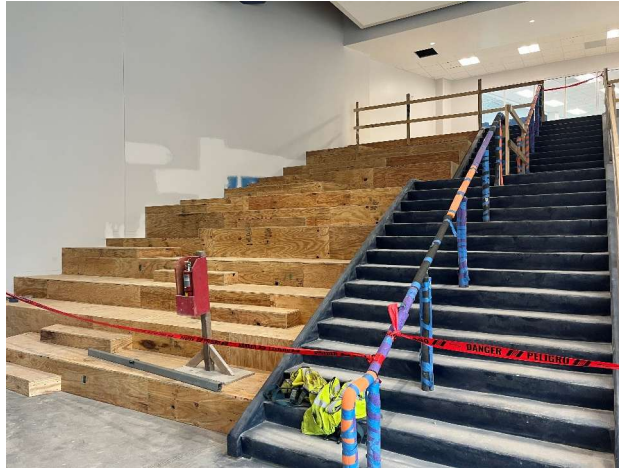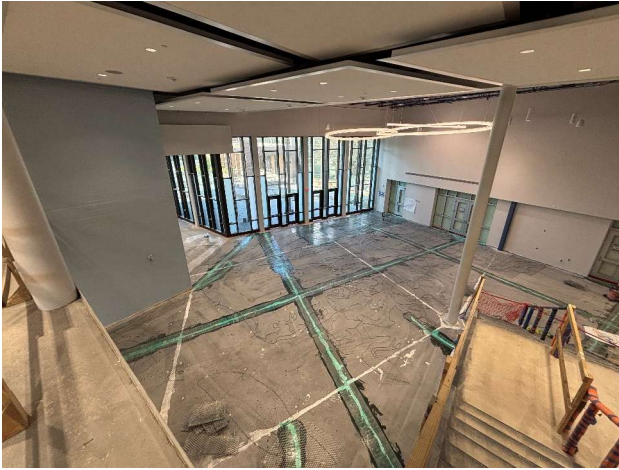

Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



Phase 1 - February 2026 Progress Photos



Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



Phase 1 - February 2026 Progress Photos



Hilton Head Island High School

(Little Diversified Architectural Consulting, Inc./MBK)



Phase 2: Contractual Substantial Completion date is December 17, 2027

- Phase 2 scope includes the demolition of the "B" and "C" wings (Academic Spaces); Construction of a new cafeteria and CTE addition; Remaining renovations/improvements for the "D" wing (Music and Fine Arts); New parking lot and courtyard
- Demo is scheduled to begin during Summer Break 2026
- Other Item(s) To Note: None at this time

Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



Phase 3: Contractual Substantial Completion date is July 31, 2028

- Phase 3 scope includes renovation of both existing gymnasiums, existing JROTC and existing cafeteria
- Work is scheduled to begin after the completion of Phase 2
- Other Item(s) To Note: None at this time

Hilton Head Island High School

(Little Diversified Architectural Consulting, Inc./MBK)



Phase 4:

- Phase 4 scope includes renovation of the existing SCC (Seahawk Cultural Center)
- Other Item(s) To Note: SCC renovation work will follow the completion of Phase 1A-2B

Beaufort High School (JCS-MPS/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
90 - Beaufort High School (MK)	CTE Addition and Renovations	●	●



Beaufort High School (JCS-MPS/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
90 - Beaufort High School (MK)	CTE Addition and Renovations	●	●

- Final permitting approval discussions with the City of Beaufort are scheduled to occur on March 3, 2026; GMP Pricing for the CTE Addition is scheduled to be presented after discussions with the City of Beaufort occur
- Other Item(s) To Note: Project schedule is not affected at the current moment

Beaufort High School (JCS-MPS/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
90 – Beaufort High School (MK)	HVAC Replacements	●	●

- Phase 1 design (9 Split Systems for the Admin Offices) is complete; Installation is being coordinated to occur during Summer Break 2026
- Phase 2 design (Remaining HVAC Systems outside of the academic wings) is scheduled for completion in April 2026; Work is being coordinated to begin during Summer Break 2026 and will continue through the remainder of the school year
- Other Item(s) To Note: None at this time

Lady's Island Middle School (Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
81 - Lady's Island Middle School Replacement (MK)	Phase 1 - New School Construction	●	●
	Phase 2 - Demo Existing School	●	●
	Phase 3 - New Athletics (Football, Softball and Baseball Fields, Lighting, Track, Restrooms, Concessions and Storage Facilities)	●	●



Lady's Island Middle School (Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
81 - Lady's Island Middle School Replacement (MK)	Phase 1 - New School Construction	●	●
	Phase 2 - Demo Existing School	●	●
	Phase 3 - New Athletics (Football, Softball and Baseball Fields, Lighting, Track, Restrooms, Concessions and Storage Facilities)	●	●



- Early release site package was approved at the February 17, 2026 BoE Meeting
- GMP Pricing is scheduled to be received in March 2026
- Other Item(s) To Note: None at this time

Riverview Charter School (Caplea Coe Architects/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
20 - Riverview Charter School (MK)	Gym Addition & Renovation	●	●



Riverview Charter School (Caplea Coe Architects/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
20 - Riverview Charter School (MK)	Gym Addition & Renovation	●	●

- CD's are scheduled to be received in March 2026
- Other Item(s) To Note: DD's presentation to the RVCS Board is scheduled to occur on March 16, 2026 at the RVCS main conference room

Technology Warehouse & Imaging Center (Jumper Carter Sease Architects/Shoreline Construction)




School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
01 - District Educational Services Center (MK)	Technology Warehouse & Imaging Center	●	●

Status Flag Comments:

1 ● See 2023 Referendum Project Contingency Log for details

- Unit start ups occurred in February 2026; Final inspection is being coordinated to occur in March 2026 pending availability from 3rd party inspectors and the State Fire Marshall
- Other Item(s) To Note: None at this time

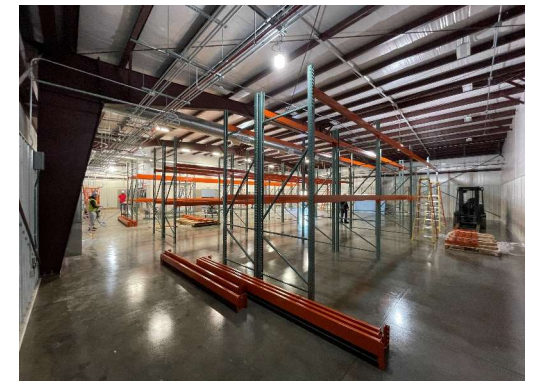

James J. David Early Childhood Center (Ward Edwards Engineering/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
52 - James J. Davis Early Childhood Center (BF)	New Parking Lot and Resurfacing of Existing Parking Lot	●	●

- CD's are progressing; Permitting is ongoing
- DD's pricing has been received
- Other Item(s) To Note: None at this time

St. Helena Elementary School (Ward Edwards Engineering/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
39 - St. Helena Elementary School (BF)	Parking Lot Reconfiguration	●	●

- DD's are scheduled to be received in March 2026
- Other Item(s) To Note: None at this time

Safety/Security Improvements – Whale Branch Cluster

Thompson Turner Construction



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
54 – Whale Branch Elementary School (BF)	Cameras at Parking Lots & Playgrounds, Access Controls, Intrusion Alarm	●	●
85 – Whale Branch Middle School (BF)	Cameras at Parking Lots & Athletic Fields, Access Controls, Intrusion Alarm	●	●
94 – Whale Branch Early College High School (BF)	Cameras at Parking Lots & Athletic Fields, Access Controls, Intrusion Alarm	●	●

- WBES: Wiring and device installation is ongoing
- WBMS: Wiring and device installation is ongoing
- WBECHS: Punchlist is scheduled for completion in March 2026
- Other Item(s) To Note: None at this time

7. 2023 Bond Referendum Financial Reports and Summary





2023 Bond Referendum Financial Reports and Summary

A. Financial Summary Report

- See handout/attachment for details

B. Project Level Financial Reports

- See handout/attachment for details

C. Contingency Use Log

- See handout/attachment for details

2023 Bond Referendum Financial Reports and Summary

FINANCIAL SUMMARY ●



Budget Summary 2/28/26

Beginning Original Budget

\$439,035,000

Current Budget

\$439,035,000

Paid and Committed Through 2/28/26

\$267,877,897 (61.02%)

Total Remaining Funds to Commit (Including Program Contingency)

\$171,157,103 (38.98%)

Program Contingency Activity in February 2026

Savings Returned

\$115,813

Contingency Used

\$728,169

Original Program Contingency Program Contingency Remaining

\$11,500,000

\$6,928,426 (60.25%)

Original Project Level Contingencies

\$17,060,756

Current Project Level Contingencies

\$6,673,267 (39.11%)

Original Contingency (Program & Project Level)

\$28,560,756

Total Remaining Contingencies (Program & Project Level)

\$13,601,693 (47.62%)

8. 2023 Bond Referendum Cash Flow Projections vs Actual Expenditures



2023 Bond Referendum Cashflow Projections vs Actual



CASH FLOW: DATA thru February 2026																
2023 BOND REFERENDUM ONLY																
Projects	Project Total (Millions)	Previously Spent	Forecasted - 2026 Expenditures												Total	% Project Budget
			January	February	March	April	May	June	July	August	Sept	October	Nov	Dec		
District Level Costs	\$21.53	\$3.09	\$0.17	\$0.42	\$0.43	\$0.43	\$0.44	\$0.43	\$0.51	\$0.41	\$0.41	\$0.41	\$0.42	\$0.41	\$7.97	37.04%
<i>actuals</i>		\$3.09	\$0.02	\$0.16											\$3.27	15.17%
Safety/Security & Tech. Enhancement Projects	\$17.95	\$3.08	\$0.94	\$0.50	\$1.00	\$0.70	\$0.53	\$0.46	\$0.65	\$0.58	\$0.52	\$0.31	\$0.30	\$0.27	\$9.83	54.79%
<i>actuals</i>		\$3.08	\$1.00	\$0.44											\$4.53	25.22%
Technology Warehouse & Imaging Center	\$3.51	\$1.40	\$0.57	\$0.61	\$0.44	\$0.49	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$3.51	100.00%
<i>actuals</i>		\$1.40	\$0.57	\$0.59											\$2.56	72.87%
Right Choices Kitchen Addition	\$2.32	\$0.00	\$0.00	\$0.00	\$0.00	\$0.05	\$0.00	\$0.05	\$0.00	\$0.06	\$0.14	\$0.16	\$0.14	\$0.32	\$0.91	39.36%
<i>actuals</i>		\$0.00	\$0.00	\$0.00											\$0.00	0.12%
Riverview Charter School Gym Addition & Reno	\$17.92	\$0.04	\$0.00	\$0.00	\$0.24	\$0.07	\$0.00	\$0.78	\$0.98	\$0.84	\$0.88	\$0.98	\$1.18	\$1.27	\$7.27	40.56%
<i>actuals</i>		\$0.04	\$0.10	\$0.13											\$0.27	1.52%
New - May River Elementary	\$59.52	\$12.17	\$1.73	\$3.05	\$4.04	\$4.13	\$3.88	\$3.76	\$3.63	\$3.78	\$3.09	\$3.34	\$2.62	\$2.91	\$52.13	87.58%
<i>actuals</i>		\$12.17	\$1.72	\$2.92											\$16.80	28.23%
New Early Learning Center (RRA Campus)	\$27.80	\$0.47	\$0.00	\$0.00	\$0.10	\$0.03	\$0.30	\$0.80	\$2.02	\$2.98	\$2.07	\$1.99	\$4.81	\$3.13	\$18.69	67.23%
<i>actuals</i>		\$0.47	\$0.00	\$0.26											\$0.73	2.62%
New Lady's Island Middle & Demo Old School	\$61.45	\$1.93	\$0.00	\$0.00	\$0.00	\$0.49	\$1.00	\$0.90	\$1.29	\$1.14	\$0.94	\$1.43	\$1.75	\$3.68	\$14.54	23.66%
<i>actuals</i>		\$1.93	\$0.02	\$0.00											\$1.95	3.17%
Hilton Head Island High New Const., Reno & Demo	\$161.12	\$61.79	\$3.04	\$3.00	\$2.60	\$2.93	\$3.47	\$3.19	\$6.24	\$4.29	\$4.29	\$4.29	\$3.75	\$3.75	\$106.64	66.18%
<i>actuals</i>		\$61.79	\$0.12	\$0.08											\$62.00	38.48%

2023 Bond Referendum Cashflow Projections vs Actual



School Furniture Replacement	\$1.81	\$0.98	\$0.00	\$0.02	\$0.00	\$0.00	\$0.00	\$0.00	\$0.81	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1.81	100.00%
<i>actuals</i>		\$0.98	\$0.00	\$0.00											\$0.98	54.25%
HVAC Replacements	\$16.18	\$2.89	\$0.00	\$0.22	\$0.05	\$0.08	\$0.00	\$1.20	\$2.50	\$3.55	\$3.23	\$2.08	\$0.22	\$0.16	\$16.17	99.93%
<i>actuals</i>		\$2.89	\$0.00	\$0.08											\$2.96	18.32%
Beaufort High CTE New Const. & Reno	\$7.78	\$0.15	\$0.00	\$0.00	\$0.43	\$0.74	\$0.79	\$0.99	\$0.95	\$0.98	\$1.12	\$0.81	\$0.29	\$0.12	\$7.36	94.59%
<i>actuals</i>		\$0.15	\$0.00	\$0.00											\$0.15	1.91%
May River High CTE New Const. & Reno	\$15.91	\$11.10	\$0.90	\$0.86	\$0.86	\$0.49	\$0.63	\$0.63	\$0.43	\$0.00	\$0.00	\$0.03	\$0.00	\$0.00	\$15.91	100.00%
<i>actuals</i>		\$11.10	\$0.01	\$0.90											\$12.02	75.52%
Bluffton High CTE New Const.	\$11.84	\$0.04	\$0.00	\$0.13	\$0.30	\$0.05	\$0.18	\$0.42	\$0.13	\$0.40	\$1.85	\$2.02	\$2.28	\$1.88	\$9.69	81.87%
<i>actuals</i>		\$0.04	\$0.00	\$0.03											\$0.07	0.58%
Parking Lot Reconfiguration & Paving Projects	\$12.40	\$1.04	\$0.00	\$0.00	\$0.24	\$0.23	\$0.04	\$0.59	\$1.36	\$1.28	\$1.00	\$3.93	\$2.07	\$0.50	\$12.27	98.92%
<i>actuals</i>		\$1.04	\$0.01	\$0.03											\$1.08	8.70%
Forecasted Sub-Total (Including District Level Costs)	\$439.04	\$100.15	\$7.35	\$8.81	\$10.71	\$10.91	\$11.25	\$14.18	\$21.50	\$20.31	\$19.54	\$21.76	\$19.83	\$18.41	\$284.70	64.85%
<i>Actual Sub-Total (Including District Level Costs)</i>		\$100.15	\$3.58	\$5.63											\$109.37	24.91%
Forecasted Total	\$439.04	\$100.15	\$107.51	\$116.31	\$127.03	\$137.93	\$149.18	\$163.36	\$184.85	\$205.16	\$224.70	\$246.47	\$266.29	\$284.70		64.85%
Actual Spent		\$100.15	\$103.74	109.37												

Total Funding	\$439,035,000
Total of Bond Sales to Date	\$307,200,000

(1st Bond Sale closed on 2/13/25 - Total Amount \$50.7M)
 (2nd Bond Sale closed on 5/29/25 - Total Amount \$132.2M)
 (3rd Bond Sale closed on 1/20/26 - Total Amount \$125.0M)

9. 2023 Bond Referendum Community Outreach



Community Outreach



- Construction outreach event occurred on March 4, 2026, at the District Educational Services Center Media Center
- RVCS Gym Addition and Renovations DD's presentation to the RVCS Board is scheduled to occur on March 16, 2026, in the RVCS main conference room

10. 2023 Bond Referendum CLOC Sub- Committee Reports/ Updates



11. 2023 Bond Referendum Forward Looking Items and Events



12. 2023 Bond
Referendum
Next Meeting
Apr. 8, 2026
(Location TBD)





Citizen-Led Oversight Committee (CLOC) 2023 Bond Referendum

Twenty-Fourth Meeting
(Okatie Elementary School - Media Center and Via Zoom)
March 11, 2026
