




2023 BOND

MAJOR PROJECTS UPDATE

JUNE 2024



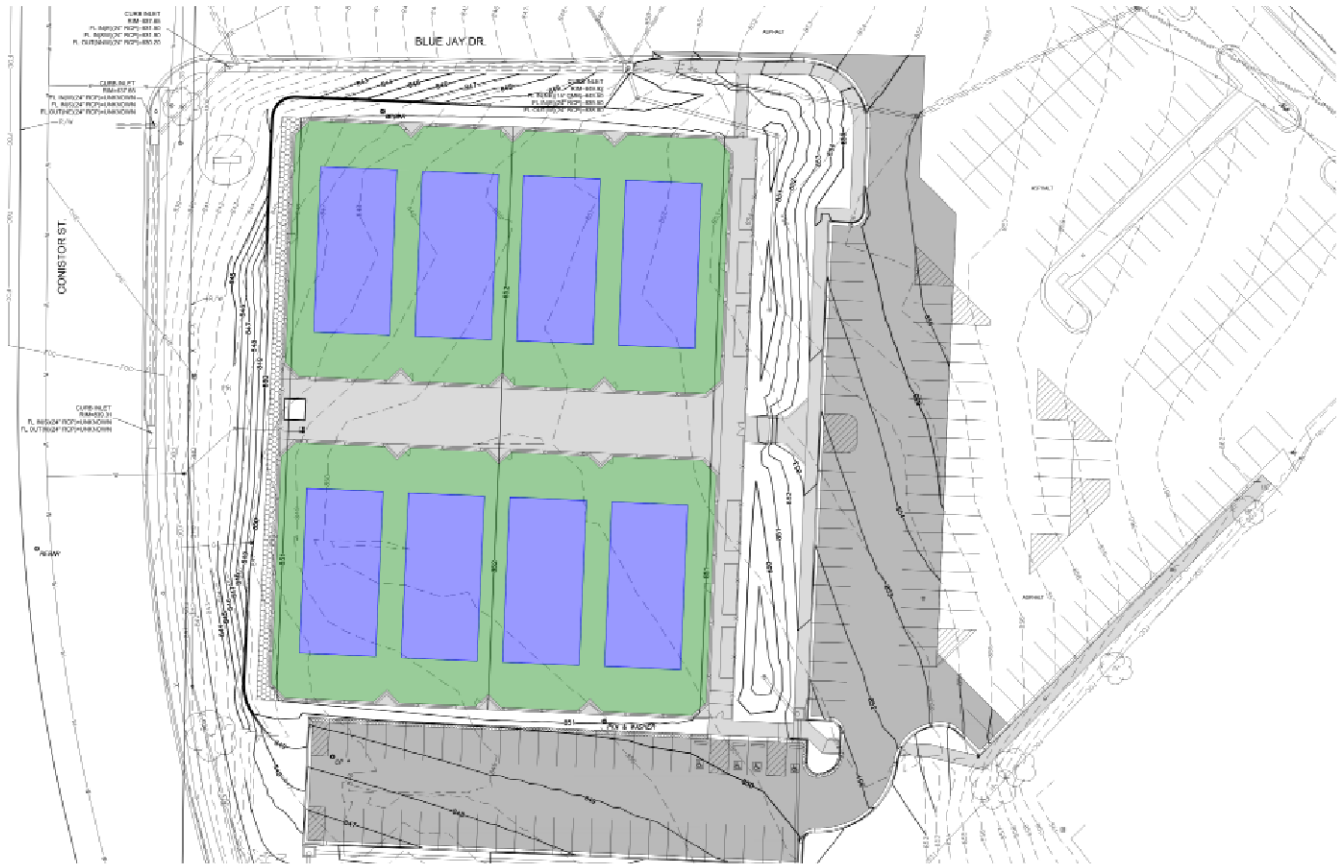

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

**WEEKLY
PROGRESS
REPORT**

Tennis Courts 11/13/2023

Liberty Public Schools



PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

UPCOMING

Project Completion October 2023




North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South

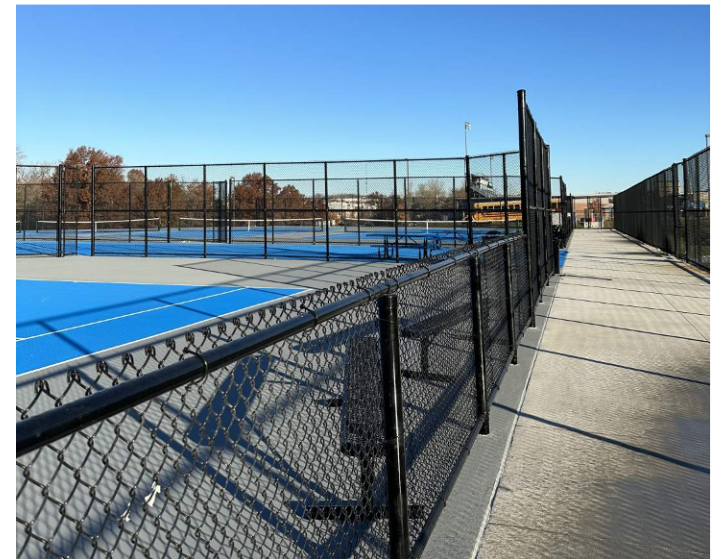

East Concourse Looking North


WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

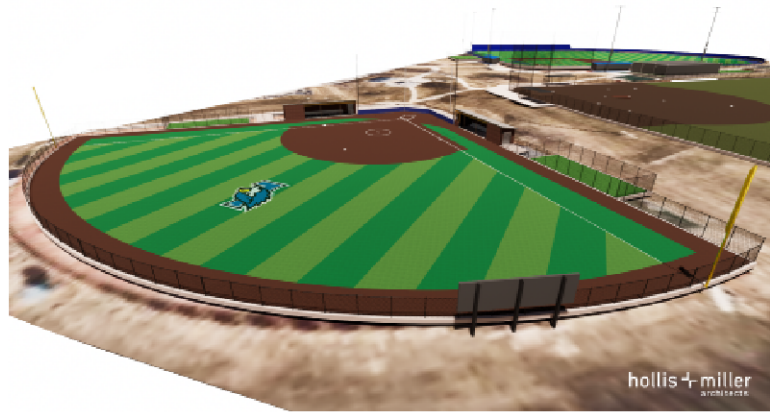

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field


- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024

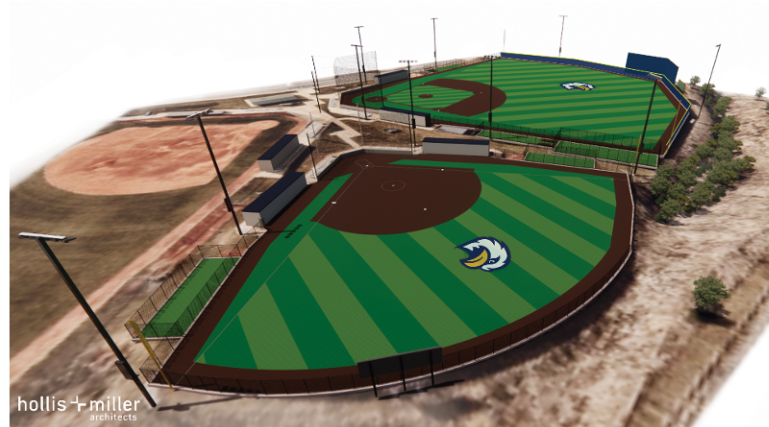

Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

**WEEKLY
PROGRESS
REPORT**

LPS Ball Fields 06/07/2024

Liberty Public Schools



PROJECT STATUS

- LNHS
- Punch List Ongoing (Baseball/Softball)
 - Added Sidewalks
 - Access Road Addition

- LHS
- Punch List Ongoing (Baseball/Softball)
 - Field Sod Complete
 - Irrigation Complete

UPCOMING

- LNHS
- Concourse Sod
 - City Inspections

- LHS
- Access Road Asphalt Repair
 - City Inspections
 - Batting Tunnel

Project Completion
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

PROJECT STATUS

South Valley MS - Upgrades Complete
Discovery MS - Upgrades Complete
EPiC Elementary - Upgrades Complete
Liberty North High School - Upgrades Ongoing

UPCOMING

Energy Inspections - All Four Schools
Emergency LED Fixtures

Project Completion
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

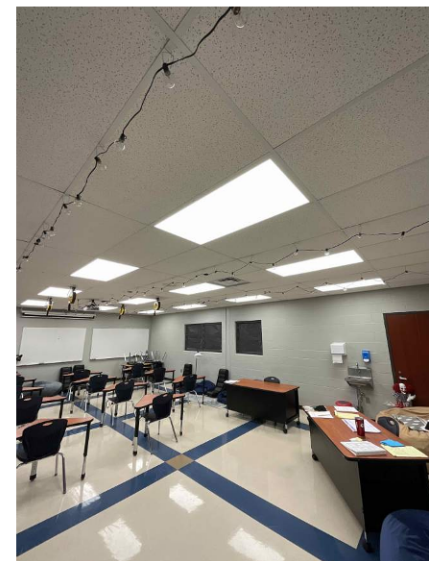

Liberty North HS

PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete

EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


UPCOMING

Energy Inspections All Four Schools
Emergency LED Fixtures

Project Completion
December 2023




South Valley Middle School

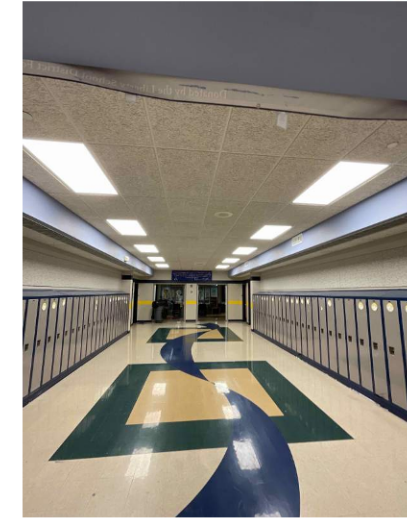

South Valley Middle School



Discovery Middle School

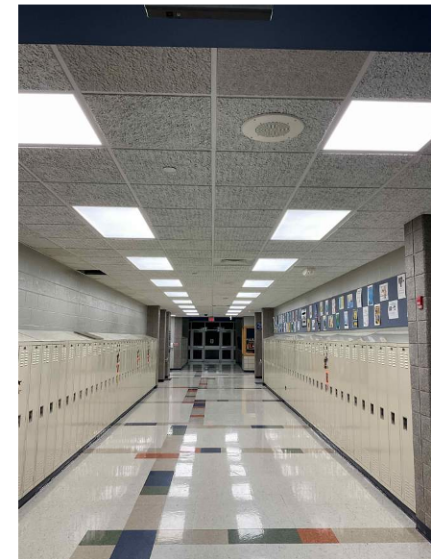

Discovery Middle School

WEEKLY PROGRESS REPORT



Epic Elementary




Epic Elementary



Liberty North High School




Liberty North High School

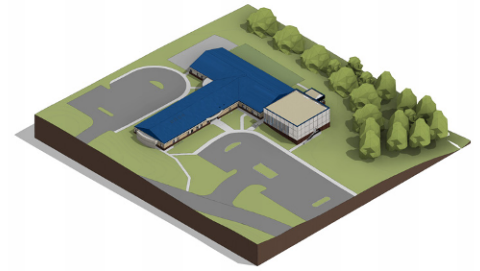


EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

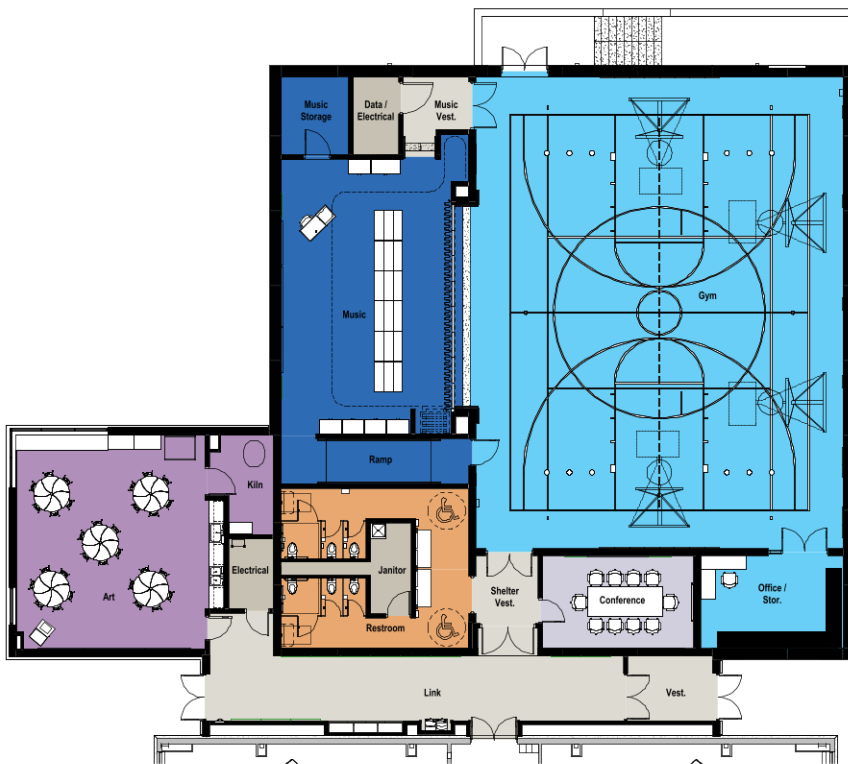

▲ Addition

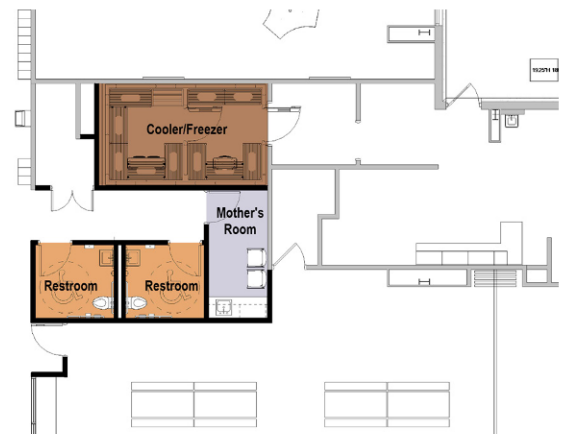

▲ Renovation Area

PROJECT STATUS

- EPiC Elementary
- Building Footings Ongoing
 - Starting on Walls 6/10
 - Target complete date for footings and walls 6/13/2024


UPCOMING

- EPiC Elementary
- Existing Building Interior Renovation
 - Foundation wall waterproofing
 - Foundation wall drainage and backfill
 - Structural Steel
 - Plumbing under-slab


Project Completion
EPiC Feb 2025/DMS&SVMS June 2025




EPiC Elementary - Footing Prep

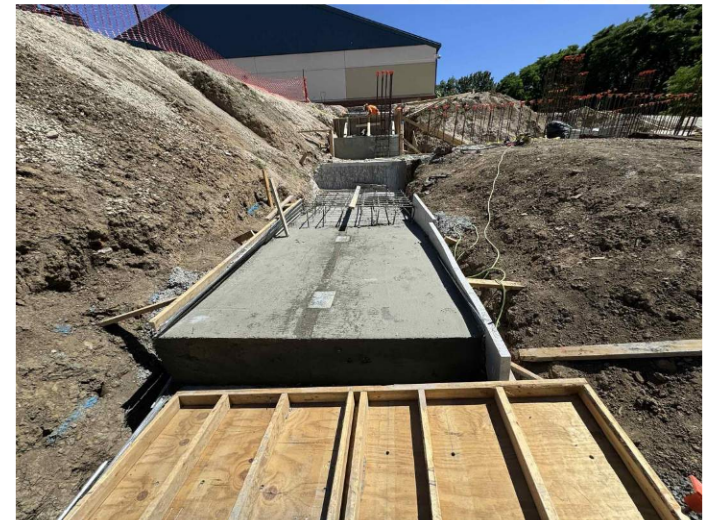

EPiC Elementary - Footings

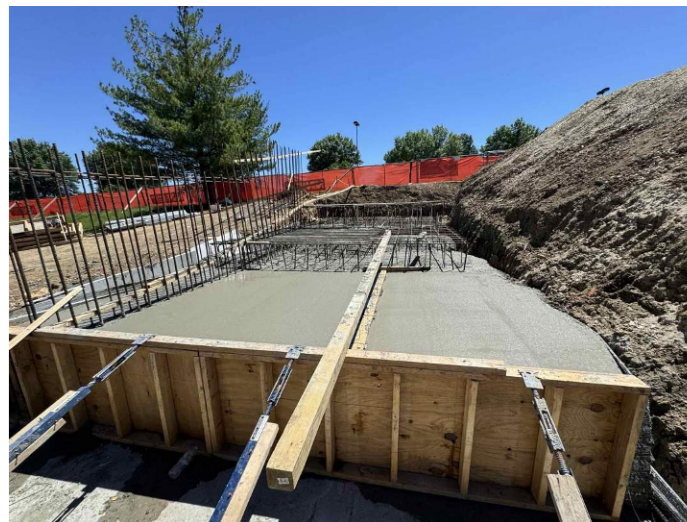

EPiC Elementary - Footings

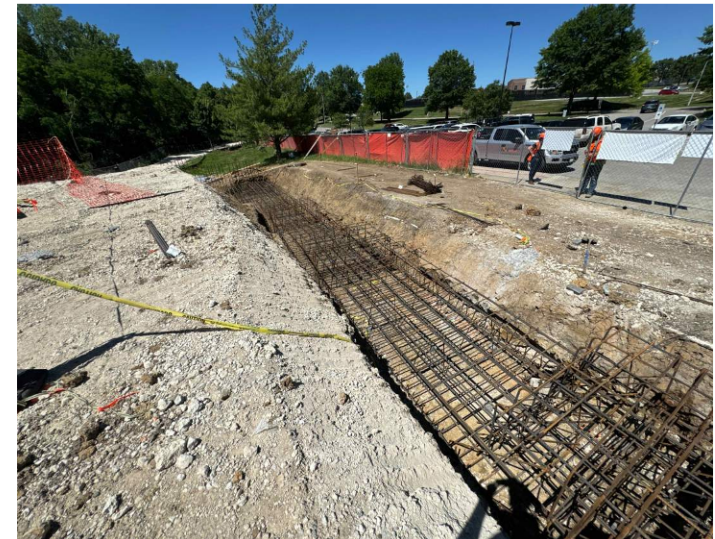



EPiC Elementary - Footing Prep



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

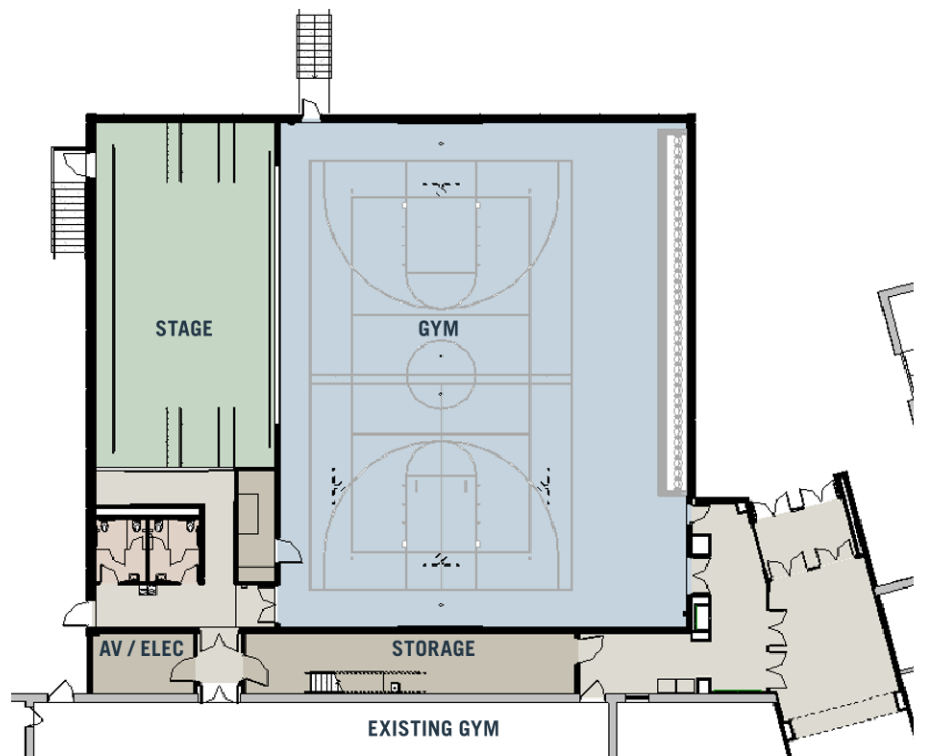

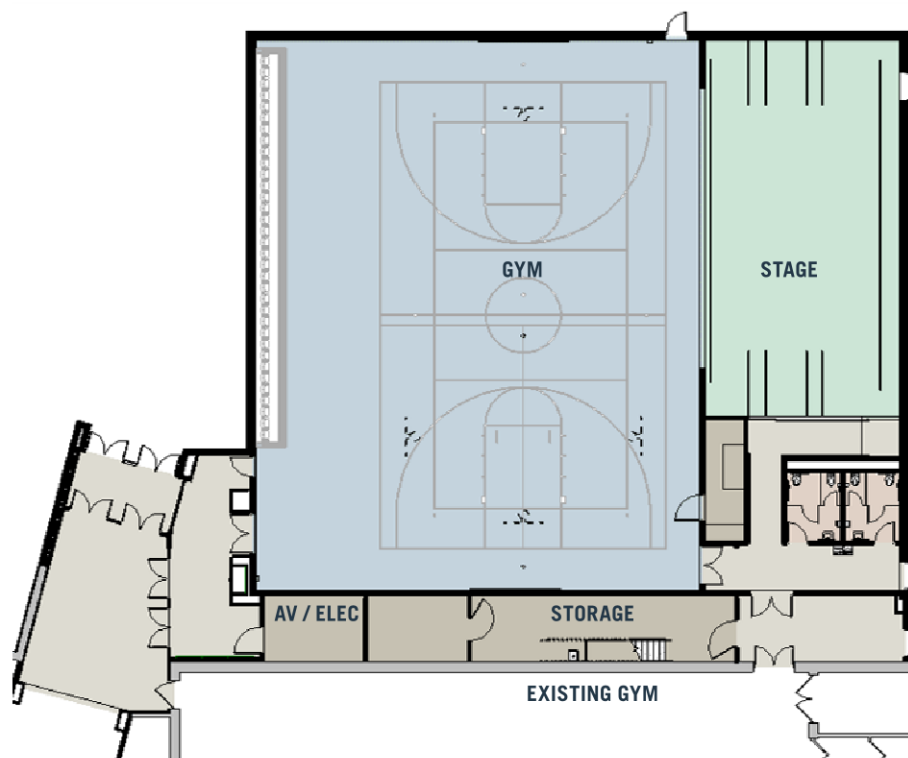

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

PROJECT STATUS

SVMS and DMS

- Demo of canopies
- Interior demo at vestibule
- Site Demo started
- Site Grading started

UPCOMING

SVMS and DMS

- Building Pad
- Site Utilities
- Overhead electrical rough in
- Overhead plumbing rough in
- Deep Sanitary install
- Footings

Project Completion
DMS&SVMS June 2025




DMS - Demo



SVMS - Site Demo



SVMS - Canopy Demo

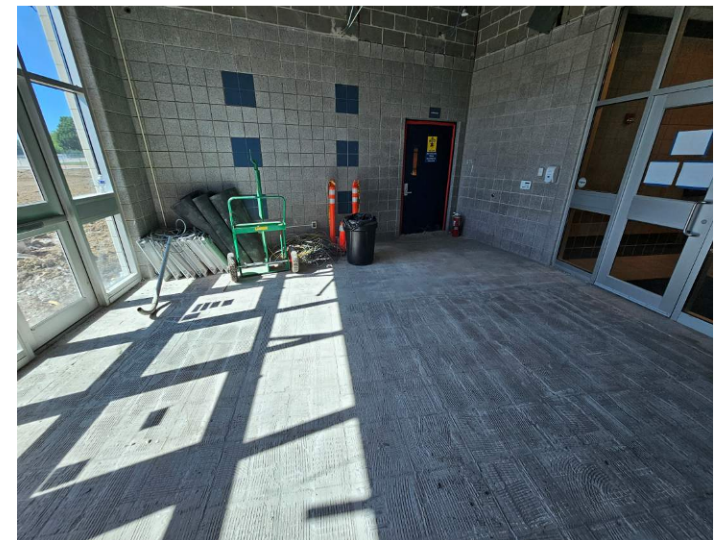

SVMS - Interior Demo



hollis + miller



hollis + miller



hollis + miller



hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



**WEEKLY
PROGRESS
REPORT**

Distribution Center 6/7/24

Liberty Public Schools



6/7/24

PROJECT STATUS

- Remaining deep fills complete
- Footing completed
- Under slab rough complete
- 8" SOG poured and finished
- Freezer mat slab complete

UPCOMING

- Prep & pour site retaining walls
- 4" SOG pour
- Storm line 2 & 6 ongoing
- Begin Structural steel

Project Completion
June 2025



South Entrance Deep Fills



8" SOG Pour



8" SOG Pour



8" SOG Pour

Fine Arts
 Kid's Zone
 Technology
 Shared Amenities
 Building Systems
 Future Phase



District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

6/7/24

PROJECT STATUS

- District Technology Center:
- Communications Install Continued
 - Continued Interior Paint
 - Began Exterior Paint
 - Continued Flooring Install
 - Door and Door Hardware Install
 - Completed Generator and Transformer Install
 - Continued Data Pod Install
 - Began HVAC Equipment Install
 - Began Landscaping and Fence Install

UPCOMING

- District Technology Center:
- Complete Data Pod Install
 - Complete HVAC Equipment Install
 - Complete Interior Door Install
 - Complete Paint
 - Complete Flooring Install
 - Complete Landscaping and Fence Install
 - Begin Future Build Finishes
 - Begin Punchlist Work

Project Completion June 2024



IT Open Office



Transformer and Generator Install



District Tech Center Exterior



Main Corridor



Fine Arts Open Office




HVAC Equipment Install



IT Department Entrance



Data Pod Install

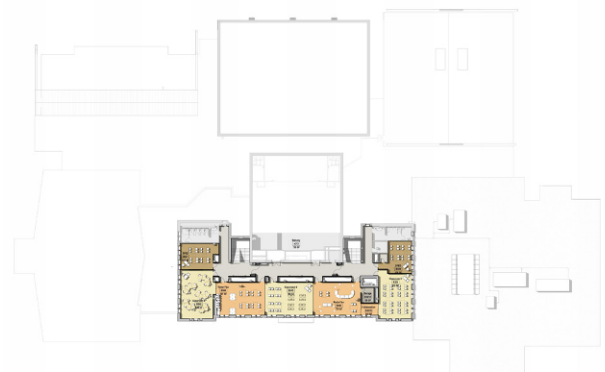

LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
 - Integrated SPED resources
- Renovated cafeteria & scramble
 - Restroom renovations
- Exterior masonry repair & window replacement
 - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

6/7/24

PROJECT STATUS

Heritage Middle School

- Demo of Kitchen
- Demo of Bathrooms near kitchen
- Demo of Bathrooms in Locker Room
- Demo of Cafeteria
- Working through existing conditions
- Prepping underground layout for saw cutting and rough in.
- Working through LED lighting replacement.

UPCOMING

Heritage Middle School


- Starting demo in 1964 Wing
- Continue demo in kitchen and bathrooms.
- Finishing demo and MEP underground prep.
- Concrete prep and pour back at kitchen area.
- Starting framing in the kitchen area.
- Underground rough in for plumbing in bathrooms.




Cafeteria Demo



Kitchen Demo

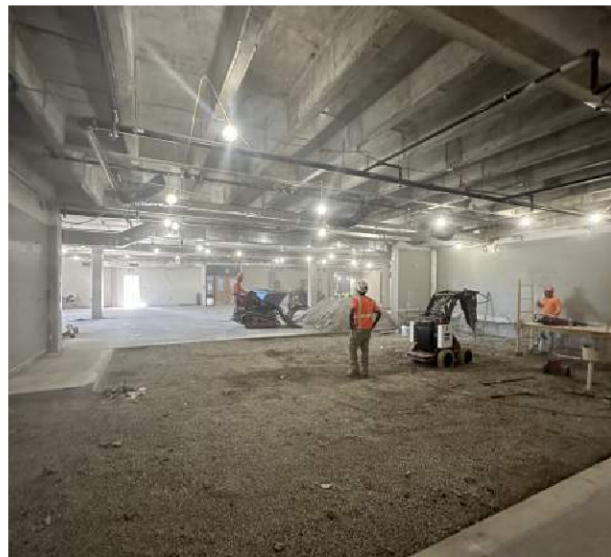

Demo of New Seating Area

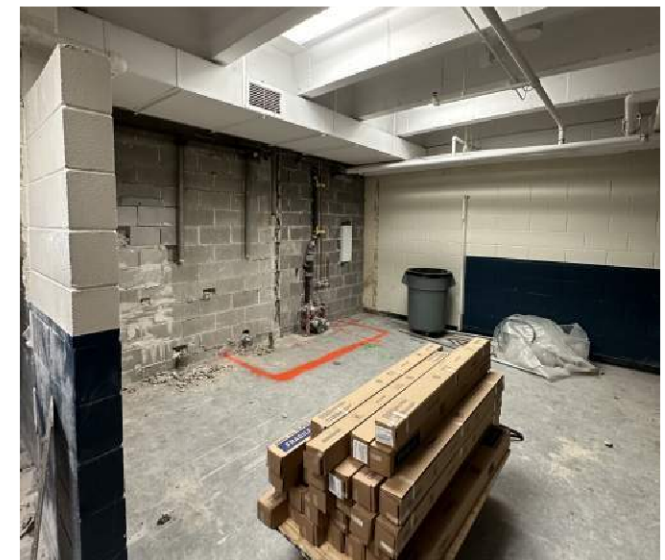


Bathroom Demo



Bathroom Demo



Bathroom Demo

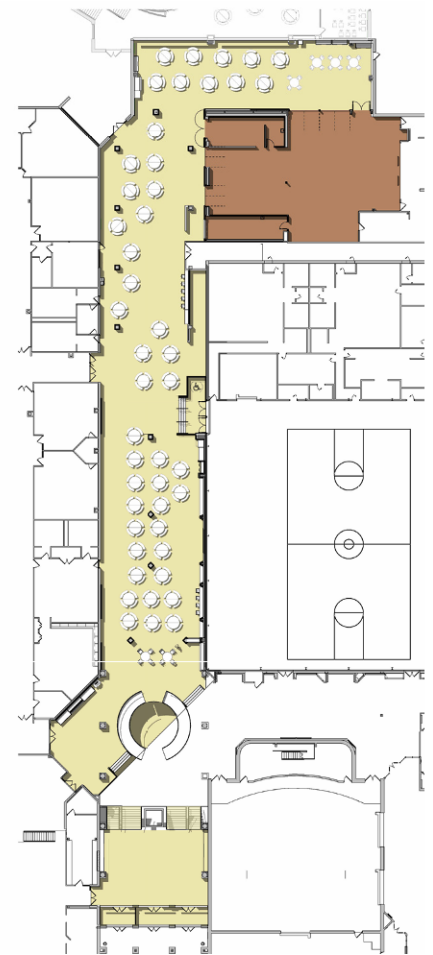

PHASE 2

Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025



PHASE 1


6/7/24

PROJECT STATUS

- Liberty High School
- Demo of 400's wing classrooms
 - Demo of 100's wing classrooms
 - Working through MEP demo of construction areas.

UPCOMING

- Liberty High School
- Framing of the 400's wing
 - Continued demo of the 100's wing.
 - Start Framing the 100's wing once we are halfway through demo.
 - Begin Light Fixture replacement.

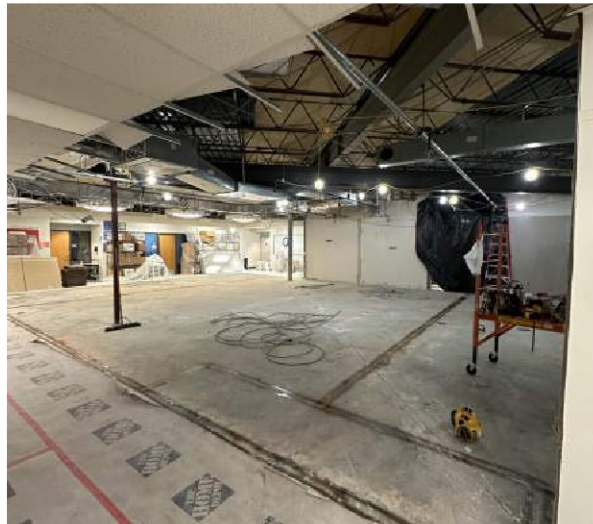


Demo 400's Wing



Demo 400's Wing



Demo 100's Wing

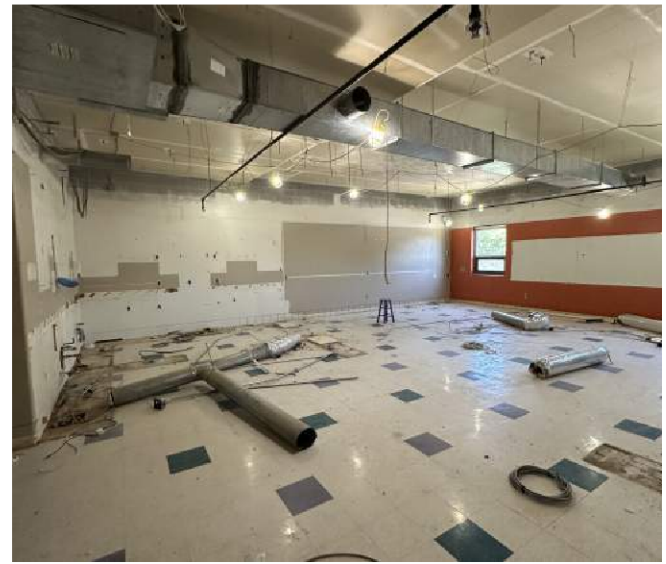

Demo 100's Wing



Demo 100's Wing



Demo 100's Wing




Demo 100's Wing



Shop Building



- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

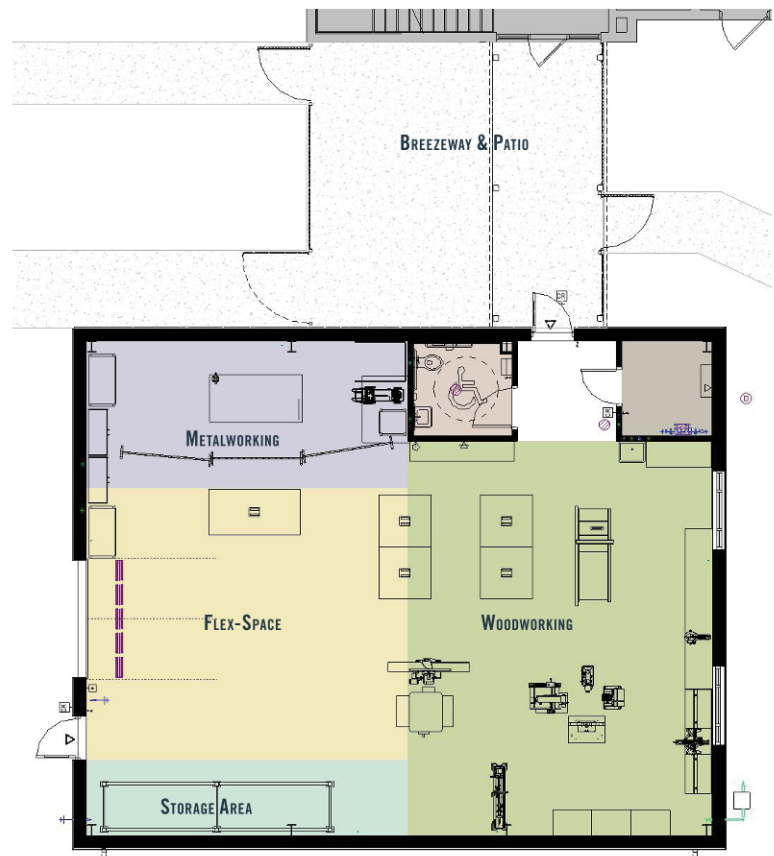

▲ Floor Plan


Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:
Spring 2024–Spring 2025

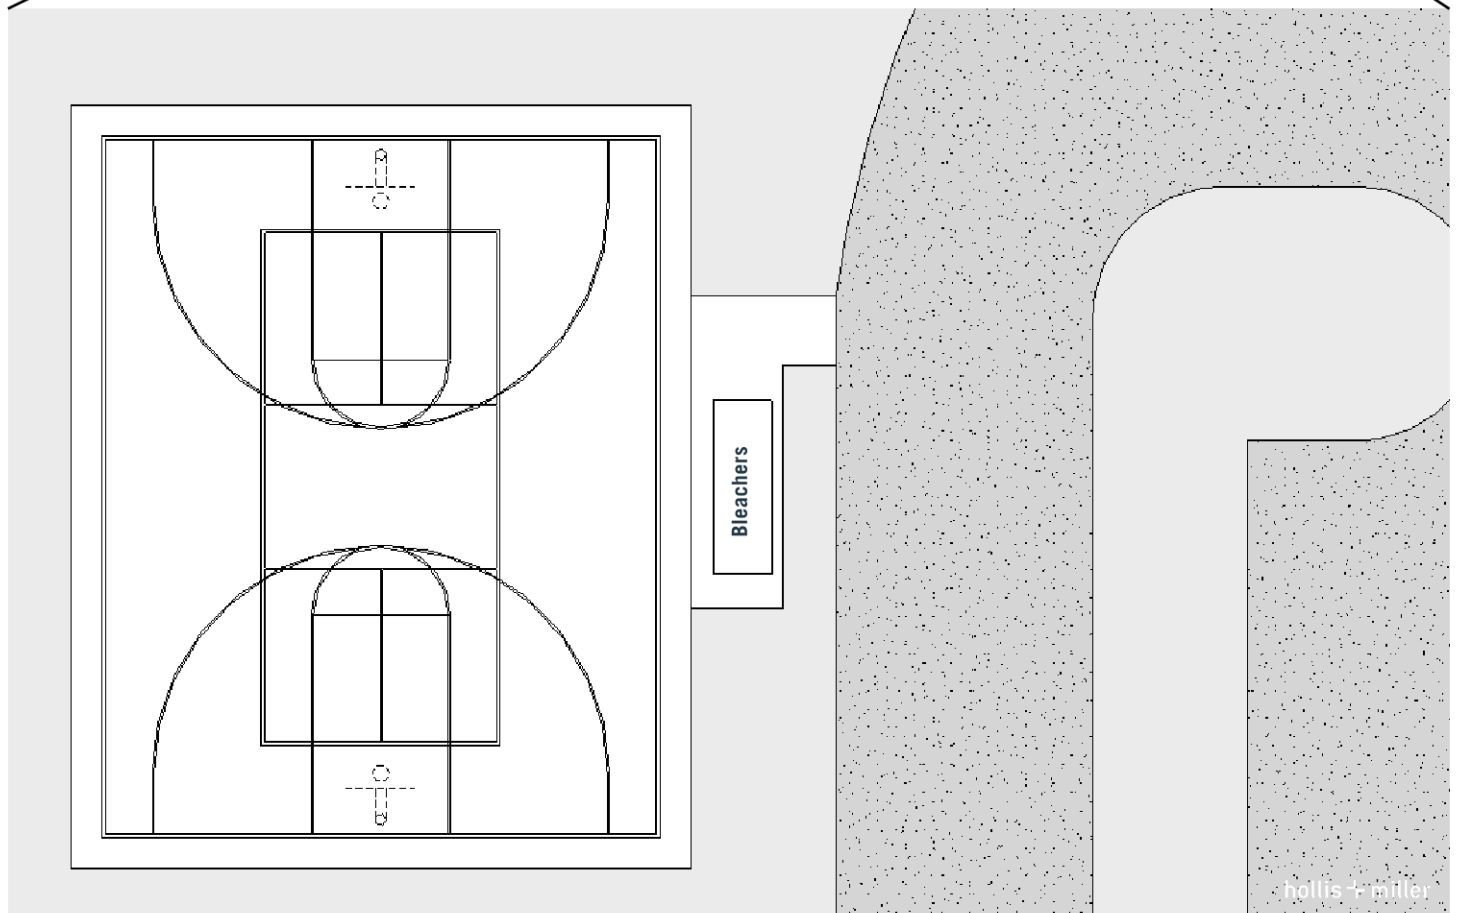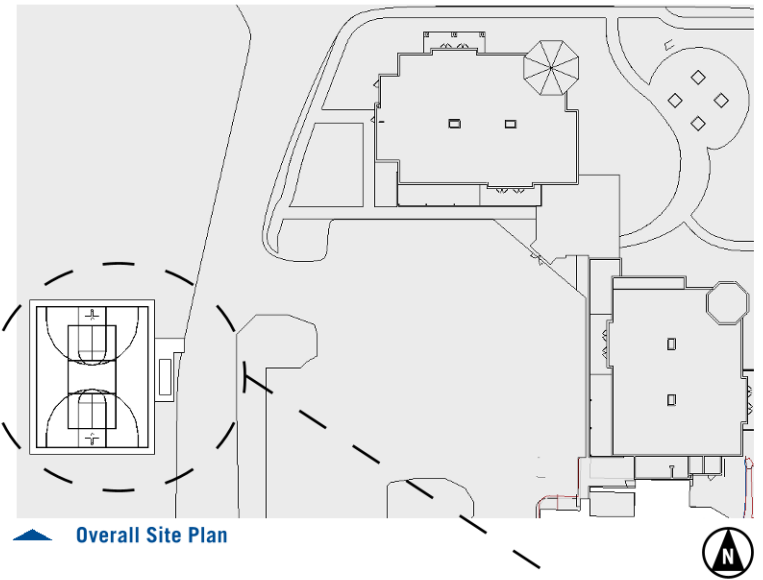

Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:
May 2024 - August 2025

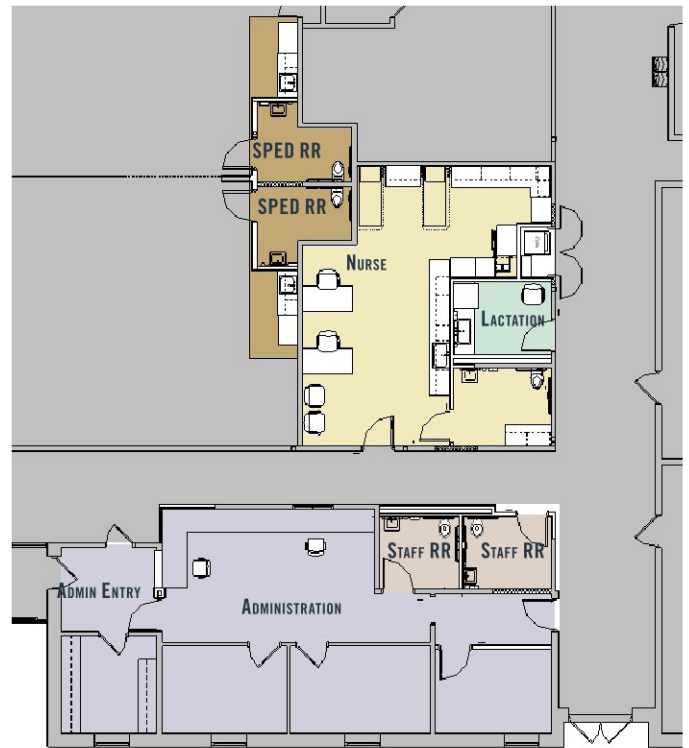

▲ Enlarged Floor Plan




▲ Overall Floor Plan

Interior Renovation


- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:
May 2024 - August 2025



Administration

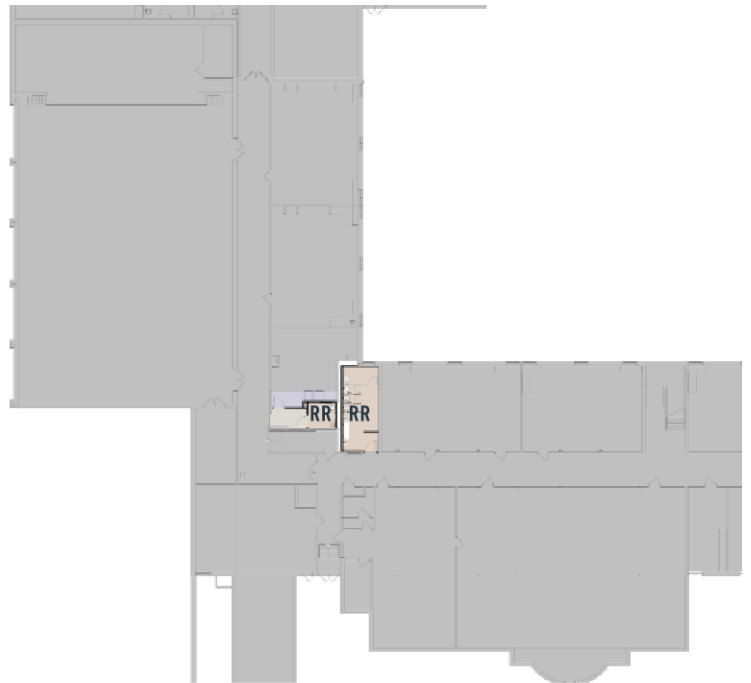

Partial First Level Floor Plan

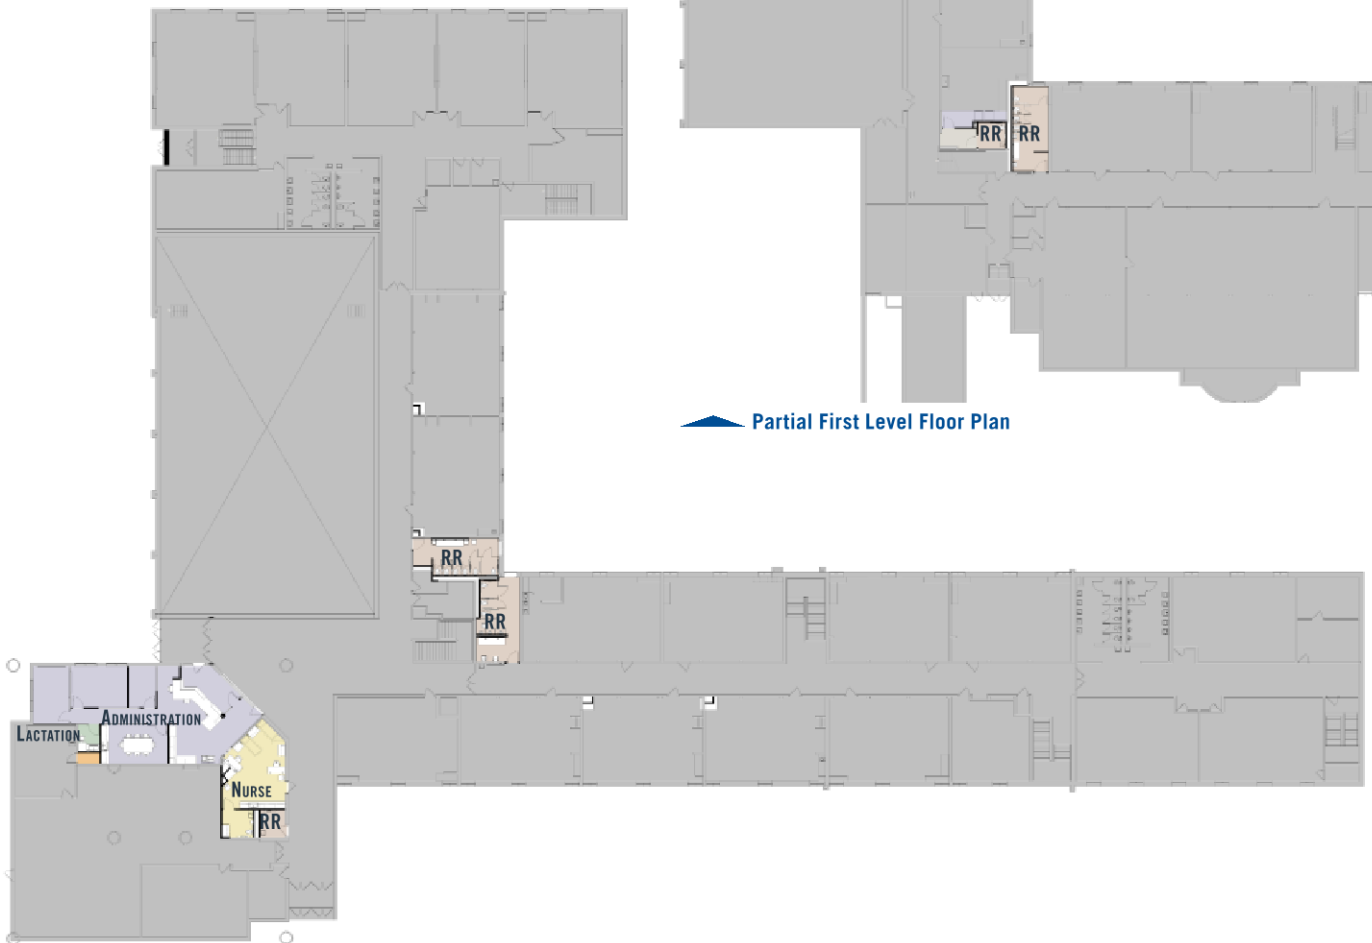


Overall Second Level Floor Plan

Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:
May 2024 - August 2025



Administration

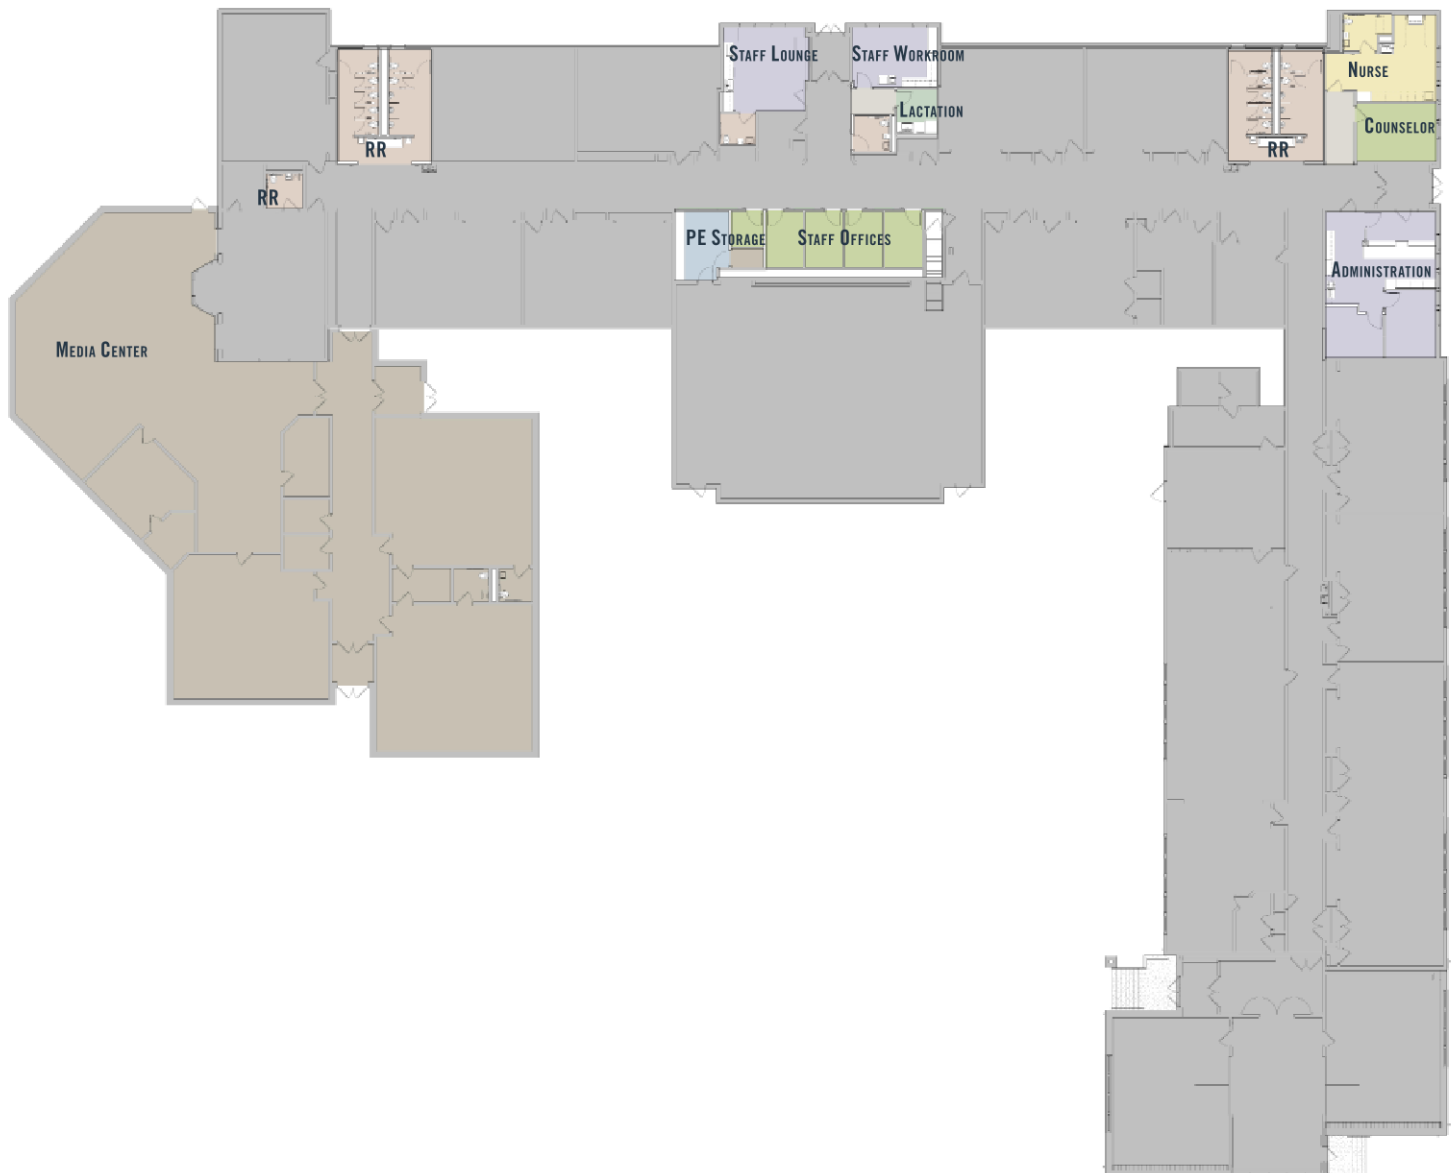

Overall Floor Plan

**WEEKLY
PROGRESS
REPORT**

**Doniphan, Franklin, and Ridgeview
Summer Renovation Projects
Liberty Public Schools**



6/7/24

PROJECT STATUS

- Doniphan, Franklin, and Ridgeview:
- Began Ceiling Demolition
 - Began Wall Demolition
 - Began Floor Demolition
 - Began MEP Demolition
 - Began Wall Framing
 - Franklin - Completed Stage Demolition
 - Ridgeview - Began Structural Steel Install for HVAC Equipment
 - Ridgeview-Complete Transformer Switchover

UPCOMING

- Doniphan, Franklin, and Ridgeview:
- Complete Ceiling, Wall, and Floor Demolition
 - Complete MEP Demolition
 - Complete Wall Framing
 - Ridgeview - Complete HVAC Equipment Install
 - Begin MEP Overhead Rough-In
 - Begin MEP In-Wall Rough-In
 - Begin Drywall Install

Project Completion: August 2024



Franklin - Stage Demolition



Franklin - Restroom Demolition



Ridgeview - Admin Office Demolition



Ridgeview - Hallway Ceiling Demolition



Doniphan - Nurse's Office Demolition



Doniphan - Teacher's Lounge Demolition



Doniphan - Admin Office Demolition



Franklin - Admin Office Demolition
