




2023 BOND

MAJOR PROJECTS UPDATE

AUGUST 2024



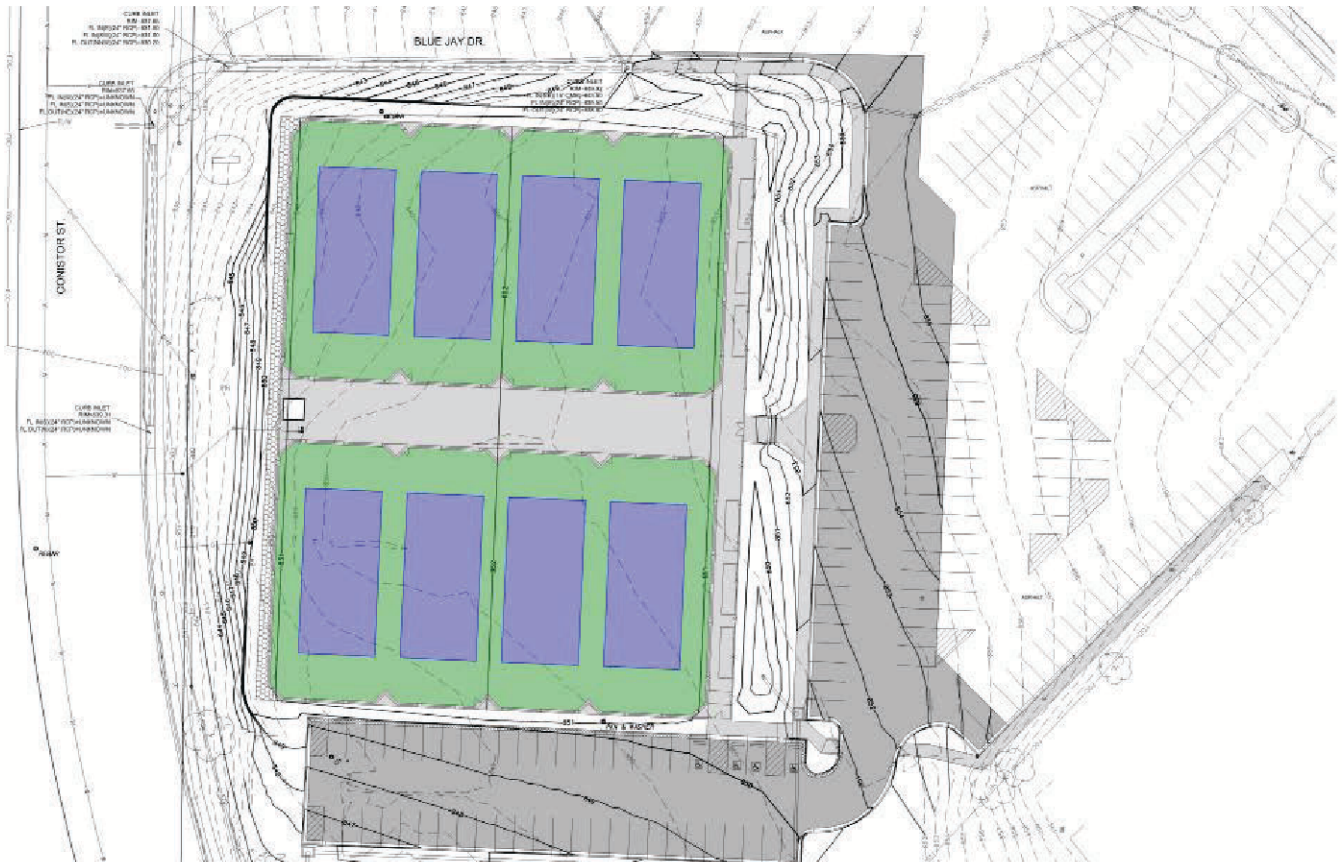

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

**WEEKLY
PROGRESS
REPORT**

Tennis Courts 11/13/2023

Liberty Public Schools



PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

UPCOMING

Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North


WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

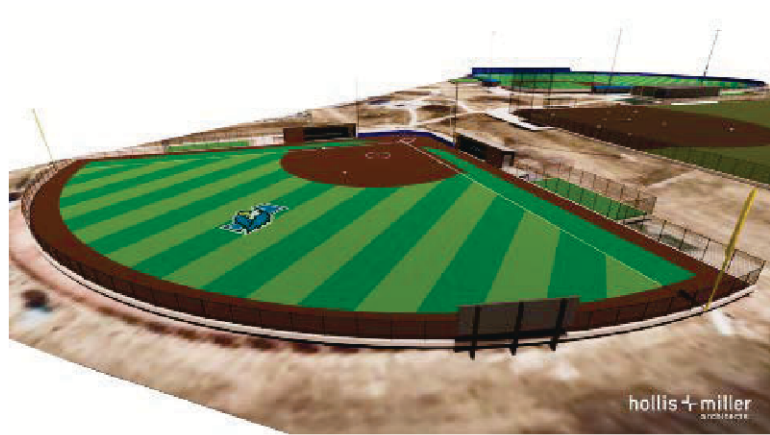

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024



Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

WEEKLY
PROGRESS
REPORT

LPS Ball Fields 08/09/2024

Liberty Public Schools



PROJECT STATUS

- LNHS
- Punch List Completion
 - Final Inspection Passed

- LHS
- Punch List Completion
 - Retaining Wall Ongoing
 - Final Sod Ongoing

UPCOMING

- LHS
- City Inspection

Project Completion
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

PROJECT STATUS

- South Valley MS - Upgrades Complete
- Discovery MS - Upgrades Complete
- EPiC Elementary - Upgrades Complete
- Liberty North High School - Upgrades Ongoing


UPCOMING

- Energy Inspections - All Four Schools
- Emergency LED Fixtures


Project Completion
December 2023




Liberty North HS

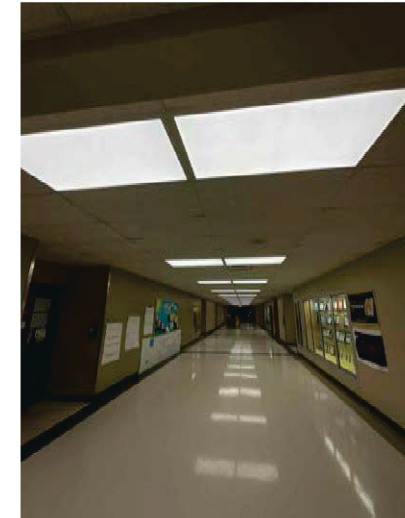

Liberty North HS

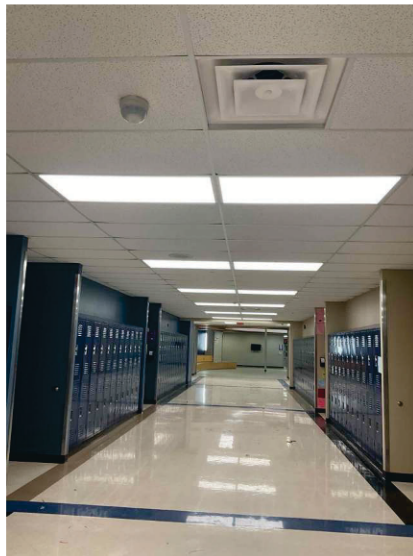

Liberty North HS

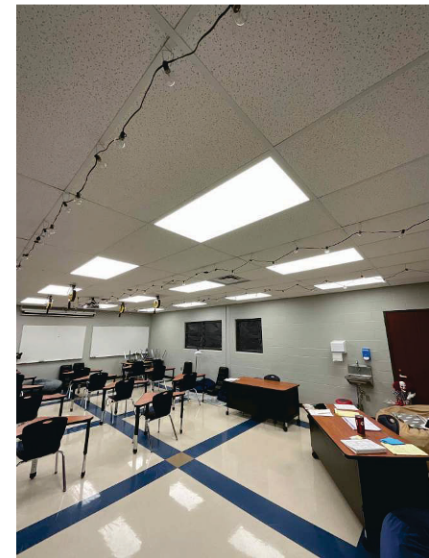

Liberty North HS

PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


UPCOMING

Energy Inspections All Four Schools
Emergency LED Fixtures

Project Completion
December 2023

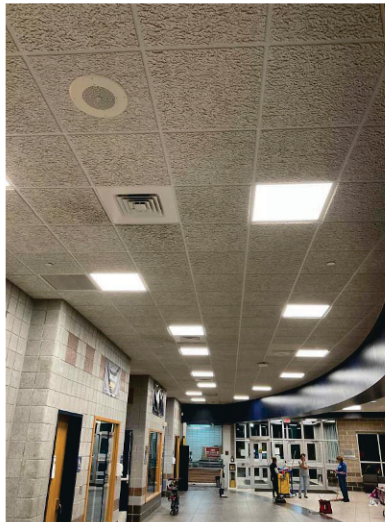


South Valley Middle School

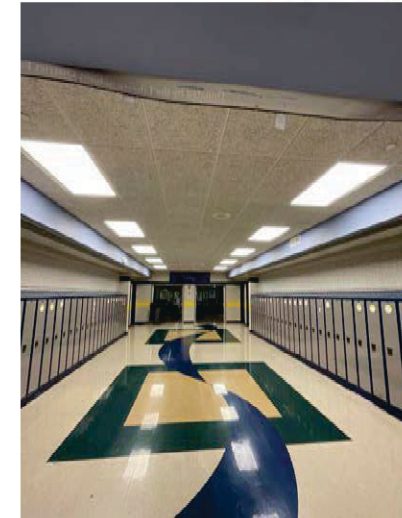

South Valley Middle School



Discovery Middle School

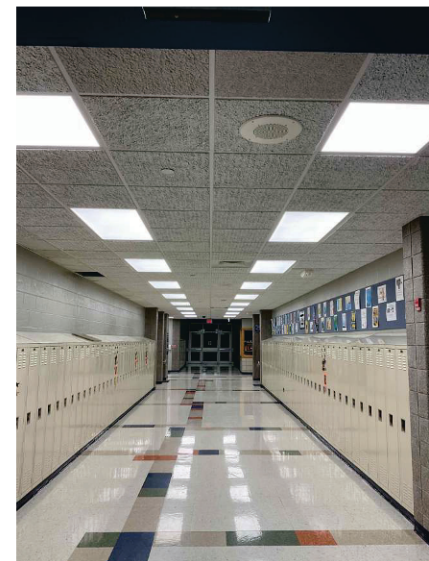

Discovery Middle School

WEEKLY PROGRESS REPORT



Epic Elementary




Epic Elementary



Liberty North High School




Liberty North High School

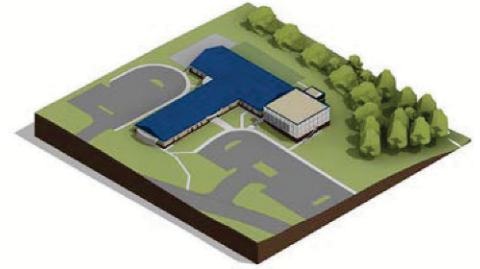

EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

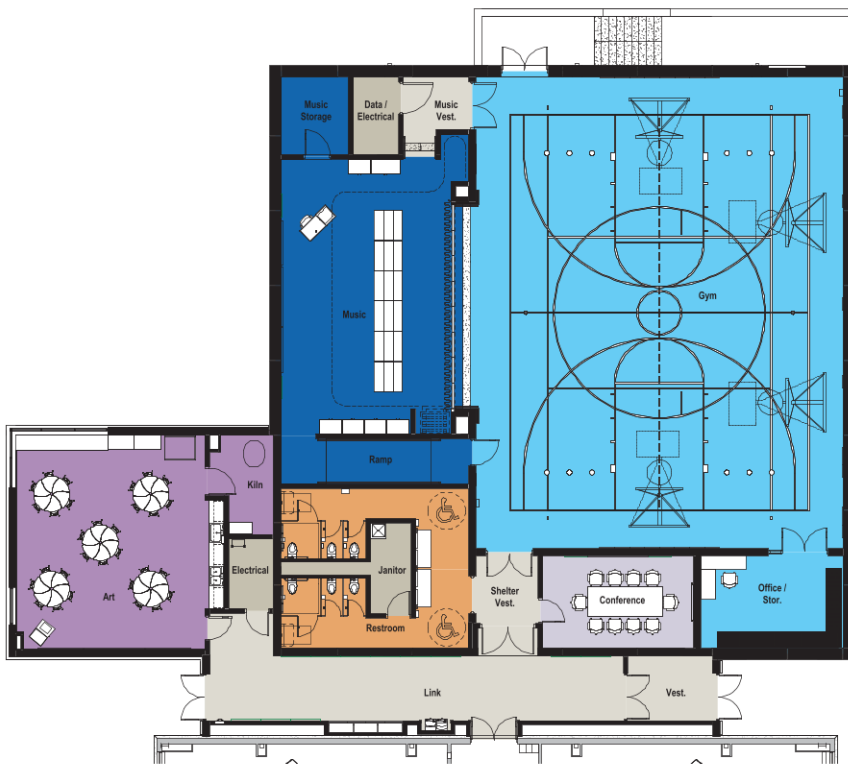

▲ Addition



▲ Renovation Area

PROJECT STATUS

- EPiC Elementary
- Interior summer work complete
 - Pre-cast Erection complete
 - Grouting of pre-cast done 8/9/2024
 - Art room foundation wall and backfill complete

UPCOMING

- EPiC Elementary
- Remaining MEP underslab
 - Geofoam
 - Slab on grade starting end of the month
 - Art Room overhead rough-in starting at end of the month



EPiC Elementary



EPiC Elementary



EPiC Elementary






EPiC Elementary



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

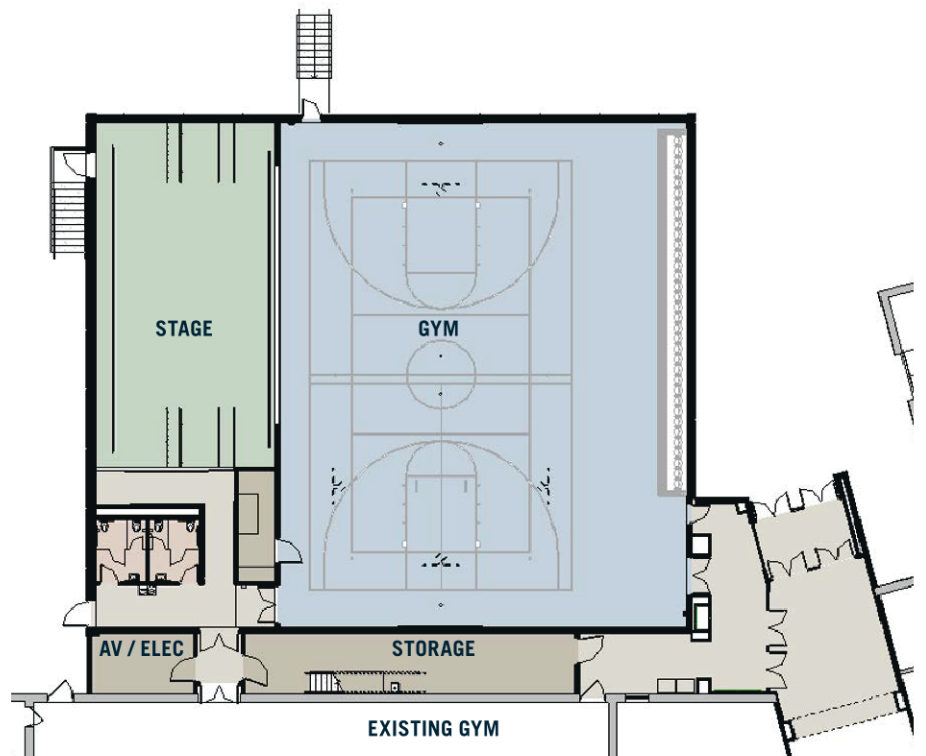

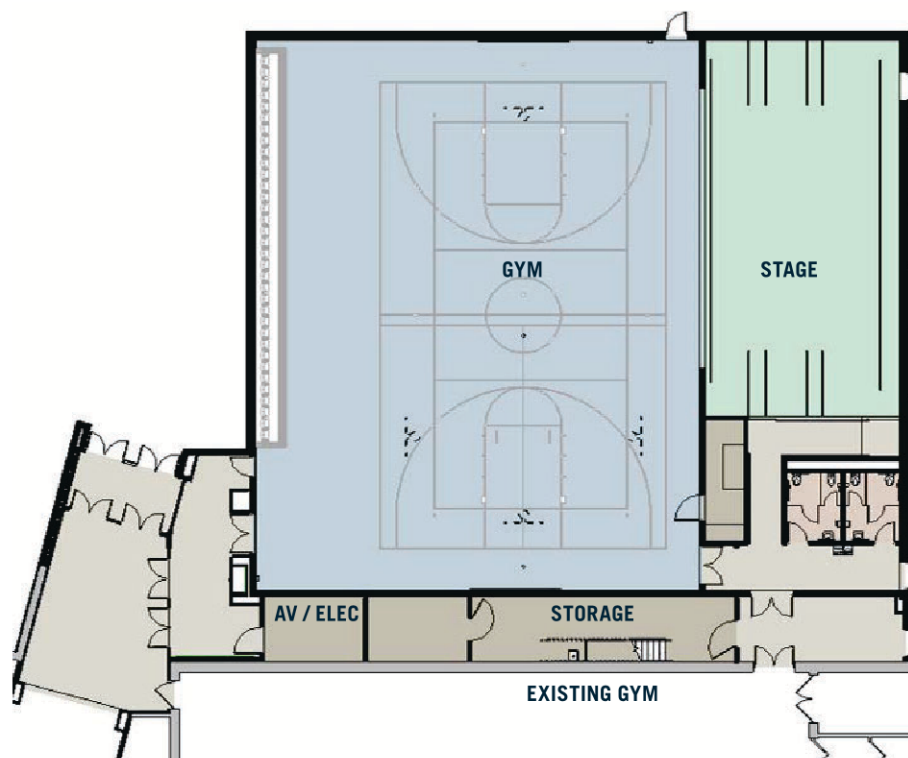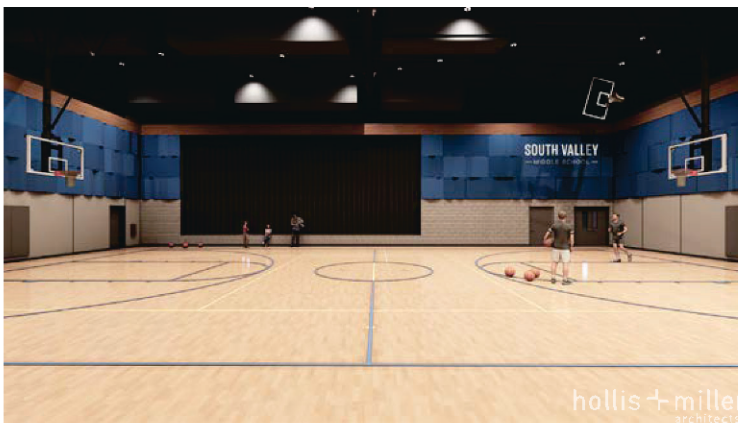

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

PROJECT STATUS

SVMS and DMS

- SVMS footings complete
- Remaining Demo of vestibule area complete at SVMS and DMS
- 1 line footing pour complete at DMS
- SVMS structural steel erection started 8/7/2024
- Remaining site utilities complete

UPCOMING

SVMS and DMS

- Remaining DMS Footings
- MEP underground
- Remaining steel for SVMS. Starting DMS steel at end of the month
- SVMS precast erection starting first week of September



SVMS - Footings



SVMS - Steel Erection



DMS - Footing Rebar



DMS -Footings



hollis + miller



hollis + miller



hollis + miller



hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



8/9/24

PROJECT STATUS

- Structural steel 100% set and detailed
- Decking 100% complete
- Frame, sheathing, & blocking at parapet 90% complete
- TPO upper roofing 25% complete
- West lost fine grading and curb complete
- Site fencing ongoing
- Rooftop curbs and roof hydrates set

UPCOMING

- MEP rough in
- TPO lower roof
- Metal panel Install
- West lost asphalt base
- Pour freezer slab
- Freezer panel install



Overall Site



TPO Install



RTU and Condensing Unit Curbs



Mezzanine



West Parking Lot



Overall Site



Overall Site



Overall Site

Fine Arts
Kid's Zone
Technology
Shared Amenities
Building Systems
Future Phase



District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

7/12/24

PROJECT STATUS

- District Technology Center:
- Completed Communications Install
 - Completed Interior Paint
 - Completed All Exterior Paint
 - Completed Floor Install
 - Completed Data Pod Install
 - Completed HVAC Equipment Install
 - Completed Landscaping/Fence Install
 - Completed Generator Install
 - Certificate of Occupancy - Received July 9th

UPCOMING

- District Technology Center:
- Complete Punchlist Work
 - Complete Furniture Move In
 - Server Switchover July 13th
 - Staff Move in July 16th

Project Completion July 2024



IT Reception



Exterior



Kid's Zone Open Office



Fine Arts Open Office



Fine Arts Workshop



Restrooms



Breakroom



Data Pod Install



Exterior





Medium Conference Room



Kid's Zone Storage



IT Open Office

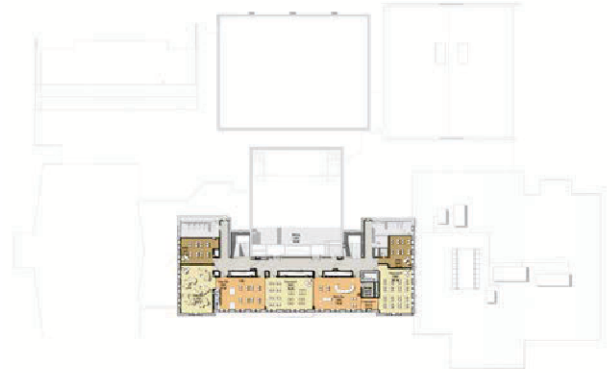

LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
 - Integrated SPED resources
 - Renovated cafeteria & scramble
 - Restroom renovations
- Exterior masonry repair & window replacement
 - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

8/12/24

PROJECT STATUS

Heritage Middle School

Summer Renovations:

- Completed Tile Install
- Completed Flooring Install
- Completed Paint
- Every Lighting Replacement

1964 Wing:

- Structural Steel Install
- Began Overhead MEP Rough In
- Began Framing
- Began In Wall MEP Rough In

UPCOMING

Heritage Middle School

Summer Renovations:

- Final Inspections
- Complete Punchlist Work
- Furniture Move In

1964 Wing:

- Complete Overhead MEP Rough In
- Complete In Wall MEP Rough In
- Install Roof Top Units
- Complete Framing
- Begin Drywall Install/Finish



Cafeteria Build Back



1964 (Area A) Progress



1964 (Area A) Progress



Kitchen Build Back



Restroom Build Back




1964 (Area A) Progress



1964 (Area A) Progress



Restroom Build Back

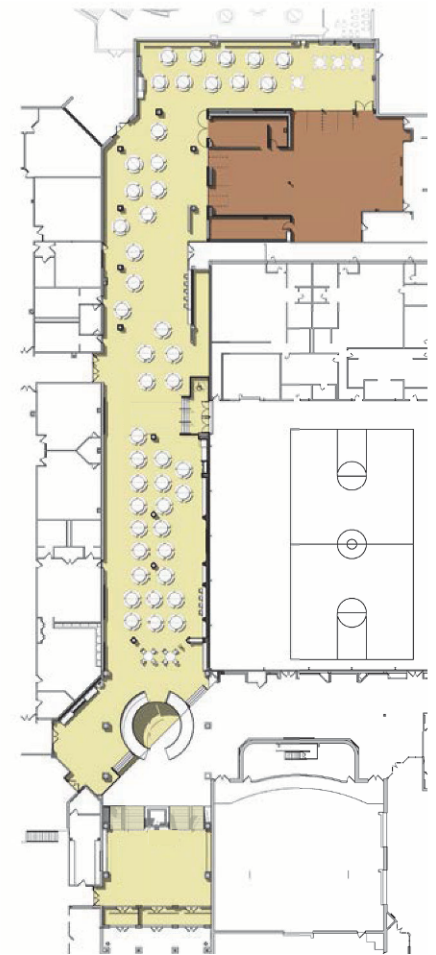

PHASE 2

Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025



PHASE 1

8/12/24

PROJECT STATUS

- Liberty High School
Build Back of 400's wing classrooms
-Completed MEP Rough In
-Completed Paint
-Completed Ceiling Grid
-Completed Final Inspections
Build Back of 100's wing classrooms
-Completed Framing
-Continued In Wall Rough In
-Continued MEP Overhead Rough In
-Began Drywall Install/Finishing

UPCOMING

- Liberty High School
-Build Back of 400's wing classrooms
-Furniture Move In
-Build Back of 100's wing classrooms
-Complete MEP In Wall Rough In
-Complete MEP Overhead Rough In
-Continue Drywall Install
-Begin Paint
-Begin Ceiling Grid

Project Completion: November 2024




400's Classrooms



Progress 100's Wing



Progress 100's Wing

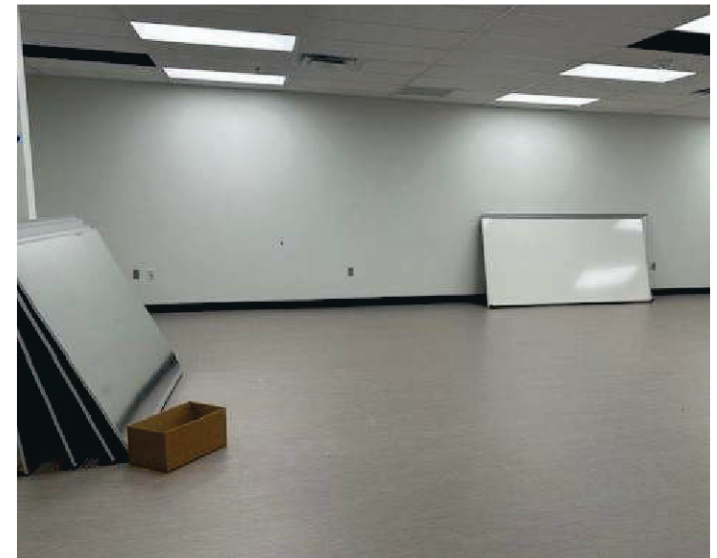


400's Classrooms



400's Corridor



Progress 100's Wing

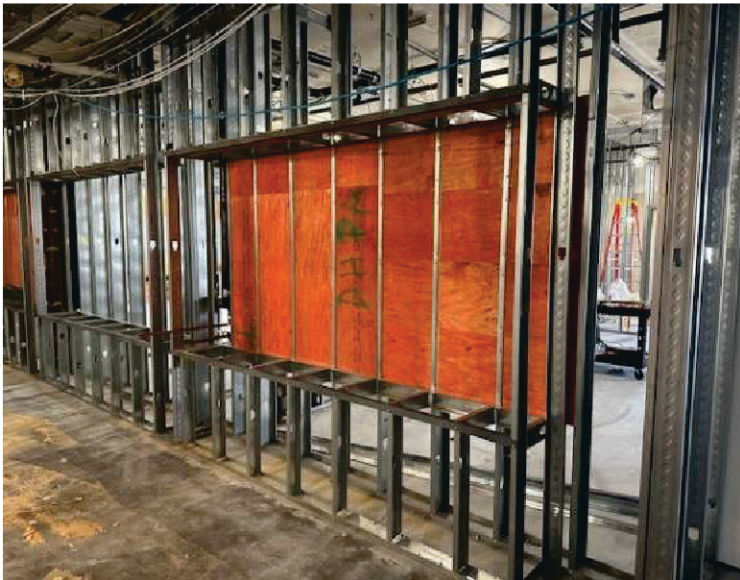

Progress 100's Wing




Progress 100's Wing



Shop Building


- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

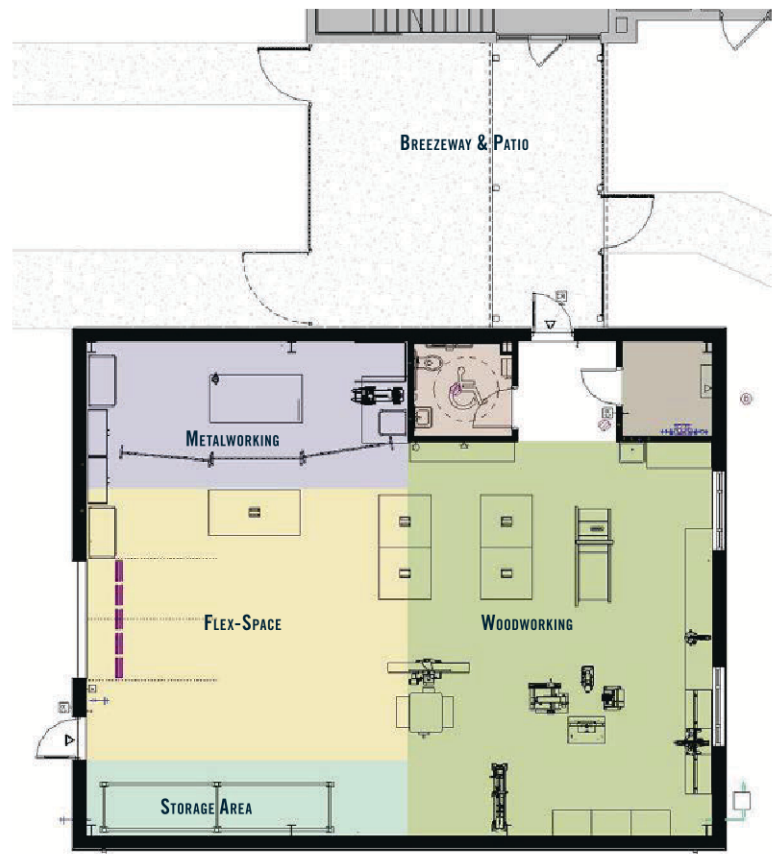


▲ Floor Plan

Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:
Spring 2024–Spring 2025

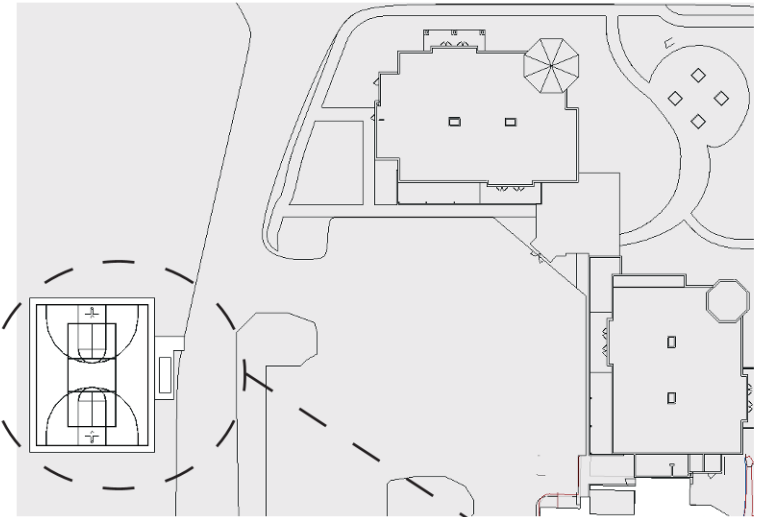


Overall Site Plan

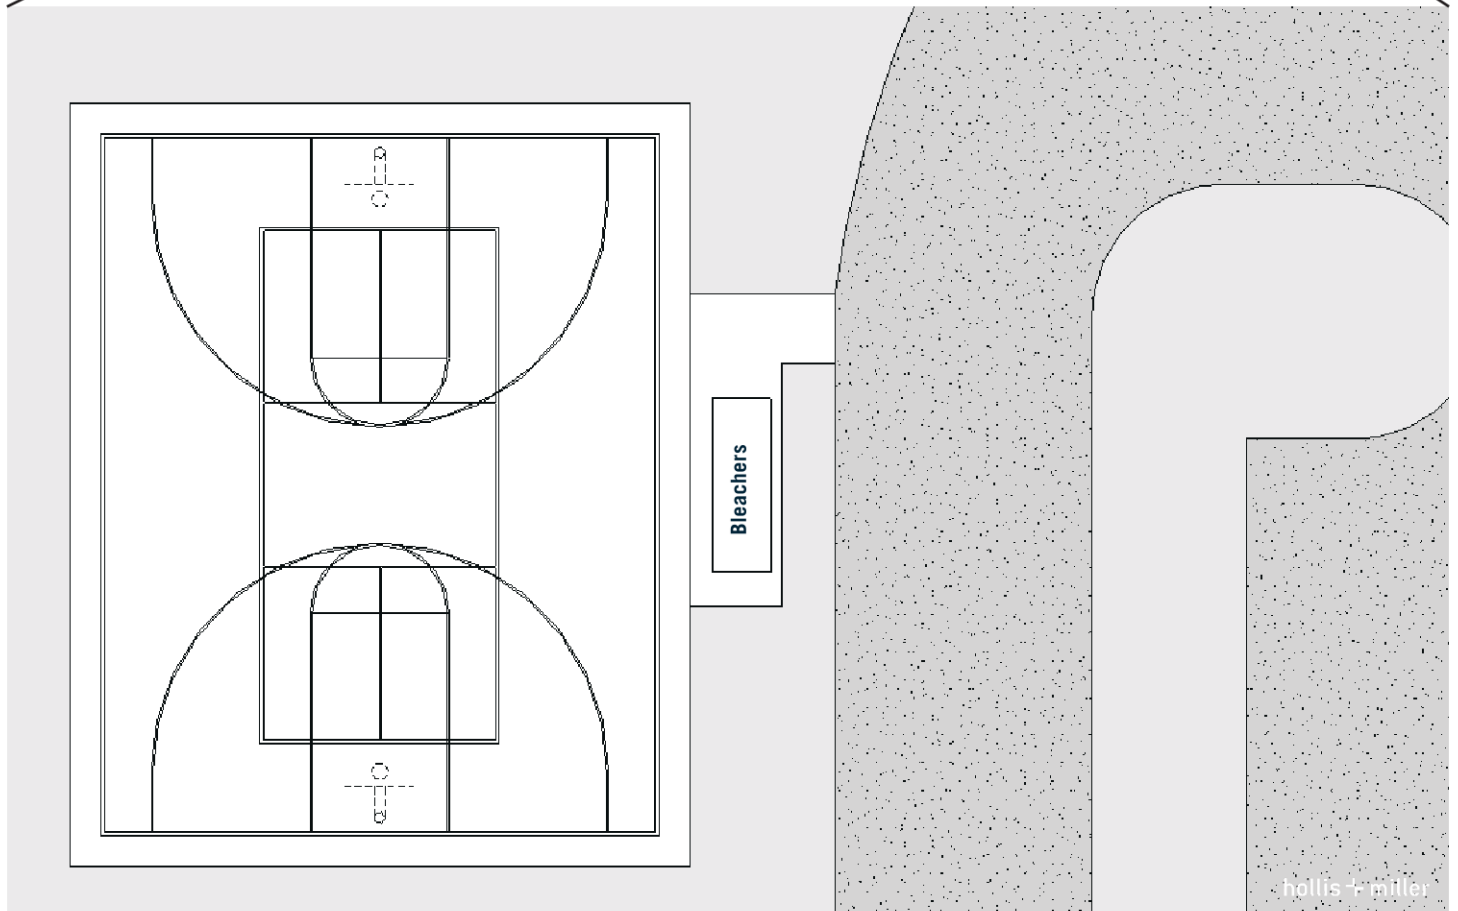

Enlarged Site Plan

Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:
May 2024 - August 2025

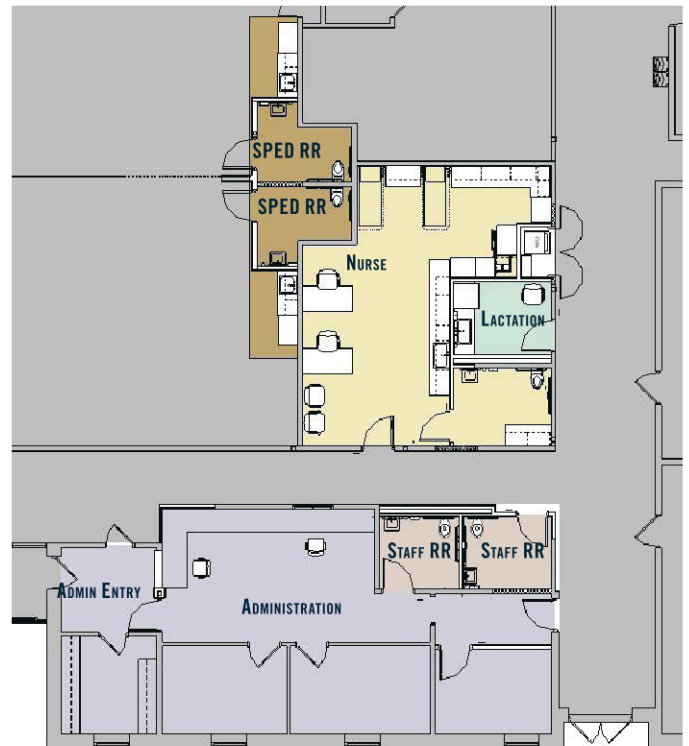

▲ Enlarged Floor Plan




▲ Overall Floor Plan

Interior Renovation


- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:
May 2024 - August 2025



Administration

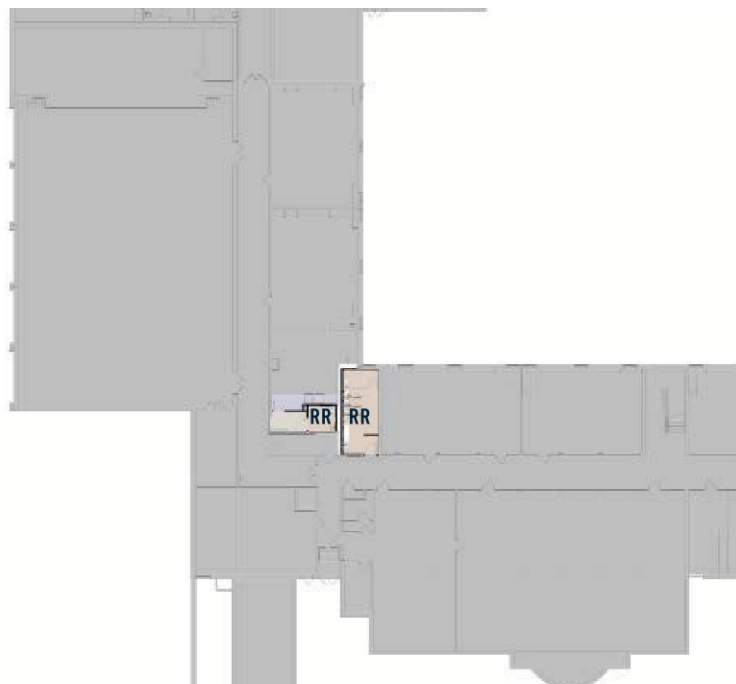

Partial First Level Floor Plan

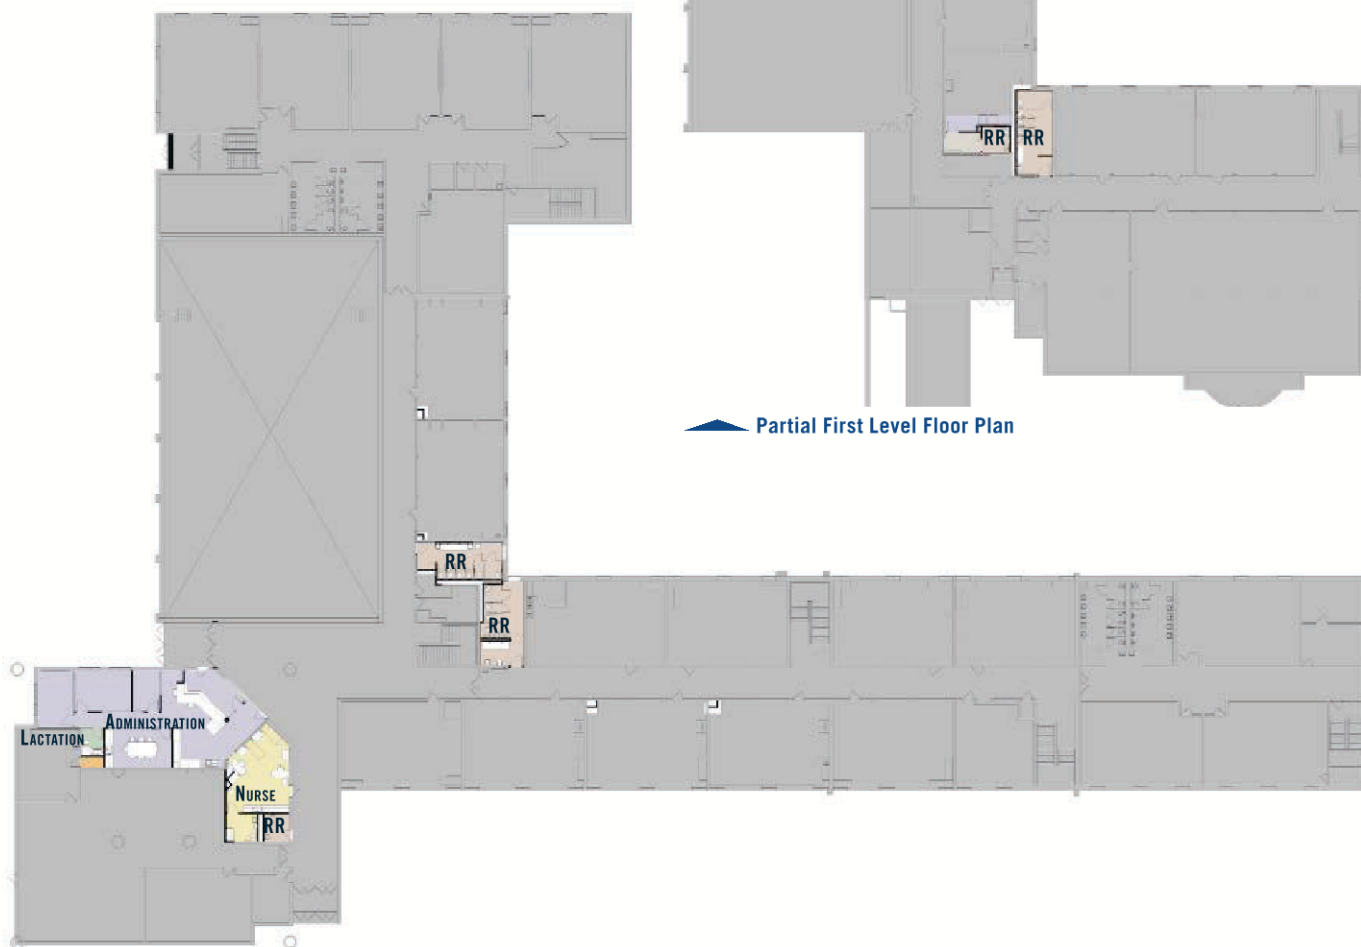


Overall Second Level Floor Plan

Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:
May 2024 - August 2025



Administration

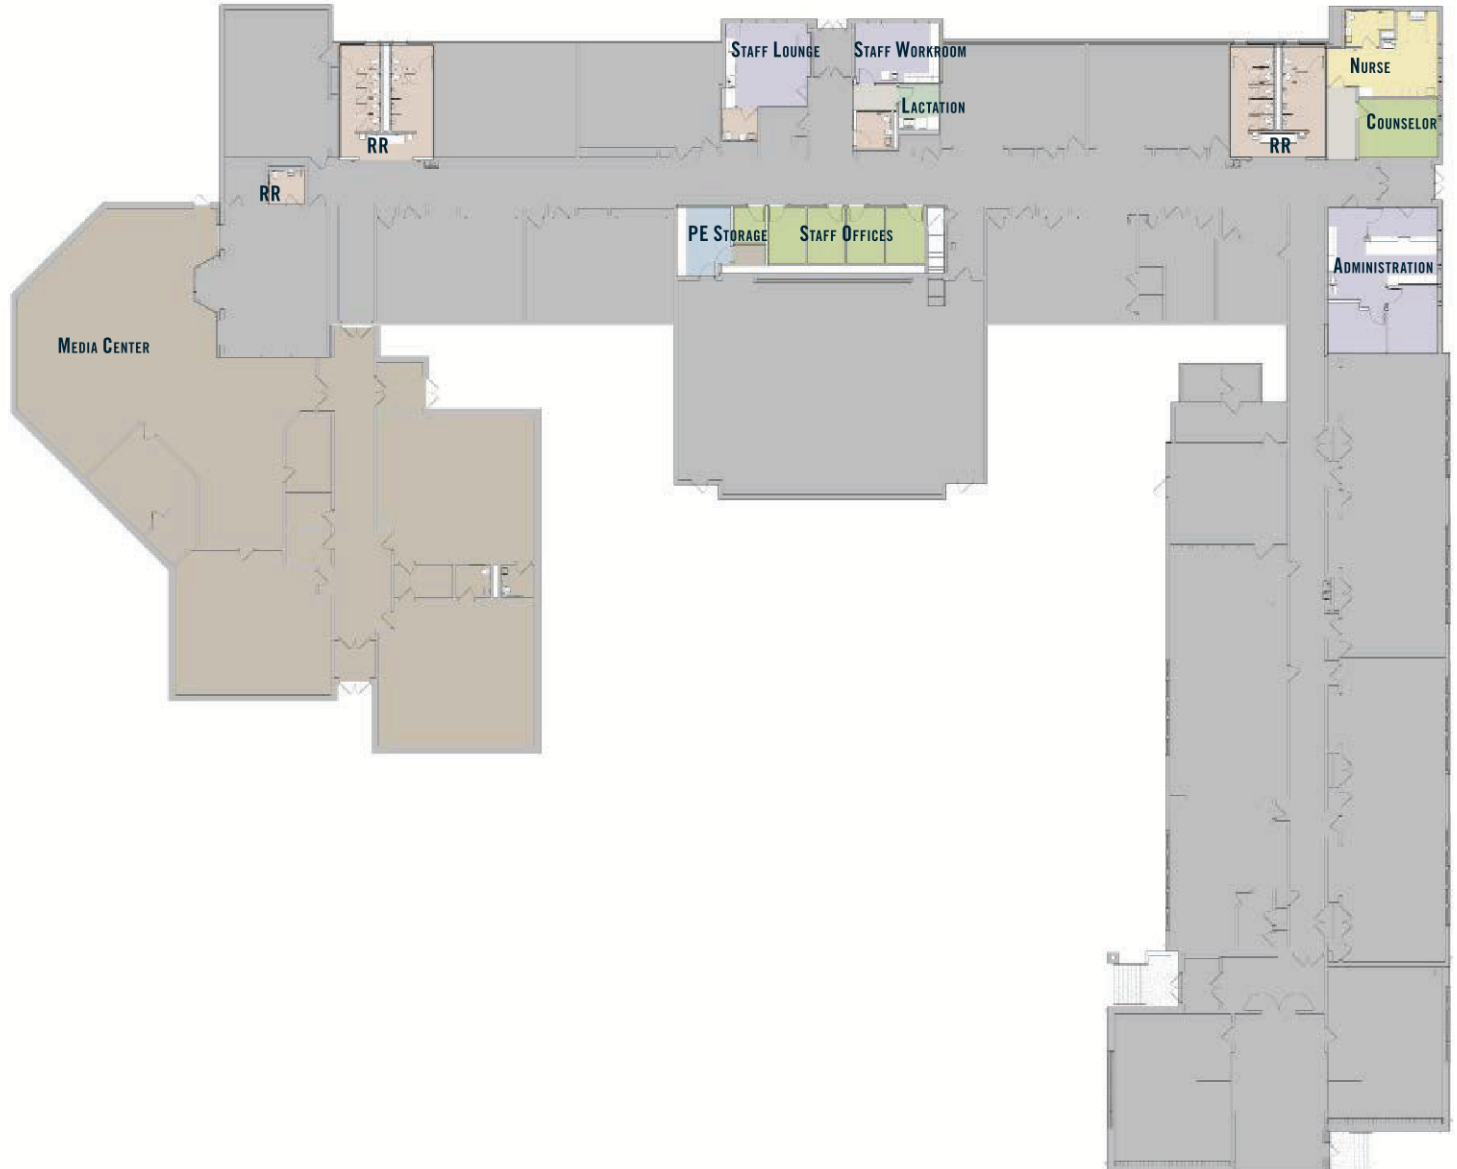

▲ Overall Floor Plan

**WEEKLY
PROGRESS
REPORT**

Doniphan, Franklin, and Ridgeview Summer Renovation Projects

Liberty Public Schools



8/9/24

PROJECT STATUS

- Doniphan, Franklin, and Ridgeview:
- Completed MEP Install
 - Completed Drywall Install
 - Completed Ceiling Grid Install
 - Completed Paint
 - Completed Tile
 - Completed Casework Install
 - Completed Flooring Install
 - Completed Epoxy Install
 - Completed Specialties Install
 - Began Punch List Work


UPCOMING

- Doniphan, Franklin, and Ridgeview:
- Complete Punch List Work
 - Complete Final Inspections
 - Furniture Move-In

Project Completion: August 2024




Franklin - Main Office

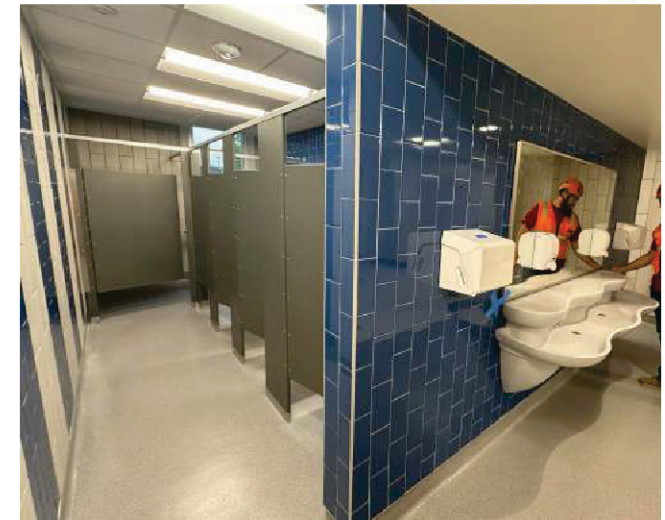

Franklin - Restrooms



Franklin - Workroom

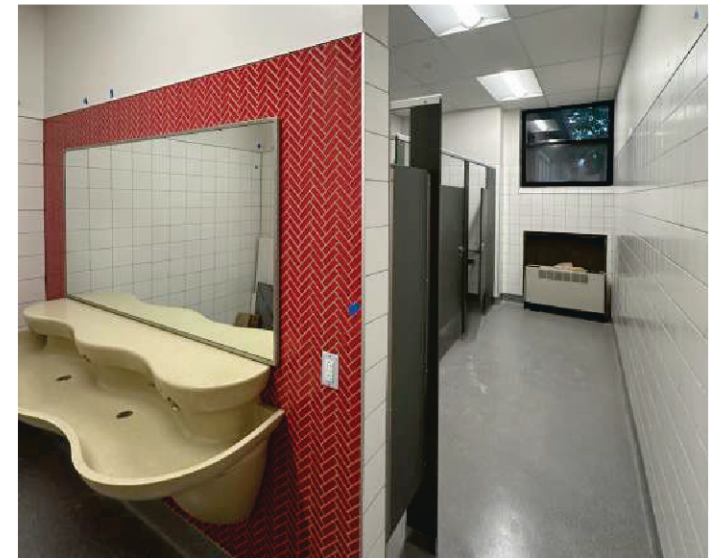

Ridgeview - Level 2 Restroom



Ridgeview - Main Office



Doniphan - Main Office



Doniphan - Assistant Principal Office



Doniphan - Teacher's Lounge
