




2023 BOND

MAJOR PROJECTS UPDATE

JULY 2024



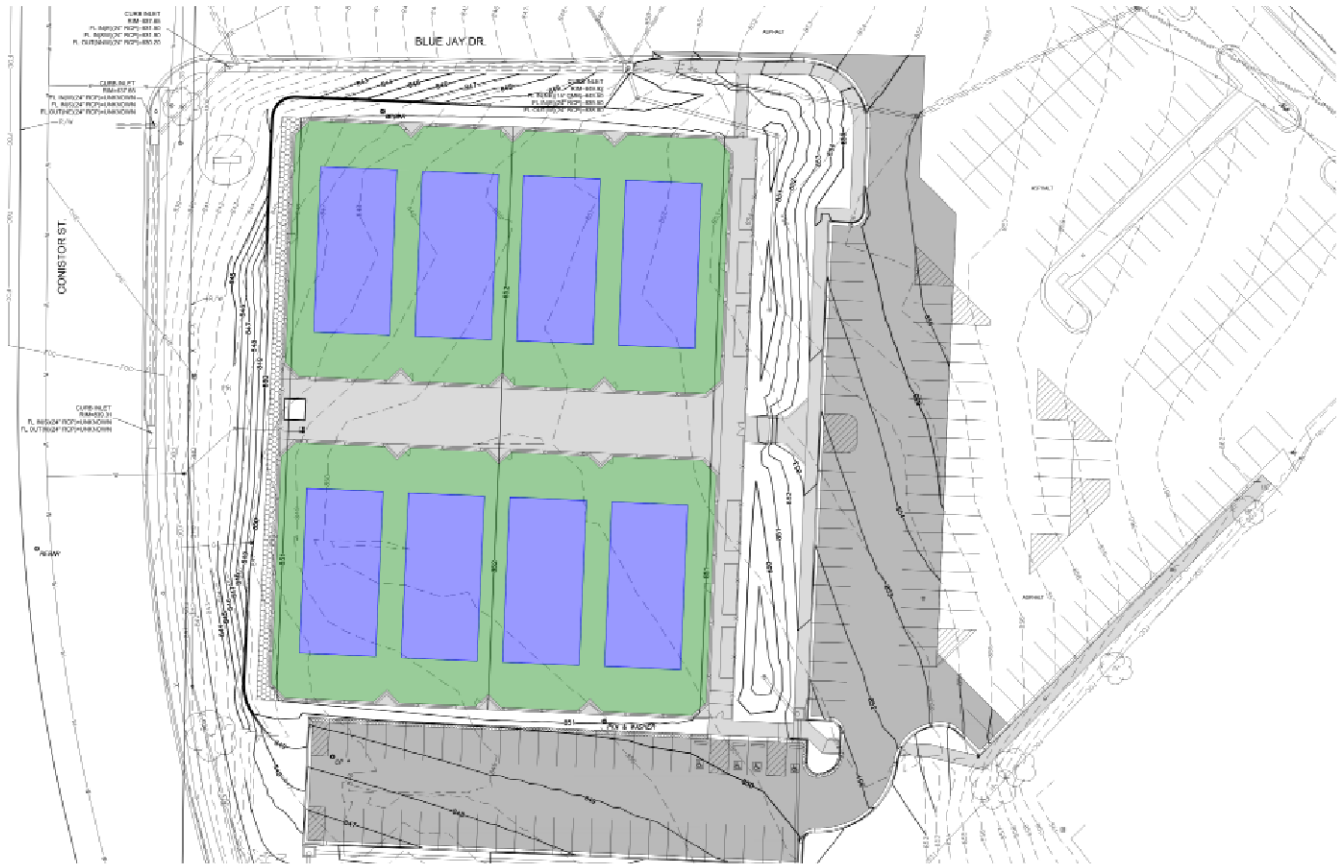

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

**WEEKLY
PROGRESS
REPORT**

Tennis Courts 11/13/2023

Liberty Public Schools



PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

UPCOMING

Project Completion October 2023




North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South

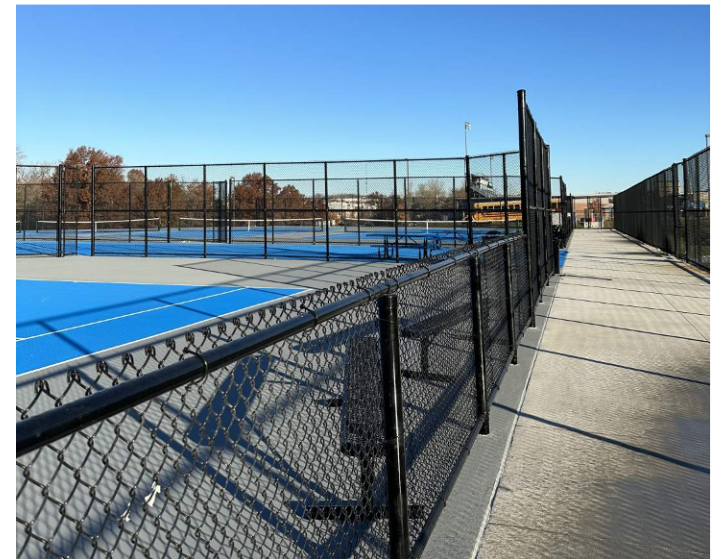

East Concourse Looking North


WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

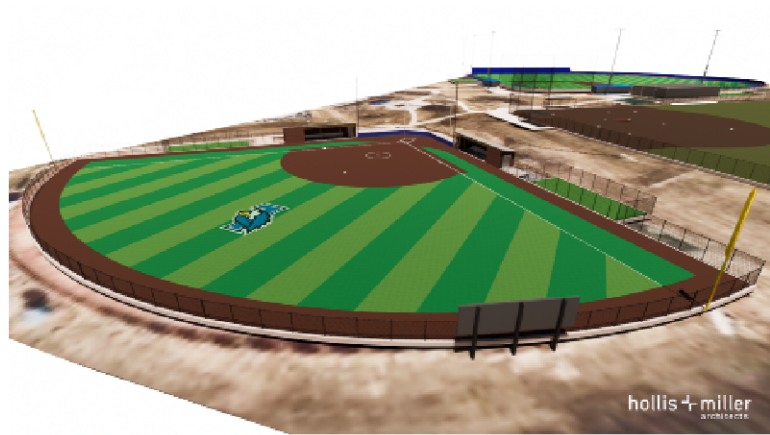

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field


- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024

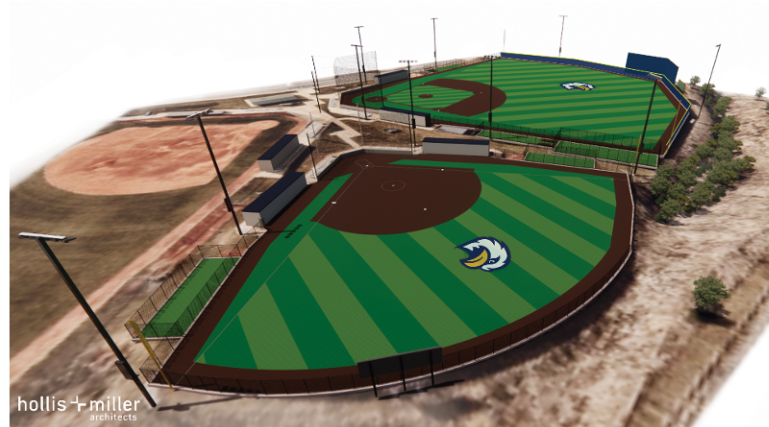

Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

PROJECT STATUS

- LNHS
- Punch List Completion
 - Final Inspection Passed

- LHS
- Punch List Completion
 - Batting Tunnel Completed

UPCOMING

- LHS
- City Inspections
 - Remaining Sod

Project Completion
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

PROJECT STATUS

- South Valley MS - Upgrades Complete
- Discovery MS - Upgrades Complete
- EPiC Elementary - Upgrades Complete
- Liberty North High School - Upgrades Ongoing

UPCOMING

- Energy Inspections - All Four Schools
- Emergency LED Fixtures

Project Completion
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

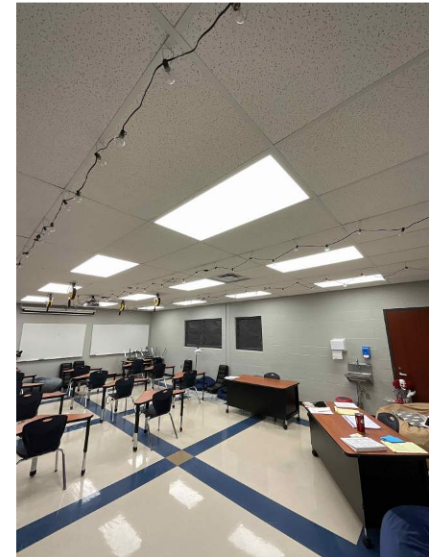

Liberty North HS

PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


UPCOMING

Energy Inspections All Four Schools
Emergency LED Fixtures

Project Completion
December 2023

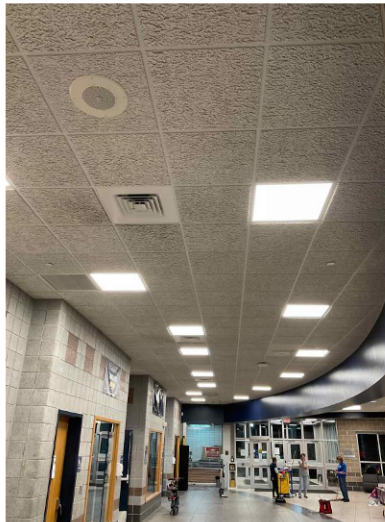


South Valley Middle School

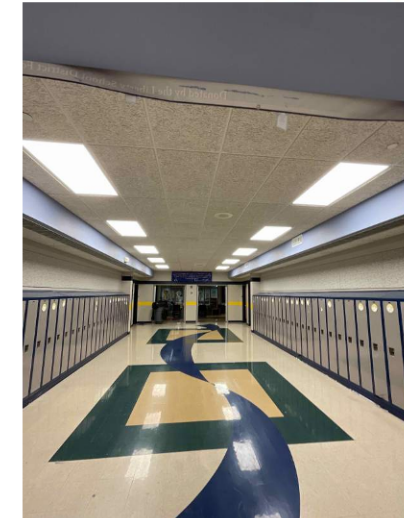

South Valley Middle School



Discovery Middle School

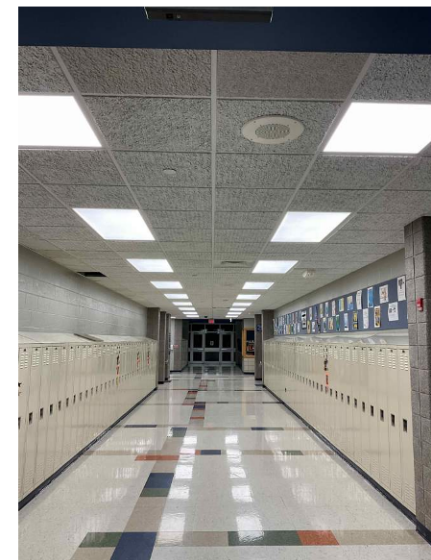

Discovery Middle School

WEEKLY PROGRESS REPORT



Epic Elementary




Epic Elementary



Liberty North High School




Liberty North High School

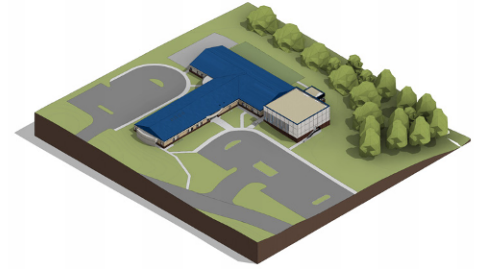


EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother’s Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

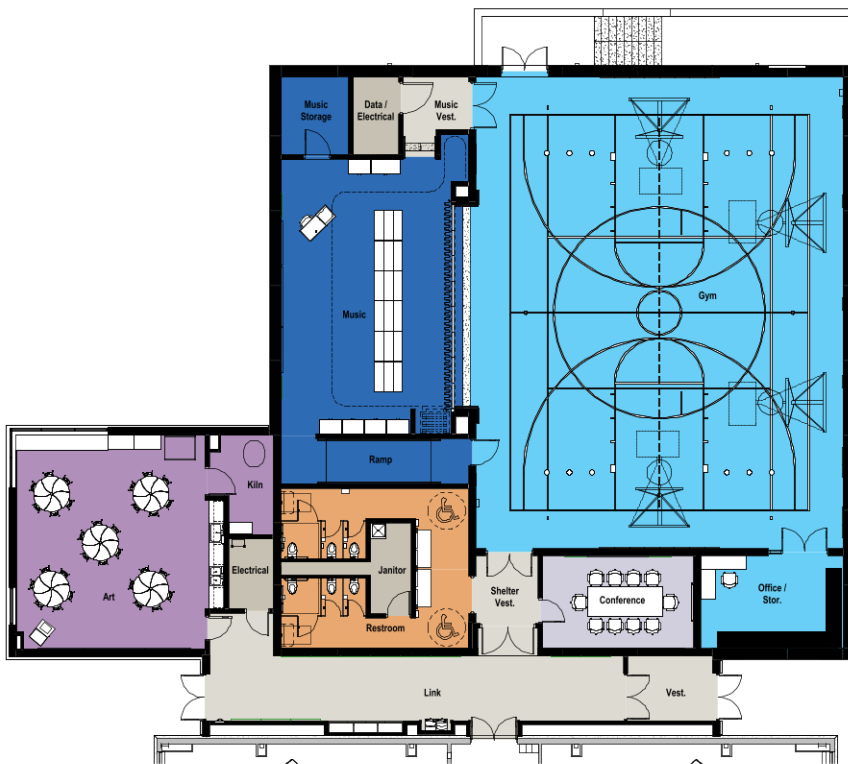

▲ Addition

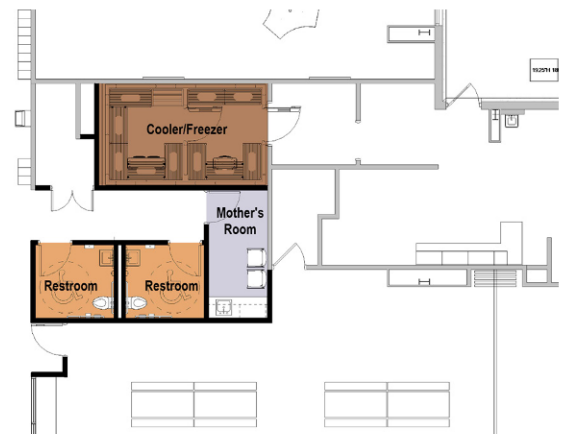

▲ Renovation Area

PROJECT STATUS

- EPiC Elementary
- Footings and foundation walls done
 - Steel Erection is complete
 - Foundation wall waterproofing starting this week
 - Backfill starting once waterproofing is done
 - Under-slab plumbing starting this week

UPCOMING

- EPiC Elementary
- Existing Building Interior Renovation
 - Precast erection starting 7/29/2024


Project Completion
EPiC Feb 2025/DMS&SVMS June 2025



EPiC Elementary - Steel



EPiC Elementary - Steel

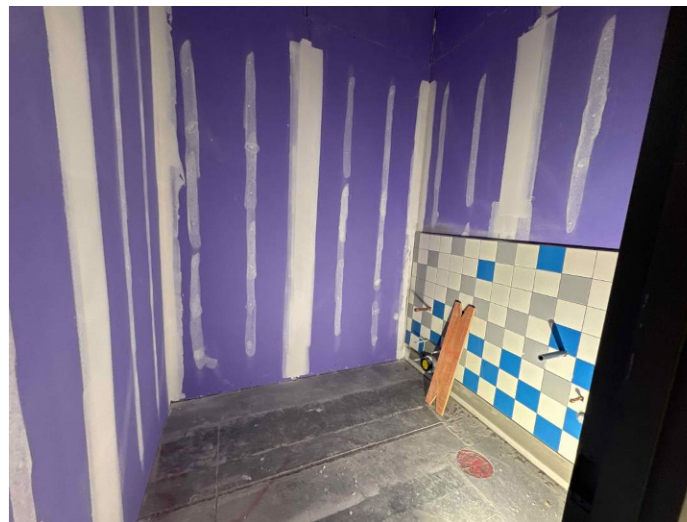

EPiC Elementary - Interior Restroom





EPiC Elementary - Interior Renovation



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

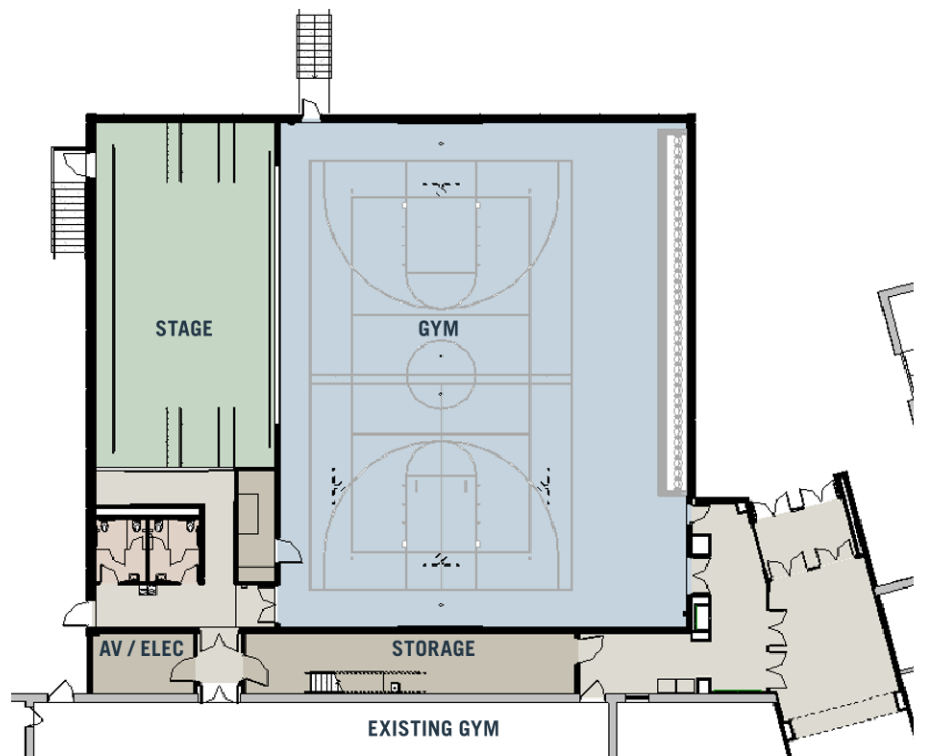

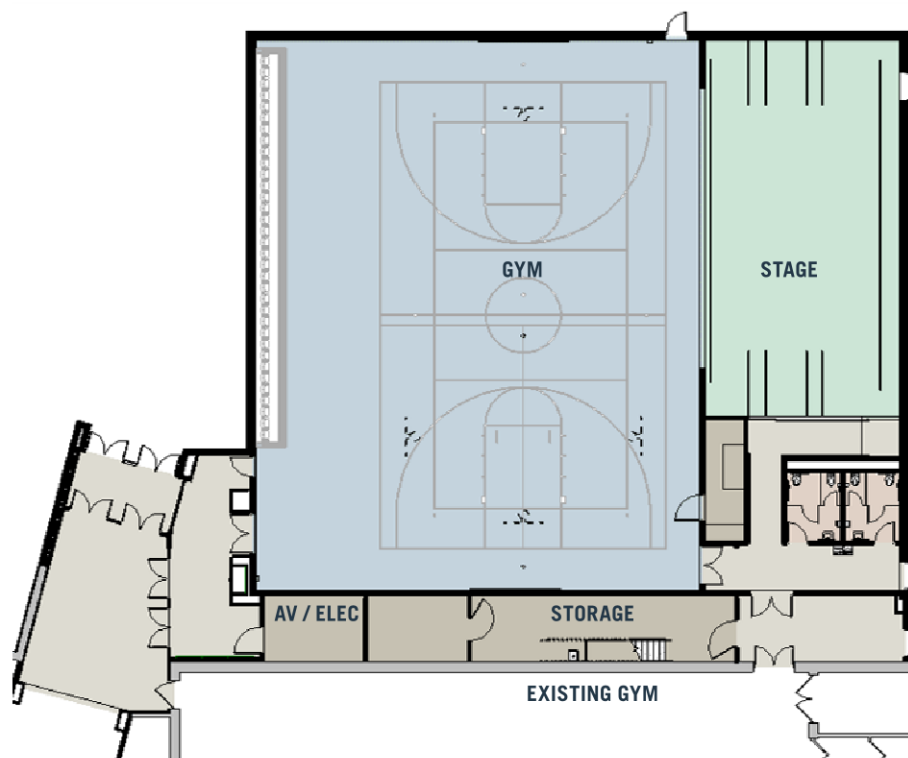

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

PROJECT STATUS

- SVMS and DMS
- Building Pad complete at SVMS and DMS
 - Site Utilities done at SVMS and DMS
 - Footings started at SVMS


UPCOMING

- SVMS and DMS
- DMS Footings starting 7/22
 - MEP underground
 - Structural Steel

Project Completion
DMS&SVMS June 2025



SVMS - Footings

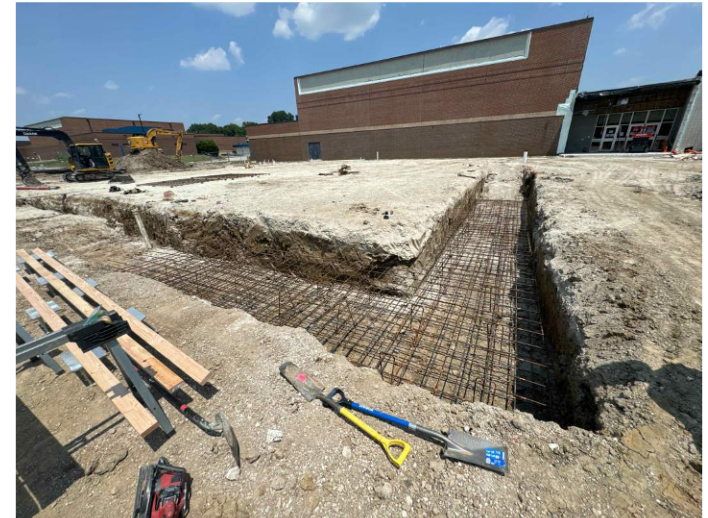

SVMS - Footings



SVMS



DMS - Building Pad



hollis + miller



hollis + miller



hollis + miller



hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



**WEEKLY
PROGRESS
REPORT**

Distribution Center 7/15/24

Liberty Public Schools



7/15/24

PROJECT STATUS

- Retaining walls complete
- Storm line 2 & 6 complete
- Detention basin rough grade complete
- 8" & 4" SOG complete
- Structural steel 100% set
- Columns grouted
- Decking 90% complete

UPCOMING

- Structural steel detailing
- Frame, sheathing, & blocking at parapet
- MEP rough in
- TPO upper roof / lower roof
- Metal panel Install
- Lower roof decking
- West lost fine grading
- Detention basin fine grade and seed



Overall Site



Overall Site



Overall Site



Overall Site



Mezzanine Stairs



Mechanical Chase



Mezzanine



Mezzanine

Fine Arts
 Kid's Zone
 Technology
 Shared Amenities
 Building Systems
 Future Phase



District Technology Center

- Renovated workspace for District’s Technology, Fine Arts, and Kid’s Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

7/12/24

PROJECT STATUS

District Technology Center:

- Completed Communications Install
- Completed Interior Paint
- Completed All Exterior Paint
- Completed Floor Install
- Completed Data Pod Install
- Completed HVAC Equipment Install
- Completed Landscaping/Fence Install
- Completed Generator Install
- Certificate of Occupancy - Received July 9th

UPCOMING

District Technology Center:

- Complete Punchlist Work
- Complete Furniture Move In
- Server Switchover July 13th
- Staff Move in July 16th

Project Completion July 2024



IT Reception



Exterior



Kid's Zone Open Office



Fine Arts Open Office



Fine Arts Workshop



Restrooms



Breakroom



Data Pod Install



Exterior




Medium Conference Room



Kid's Zone Storage



IT Open Office

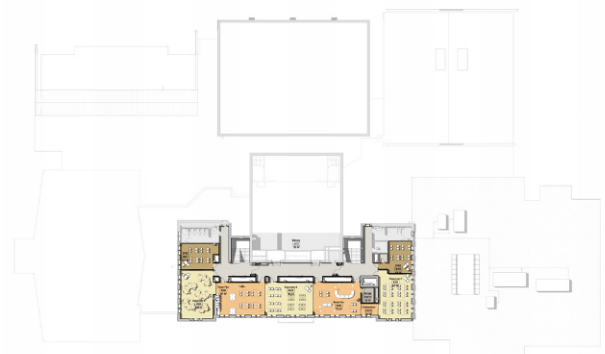

LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
 - Integrated SPED resources
- Renovated cafeteria & scramble
 - Restroom renovations
- Exterior masonry repair & window replacement
 - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

7/12/24

PROJECT STATUS

Heritage Middle School

- Framing and CMU install at Kitchen and Bathrooms with Area C
- Paint in the Kitchen and Scramble Area
- Door Frame Install in area C
- Every Lighting replacement continued.
- Demo Continued in the 1964 portion of the building.
- Structural Steel install in the 1964 (Area A) started.

UPCOMING

Heritage Middle School

- Area C Resinous flooring is starting 7.15.24
- Area C tile is starting 7.15.24
- Paint will be continuing throughout Area C.
- Overhead Rough in will be starting in the 1964 wing (Area A).
- We will be continuing with structural steel install in the 1964 wing (Area A)



Cafeteria Build Back



Kitchen Build Back



New Seating Area Progress



Bathroom Build Back



1964 (Area A) Progress




1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress

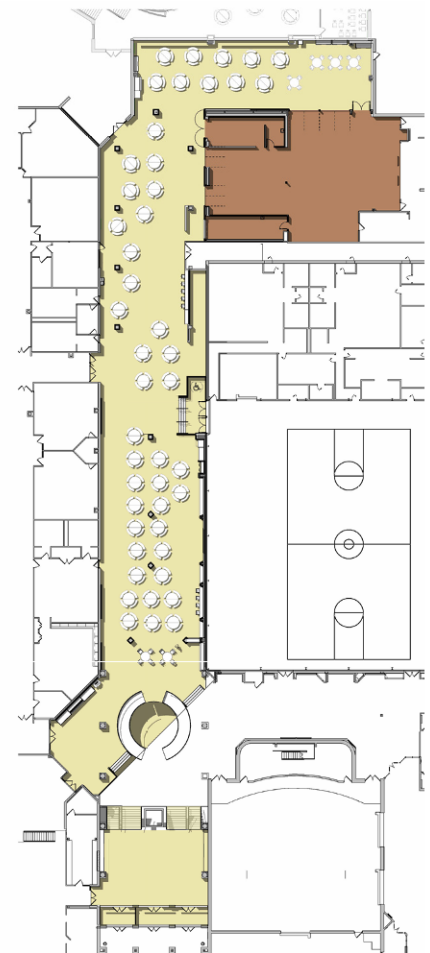

PHASE 2

Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025



PHASE 1

**WEEKLY
PROGRESS
REPORT**

Liberty High School

Liberty Public Schools



7/12/24

PROJECT STATUS

- Liberty High School
- Build Back of 400's wing classrooms
 - MEP Rough In
 - Drywall
 - Paint
 - Ceiling Grid
 - Build Back of 100's wing classrooms
 - Framing
 - MEP Overhead Rough In
 - MEP In Wall Rough In

UPCOMING

- Liberty High School
- Build Back of 400's wing classrooms
 - MEP Trim Out
 - Flooring
 - Door Install
 - Build Back of 100's wing classrooms
 - MEP Rough In
 - Drywall
 - Paint



Build Back 400's Wing



Build Back 400's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing




Progress 100's Wing





Shop Building



- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

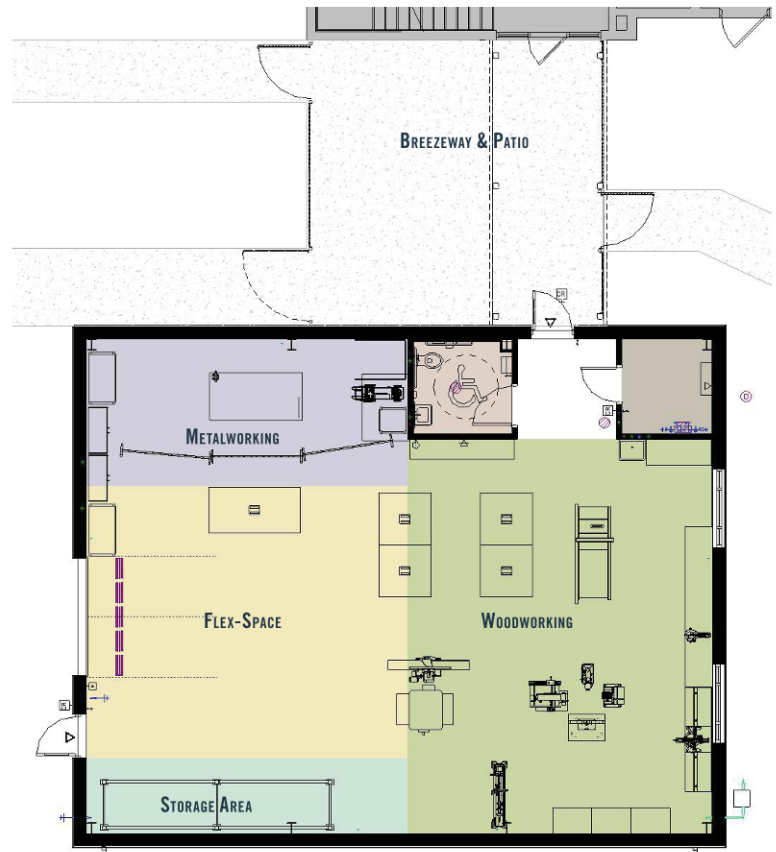

▲ Floor Plan


Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:
Spring 2024–Spring 2025

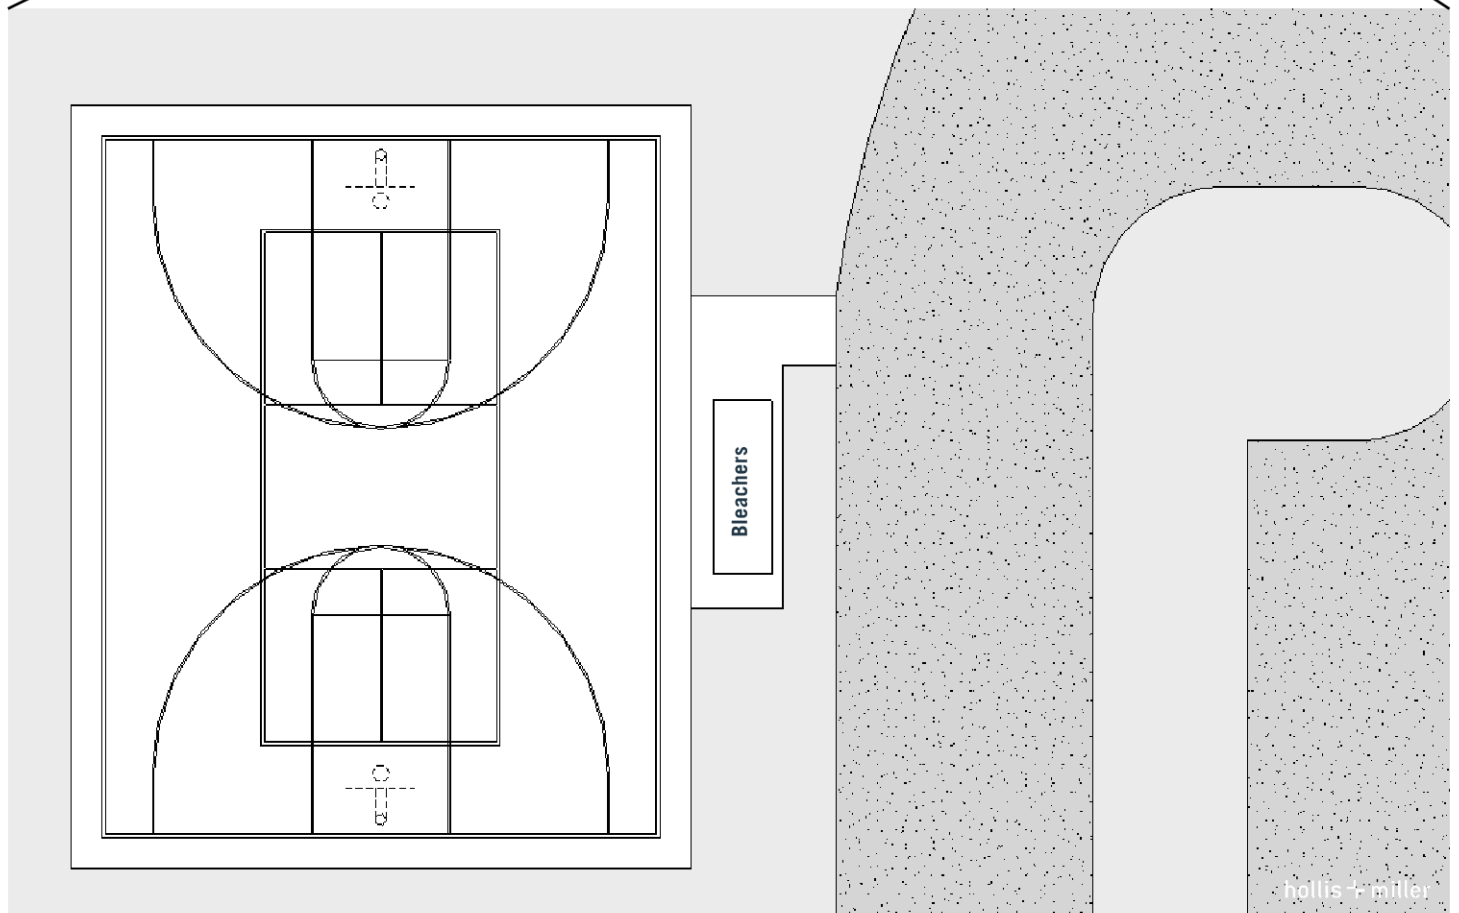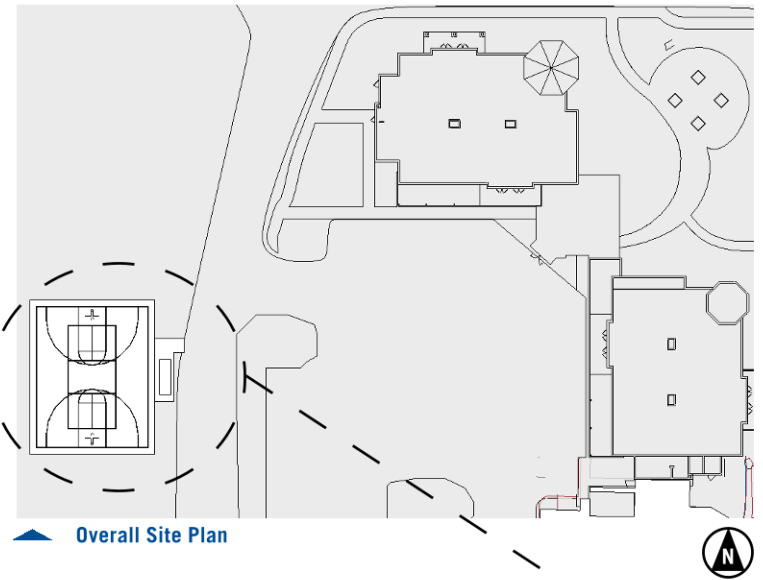


Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:
May 2024 - August 2025

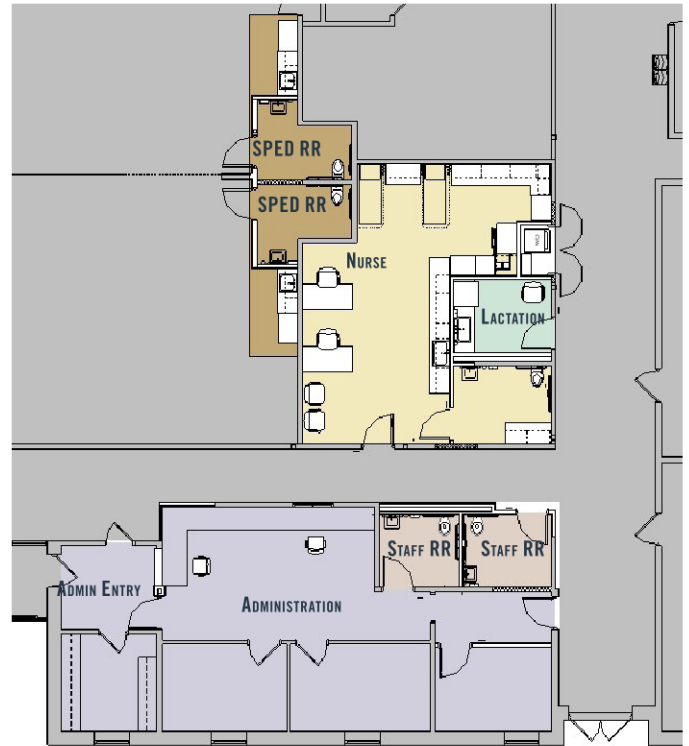

▲ Enlarged Floor Plan

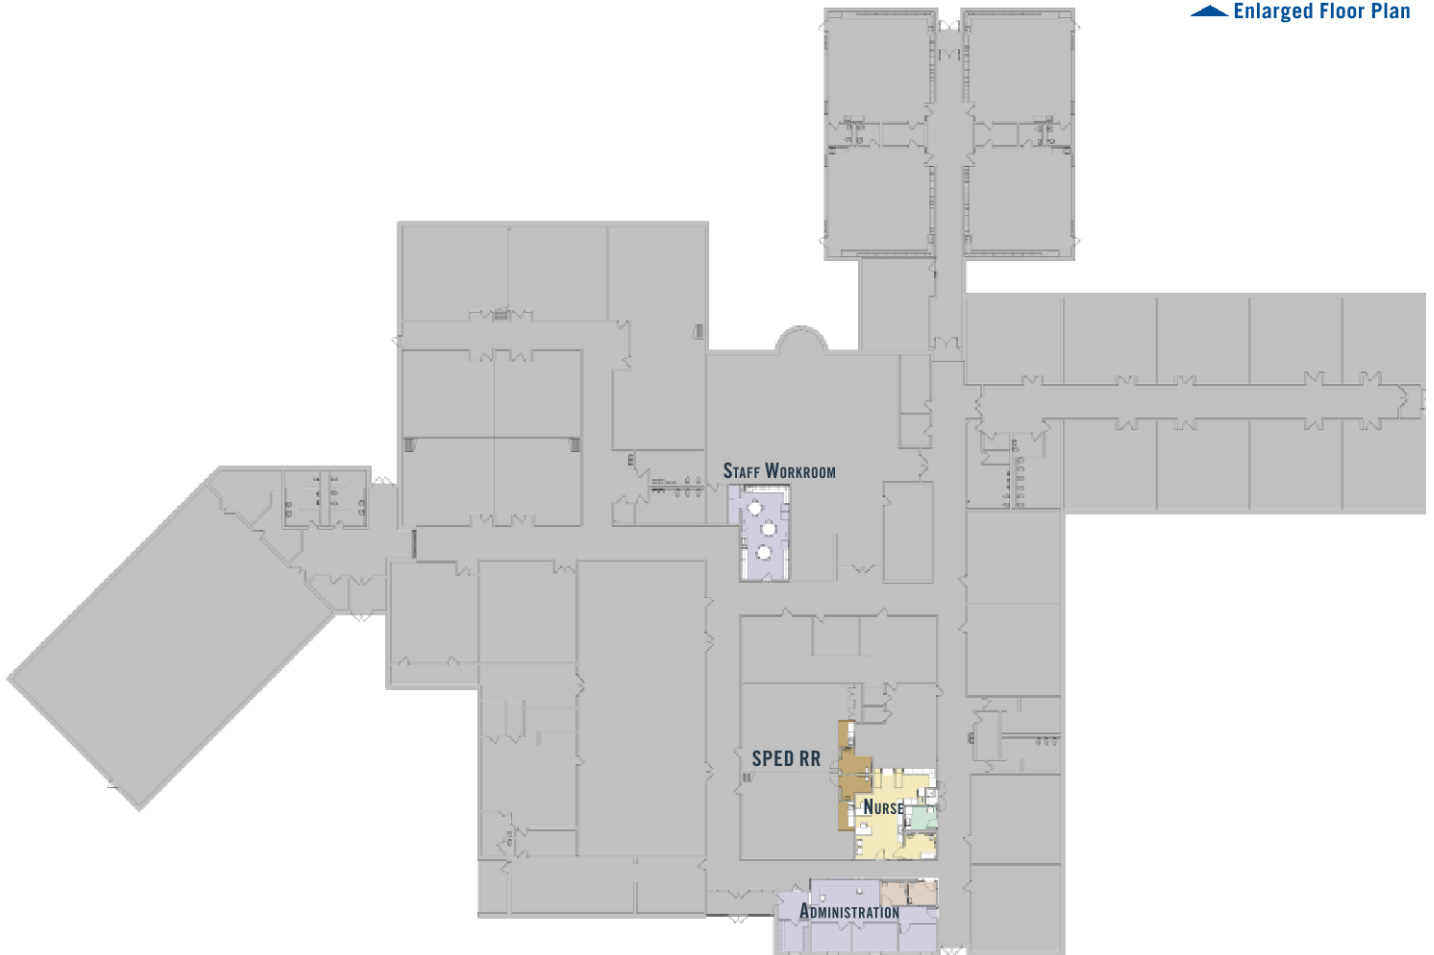


▲ Overall Floor Plan

Interior Renovation


- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:
May 2024 - August 2025



Administration

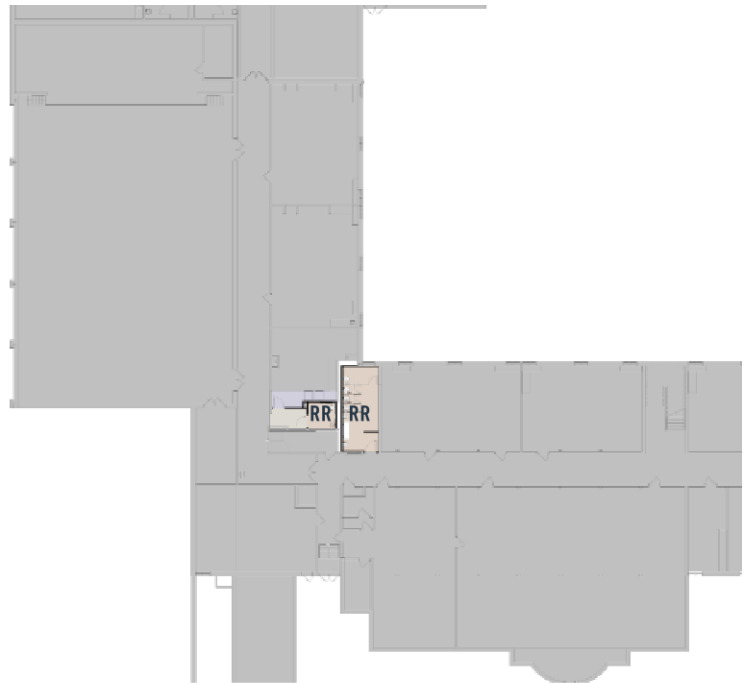

Partial First Level Floor Plan

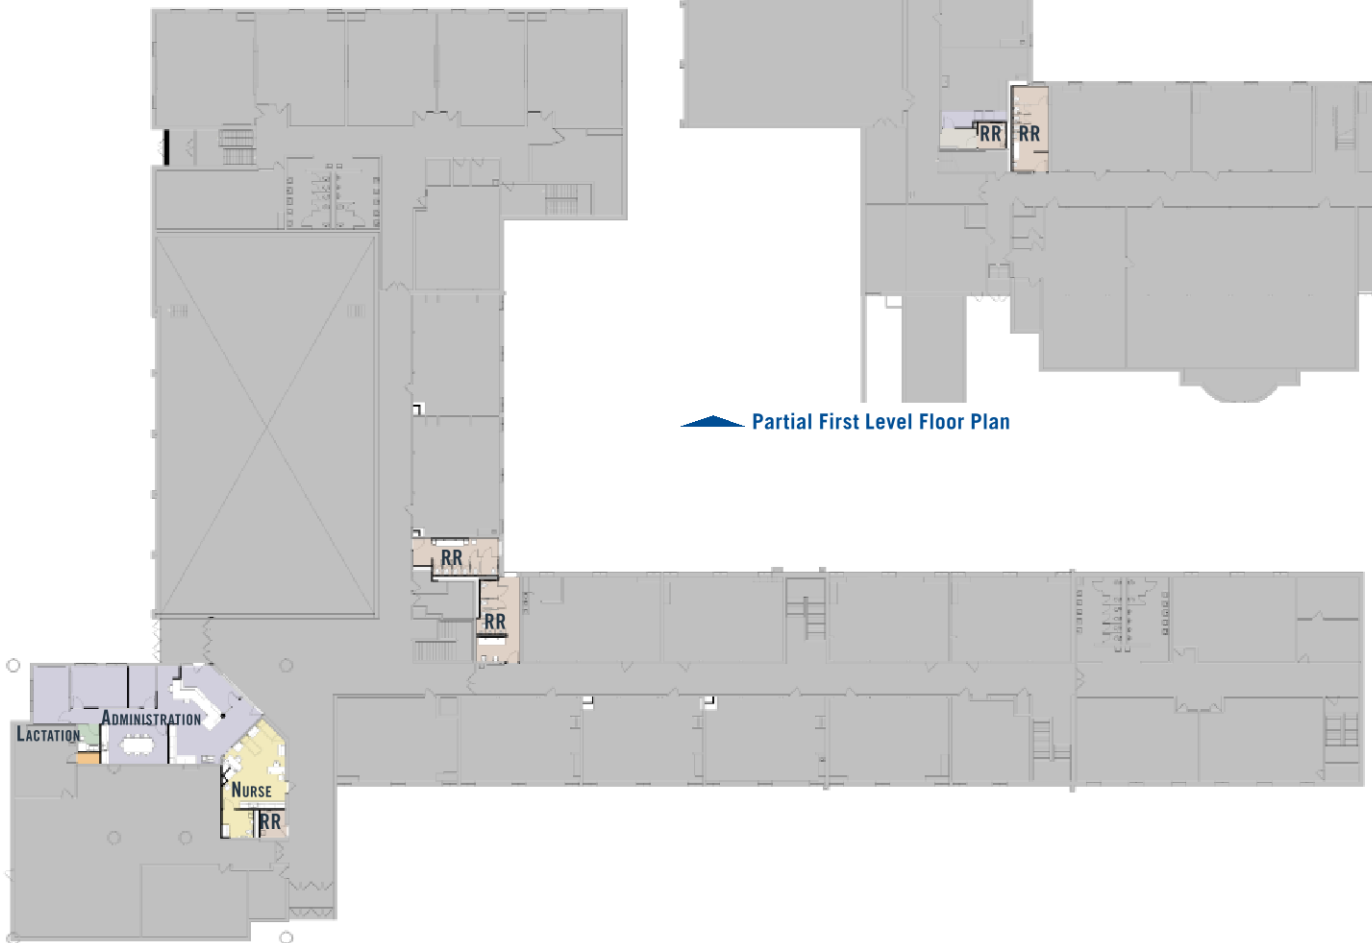


Overall Second Level Floor Plan

Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:
May 2024 - August 2025



Administration

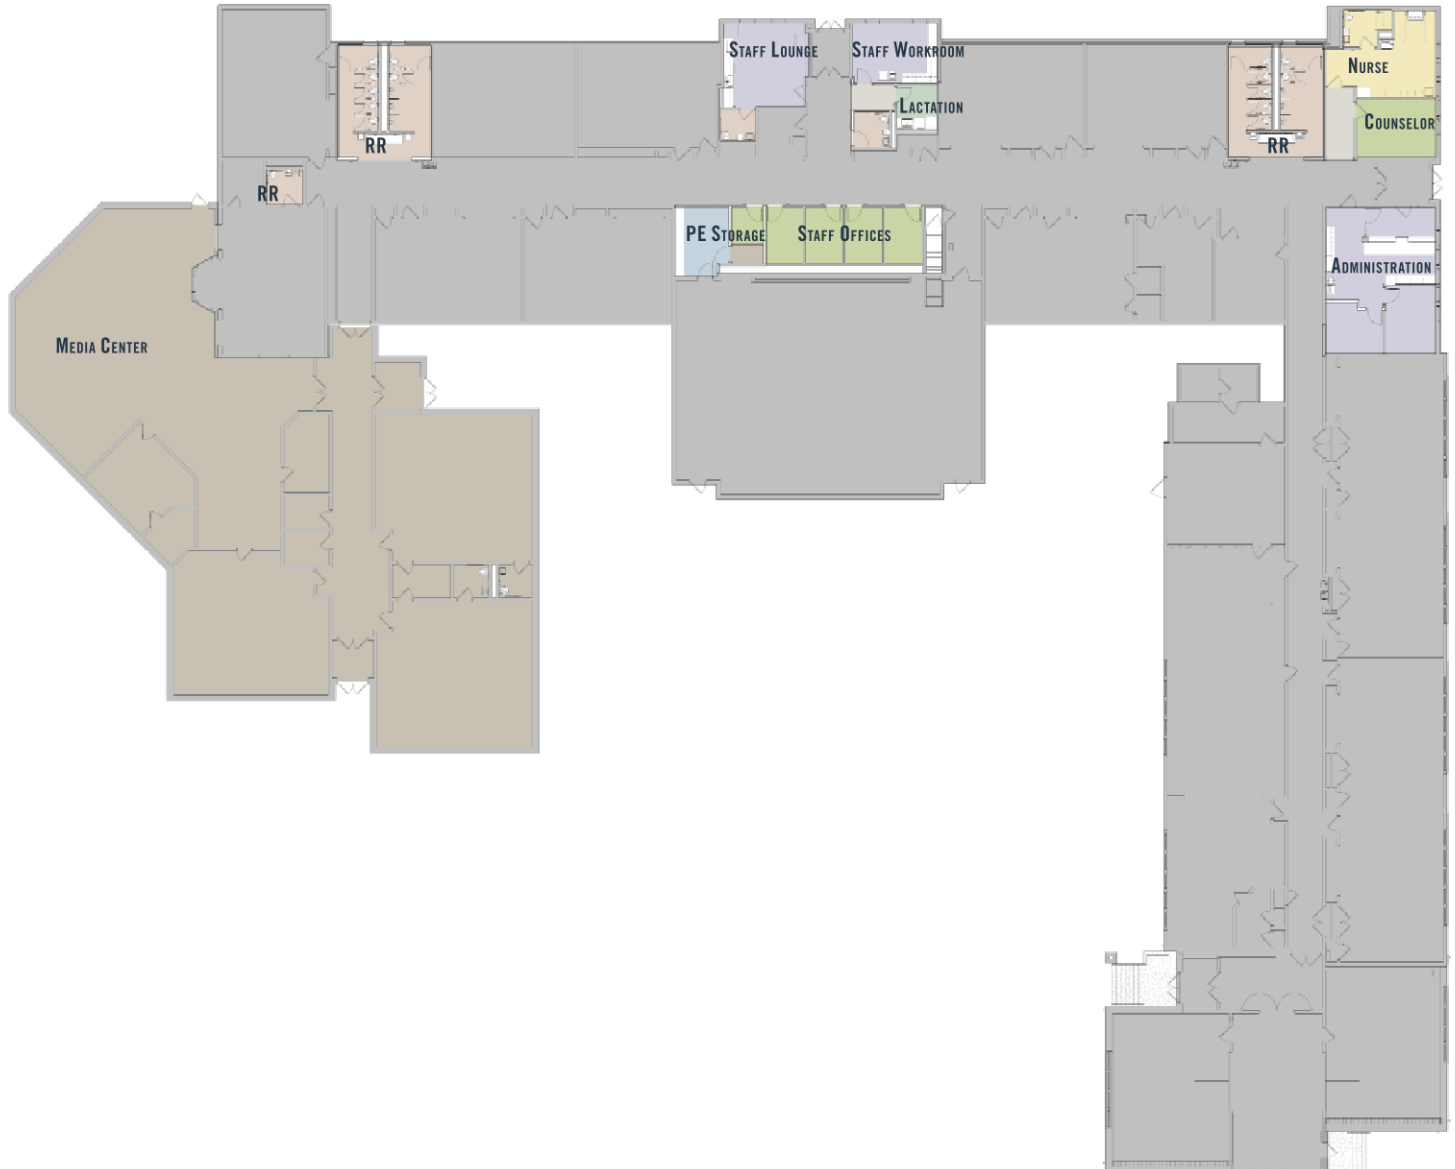

Overall Floor Plan

**WEEKLY
PROGRESS
REPORT**

**Doniphan, Franklin, and Ridgeview
Summer Renovation Projects
Liberty Public Schools**



7/12/24

PROJECT STATUS

- Doniphan, Franklin, and Ridgeview:
- Completed Demolition
 - Completed Wall Framing
 - Ridgeview HVAC Equip. Install
 - Continued MEP Overhead/In Wall Rough-In
 - Continued Drywall Install/Finishing
 - Began Paint
 - Began Tile Install
 - Began Ceiling Grid Install

UPCOMING

- Doniphan, Franklin, and Ridgeview:
- Complete MEP Install
 - Complete Drywall Install
 - Complete Ceiling Grid Install
 - Complete Paint
 - Complete Tile
 - Complete Casework Install
 - Complete Flooring Install
 - Complete Epoxy Install
 - Complete Specialties Install

Project Completion: August 2024



Franklin - Main Office



Franklin - Restrooms



Franklin - Staff Lounge



Ridgeview - Level 2 Restroom



Ridgeview - Corridor MEP Install



Ridgeview - Main Office



Doniphan - Staff Lounge



Doniphan - SPED Restroom Remodel
